

District Report

Dhading

27 July – 3 August 2017

Activity Summary

HRRP

❖ Distribution of Info Pack to all Government Agency

Info Pack Include following Documents

- ii) Meeting Minute of 18th July 2017.
- iii) District profile as of 10th July 2017
- iv) Weekly bulletin of 24th and 31st July 2017.
- v) Field visit report of Salyantar.

We have distributed and shared info pack to given government key stake holders like;

CDO	-Mr.Mahesh Acharya
DFO	- Mr. Yamanth Poudel
DCC Planning officer	- Yubraj Acharya
Asst. Mayor	- Mr. Man Raj Bhandari
DUDBC SDE	- Er. Dillip Bhandari
NRA Chief	- Er. Rabi Panjiyar

❖ Regular Meeting with all government Agency

❖ Field Visit at Salyantar

❖ Collection of Building Typology

Upcoming Events & Meetings

HRRP

Technical Coordination Meeting – 2017/08/08

Partner Organizations

CCCM training at Gorkha district by IOM to all major government bodies of Dhading and HRRP from 15th August to 17th August, 2017.

News & Updates

[Protest from Niklantha Municipality at District Coordination Committee for not having proper Official Building for work from 2nd August, 2017. Municipality wants to take District Coordination Committee building as their office building so they wanted DCC to shift somewhere but DCC is not agree for this] Some Snap are attached here.



Field Visit Report

Objective

■ Reconstruction progress and overview

Salyantar VDC has plain land area in comparison to other neighboring VDCs. As it is well connected with road access, it has been the major center area for settlement. At least 43 families of Kapurgaun of Lapa were taking shelter at open pasture of Pauwa, Salyantar- 1 after their home village was ravaged by the April 25 earthquake till March, 2016. Most of beneficiaries of Salyantar VDC are focused for construction of RCC designed buildings. This field visit gave an opportunity of observing current reconstruction of Salyantar VDC.

■ Interaction with implementing partners and local people

With the help of MoFALD-DLPIU enrolment data till date, Salyantar VDC has 1750 enrolled beneficiaries out of which the received number of first installment of grant is 1489 HHs. Accordingly of which only 5 HHs has received the second grant. The visit provided chances to find enquiries and verify them as per our information. Open conversation was made between local people and interactive talks were carried out regarding reconstruction and related issues. People were unaware of when in future for receiving further tranches.

● Observation of newly constructed houses

During the visit, HRRP saw that houses at Salyantar VDC are being built using rod, cement and bricks. People seem to follow RCC structured houses. A concept has been built that pillar system houses are much stronger than traditional ones. This has led to promote RCC structure houses within the VDC. Having some benefits out of it, there are hidden disadvantages as well. RCC structured houses requires specific materials without which it may be impossible to construct. Such materials are very costly at such places due to difficulty of transportation. The beneficiaries will have to spend high amount of money to build them.

Date	Location	Participants
27 th July, 2017	Salyantar	PrabinGautam, Chandrakantalal Karna



[General Coordination Meeting Photos and caption]



[Site Photos]

Challenges and issues identified

- Inconsistency in decision of Government body.
- NRA lengthy approval process (community buildings, mason trainings, Shelter).
- Difficulty in selection of beneficiary during training, community building construction, etc.
- Less coverage of VDC area by organization in particular location.
- Water scarcity hindering the construction of buildings at villages.
- Unavailability of government engineers for technical support to beneficiaries at municipalities and rural municipalities.
- Challenge in transportation of construction materials at most of the areas of Dhading.
- High number of non-compliance houses at rural-municipality and even at municipalities.
- Lack of monitoring of trained masons at their locality.
- Different perception and view of newly elected ward leaders has created obstacles in work as they have high expectation from Partner Organizations (POs).
- Due to inconsistency in transportation rate, the construction cost hikes with it.

Housing Typology Report



[Salyantar]
Load Bearing Structure
[Remarks]



[Salyantar]
[Brick masonry with mud mortar]
[Remarks]



[Salyantar]
[RCC structure with brick masonry in cement mortar]
[Remarks]



[Salyantar]
[Earthquake resilience bldg, brick masonry in cement mortar]
[Remarks]



[Dhading Nilkantha Municipality]
RCC Structure
[Remarks]



[Dhading Nilkantha Municipality]
RCC Structure
[Remarks]



[Salyantar]
[Tripura Sundari Gaupalika Office]


Questions Collected

Key Questions details


During the visit and meeting the following questions were asked:

S. No.	Question	Asked by	Response provided
1	When will the government provide us 2 nd tranche ?	Salyantar-8, local people	Team: Government will provide you the 2 nd installment grant once you have completed the plinth level construction and call NRA engineers to inspect it. Once it confirms that the house is OK for further proceeding, and then you will be illegible and be able to get the money.
2	Will there be any support in transportation of materials at this location as the cost of materials goes up with transportation?	An earthquake affected locals.	We have not heard of this provision now but will convey this message to relevant district authorities.

Non Compliance Cases in Dhading

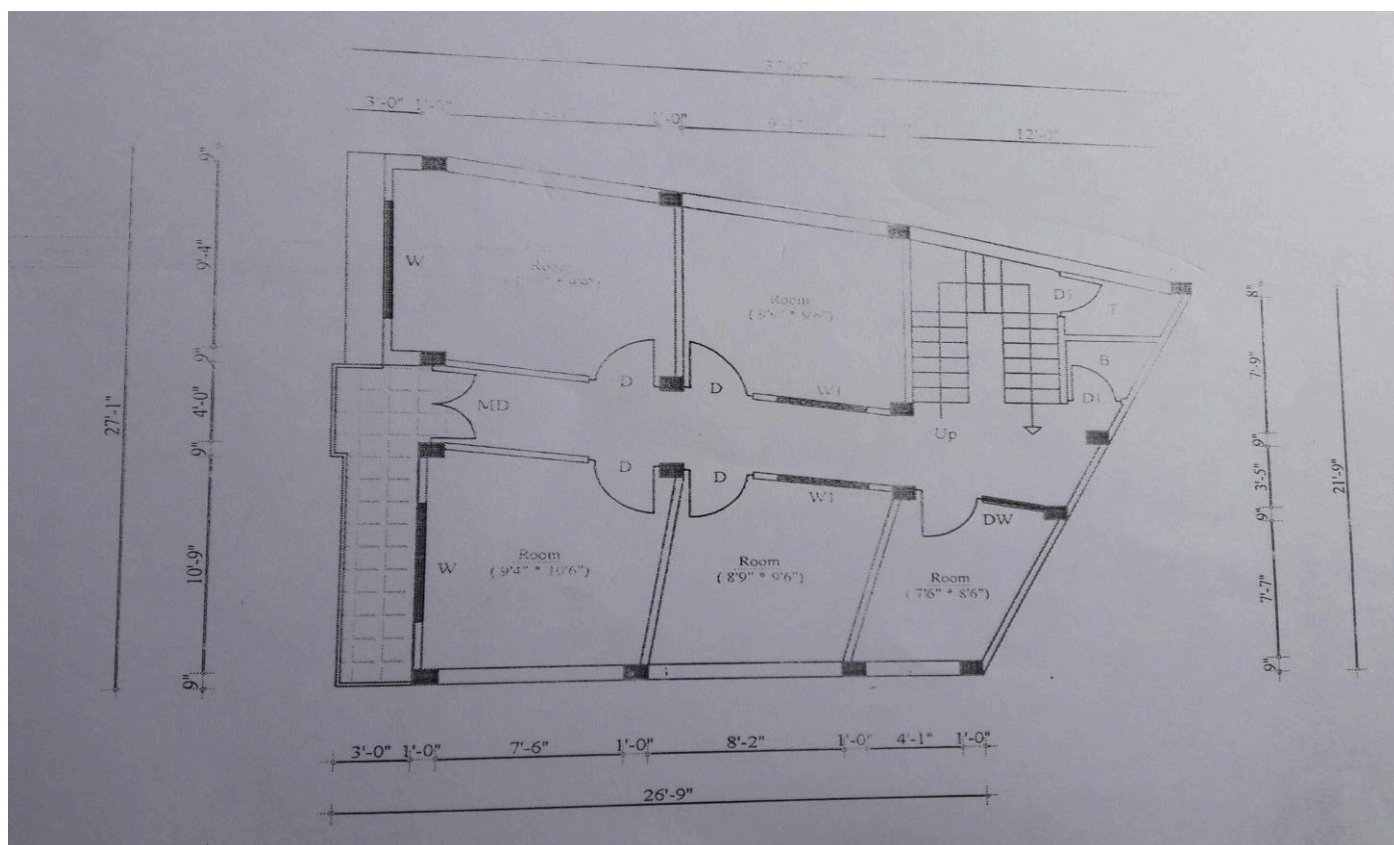

3 Storey RCC building, Column are not in same Grid

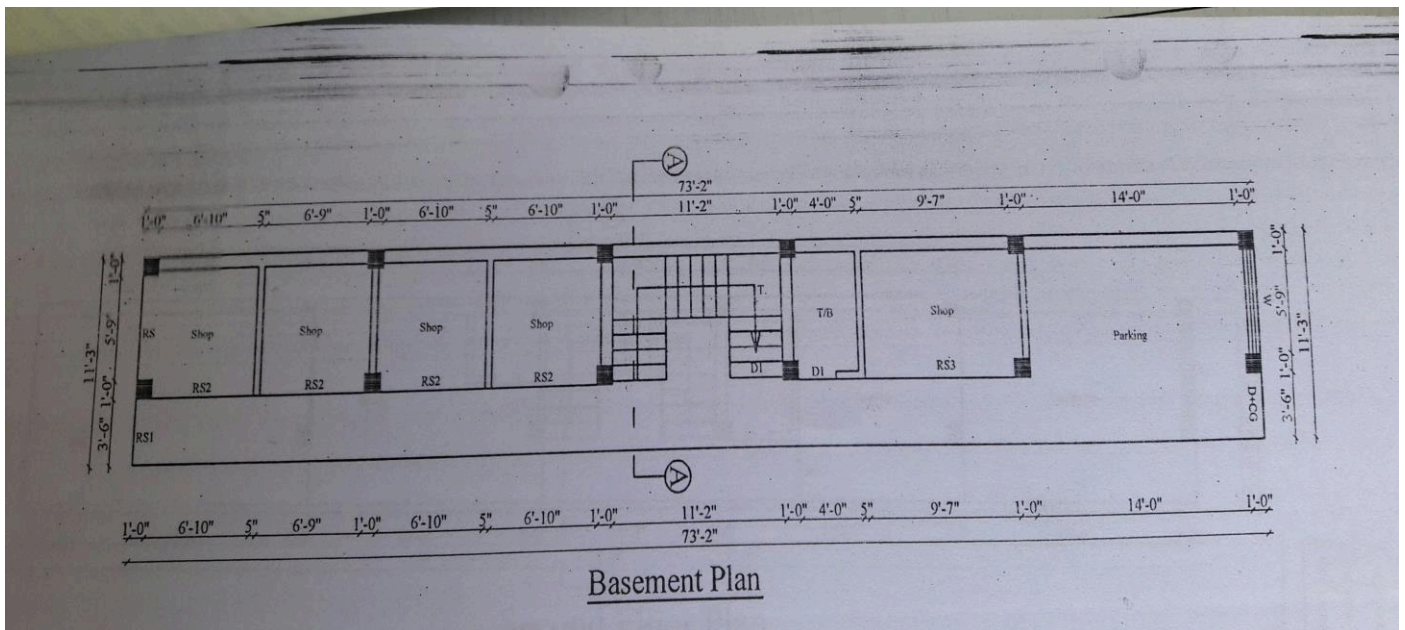

1 Bay Building (11'3"x73') Four Storey building

