


FACTS AND FIGURES

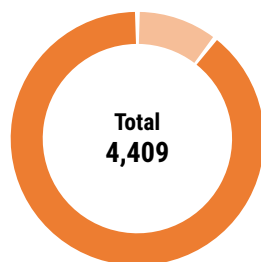

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Adobe Structures	42.64%	34.86%
Brick and Mud Mortar Masonry	30.09%	18.14%
Stone and Mud Mortar Masonry	16.97%	39.28%
Brick and Cement Mortar Masonry	6.04%	4.51%
Others	4.27%	3.22%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	3,669
PA Agreement	3,096
I st Tranche received	3,068
II nd Tranche received	858
III rd Tranche received	711

Houses

Under Construction: -

Completed: -

Retrofitting Status

Total Eligible HHs	83
PA Agreement	31
I st Tranche received	29
II nd Tranche received	83

Grievances

Registered: 927

Addressed: 822

Non-compliances

Registered: -

Addressed: -

Data Updated on: 2019-05-16 00:00:00

P0 Presence

Active: No POs Reported

Phased Out: DCA (DRM) , DCA (Education) , DCA (Livelihood) , DCA (Health) , DCA (Shelter) , DCA (Hygiene) , LUMANTI (Shelter) , LUMANTI (Hygiene) , NRCS (Agriculture) , NRCS (Education) , NRCS (Livelihood) , NRCS (Health) , NRCS (Shelter) , NRCS (Hygiene) , NYF (Health) , OXFAM-GB (Shelter) , PLAN (GESI)

OTHER SECTORS



Schools

Damaged: 20
Under Construction: 15
Construction Completed: 15



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	19,483	-	-
Aggregate	m ³	18,875	-	-
Sand	m ³	2,070	-	-
Timber	cu. ft.	2,351	-	-
Cement (PPC)	Sack	-	-	-
Cement (OPC)	Sack	62,796	-	-
Rebars	kgs.	212,964	-	-
Tin	bundle	2,565	-	-
Bricks	pcs.	285,121	-	-

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

-/-
-/-

KEY CONTACTS

Municipal Office

Rameshwor Shrestha
Mayor
9851201654

Municipal Office

Angana Shrestha
Focal Person
9841100837

Municipal Office

Nirmala Thapa
Deputy Mayor
9851202654

GMA/INRA

Bir Bahadur Rawal
NRA Chief-District
9851201088

Municipal Office

Laxmi Prasad Regmi
Administration Officer
9851250015

DLPIU-Building

Chandra Kaji Gurung
DUDBC.DLPIU Chief
9841576783

HHs WITH LAND ISSUES

No Reported Land Issues

STATUS OF TECHNICAL STAFF

Staff	Available Nos.	Additional Req. Nos.
Engineers	10	-
Sub-Engineers	3	1
Asst. Sub-Engineers	-	2
Masons	- (7 days) 18 (50 days)	- (7 days) 133 (50 days)


Source: Municipal survey

MASON TRAINING

Trainings (# out of total required)

7 days Training

50 days Vocational Training




Reached

Remaining

Source: HRRP Analysis

TA ACTIVITIES MAP

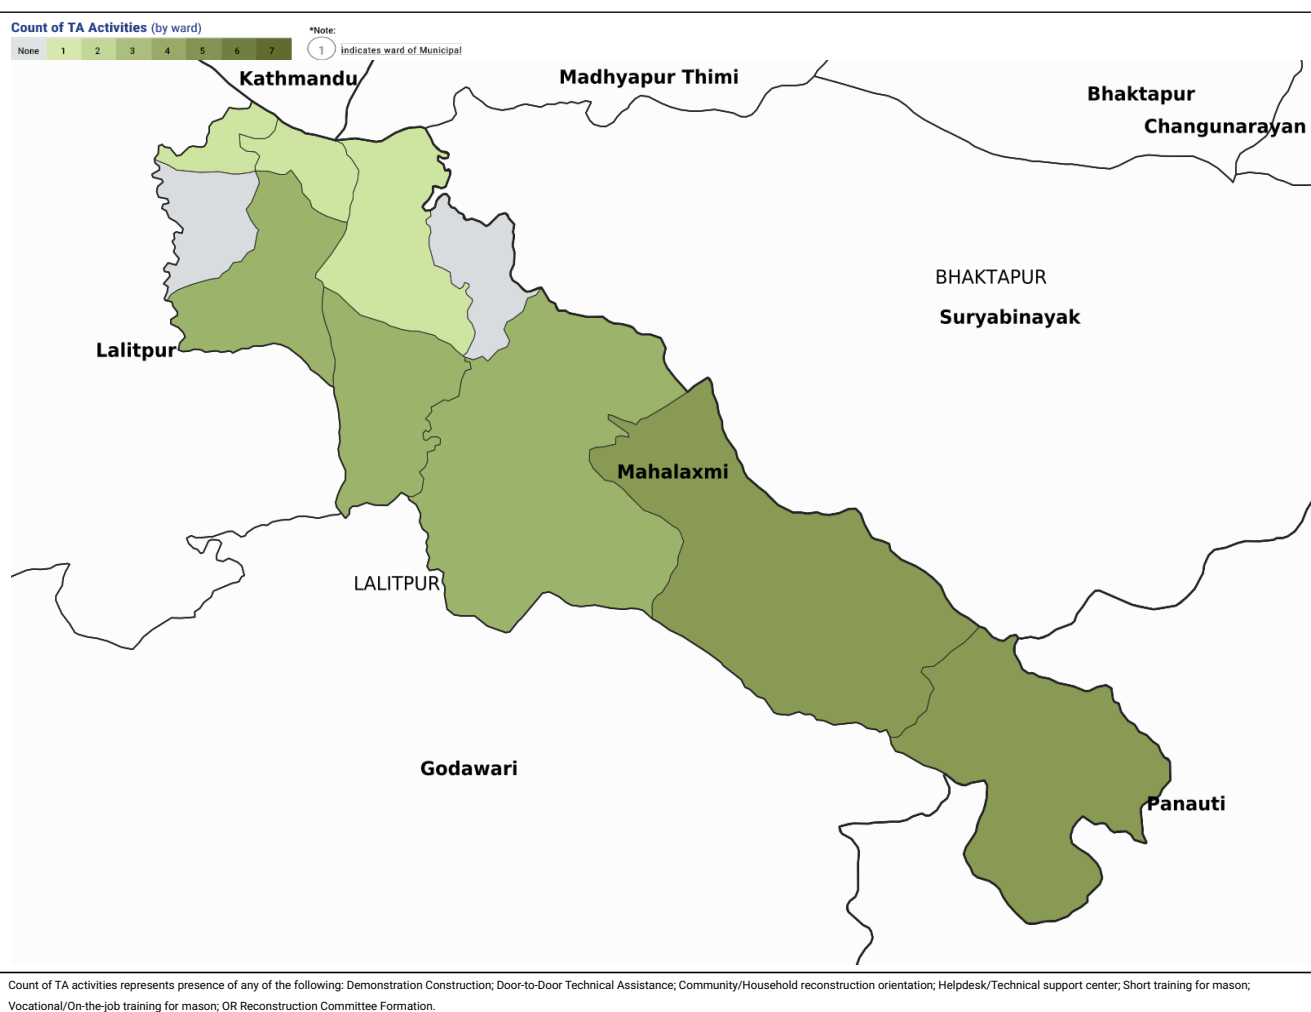

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. Ambika Amatya (District Coordinator) 9841356409 2. (District Technical Officer) 9861796464 3. Sachin Malego (District Information Management Officer) 9849166793
