

District Report

Nuwakot

15 March – 11 April 2019

Summary of events during this period					
Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Palika Level Reconstruction Planning preparation and follow up the upload to respective Plika's website. 2 Municipality and 10 Rural Municipality have uploaded to website and send signed copy to HRRP	March 15 , 2019			dc.nuwakot@hrrpnepal.org	
Meeting with Partners and GMALI for good Coordination.	March-18-20			dc.nuwakot@hrrpnepal.org	
Visit to DUDBC for for tranhe update.	March- 22			dc.nuwakot@hrrpnepal.org	
Contact and calendar update	March 26			dc.nuwakot@hrrpnepal.org	
District Coordination Meeting: Purnima Project (UK AID) is working for mainly 4 components in Shivapuri, Dupcheswar and Tadi Rural Municipalities: a. Technical Assistance to Palika: b. Support to Reconstruction: c. Private sector support: d. Leave no Behind. Oxfam and its implementing partners are working for relocating family from Lachyang, Urleni Bhalche, Kimatang, Gyangphedi and Rasuwa. Lachyang, Urleni and Bhalche are in final stage and plan to complete with in June 2019. UNOPS/Government of India is working support to Housing Reconstruction in Nuwakot district has started to work from March 2018. It has plan to support to 23088hh as STFC service and others. 174 GOI beneficiaries have received banking support. 91 have	March 28 , 2019	15	1	dc.nuwakot@hrrpnepal.org	Meeting Minute

Summary of events during this period

received support to obtain building permits and 844 have received drawings. Total no visited TSC are 7625 and 5301 beneficiaries have visited TSCs.					
Meeting with GMALI and UNOPS Team				dc.nuwakot@hrrpnepal.org	
Field Visit: Meghang RM ward no 5 and 6, Samari.	April 9-10			dc.nuwakot@hrrpnepal.org	<i>See detail in field visit Section</i>
Ward Level Meeting: Meghang Rural Municipality ward no 3. Chairperson Ram Bdr Tamang has claimed that 85 percent of reconstruction has completed in ward on 5. The meeting has concluded to search the beneficiaries who are not enrolled and not received 2 nd tranche yet. The ward engineers and UNOPS focal person will prepare a report and send to Ward and GMALI.	April 9, 2019	6	0	dc.nuwakot@hrrpnepal.org	
Meeting with UK AID Team: INGO and Local partners who are implementing different projects in Rasuwa and Nuwakot. Most of the projects are related to water supply and sanitation. Purnima project is recently started in Rasuwa and Nuwakot though most of the WSS projects are on conclusion through ACF, OXFAM, Save the children.	April 11			dc.nuwakot@hrrpnepal.org	

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location	Organizer	Contact Person
District Level Coordination Meeting		HRRP Nuwakot	dc.nuwakot@hrrpnepal.org

Tranche Status												
Rural /Municipality	Belkotgadhi NP	Bidur NP	Dupcheshwor RM	Kakani RM	Kispang RM	Likhu RM	Meghang RM	Panchkanya RM	Shivapuri RM	Suryagadhi RM	Tadi RM	Tarkeshwaor Rm
Total HHs Surveyed	9409	11203	5448	6157	1816	4003	4052	3692	5616	4197	4231	3760
Total HHs Eligible	11037	12893	5873	6916	4788	5109	4510	4460	6514	5019	4590	4707
Total HHs Enrolled	10348	11960	5661	6395	4510	4726	4263	4239	6108	4879	4468	4318
First Tranche	10348	11960	5661	6395	4274	4726	4263	4239	6108	4879	4468	4318
Second Tranche	8923	10578	5346	5598	3872	3817	3992	3687	5249	4151	4096	3874
Third Tranche	3022	7093	4051	3466	2693	2631	3522	2509	3592	2599	3095	3082
Total HH Constructed												
Grievance Registered	2271	1693	425	1389	809	1329	511	910	995	923	701	672
Grievance Addressed	1627	1464	425	759	553	1104	448	534	897	822	373	593
RF HH Eligible	256	236	35	160	25	154	141	88	63	16	23	247
RF HH Enrolled		18	1	44		9		18	1	44		9
RF 1 st Tranche		18	1	44		9		18	1	44		9

as of April 3, 2019.


Source: GMALI Nuwakot

Graph of Tranche Status:

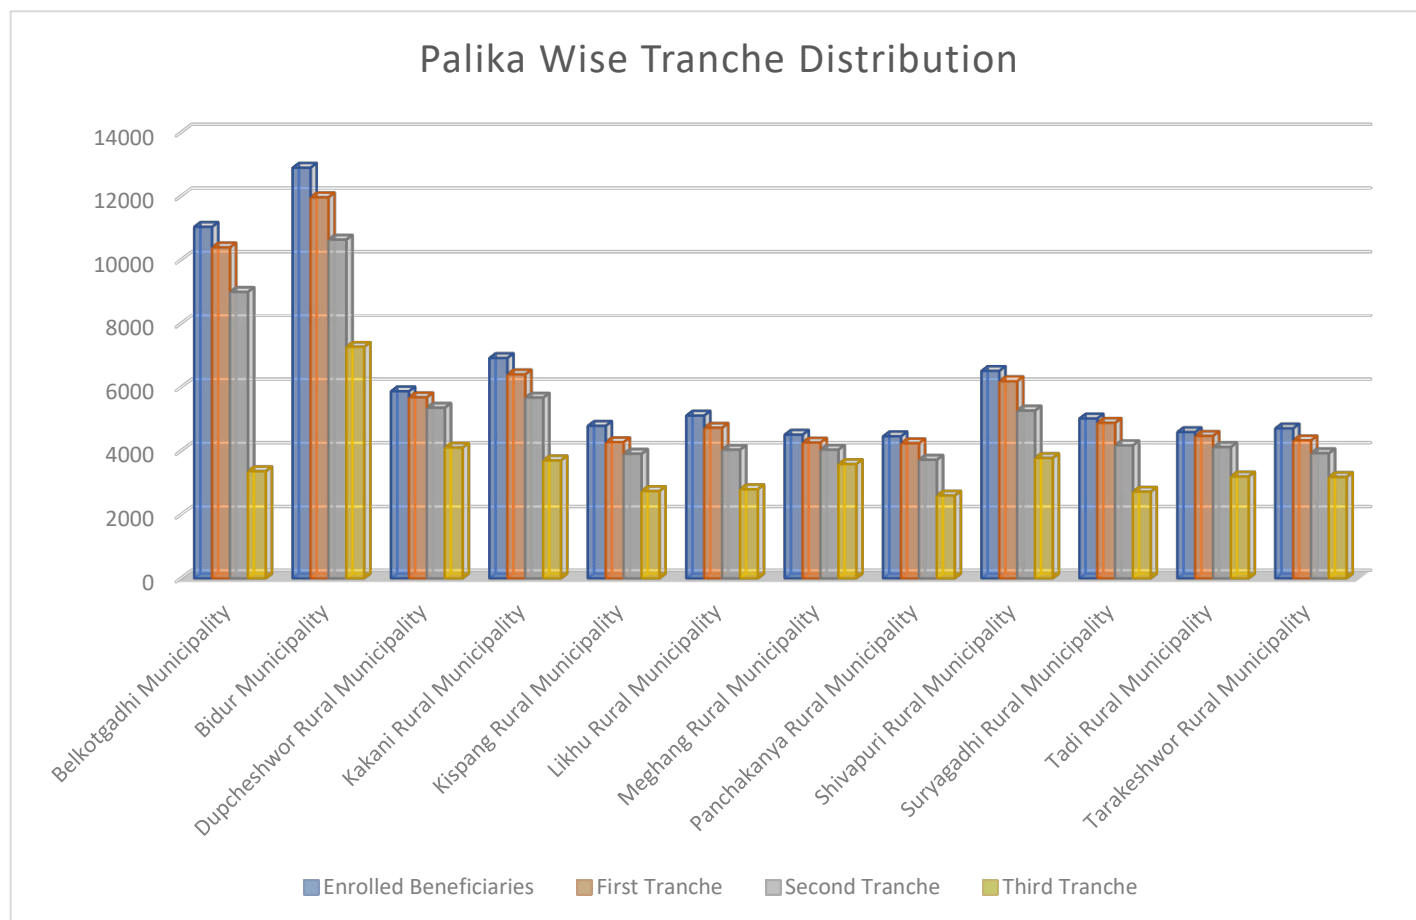

Graph for Retrofitting Status: NA

Graph for Grievance Status:

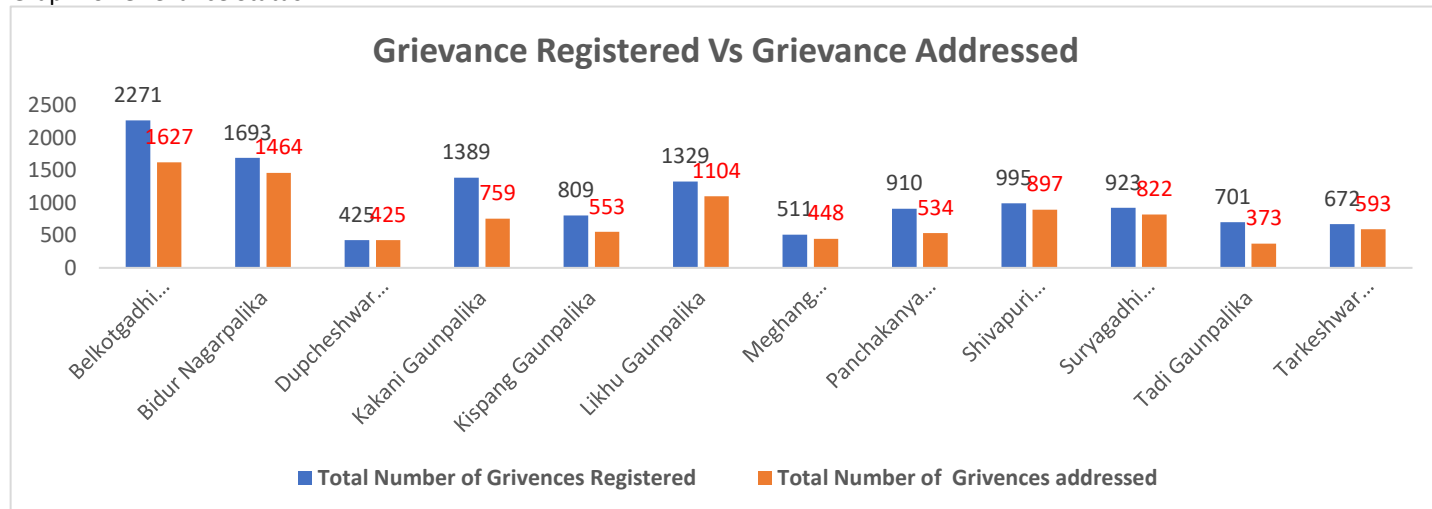

Field Visit /Joint Field Monitoring Visit Reports

Visit 1			
Date	Location	Participants from HRRP and stakeholders	
April 9-10, 2019	Meghang Rural Municipality Ward no 5-6, Samari, Jorchautar a	• Badri Pyakurel, DC HRRP • Satyanarayan Chaudhari, M&E Specialist Gmali Nuwakot • Kiran Shrestha, AFP/UNOPS	
Objective(s)			
• Objective 1: Monitoring of Field level and ward level Meeting • Objective 2: To know the reconstruction trend and highlighting the issues related to grant • Objective 3: To understand the field challenges and best practice			
Summary			
Samari VDC is now falls under Meghang Rural Municipality ward on 5 &6. Ward no 5 (Former wards 1,4,7,8,9), Meghang 6 (Former wards 2, 3, 5, 6). It has 1439 eligible beneficiaries got first tranche, 1403 have received second tranche and 1189 have received third tranche and 70 have approved for 3rd tranche. As per the data progress of reconstruction has quite satisfied. UNOPS is supporting for socio technical support through technical center. We can find some issue on reconstruction as the other place of district. Majority of construction in rural is a challenging issue of quality construction which may lead to non-compliance construction which called their own house. We find some house started to change in vertical and horizontal expansion after getting 3rd tranche that can be burning issue.			
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Quality Construction	Regular monitoring and develop the policy not to approve one room who are not eligible.	technical and RM/Ward Office	Regular
Changed of Houses into non compliance	Monitoring before issue the construction completion certificate and other facility.	POs, Ward offices	Regular
Support to Vulnerable People	Pos and governmental Office should keep priority to support Vulnerable people who are beyond the construction.	POs and NRA	Regular
Photos			
			
Ward Level meeting: Chairperson Ram Bdr. Tamang has chaired the meeting. The meeting has concluded to		Beneficiaries Name: Madhav Sapkota and Dichuk Sapkota.	

search the beneficiaries who are not enrolled and not received 2nd tranche yet. The ward engineers and UNOPS focal person will prepare a report and send to Ward and GMALI.


Address: Meghang-6, Nuwakot
The house is seemed one but it is owned by two beneficiaries. Owner claimed that they merged and made upstairs after getting 3rd tranche.

Housing Typology Report



House Owner: Rameshwar Khadka
Location: Meghang-5, Samari
Typology: BMC with Attic
Tranche Status: received third tranche

Photo: Badri Pyakurel

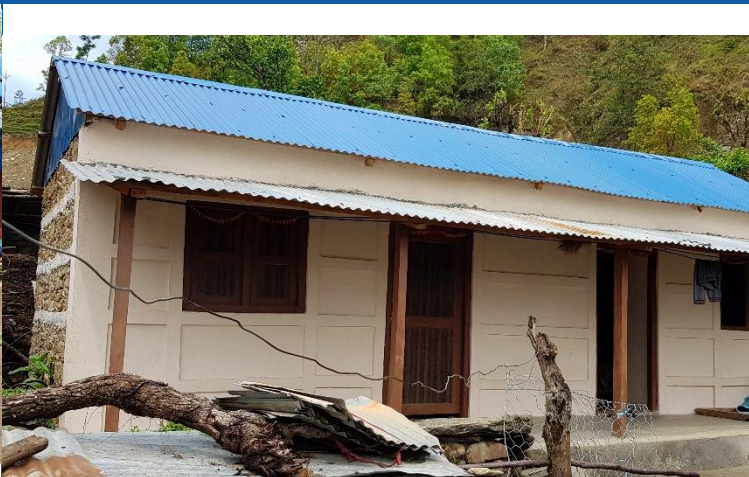

House Owner: Sanuraj Shakya
Location: Meghang-5, Kavrebas
Typology: Stone Mud Mortar
Tranche Status: received third tranche

Photo: Badri Pyakurel



House Owner: Kokila Thapa
Location: Meghang-5, Samari
Typology: BMC
Tranche Status: received third tranche

Photo: Badri Pyakurel



House Owner: Shyam Sapkota
Location: Meghang-6, Jorchautara
Typology: BMC
Tranche Status: has applied for 2nd tranche. (the beneficiaries has disability) UnOPS/GOI has conducted OJT for the construction.

Photo: Badri Pyakurel



House Owner: Krishna Prasad Sapkota

Location: Meghang-6, Jorchautara

Typology: BMC (Roof is not stable)

Tranche Status: waiting for 3rd tranche

Photo: Badri Pyakurel

Case Story

Drinking Water: A Journey for Water

Kharanitar, a busy area of Tadi Rural Municipality is strongly hit by water scarcity few years back. The community disputes and arguments were common in the area for drinking and irrigation water. After the devastating earthquake, the water scarcity problem further worsen and the community member started moving early in the morning and evening for drinking water for more than 15 minutes.

The day becomes the happiest to the local communities when Rural Municipality, CARDSDN, Oxfam International and Purnima Project signed an agreement for the construction of the water supply scheme at Kharanitar. “It was my fortune that i am again working for the same project that was started by my father 20 years back,” said the Rural Municipality Chairperson, Mr. Narayan Pandey with smile in his face. This will benefit 384 households in this area including 71 Households displaced communities residing in the integrated settlement at Budune, Kharanitar.

The households at Kharanitar who were drinking water from distance and few from the community tap are now provided with yard connection. Ram Maya Upreti, Local Beneficiary expressed her happiness that we are now

provided with household tap and now i hope that we need not argue for the drinking water in coming days nor we have to spend our time on collecting and fetching water from nearby jungle.

The water scheme is important not only to the local communities at the Kharanitar area but also to the earthquake affected displaced communities who are busy in building their house in integrated settlement area, Budune. “We are internally displaced by Earthquake and Landslide. We are afraid that water will be very big problem to our community, Said Nar Bahadur Tamang, Chairperson of Budune Integrated Settlement. He further added that the help from local authority, community and agencies contributed a lot to overcome the various problems including drinking water.



Figure 1 : Intake protection at Kharanitar Drinking Water Supply Scheme



Figure 2 : 33 Cum RVT at Kharanitar Drinking Water Supply Scheme

The local communities are happy that they will be getting drinking water at their homes with the structures constructed at the scheme. A sedimentation tank for settling the sand and other dust particles and 5 RVTs of various sizes from 5 Cubic Meter, 14 Cubic Meter, 18 Cubic Meter, 20 Cubic Meter and 33 cubic meter will be very useful and enough to serve the water of Kharanitar and Budune, Said the technical person from CARDSDN, Mr. Marichman Rawat. Tarrif collection, provision of village maintenance worker and linkage with Rural Municipality and Ward help in the sustainability of the project, he further added.
