

Monthly District Report

Makwanpur, Chitwan, Nawalparasi

27 September - 21 October 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Makwanpur	To participate in the one day seminar on "Private Housing Reconstruction" at Hetauda, Makwanpur.	16 th Oct, 2019	Hetauda, Makwanpur	makwanpur@hrrpnepal.org	Click for event photos and action plan
	District Facilitation committee Meeting of Reconstruction	20 th Oct, 2019	DCC Hall, Hetauda	makwanpur@hrrpnepal.org	Minute click here..
	GMaLI Regular meeting with involvement of all staffs	17 th Oct, 2019	GMaLI office, Hetauda	makwanpur@hrrpnepal.org	Minute click here...
	Joint meeting between DLPIUs Building and GmaLI	18 th Oct, 2019	GMaLI office, Hetauda	makwanpur@hrrpnepal.org	Meeting minute click here..
	Update Palika Profile data of Makwanpur	18 th Oct, 2019			
	Contact list updated in GD	18 th Oct, 2019			Contact List
Chitwan	Contact list updated in GD	18 th Oct, 2019		chitwan@hrrpnepal.org	Contact List
	Update Palika Profile data of Nawalpur	18 th Oct, 2019			Palika Profile Data
Nawalpur	Contact list updated in GD	18 th Oct, 2019		nawalparasi@hrrpnepal.org	Contact List
	Update Palika Profile data of Nawalpur	18 th Oct, 2019			Palika Profile Data

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
District Facilitation Meeting	Tentative 21 th Nov, 2019; DCC Hall, Hetauda, Makwanpur	DCC/GMaLI/HRRP	makwanpur@hrrpnepal.org
Joint Monitoring visit, follow up for action plan, status of retrofitting	12 th Nov to 14 th Nov, 2019	GMaLI/Building/HRRP	makwanpur@hrrpnepal.org

News & Updates

Makwanpur, around 75% reconstruction has been completed in private housing reconstruction sector with compared to PA signed but in retrofitting no any HHs received the second tranche. There are around 12K HHs eligible for retrofitting among them around 55% received the first tranche of retrofit but nobody have received the second tranche. Now, we have prepared action plan in the district from the one day orientation program. The seminar program was organized by central authority on 16th Oct, 2019. The program was fruitful for reconstruction because for action plan and start for its implementation.



Figure 1: Group photo after completed an orientation program on "Private Housing Reconstruction" on 16th Oct, 2019 at Hetauda, Makwanpur.



Figure 2: DCC Chief Mr. Raghu Nath Khulal speech about the latest issues and challenges of Makwanpur reconstruction during orientation program.

Task Force Update

Now, Task force has completed the half day orientation program in district for "Retrofit Task Force" on 23th Sept, 2019 at Hetauda, Makwanpur. There were around 25 technicians participated in the event from the different rural municipalities of Makwanpur district. The orientation program was facilitated by DLPIU Building and organized by NRA-DLPIU-GMaLI. The program was focused on retrofitting tasks and how to scaling up and how to achieve the target with current planning schedule. There were two sessions in the event; namely Data collection, Building Typology Categorization and retrofitting Methods with power point presentation. Similarly the second session was MIS non compliance issues and its solution.

The 1st session was presented by DSE and focused on the following points;

We are regularly reporting about challenges and issues of housing reconstruction and almost issues are addressed by NRA. We are continue working in retrofit for awareness programs, interaction with focal persons and also this program supported to us for retrofitting scaling up. The first session also focused on methods of retrofitting and retrofitting manual oriented. We concluded the following method are most suitable for our context where materials are easily available in the market, quick access for implemented by technicians and also access for beneficiaries and skilled manpower who are working in reconstruction.

- Concrete jacketing with steel bar mesh

- Jacketing with G.I. wire mesh and cement plaster

- Splint and Bandage: For masonry building with weak mortar like brick stone in mud building, Splint and Bandage method can be used to increase the strength of buildings and low cost materials like PP band/ gabion wire mesh jacketing can be done in remaining part to prevent local failure of masonry to make retrofit more economical.


Similarly second session was presented by DLPIU- Building MIS Specialist; He focused on how to complete the digitization with compliance. He clearly said, " we found the maximum errors in digitization so first priority is to reduce them".

Tranche Status (Makwanpur)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	6039	2512	2318	2309	1646	1168	2176	1489	1489	0
Bakaiya Gaunpalika	8593	4019	2687	2687	1882	1104	1960	668	668	0
Bhimphedi Gaunpalika	5236	2698	2227	2209	1857	1684	932	608	608	0
Hetauda Upamahanagarpalika	32696	6363	4947	4705	2853	2458	2024	1076	1076	0
Indrasarowar Gaunpalika	3726	2923	2581	2572	2049	1500	254	166	166	0
Kailash Gaunpalika	4737	2614	2157	1528	1238	998	731	390	390	0
Makawanpurgadhi Gaunpalika	5516	2216	1839	1814	1328	1041	1437	949	949	0
Manahari Gaunpalika	8841	2337	1287	1287	1059	917	1487	733	733	0
Raksirang Gaunpalika	5091	1715	1580	1580	1431	1157	576	467	467	0
Thaha Nagarpalika	10519	6919	6211	5465	4283	3106	1369	693	693	0

Graph of Tranche Status:

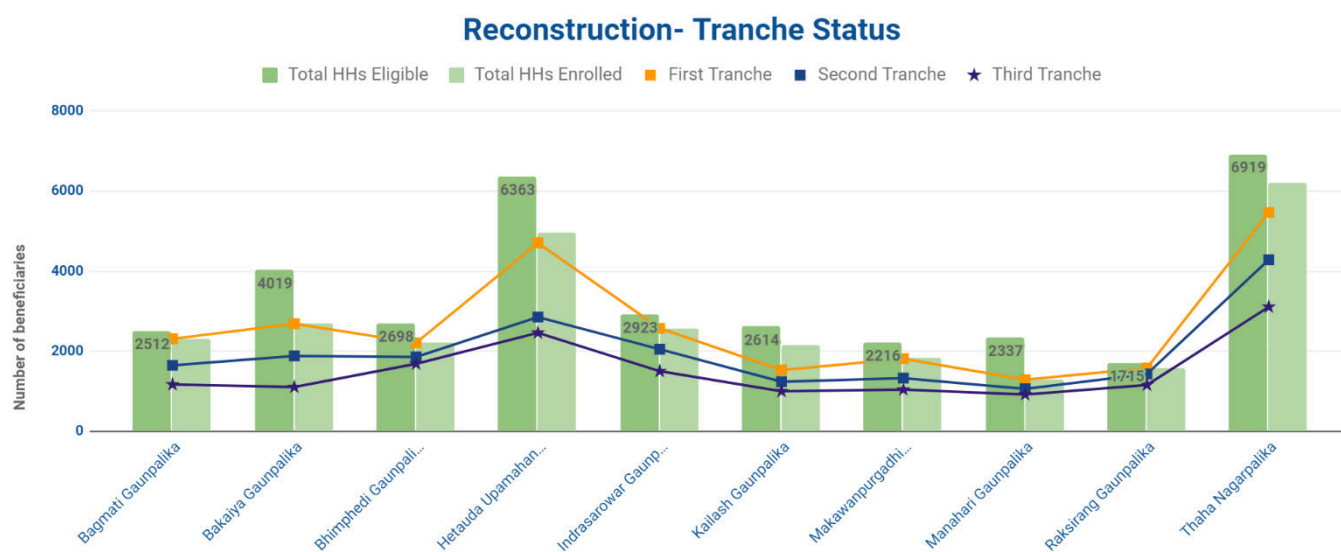

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

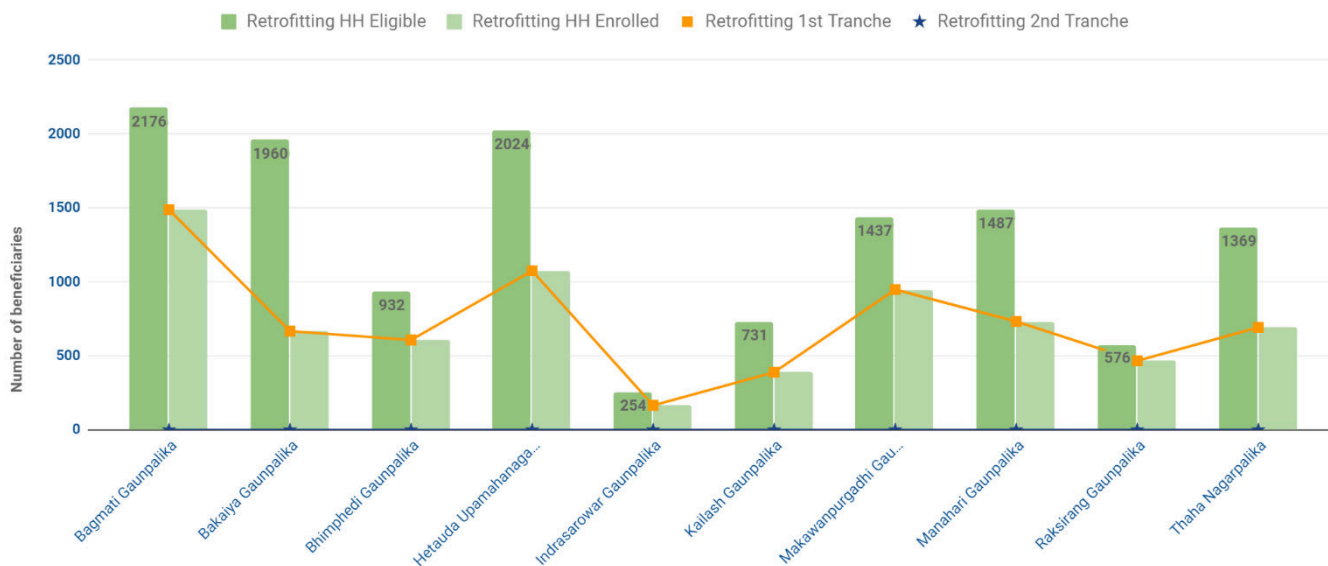


Tranche Status (Chitwan)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bharatpur Mahanagarpalika	2087	710	660	660	387	156	38	9	9	0
Ichchhyakamana Gaunpalika	3571	2353	2106	2106	1854	1366	248	196	196	0
Kalika Nagarpalika	2565	916	792	792	447	227	42	27	27	0
Khairahani Nagarpalika	1566	559	529	529	273	251	4	4	4	0
Madi Nagarpalika	123	23	23	23	21	16	15	13	13	0
Rapti Nagarpalika	3594	2043	1862	1862	898	578	71	18	18	0
Ratnanagar Nagarpalika	1763	731	657	657	425	381	175	164	164	0


Graph of Tranche Status:

Reconstruction- Tranche Status

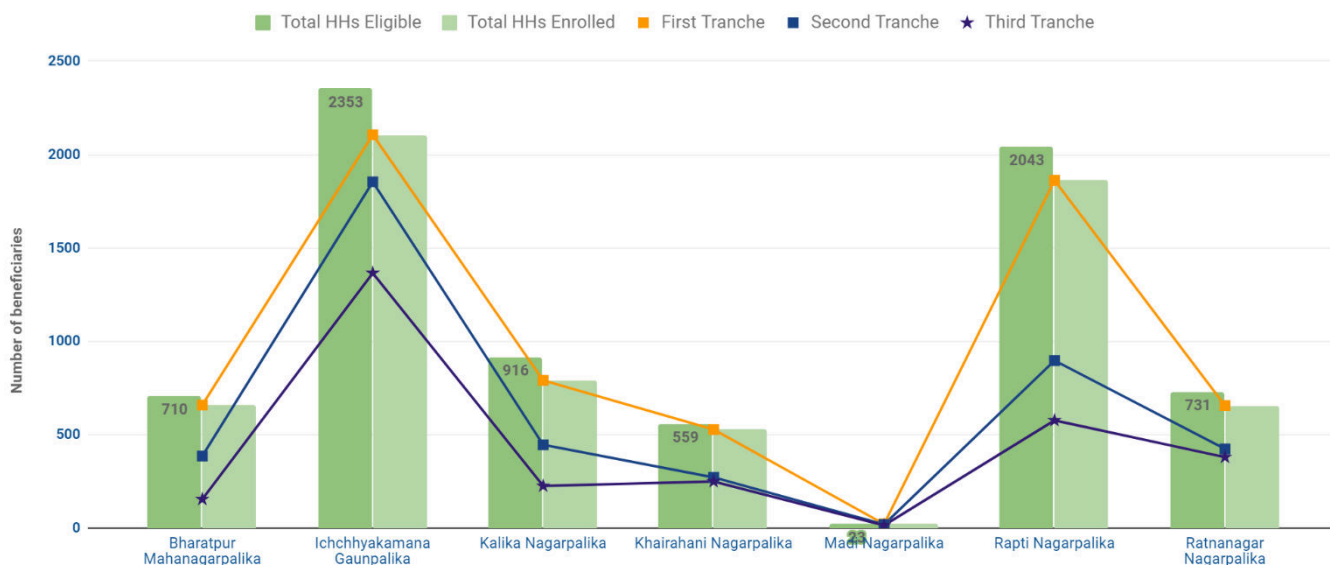

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

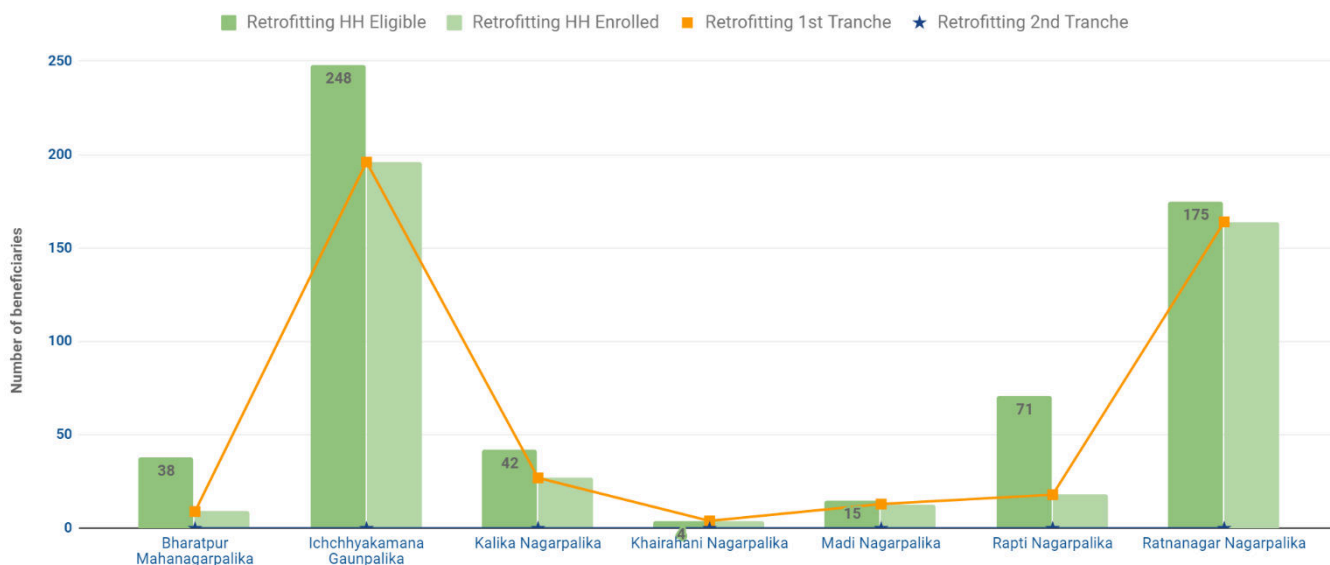


Tranche Status (Nawalparasi)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bardaghat Nagarpalika	4	4	4	4	4	3	0			
Binayee Tribeni Gaunpalika	70	66	66	65	65	56	2			
Bulingtar Gaunpalika	280	264	262	262	260	242	5			
Bungdikali Gaunpalika	133	72	72	72	67	67	1			
Devchuli Nagarpalika	177	177	177	177	171	156	1			
Gaidakot Nagarpalika	103	49	49	49	43	42	0			
Hupsekot Gaunpalika	155	139	139	139	134	108	2			
Kawasoti Nagarpalika	4	4	4	4	4	3	0			
Madhyabindu Nagarpalika	41	85	85	85	80	67	3			
Palhi Nandan Gaunpalika	1	4	4	4	3	3	0			
Pratappur Gaunpalika	6	3	3	3	3	3	0			
Ramgram Nagarpalika	3	1	0	0	0	0	0			
Sarawal Gaunpalika	4	4	3	3	2	0	0			
Sunwal Nagarpalika	2	2	2	2	2	1	0			
Susta Gaunpalika	2	3	3	3	2	1	0			


Graph of Tranche Status:

Reconstruction- Tranche Status

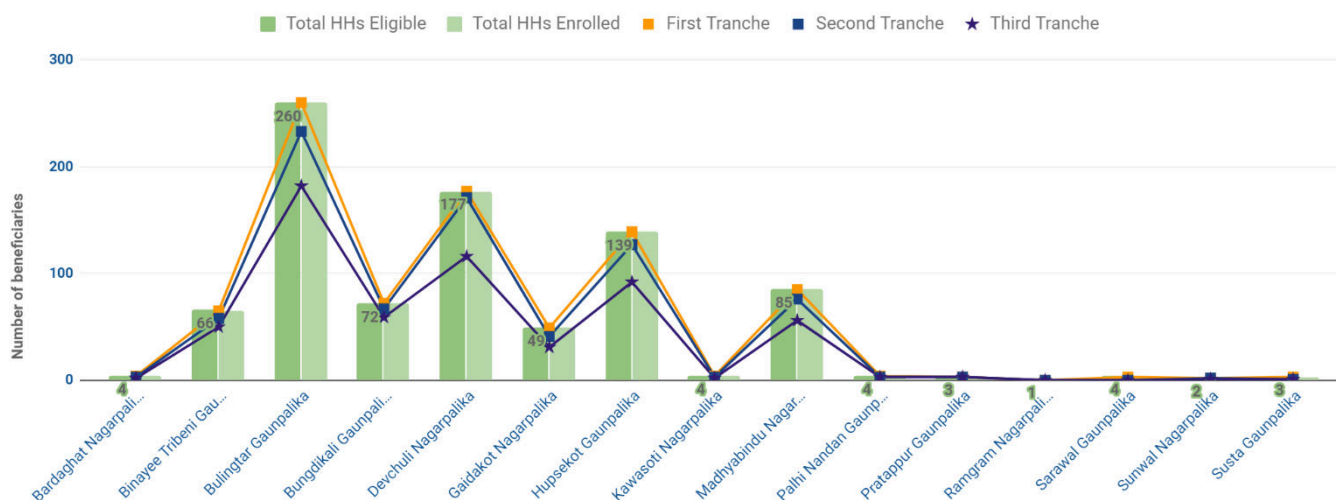

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

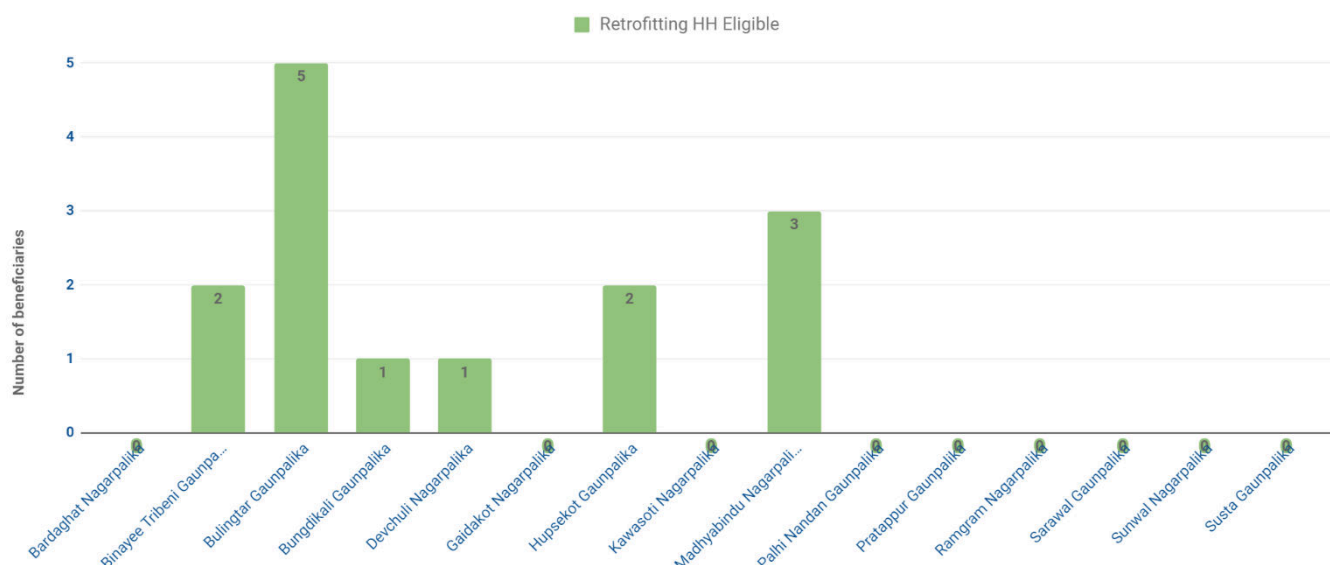

Retrofitting Status in Makwanpur;

DFID RETROFITTING SCALE UP model house has been constructed at four palikas of Makwanpur district namely Thaha Municipality, Bhimfedi Rural Municipality, Bakaiya Rural Municipality and Manhari Rural Municipality.

Name of Beneficiary	PA number	Palika	Ward
Jang Bahadur Jogi	R-31-9-9-0-0003	Manhari	9
Kanchi Bal	R-31-44-3-0008	Thaha	11
Man Bahadur Bal	R-31-7-4-0-0029	Bhimfedi	5
Prem Lal Ghising	R-31-5-4-0-0059	Bakaiya	4

Overall Retrofit progress, Makwanpur

Palikas	Engineers	Masons	Completed	Ongoing	Finalize to start	Total House
Manahari	10	5	1	0	0	1
Thaha	21	76	16	0	0	16
Bhimphedi	22	64	8	4	0	12
Bakaiya	11	5	0	1	0	1
Total	64	150	25	5	0	30

They have well done in retrofitting like as regular field visit; supervision, involvement of technicians and trained for masons; who have been involving in post-earthquake. We have been reporting of retrofitting while they had started the program and had suggested also for splint and bandage and also jacketing (GI wire Mesh/Steel/Wood) because of excess of technicians, retrofitting manual addressed the standards of norms and guide line and for similarities at all municipalities of district. So we request and suggestion these methods also should be implementation in grass root level as a demonstration.

Field Visit																							
Date		Location		Participants																			
21 th and 22 th Oct,2019		Kailash Rural Municipality-03, 07 (Previous Bharta and Kalikatar VDCs)		GMAI MIS Specialist, Social Development Specialist, Financial specialist, District Support Engineer, HRRP and CSRC.																			
Objective(s)		- To organize orientation program with presence of ward presidents, ward technicians and local government. - Sharing the information about latest prepared action plans, time line of reconstruction ,follow up retrofitting data update and carryout field visit.																					
Why was the visit carried out in this location?																							
- It was a duplication between 1st tranche received between NGOs and government so find out the real case in the field. - To organize the orientation programin palika with presence of all wards president, ward technicians and local government. - To follow up the retrofitting data collection and typology, to know the present status of reconstruction, status of CS entry and distribution of completion certificate. - To promote the digitized all documents; - To carry out field monitoring visit; collecting the housing typology, interaction with beneficiaries;																							
Summary																							
We have successfully completed an orientation program with presence of wards presidents, ward technicians and local government. There were around 30 participants in the event. The agendas were; information sharing of action plan, presentation of MIS data, presentation of DSE about retrofit issues and challenge and at second half wards president presented about challenge and issues in their respective wards. found that and conviance them, they are agreed about time line of reconstruction and action plan and also time line of retrofitting data collection. The reconstruction progress is rapidly increasing but in similar way, we could not find out that, there is not starting of the retrofitting. The rural municipality has not started completion certificate distribution and donot have maintain gap between I tranche and II tranche at Municipality. It is a vital problem in the overall wards of rural municipality. GMAI MIS specialist The progress of housing reconstruction is as follows with tabular forms; <table><tr><td>1st tranche received HHS</td><td>Verified for 2nd tranche HHS</td><td>Received HHS</td><td>2nd</td><td>Verified for 3rd tranche</td><td>Third tranche received HHS</td><td>Completed HHS</td><td>Remarks</td></tr><tr><td>2159</td><td>1950</td><td>1931</td><td></td><td>1670</td><td>1641</td><td>1550</td><td></td></tr></table>								1st tranche received HHS	Verified for 2nd tranche HHS	Received HHS	2nd	Verified for 3rd tranche	Third tranche received HHS	Completed HHS	Remarks	2159	1950	1931		1670	1641	1550	
1st tranche received HHS	Verified for 2nd tranche HHS	Received HHS	2nd	Verified for 3rd tranche	Third tranche received HHS	Completed HHS	Remarks																
2159	1950	1931		1670	1641	1550																	
Challenges / Issues Identified		Solutions Provided			Responsible		Timeframe																
Intentionally they have not started the reconstruction and waiting for his/her favor of time as well many beneficiaries have already houses.		Strongly implementation the time line of NRA and as well action plan, more to more communitie and information sharing to ward level. Conduct orientation program, awareness.			DLPIUs, Local Government, Ward technicians		Regular																
CS entry and certificate distribution		After final inspection and CS entry, planning to organize completion certificate distribution with in Bhadra Masant.			Local Government, Ward technicians		Regular																
Photos																							



Figure 1: Orientation program has conducted on private housing reconstruction on 21th Oct, 2019 at Kailash Rural Municipality.



Figure 2: Group photo took after the Interaction program at Kailash RM -8 previous Bharta VDC.

Housing Typology Report



Figure 1: House owner; Janak Lal Praja, the location of house is Kailash-07, load bearing stone in mud mortar, two rooms and it is compliant. All vertical reinforcement provided like as vertical post, horizontal members. The has verified for second tranche and already received first tranche.



Figure 2: House owner; Kumar Baruwal, location is Kailash Rural Municipality-03, this house lies in retrofit and beneficiary received first tranche and he does not have any idea about what is further process of retrofit. We suggested him now we are collecting the data and typology for retrofit. And he has agreed for retrofit. The situation of this house is 6rooms with two storey and an attic, gable wall is heavy material. For retrofit we have given suggestion how to constructed with suitable methodology. We recommended splint and bandage with GI wire mesh and remove the heavy gable wall and replace with light wall and replace the roof and also remove the more opening.



Figure 3: House owner Bishnu Praja, Kailash Rural Municipality-07, two rooms with planning one storey and an attic, flexible roof. Positive impact of NRA time line of private housing reconstruction. house owner received first tranche and he is waiting for second tranche and also his house is verified for second tranche. He is planning to use local materials like as stone in mud and locally available timber.

Figure 4: House owner; Sher Bdr Chepang, Kailash Rural Municipality-07, he is not a beneficiary of reconstruction but he has built his house with compliant himself. Hybrid structure: two types of materials used in ground floor stone in mud mortar with RCC band and in first floor he has used timber materials and finally his house is compliant like as connection is up to roof band and strongly connected to members. Light timber used in first floor with properly connected. It is good for us and good message deliver to community about how to construct earthquake resistant structure.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Before ashad, we received the all tranches around within 15-20 days but now dealy in tranche received and in some cases very far to receive tranche, what is problem in the tranche release process?	Kaiaash-09 ward president	We have been continuing for this work to deliver the tranche on time for starting and last 1.5year, we are continuing deliver from the district within around 20 days from the receive date of inspection form from the technicians/ward office. Also it was a gap between form fill up VS send date of file. Hope, we are continueing for deliver to process of tranche releases. We follow up in tranche tracking.

Challenges and Way Forward

Challenge	Way Forward
Retrofitting and its implementation	- Now, UNOPS/Build Change is constructing demonstration at every palikas of Makwanpur district with involving of ward technicians. But they have only one method of retrofitting such as strong back but it is not sufficient for filed. So it is necessary to technician's linkage with retrofitting manual for easy access of different method of retrofitting. Here is one method is common; splint and bandage with GI wire mesh so that also it gives the option to beneficiaries. May be technicians, skilled manpower and beneficiaries have motivate fast and they have quick access of materials and construction process. - For load bearing up to two storey and an attic clearly defined the retrofitting methodology so Refer the retrofitting manual for load bearing and RCC frame structure. We are collecting the data and typology for retrofit after that at starting month of Mangsir, we will start of construction. Necessity to organize an awareness program at different palikas of district. We have organized awareness program in Thaha Municipality with convince the beneficiaries but they don't believe on financial cost, material and methodology and also skilled manpower, we have not any skilled manpower in field. We have decision made for sample two house will have retrofitting.
Final inspection, CS entry and complete certificate distribution	Now the progress of CS entry is satisfactory and challenges is for minimize the errors. We found that

Challenges and Way Forward

Challenge	Way Forward
	maximum errors so reduce it is another important task of technicians. Now we can see in field the HHs is modified after received the all tranches so the distribution of completion certificate on time is next priorities of task.
Filtration of fake beneficiaries	• Much more beneficiaries may be lies on fake like as they have already shelter. Now, we have prepared action plan from the last one day orientation program. Timeline of reconstruction should be strickly implement as well action plan. Rapidly increase the monitoring visit, conduct orientation program in ward level and information sharing and time time to cmmunite in to ward level.
