

Monthly District Report

Makwanpur, Chitwan, Nawalpur, Parasi

14 June - 14 July 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Makwanpur	District Facilitation and Coordination Meeting	18 th June 2019	DCC Hall, Makwanpur, Hetauda Sub-Metropolitan	makwanpur@hrrpnepal.org	Meeting Minute click here..
	Update Palika Profile data of Makwanpur	7 th June 2019		makwanpur@hrrpnepal.org	Palika Profile Data
Chitwan	District Coordination Meeting	26 th June 2019	Chitwan GMaLi Hall	chitwan@hrrpnepal.org	Meeting Minute click here...
	Organized interaction program in GMALI DLPIU and Building DLPIU at Chitwan	24 th June, 2019		chitwan@hrrpnepal.org	
	Organized Technical Coordination Meeting in Plika level at Kalika Municipality	26 th June, 2019	Kalika Municipality Office	chitwan@hrrpnepal.org	Report Available Below
Nawalpur	Organized Technical Coordination Meeting in ward level at Hupsekot Rural Municipality	27 th June 2019	Hupsekot Rural Municipality Office	nawalparasi@hrrpnepal.org	Report Available Below
	Field visit Carry out	27 th June, 2019	Devchuli Municipality		
Parasi	Update Palika Profile data of Nawalpur	12 th June 2019		nawalparasi@hrrpnepal.org	Palika Profile Data

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
District Facilitation and Coordination Meeting	Tentative 19 th July, 2019; DCC Hall, Hetauda, Makwanpur	DCC/GMaLi/HRRP	makwanpur@hrrpnepal.org
Technical Coordination Meeting in Ward level and Joint Field Monitoring Visit Participants: M&E Specialist, DSE, HRRP team, Ward representatives, local technicians and Beneficiaries.	24 th July to 26 th July, 2019 Bakaiya Rural Municipality, Makwanpur Gadhi and Hetauda Sub-Metropolitan	Joint Monitoring Team	makwanpur@hrrpnepal.org

News & Updates

Retrofitting issues which becoming a vital problem in the district of Makwanpur but now UNOPS/Build Change started the retrofitting demonstration/model houses in different palikas of district and also we have encourage to beneficiaries for retrofitting; for this purpose, we have conducted orientation program and decision made at Thaha Municipality-07 previous Agra VDC.

[Meeting Minute Thaha Municipality-07 click here....](#)

Positive impact of our field visit and meeting. We had decision made in certificate distribution during field visit. now we have organized certificate distribution ceremony with lead of Thaha-07 and supported by Thaha Municipality;



Figure 1: Private housing reconstruction completion certificate distribution ceremony was organized at Thaha Municipality-07 on 21th June, 2019.


Tranche Status (Makwanpur)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	6039	2512	2226	2226	1510	945	2176	1137	1125	0
Bakaiya Gaunpalika	8593	4017	2643	2599	1787	864	1960	691	565	0
Bhimphedi Gaunpalika	5236	2698	2213	2195	1821	1605	932	591	578	0
Hetauda Upamahanagarpalika	32696	6363	5302	4684	2722	2260	2024	1055	1055	0
Indrasarowar Gaunpalika	3726	2923	2562	2548	1930	1243	254	174	161	0
Kailash Gaunpalika	4737	2613	2112	1483	1177	886	731	324	320	0
Makawanpurgadhi Gaunpalika	5516	2216	1788	1763	1263	963	1437	746	746	0
Manahari Gaunpalika	8841	2337	1274	1274	1021	870	1487	622	622	0
Raksirang Gaunpalika	5091	1711	1547	1547	1415	1043	576	431	431	0
Thaha Nagarpalika	10519	6919	6072	5319	4044	2743	1369	655	651	0


Graph of Tranche Status:

Reconstruction- Tranche Status

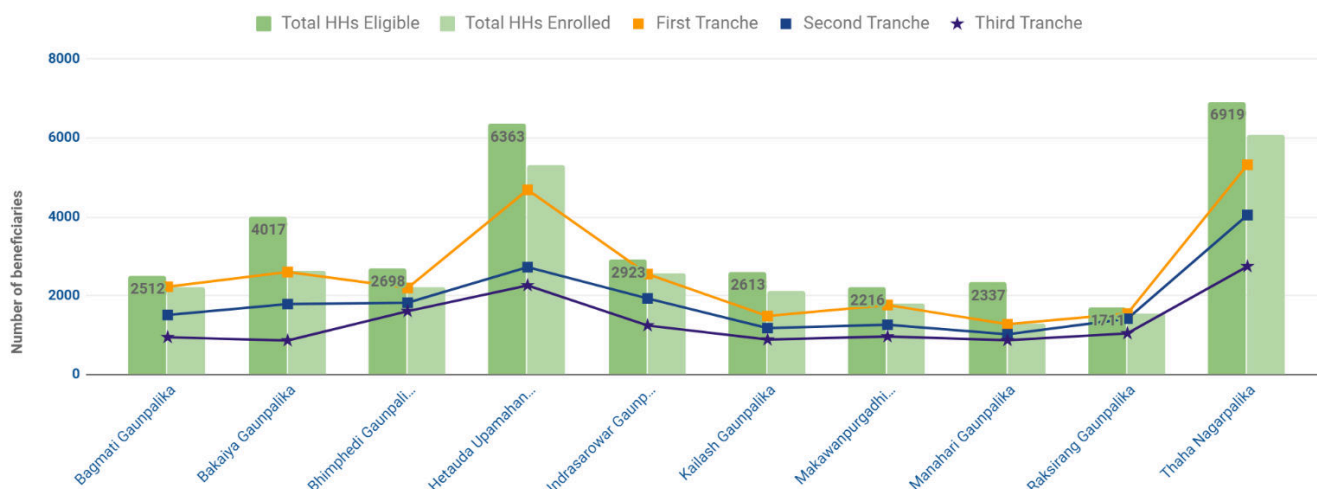

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

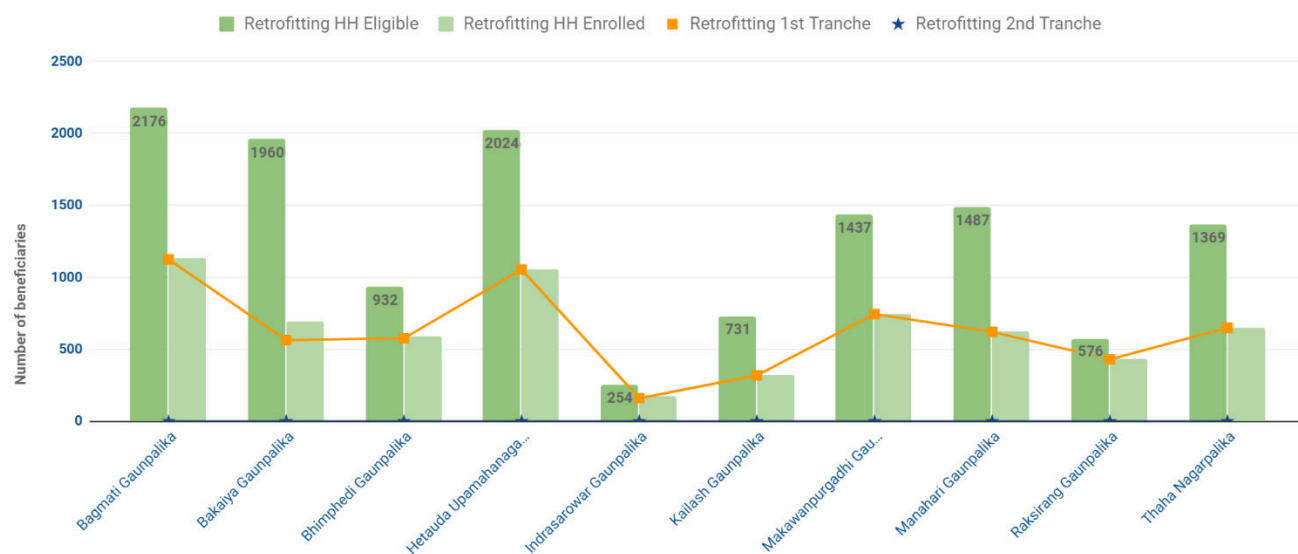


Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bharatpur Mahanagarpalika	2087	710	655	655	156	61	38	9	9	0
Ichchhyakamana Gaunpalika	3571	2353	2043	2043	1724	815	248	196	196	0
Kalika Nagarpalika	2565	916	611	611	341	97	42	27	27	0
Khairahani Nagarpalika	1566	559	523	523	237	178	4	4	4	0
Madi Nagarpalika	123	23	23	23	19	15	15	13	13	0
Rapti Nagarpalika	3594	2043	1266	1266	676	278	71	18	18	0
Ratnanagar Nagarpalika	1763	731	650	650	396	334	175	164	164	0

Tranche Status (Chitwan)

Graph of Tranche Status:

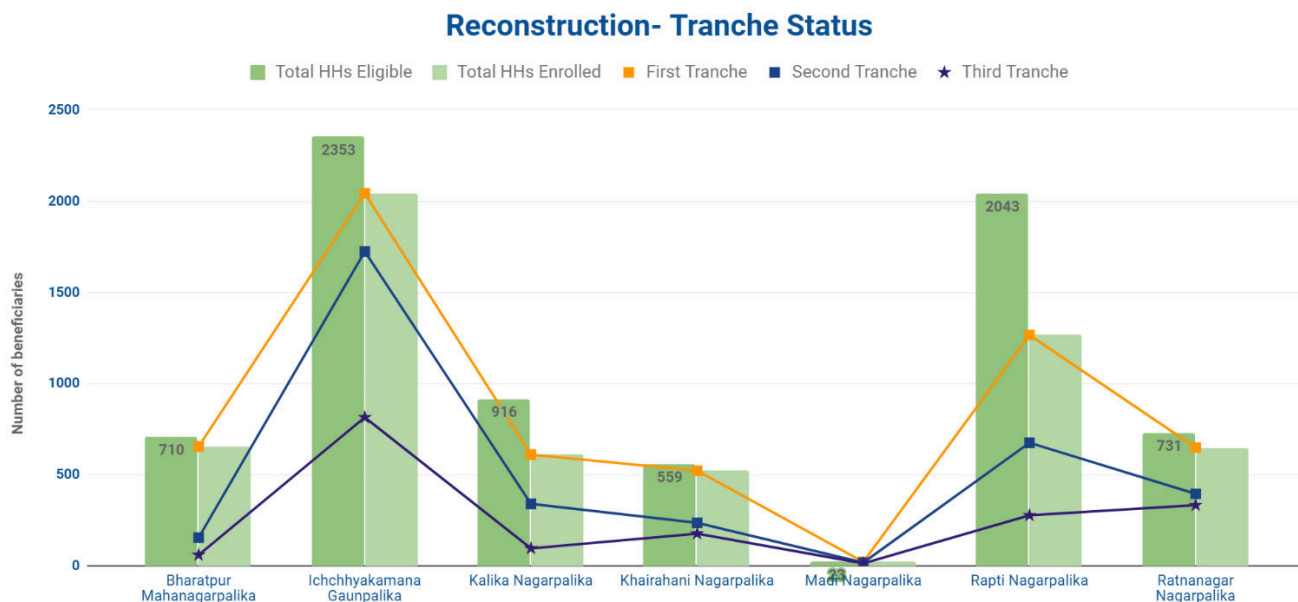

Graph for Retrofitting Status:

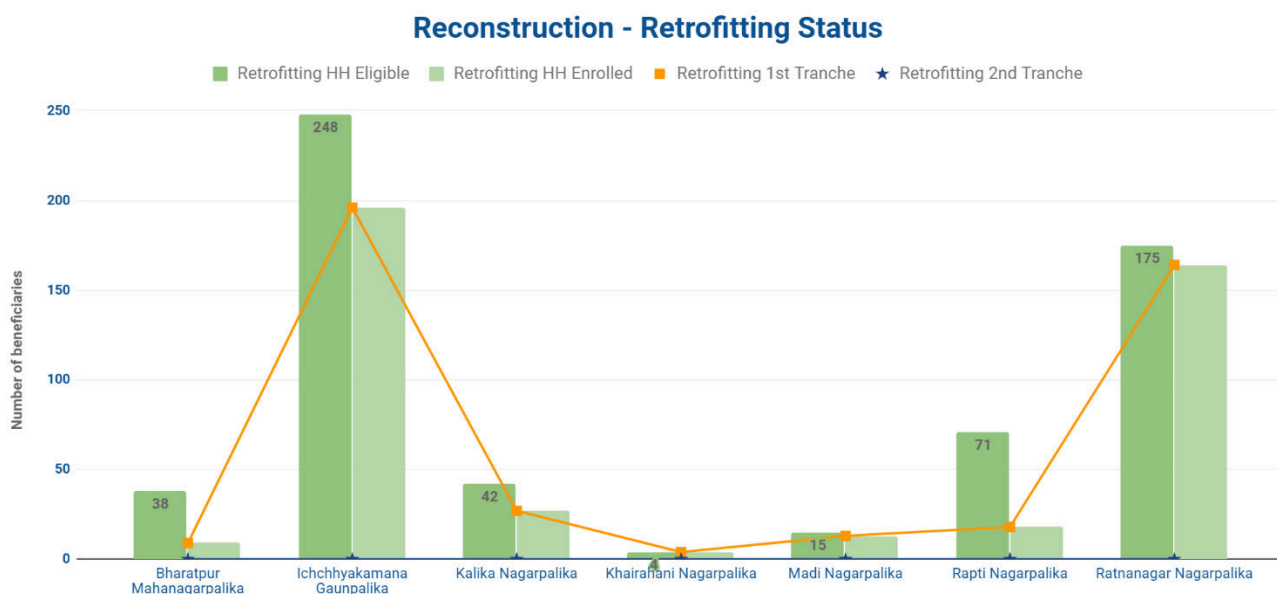


Tranche Status (Nawalparasi)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bardaghat Nagarpalika	4	4	4	4	3	2	0			
Binayee Tribeni Gaunpalika	70	66	65	65	58	50	2			
Bulingtar Gaunpalika	280	260	260	260	233	182	5			
Bungdikali Gaunpalika	133	72	72	72	67	59	1			
Devchuli Nagarpalika	177	177	177	177	171	116	1			
Gaidakot Nagarpalika	103	49	49	49	41	31	0			
Hupsekot Gaunpalika	155	139	139	139	127	92	2			
Kawasoti Nagarpalika	4	4	4	4	3	2	0			
Madhyabindu Nagarpalika	41	85	85	85	76	56	3			
Palhi Nandan Gaunpalika	1	4	4	4	3	3	0			
Pratappur Gaunpalika	6	3	3	3	3	3	0			
Ramgram Nagarpalika	3	1	0	0	0	0	0			
Sarawal Gaunpalika	4	4	3	3	0	0	0			
Sunwal Nagarpalika	2	2	2	2	2	1	0			
Susta Gaunpalika	2	3	3	3	1	1	0			


Graph of Tranche Status:

Reconstruction- Tranche Status

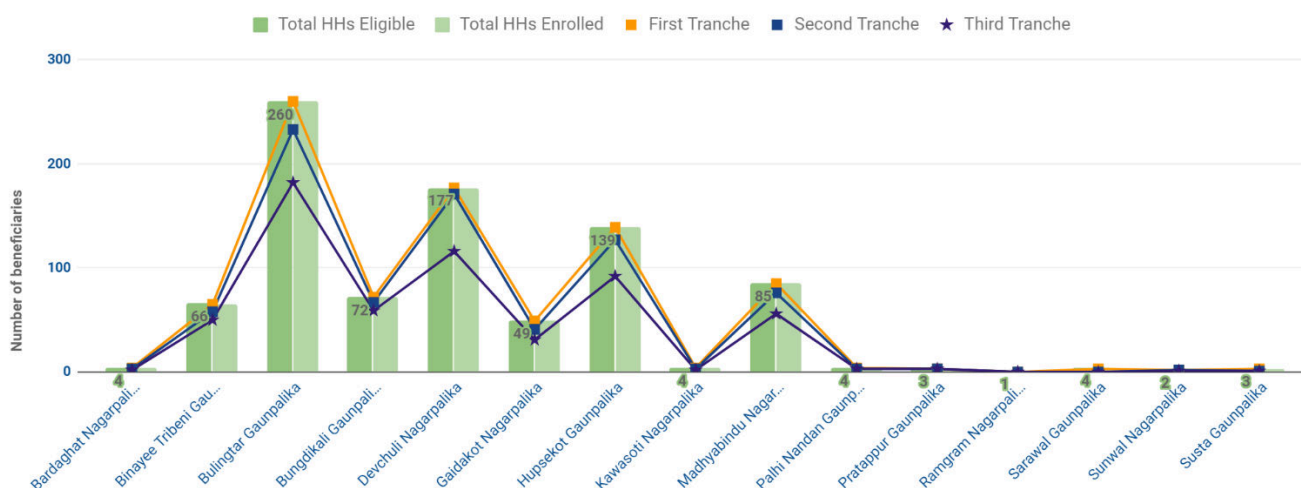

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

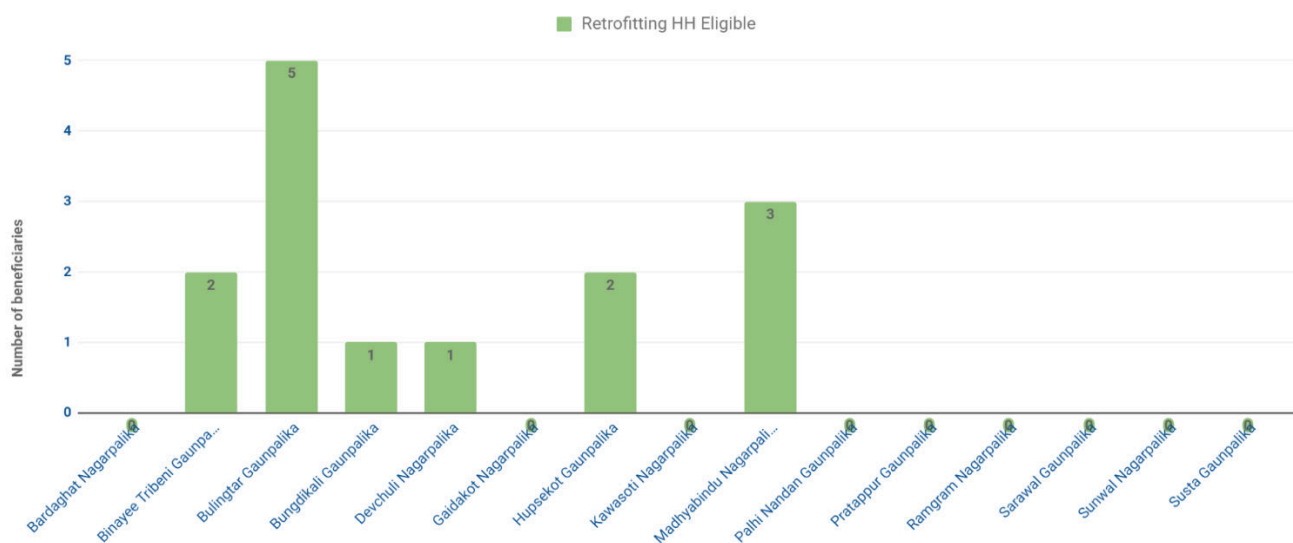

Field Visit Reports (Chitwan and Nawalparasi)

Visit 1

Date	Location	Participants
26 th June, 2019	Kalika and Rapti Municipalities, Chitwan	District Support Engineer, HRRP team, Local Government, Ward Technicians and Beneficiaries.
Objective(s)	- To know present scenarios of reconstruction in the palikas. Solve the technical problems and noted the major issues if any faced by technicians and beneficiaries. - To organize technical coordination meeting in palika level and also interaction with technical persons, beneficiaries etc. - To carryout field visit and collect to housing typology in Kobo application.	

Why was the visit carried out in this location?

- Promote to start up the correction and retrofitting for retrofitting beneficiaries.
- To know the status of reconstruction as well as CS entry, final inspection done or not and status of certificate distribution.
- To know the status of resurvey and re-verification & how is it conducting in wards?
- Solve the technical problems and suggest feedback for noncompliance issues and recommendation for measures and also collected if any major issues.

Summary

Chitwan, one of the moderate earthquake victim district where we have successfully carried out field visit and organized technical coordination meeting at palika level. In Kalika Municipality around 50% private housing reconstruction has been completed which is a good progress and a positive message for reconstruction. Most of the houses were built before deployment of the government technicians. But now, NRA has addressed this issues with follow up certain processes. Some houses have been made with compliance with correction and are receiving tranches.

After the meeting with Mayor of Kalika Municipality, focal person, ward technicians and DSE; we found that; the reconstruction progress is rapidly increasing but in similar way, we could not find out that, there is not starting of the retrofitting. The municipality has yet not started completion certificate distribution and gap between I tranche and II tranche at Municipality. It is a vital problem in the overall palikas and also faced by both Kaliak and Rapti Municipality. We have discussed with technicians about retrofitting, CS entry, certificate distribution and gap maintain; how is it going in both municipalities. They said, "we are trying to motivate the beneficiaries for retrofitting and complete the reconstruction on time but they are not assured in the economical, quality, availability of materials and manpower". In the wards, there is more submitting the grievances. Still engineer has completed the resurvey and re-verification except clearance till to visit date. No any major issues in these wards of municipality. **Around 116nos. of noncompliance issues in Kalika and 103nos. of noncompliance files have been solved in Rapti Municipality.**

The latest reconstruction data as given below in tabular form;

Name of R/Municipalities	1st tranche received HHs	Verified for 2nd tranche HHs	Received 2nd HHs	Verified for 3rd tranche	Third tranche received HHs	Completed HHs	Remarks
Kalika Municipality	630	430	417	205	190	205	
Rapti Municipality	1564	950	909	470	467	470	

Challenges / Issues Identified	Solutions Provided	Responsible	Timeframe
Maintain the gap between tranche distribution	Now huge gap between I and II tranche in Rapti Municipality and also same gap in Kalika Municipality so we suggested the technicians if beneficiaries completed their houses and full fill the all requirements inspectin on time and also file submit on time in district. Also we include this agenda in the meeting ; they all positive reponse and said we follow up the last NRA time schedule of reconstruction.	Local government, ward technicians and district agencies	Regular
CS entry, final inspection and distribution completion certificate with proper recording.	- Now, huge progress in CS entry and final inspection of houses but certificate distribution has not started yet. So we advised to the technicians and in the meeting plan to distribute the completion certificate. - After final inspection and CS entry, planning to organize completion certificate distribution.	Ward technicians and local government	Regular
Retrofitting and its implementation	Refer retrofitting manual for load bearing and RCC frame structure. Necessity to organize an awareness program at different palikas of district. And convince the beneficiaries financial cost, material and methodology as well quality.	Ward technicians and local government	Regular

Photos



Figure 1: Technical coordination meeting has been organized at Kalika Municipality Chitwan. There were around 9nos. of participants in the meeting.



Figure 2: House owner; Kamala Damai; Rapti Municipality-07, Chitwan. This house made just after the gorkha earthquake. House owner faced the economical problem during construction and now 10*8 sizes two rooms and CGI sheet roof. Any how she built the house with absent of technicians supervision. So there are not provided any seismic reinforcement and vertical members. Finally this house became a non compliance. During field visit we recommended the beneficiaries for some correction such as inner and outer side of wall provide the GI wire mesh and should be anchoring properly with below tie beam and briefly we discussed with engineers about this issues with presence of DSE for correction so we encourage to beneficiaries for correction and regularly contact to engineer for how do it and its processes.

Visit 2:		
Date	Location	Participants
27th June,2019	Devchuli Municipality and Hupsekot Rural Municipality	GMaLI Focal Person, HRRP, Local Government, Ward Technicians and Beneficiaries.
Objective(s)	- To organize technical coordination meeting in palika level and also conduct an interaction program with technical persons and beneficiaries etc. - Know the present scenarios of reconstruction in wards of Hupsekot Rural Municipality. - To carryout field visit and collect to housing typology in KOBO application, find out the major issues and solve the problems.	
Why was the visit carried out in this location?		
To organize the technical coordination meeting and carryout field visit with followings specific points; how resurvey and reverification are going in the R/Municipality of wards; know the present scenarios of reconstruction; give strong feedback and procedure on the spot for noncompliance issues; retrofitting issues and its implementation; noted the major issues if any in the municipality for reporting to central level from the palikas;		
Summary		
Around 75% private housing reconstruction has been completed in Nawalparsi district. The progress is very well but in case of retrofitting and completion certificate distribution have not started yet. Hupsekot Rural Municipality; the reconstruction progress is around in completion phase. The resurvey and reverification have been completed. Decision Made of the meeting We briefly discussed in the meeting; Completion certificate distribution and completed the private housing reconstruction. noted that technicians final the all inspection and CS entry and inform to palika and after that Palika is planning to organize the completion certificate distribution ceremony.		

During visit we have given feedback about don't modify the houses after received the third tranche. we advised the beneficiaries receive also the completion certificate and concern with Rural Municipality. during visit we have collected around 7-8nos. of housing typology in KOBO collection.

The latest reconstruction data as given below in tabular form;

Name of R/Municipalities	1st tranche received HHs	Verified for 2nd tranche HHs	Received 2nd HHs	Verified for 3rd tranche	Third tranche received HHs	Completed HHs	Remarks
Devchuli Municipality	177	171	171	116	116	116	
Hupsekot Rural Municipality	139	127	127	102	102	102	

Challenges / Issues Identified	Solutions Provided	Responsible	Timeframe
CS entry, final inspection and distribution the completion certificate with proper recording.	- Now, for incentive; the weightage of CS entry is more so it should be complete to all inspections form with in Ashad Masant. - After final inspection and CS entry, planning to organize completion certificate distribution with in Bhadra Masant.	Ward technicians and local government	Regular

Photos



Figure 1: Technical coordination meeting has been organized in Palika level at Hupsekot Rural Municipality Nawalpur.



Figure 2: House owner Thulman Magar; Devchuli Municipality-06, Nawalparur. Load bearing stone and mud mortar use. Cement plastering in outer face of house but inner face of rooms, wall he does it and we suggested can be use mud mortar for plastering. He has received all tranches of government reconstruction grants. all seismic reinforcement elements provided, wood band used. The total construction cost is around 3.5lakh.

Housing Typology Report



Figure 1: House owner; Bal Dev Mahato, the location of house is Kalika Municipality-04, Chitwan. RCC frame structure and he received all tranches of government reconstruction grant and this house is compliant.



Figure 2: House owner; Rishi Ram Pandey, rapti Municipality-07, load bearing brick and cement mortar used. One storey with light roof, four rooms and all seismic reinforcement elements provided. He received all tranches of government reconstruction grant. The total construction was around 13lakh.



Figure 3: House owner Dhan Bahadur BK, Hupsekot Rural Municipality-04; Nawalpur. Load bearing brick and cement mortar used, two rooms, one storey with light CGI sheet. It is an earthquake resisitant house; all earthquake resisitant elements are provided such as vertical members at every corner, T-Junction and left -right of openings as well as horizontal reinforcements (all horizontal bands). The total construction cost was around 12lakh with including all costs.



Figure 4: House owner; Nanda Bahadur Wantakki, Devchuli Municipality-06, Nawalpur. Load bearing stone and mud mortar with one storey and an attic and also light CGI sheet. Two rooms with all horizontal bands and vertical members. The total construction cost was around 5lakh with including all costs.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Engineer fill the check list for second tranche on time but why they are not filling the check list for third tranche at same time when we completed the house?	Hupsekot Rural Municipality-04 Beneficiary	Engineer can inspect the house for both tranches at same time. We coordinated the ward level technicians and they accept the issues and response to them. And said " we are early coming to inspection for II and III tranches at same time and file will be forward at same time. Also this type of case, ward member coordination with technicians and beneficiaries. Onwards in every week, check list of second and third

Questions Collected

tranches submit to MoUD-DLPIU.

Challenges and Way Forward

Challenge	Way Forward
Final inspection, CS entry, complete certificate distribution and maintain the tranche gap.	- Engineer should be responsible for these tasks and also district agencies have coordination with the local authorities. - In period of inspection it should be carried out. Similarly completion certificate distribute and properly recorded. - Now the progress of CS entry is very high due to NRA announces for incentive and it is weightage is 30% so we complete the CS entry and final inspection. Final inspection is more important because of in field level beneficiaries modify their house in some places so it should be finalize who have full the all requirements and eligible for final inspection.
Retrofitting and its implementation Maintain the gap between the tranche distribution	- Refer retrofitting manual for load bearing and RCC frame structure. Necessity to organize an awareness program at different palikas of district. And convince the beneficiaries financial cost, material and methodology as well quality. We have not any skilled labor for retrofitting so it is necessary to conduct OJT type training at each palikas of Chitwan and cluster wise in Nawalparasi. - For gap maintain strongly follow up the last time frame of reconstruction and deliver the notification to all palikas and conduct interaction program at every palikas as for as possible in wards.
