

District Report

Ramechhap

4 - 17 January 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Ramechhap team has successfully completed the Field visit to Ramechhap Municipality starting from 9-11 th January 2019. During the field visit team had conducted ward level meeting at Sanghutar and Ramechhap with local representative and technical person. Similarly, team has observed the topology of private housing construction in the area. A total of 4 person was participated in the field visit program from DLPIU-Building and HRRP.	9-11 th January 2019	4		Mr. Prakash Bishwakarma	Report
HRRP Ramechhap team has successfully participated in the Earthquake safety day organized by DAO Ramechhap. In the Earthquake Safety day, rally was organized from Devkota chowk to Katarbot with Earth quake safety slogan. After the rally there was a short workshop organized at DDC compound. The program was chaired by DAO Mr. Krishna Parshad Sharma and guest were district chairperson, Vice Chairperson, Mayor of Manthali Municipality and other government officer and representatives of I/NGOs. The program was started with National Anthem and welcome speech of Local Coordination officer Mr. Rajendra KC. A total of 5 students from respective school presented their poem with earthquake message. The program was closed with the remarks from the respective guests.	16 January 2019				
Info pack was distributed to the Technical person and local representative at Sanghutar and Ramechhap.					

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
General Coordination meeting	22 nd January 2019, 11 am onward, ITO office meeting hall.	HRRP	Prakash Bishwakarma
Joint monitoring Field Visit	22 nd January 2019, 1pm onward to Sunapati RM	HRRP	Prakash Bishwakarma

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
9-11th January 2019	Ramechhap Municipality wardno-3 and 8 (Sanghutar and Ramechhap)	✓ Keshav Raj Pandey District Support Engineer, DLPIU Ramechhap ✓ Jagdish Chand, Focal Person Engineer, DLPIU, Ramechhap ✓ Prakash Bishwakarma, District General Coordinator-HRRP ✓ Tulasi Ram Lamichhane, District Technical Coordinator-HRRP

Objective(s)	• To observe the reconstruction status of the beneficiaries • To provide inputs to the beneficiaries in regards of housing reconstruction and non-compliances issues. • Interaction with the local representatives and beneficiaries to find the challenges and issues in the reconstruction.
--------------	---

Summary	Description of field visit (maximum 300 words)
---------	--

Ramechhap District is a part of Province No. 3, is one of the districts of Nepal, a landlocked country of South Asia. The district, known as Kirat Ramechhap, with Manthali as its district headquarters, covers an area of 1,546 km² and has a population (2011) of 202,646 and a density of 137.4 per km². According to LLRC Nepal there are now eight local administrations in the district: Manthali Municipality, Ramechhap Municipality, Umakunda Rural Municipality, Khandadevi Rural Municipality, Gokulganga Rural Municipality, Doramba Rural Municipality, Likhu Rural Municipality and Sunapati Rural Municipality. Ramechhap district is one of the 14 most earthquake affected districts. The area was severely damaged during the Gorkha Earthquake 2015. The field monitoring visit was successfully from 9-11th January 2019 with the presence of DLPIU DSE, Engineer and HRRP team.

Sanghutar ward-3 Ramechhap Municipality

The reconstruction status of the Sanghutar ward-3, Ramechhap Municipality is as below:

Total Beneficiaries	Total Agreement	1 st Tranche	2 nd Tranche	3 rd Tranche	Retrofitting beneficiaries
570 + 90 (Grievance)	638	550	541	413	55

Key point of the visit at Ward-3, Ramechhap

- Local body representative is quite satisfied with the presence and mobilization and work of the technical person of the area. In this regards they are very cooperative with the technical person as a result the reconstruction status was also satisfaction.
- In the meeting it was also reported that the technical person has frequently visit to the beneficiaries' house and regular interaction with them regarding the reconstruction.
- Lack of skilled labor and mason available in the village has made reconstruction house difficult in time. However, skilled labor and mason are bought to the village from other district the reconstruction work has been started in the village reported at meeting. Through the community mobilization was found very good and positive in Sanghutar.

- A total of 20-25 household are identified as a non-compliance and all files are transferred to the DLPIU office.
- Maximum beneficiaries have been already sifted to their new house. Community people are very helpful and supported in reconstruction reported by technical person in the meeting.
- A total of 55 beneficiaries are in the retrofitting beneficiaries and till the data no any beneficiaries has been done agreement to the government for the grant.
- Technical person reported that it would be better if technical person shall get time to time technical orientation that has provided by NRA/CLPIU and government policy in reconstruction.
- In Sanghutar there was problem of skilled construction man power, so I would like to recommend for the mason training to the community people.
- The technical person of Sanghutar said that it would be grateful if there shall be the TOT training for the technical person.

Reconstruction Status of Ramechhap-8

Reconstruction status of Ramechhap Municipality-3 is as below:

Total Beneficiaries	Total Agreement	1 st Tranche	2 nd Tranche	3 rd Tranche	Retrofitting
842	842	833	648	410	120

Key point of the visit at Ward-8, Ramechhap Municipality

- A total of 120 beneficiaries are in retrofitting beneficiaries and they are not interested do agreement in retrofitting beneficiaries due to thinking that with in only 1 lakh it is not enough for the house retrofitting.
- Executive officer of Municipality was satisfaction with the mobilization of technical person in Ramechhap municipality for reconstruction till date, but it would be very fruitful if the coordination and reporting mechanism between municipality and technical person shall strong.
- Regarding the issue and challenge faced in the reconstruction or field that challenges was short out with in ward reported by Engineer Mr. Keshav Dev.
- About 65% of houses were already constructed in the municipality So that technical persons are working in the inspection activities for the completion certificate.
- The non-complains issue was identified in Ramechhap Municipality in the two-story houses and band missing and all the non-complains were corrected.
- Executive officer of Ramechhap Municipality says that CLPIU shall make motivation plan to make technical person more active in the field.

Some photo of Activities during the period



DLPIU Technical person providing inputs to the beneficiaries about housing reconstruction.



RCC house reconstruction at Ramechhap Municipality ward-3, Sanghutar.



Earthquake Safety Day rally at Ramechhap, Manthali organized by DAO, Ramechhap




Student presenting the poem regarding earthquake message in the earthquake safety day at DCC, Manthali, Ramechhap.

Tranche Status


Rural/Municipality	Doramba	Gokulgang	KhadaDev	Likh	Manthal	Ramechha	Sunapat	Umakunda
Total HHs Surveyed & GR	5085	6343	5210	5685	11103	6581	3669	4984
Total HHs Eligible	5085	6343	5210	5685	11103	6581	3669	4984
Total HHs Enrolled	4658	5526	5039	5488	10452	6184	3461	4426
First Tranche	4655	5525	5035	5488	10437	6184	3458	4426
Second Tranche	3524	4916	4473	4701	9117	5387	3048	3840
Third Tranche	2059	3723	3417	3696	6623	4274	1630	2269
Total HH Constructed	2200	3890	3590	3790	7060	4390	2150	2350
Grievance Registered	2448	1031	2007	1562	2815	1841	1392	843
Grievance Addressed	2448	1031	2007	1562	2815	1841	1392	843
RF HH Eligible	344	58	620	235	258	154	350	130
RF HH Enrolled								
RF 1st Tranche								
RF 2nd Tranche								
Non-Compliance Registered	31	57	7	69	78	26	7	2
Non-Compliance Addressed	31	57	7	69	78	26	7	2

Source: DLPIU-Building, GMALI

Graph of Tranche Status:

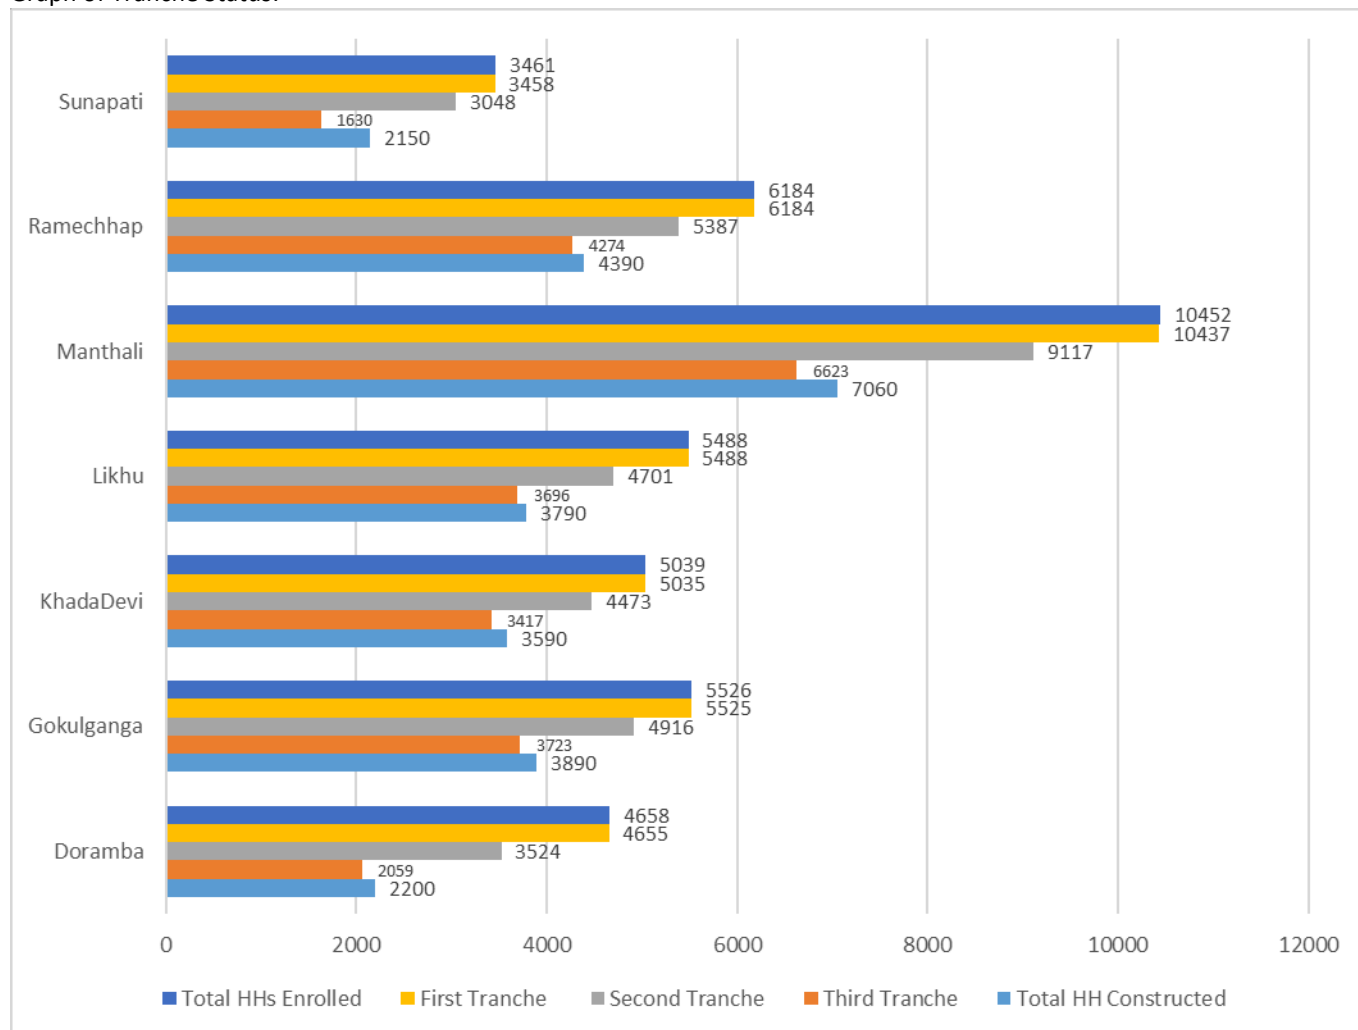

Graph for Non - Compliance Status:

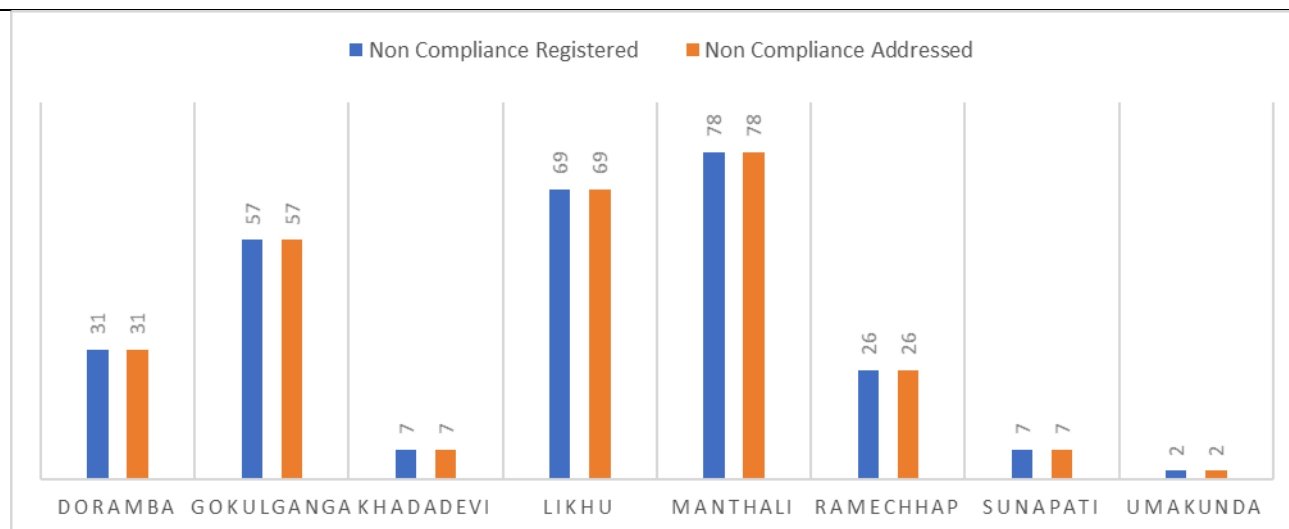

Housing Typology Report



The house of Madan Bhaukaji constructed in Sanghutar, Ramechhap Municipality-3. The house has been constructed using walls made from bamboo which is concreted from outside upto 4 feet height and the remaining wall is constructed with CGI Sheet. The hollow steel post has been erected from the foundation level. The DPC has been provided in the house. The house was constructed in Bhadra 2072 before arrival of technical persons.



The house of Chatra Bahadur Pradhan constructed in Sanghutar, Ramechhap Municipality-3. The house has been constructed with load bearing structure in ground floor. The ground floor has been constructed by using brick in cement mortar. The RC bands has been provided in the house. The house is provided with Excess openings. The first floor is constructed by using timber and CGI Sheet. There is no proper connection between two floors. The house is considered as hybrid Structure. The house owner has received first tranche of reconstruction grant.



The house of Diwat Kumar Shrestha constructed in Sanghutar, Ramechhap Municipality-3. The house is constructed on a single bay. The SAP analysis is done for the house to proof the earthquake resilience structure. The house constructed is RCC structure. The house owner has received all three tranches of reconstruction grant.



The house of Narayan Das Shrestha constructed in Sanghutar, Ramechhap Municipality-3. The house is constructed using prefab. The house is considered as semi-permanent structure. The house owner has received first tranche of reconstruction grant. The house is registered as non-compliant case.



The house of Sanjeev Shrestha constructed in Sanghutar, Ramechhap Municipality-03. The house is a RC Frame structure. It has been provided with 4-16 dia and 4-12 dia bars in column. The size of column is found to be 12"x12". The house is constructed using double tie beam. The house owner has received second tranche and has been forwarded for third tranche of reconstruction grant.



The house of Raj Babu Bhaukaji constructed in Sanghutar, Ramechhap Municipality-03. The house is a RC Frame structure. It has been provided with 4-16 dia and 4-12 dia bars in column. The size of column is found to be 12"x12". The house is constructed using double tie beam. The house owner has received second tranche and has been forwarded for third tranche of reconstruction grant.



The house being constructed in Sanghutar, Ramechhap Municipality is being claimed by the house of two brothers Tula Bahadur Magar and Prem Bahadur Magar. Both brothers are in the reconstruction beneficiaries list. The two brothers claim that they donot have any land in other place. The case has been forwarded to GMall for further decision.



The house of Dinesh Ghimire being constructed in Bhaisheswar, Manthali Municipality-1. The house is a RC Frame structure. The house is being constructed without providing sufficient foundation depth. The foundation is being exposed on the ground level.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
What is the process of getting loan from bank for reconstruction process?	Hari Pradhan	The loan upto 3 lakhs is permissible for the loan. NRA will subsidize the loan percentage by 5% and the remaining has to be paid by the house owner. Regarding the process, details can be available in GMALI Office. (Keshav Raj Pandey)

Questions Collected

What is the provision for the houses constructed before arrival of engineers?	Sagar Babu Pulami	NRA has stated to provide the list of beneficiaries who constructed houses before arrival of engineers. The letter from PM has stated to provide all tranches at once if it is found earthquake resilient.
---	-------------------	--

Challenges and Way Forward

Challenge	Way Forward
Only 34 masons are registered in Sanghutar	Conduct Mason trainings soon.
