


FACTS AND FIGURES

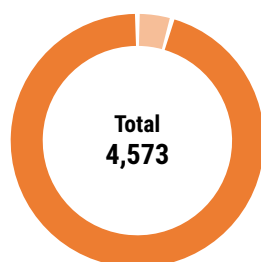

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	98.42%	89.07%
Reinforced Cement Concrete (RCC) Frame	0.57%	3.05%
Brick and Cement Mortar Masonry	0.33%	2.11%
Adobe Structures	0.33%	4.25%
Others	0.36%	1.52%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	4,713
PA Agreement	4,336 377
I st Tranche received	4,336 377
II nd Tranche received	4,000 713
III rd Tranche received	3,326 1,387

Houses

Under Construction: - Completed: 3,023

Retrofitting Status

Total Eligible HHs	254
PA Agreement	3 251
I st Tranche received	3 251
II nd Tranche received	- 254

Grievances

Registered: 672
Addressed: 593

Non-compliances

Registered: -
Addressed: -

Data Updated on: 2019-05-27 00:00:00

P0 Presence

Active: No POs Reported

Phased Out: ACF (Shelter), GIZ (Health), NRCS (Health), OXFAM-GB (Agriculture), OXFAM-GB (Livelihood), OXFAM-GB (Shelter), OXFAM-GB (Hygiene), PA (Shelter), RoomTR (Education), SCI (DRM), SCI (Education), SCI (Livelihood), SCI (Shelter), SCI (Social Protection), SCI (Hygiene)

OTHER SECTORS



Schools

Damaged: 42
Under Construction: 13
Construction Completed: 13



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	76,162	Y	6,000
Aggregate	m ³	79,252	N	12,000
Sand	m ³	8,142	N	9,000
Timber	cu. ft.	9,433	Y	3,500
Cement (PPC)	Sack	-	Y	900
Cement (OPC)	Sack	262,074	Y	1,000
Rebars	kgs.	823,462	Y	98
Tin	bundle	10,710	-	-
Bricks	pcs.	618,317	Y	16

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

1,200 /-
1,000 /-

KEY CONTACTS

Municipal Office

Ramesh Wosthi
Mayor
9841291082

Municipal Office

Dipak Kumar Yadav
Focal Person
9844458865

Municipal Office

Taradevi Rimal
Deputy Mayor
9841548330

GMaLI/NRA

Bickey Lakha
NRA Chief-District
9849179333

Municipal Office

Ashok Prasad Dahal
Administration Officer
9851246206

DLPIU-Building

Koshnath Adhikari
DUDBC.DLPIU Chief
98550465884

HHs WITH LAND ISSUES

3

250

Landless

Guthi land

STATUS OF TECHNICAL STAFF

Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)


Source: Municipal survey

MASON TRAINING


Trainings (# out of total required)

7 days Training

50 days Vocational Training




Reached



Remaining

Source: HRRP Analysis

TA ACTIVITIES MAP

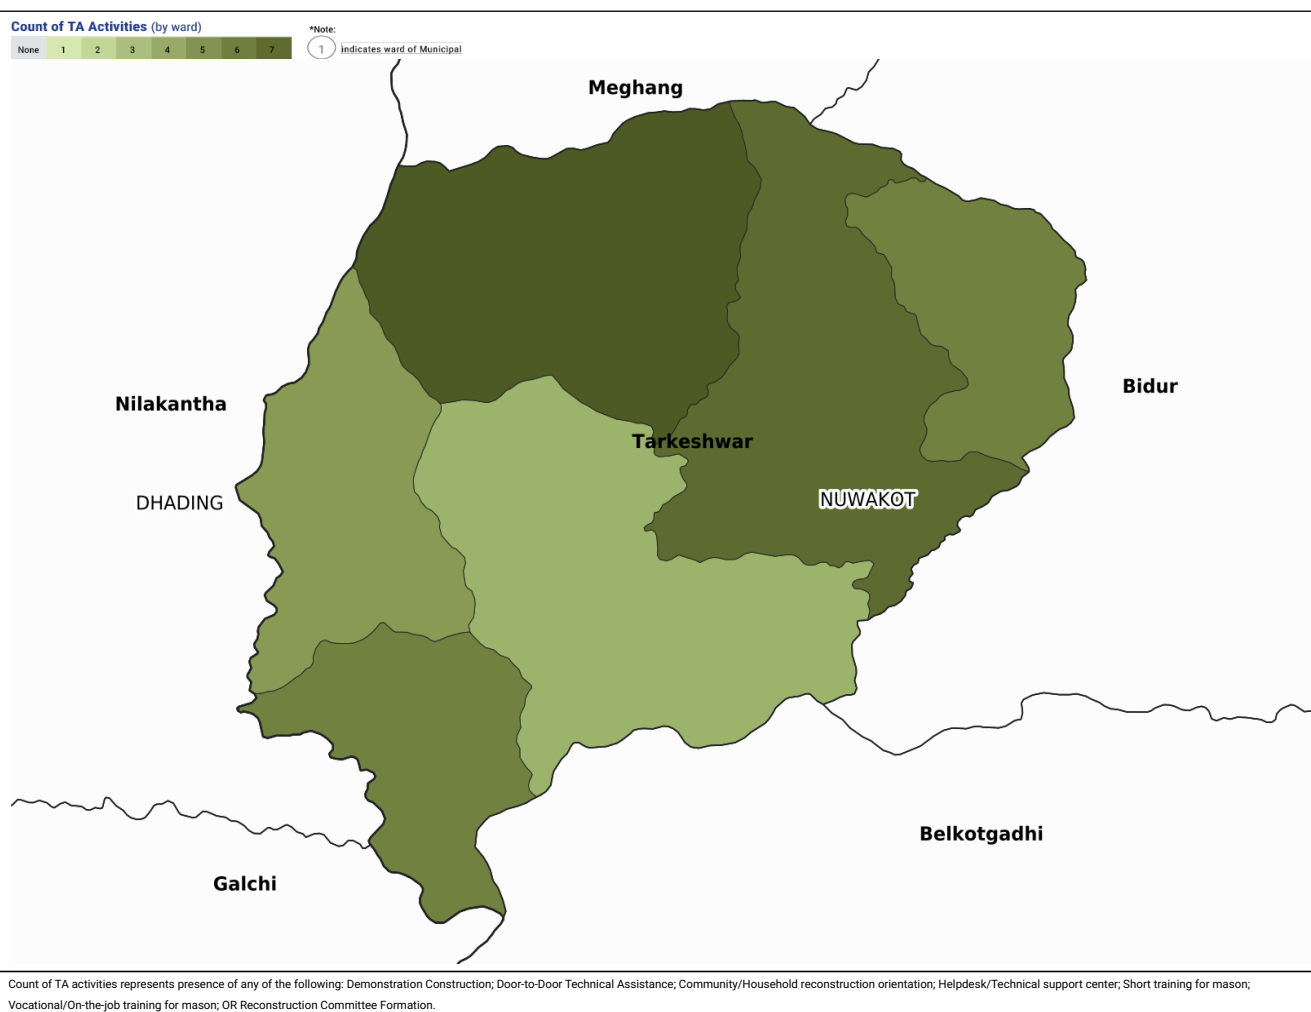

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information

1. Badri Pyakurel (District Coordinator) 9851154201	2. Sachin Sapkota (District Technical Officer) 9847621292	3. Manisha Rai (District Information Management Officer) 9842062006
--	--	--
