

Monthly District Report

Nuwakot, Rasuwa

9 May - 13 June 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Nuwakot	Joint Monitoring Field Visit with CLPIU/DLPIU building	4-Jun-19	Nuwakot, Belkotgadhi Municipality, Ward 8,9	Badri Pyakurel District Coordinator badri.pyakurel@hrrp.nepal.org	Meeting Minutes
	Joint Monitoring Field Visit with CLPIU/DLPIU building	28-May-19	Nuwakot, Bidur Municipality, ward no. 3	Badri Pyakurel District Coordinator badri.pyakurel@hrrp.nepal.org	
	District Facilitation and Coordination Meeting	23-May-19	Nuwakot, Bidur Municipality, DCC Hall	Satya Narayan Chaudhary satya.isha95@gmail.com	http://www.hrrpnepal.org/recent-minutes/522 Photo
	POs field visit jointly with stakeholders	20-May-19	Nuwakot, Bidur Municipality & Kispang Rural Municipality	Bishal Gautam Program Coordinator Sahayata Samajik Sanstha (SSS) bishal.gautam@gmail.com	
Rasuwa	District Facilitation and Coordination Meeting	18-May-19	Rasuwa, Naukunda Rural Municipality	Badri Pyakurel District Coordinator HRRP Cluster 5 badri.pyakurel@hrrp.nepal.org Contact: 9851154201	Meeting Minutes Photo
	Participate in reconstruction Policy dialog organized by Human Right Alliance and HRCDC	19-May-19	Rasuwa, Dhunche	Badri Pyakurel District Coordinator HRRP Cluster 5 badri.pyakurel@hrrp.nepal.org Contact: 9851154201	Concept Paper

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
District Facilitation and Coordination Meeting	TBC in Nuwakot	DLPIU-GMaLI	Satya Narayan, satya.isha95@gmail.com

News & Updates

District Facilitation Meeting in Nuwakot

A district facilitation and coordination meeting of reconstruction committee was organized by DLPIU-GMaLI in DCC hall, Bidur Nuwakot on 23 May 2019. The meeting was chaired by DCC chief in the presence of 30 participants including a team from central NRA (Dhruba P. Sharma, executive Committee member and team), Geologist team from NRA, Department of Mines and Geology, IOE, all the district chief i.e., DLPIU-GMaLI, Building, Education, survey, Land and revenue, Financial Comptroller General Office, chairperson and representatives from three Rural Municipalities and representatives from Durable solution program.

The forum had discussed over the agendas regarding relocation, displaced and landless beneficiaries and demolition the houses damaged by EQ. The team for geological survey from central NRA will resurvey and observe the vulnerable areas where many displaced beneficiaries (under category 3) have reconstructed their house even though the area was considered to be geologically unsafe. Depending on the survey result NRA will take further action accordingly. Similarly, the forum discussed over the issues of 40 beneficiaries have submitted application asking for tranche release. These beneficiaries were listed under Category 3 but had safer house in another place, so the tranche release of those beneficiaries was stopped. Further decision was made to verify and inspect the reconstructed house by technical team and the tranche can be released tranches if their house is constructed after EQ 2015 and are per the Government housing grant criteria. Regarding the demolition of damaged houses, it decided to circulate information and letter to local bodies at ward level.

District Facilitation Meeting in Rasuwa

The first district facilitation and coordination meeting of reconstruction committee was organized by DLPIU GMaLI on 18 May 2019 in Rasuwa. The meeting was chaired by DCC chief Mr. Kul Prasad Bhatta and had participation of 23 attendees including representatives from DLPIU-building, DLPIU-education, district land management office, Financial comptroller office, PO (durable solution) and HRRP. The main agenda of the meeting was to discuss over the challenges on relocation cases and its way forward.

A brief update on reconstruction progress from all DLPIUs and HRRP were presented. Furthermore, decisions over some cases of displaced and landless beneficiaries were made. Following decisions were made in the meeting

- Follow up and coordinate with municipality and wards to settle the issue between host community and the of 14 displaced beneficiaries in Uttargaya rural municipality, where land was purchased with NRA land grant under process of relocation.
- Regarding the 24 displaced beneficiaries of Rasuwa who had purchased land under high transmission line in Shantibazar, Nuwakot. The district reconstruction committee will request and recommend to central NRA for process of purchasing land in another place and the land transformation to the Nepal government.


Tranche Status (Nuwakot)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Belkotgadhi Nagarpalika	10719	11037	10441	10441	9266	4070	256	7	7	0
Bidur Nagarpalika	15204	12933	12014	12014	10965	7632	240	90	90	0
Dupcheshwar Gaunpalika	5827	5884	5691	5691	5356	4416	35	1	1	0
Kakani Gaunpalika	6905	6954	6472	6472	5767	3823	175	49	49	0
Kispang Gaunpalika	4637	4788	4387	4387	4115	3739	51	1	1	0
Likhu Gaunpalika	4973	5109	4742	4742	4124	2907	155	15	15	0
Meghang Gaunpalika	4739	4516	4275	4275	4102	3609	152	1	1	0
Panchakanya Gaunpalika	4243	4528	4283	4283	3768	2693	96	6	6	0
Shivapuri Gaunpalika	6292	6522	6239	6239	5337	3947	65	0	0	0
Suryagadhi Gaunpalika	4560	5023	4896	4896	4279	3023	17	1	1	0
Tadi Gaunpalika	4476	4592	4472	4472	4156	3344	23	3	3	0
Tarkeshwar	4573	4713	4336	4336	4000	3326	254	3	3	0

Graph of Tranche Status:

Reconstruction- Tranche Status

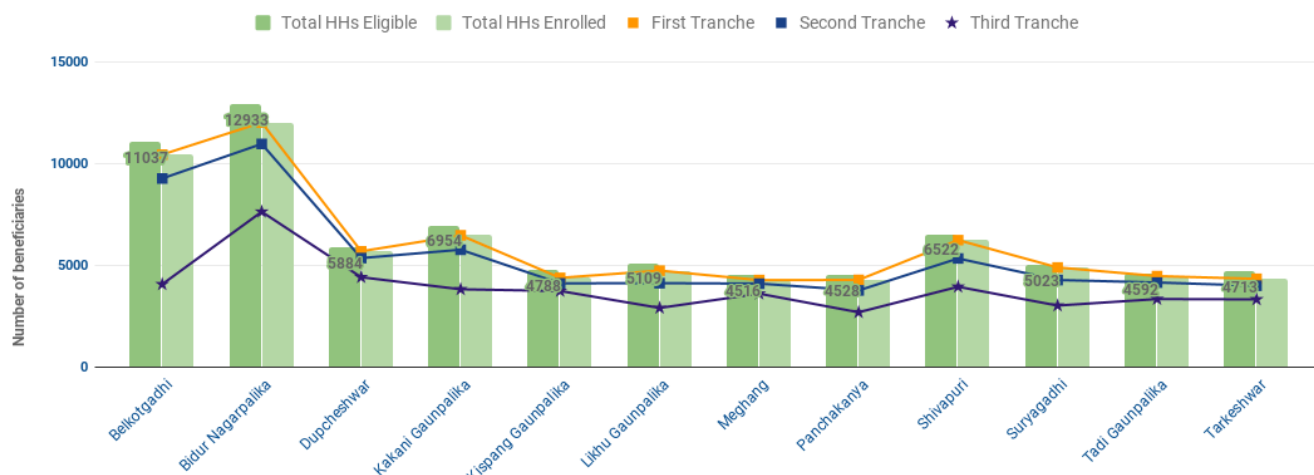

Graph for Retrofitting Status:

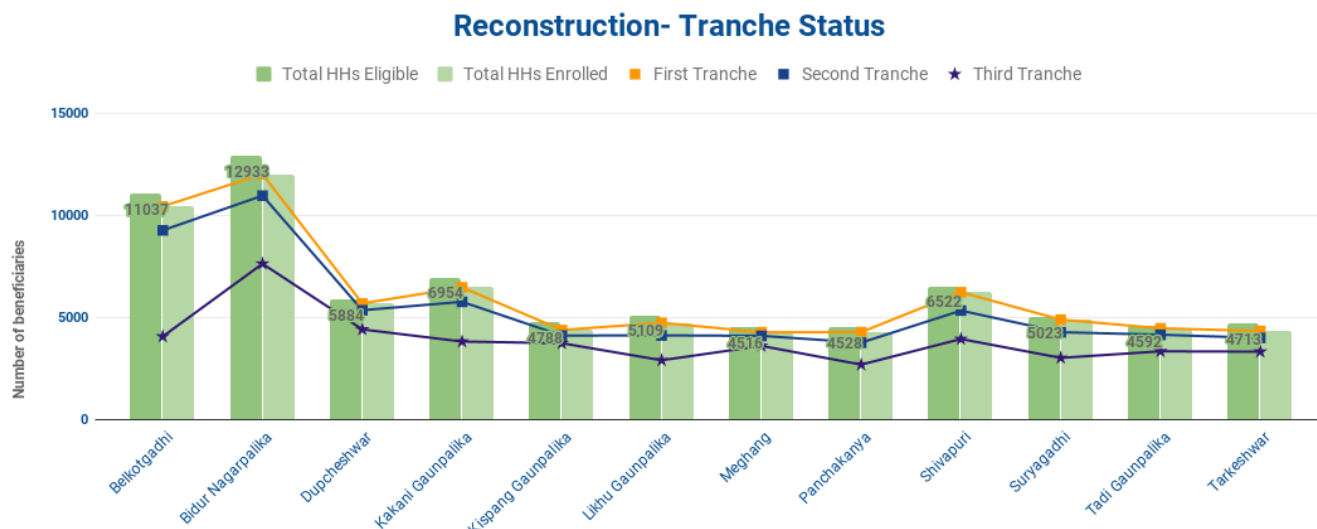


Tranche Status (Rasuwa)


Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Gosaikunda Gaunpalika	2224	1964	1868	1850	1743	1425	84	65	65	0
Kalika Gaunpalika	2530	1979	2472	2472	2422	2300	33	12	12	0
Naukunda Gaunpalika	3298	2591	3307	3307	3181	2997	18	13	13	0
Parbati Kunda Gaunpalika	1981	3349	1819	1819	1682	1405	59	2	2	0
Uttargaya Gaunpalika	2611	2631	2304	2304	2049	1899	25	11	11	0

Graph of Tranche Status:

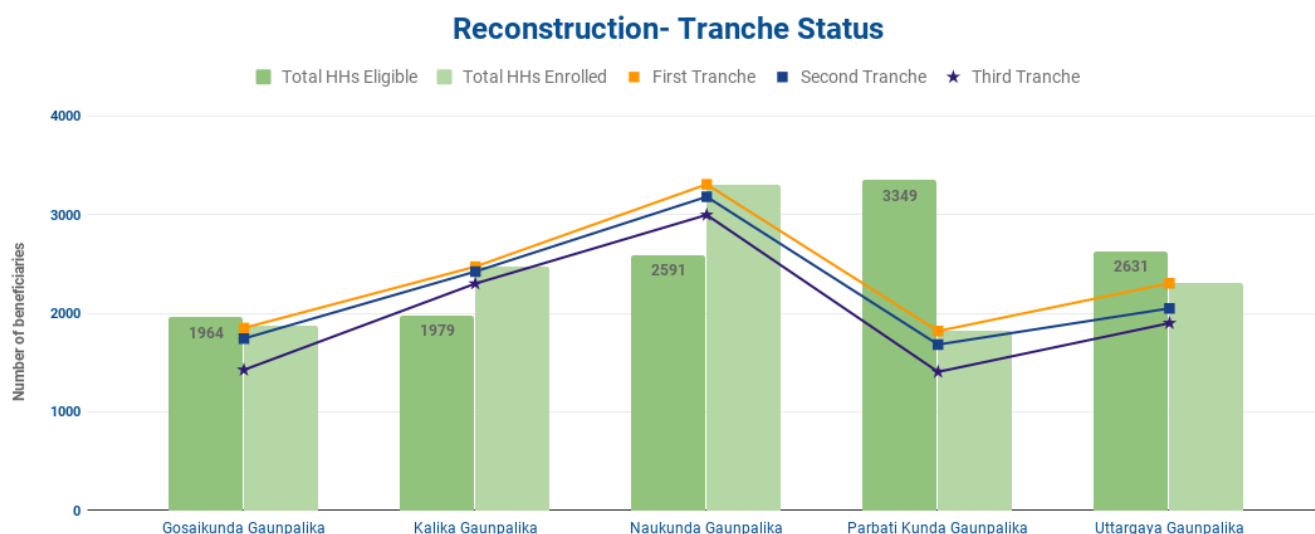

Graph for Retrofitting Status:

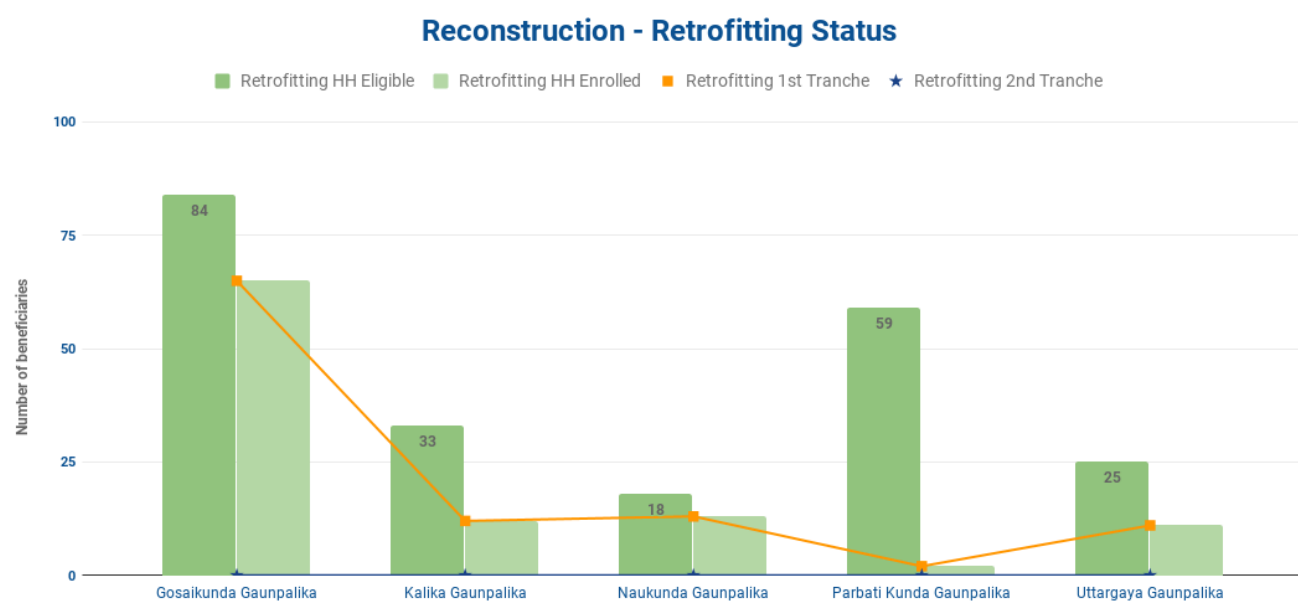

Field Visit Reports (Nuwakot)

Visit 1

Date	Location	Participants
20-May-19	Ward no. 9, Bidur Municipality and ward no. 5, Kispang Rural Municipality	- Deputy Chairperson, DCC Nuwakot - Deputy Mayor, Bidur Municipality - Ward chairperson - SSS representatives (field visit organizer) - Media - Badri Pyakurel, Cluster Coordinator, HRRP - Manisha Rai, Cluster Information Management Officer, HRRP
Objective(s)	- To observe the integrated settlement supported by OXFAM/SSS. - To interact with the beneficiaries to understand their status - To interact and get feedback from the local bodies and other stakeholders.	

Why was the visit carried out in this location?				
HRRP Nuwakot team joined a field visit along with the DCC, Municipal representative and ward representatives along with media to ward no 9 and 5 of Bidur Municipality and Kispang Rural Municipality respectively. The visit was organized by Sipradian Sahayata Sanstha (SSS) with an objective to monitor the three settlements supported by the organization as an implementing partner of OXFAM-GB.				
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'				
Summary Field Visit: - No. of HHs visited: 3 integrated settlements - No. of meetings with engineers: 0 - No. of meetings with local officials: 0 Under the Nepal Earthquake Recovery and Reconstruction Program, SSS with funding support from OXFAM intervened for the 3 integrated settlement in Nuwakot for displaced beneficiaries of the vulnerable places. In total 55 houses are supported by the partner in the settlements named Borthok Ghale tole (in handover phase), Mathillo Shantibazar and Tallo Shantibazar which are under construction phase. In coordination with NRA, durable solution project and other stakeholders, OXFAM/SSS supported in land management and constructed houses using the interlocking block with CGI roof. Out of total 55 houses, 43 are 3 roomed and 12 are 2 roomed structure based on the family size (up to 3 members). Along with the construction of the house the organization in coordination with the municipalities has also supported in the toilet construction, drinking water distribution, drainage and sewage system, sanitation and livelihood for all the settlements. All the beneficiaries were displaced listed on category 3. The places of their original settlements were identified as vulnerable and listed as eligible for land grant and relocation. 1. Barthok Ghaletole integrated settlement, Japhati, Bidur 9 - (18 HHs) The original settlement of 18 displaced HHs is Bhalche, ward no. 1 of Kispang Rural Municipality. Three houses are designed for two rooms and rest of are of three roomed houses. The duration of construction in this site was from April 2018 to March 2019. Almost all the families have shifted to their allocated houses and enrolled their children in nearby school as well. 2. Mathillo Shantibazar, Kispang RM 5 - (16 HHs) Out of 16 families, 6 are up to family size of three members. So, depending on the family sizes 10 structures are of 3 rooms and remaining are of 2 rooms. They are displaced from different areas of Rasuwa district listed under NRA category 3. The construction period is from October 2018 to June 2019. 3. Tallo Shantibazar, Kispang RM 5 - (21 HHs) 21 houses under construction in this site are of the displaced beneficiaries from the various vulnerable areas of Rasuwa. Three structures have 2 room and rest of are of 3 room. The construction duration for this site is from October 2017 to June 2019.				
Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Some basic facilities are lacking in relocated integrated settlement such as electricity, drinking water, livelihood option.	The supported partner should facilitate, manage such parts with coordination and ward representatives and municipality.		Partner, Municipality, settlement committee and beneficiaries	As soon as possible, before monsoon
Photos				



A view of Barthok, Ghaletole integrated settlement in Jafati, ward no. 9 of Bidur Municipality. Total 18 displaced HHs are relocated under the process of NRA and construction Supported by OXFAM/SSS. All the structures are built using with interlocking block and flexible roof.



Ongoing construction of 16 houses of displaced beneficiaries in Mathillo Shantibazar integrated settlement in Kispang Gaupalika under NRA relocation process and supported by OXFAM/SSS

Field Visit Reports (Nuwakot)

Visit 2

Visit 2

Date	Location	Participants
28-May-19	Majhigaun, Khadgabhanjyang, Ward no. 3, Bidur Municipality	• Prabhu Ram Pokherel, M/E consultant-CLPIU • Srijana Chaudhary, Sub-Engineer, DLPIU-Building, Bidur N.P. - 3 • Sangita Kumari Yadav, Asst. Sub-Engineer, DLPIU-Building, Bidur N.P.- 3 • Badri Pyakurel, Cluster Coordinator, HRRP-Nuwakot • Manisha Rai, District Information Management Officer, HRRP-Nuwakkot
Objective(s)	• To observe the non-compliant houses and to provide way forward regarding the technical assistance. • To interact with beneficiaries to understand the reconstruction issues and status • To collect housing typology	
Why was the visit carried out in this location?		
The main objective of the field monitoring was to observe the non-compliance houses and interact with the beneficiaries to provide them way forward for remaining tranches.		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		
Summary		

Field Visit:

- No. of HHs visited: 11
- No. of meetings with engineers: 0
- No. of meetings with local officials: 0

HRRP Nuwakot district team along with M & E Consultant from DLPIU NRA Building conducted joint field monitoring at Ward no 3 of Bidur Municipality, Nuwakot district. Among the 11 observed houses, 5 were in pipeline of decision for third tranche which were listed as non-compliance due to issues such as larger attic height, bands missing, 9"X12" column. M/E specialist suggested two houses to be complaint and can be forwarded for remaining tranche. Similarly, two non-compliant houses were found to be built immediately after earthquake before the NRA guideline. So, structural analysis was recommended for one, whereas for another it was suggested to be included in the list of houses constructed immediately after earthquake and forward to central NRA for possible solution.

Interaction with TSC team of UNOPS, ward no. 3, Bidur Municipality

A brief interaction and discussion on reconstruction was conducted with TSC team in the UNOPS ward TSC office in ward no. 3. UNOPS is working since one year on socio technical facilitation. However, out of total 1607 beneficiaries, UNOPS reported that 1358 houses are completed and 233 are under construction in the ward. As per UNOPS tracking report, the major constructed housing typology is BMC which is more than 58 percent and about 20 percent followed by SMM design. The team have provided 68 drawing to the beneficiaries in the ward as well.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Houses damaged by EQ is difficult to demolish as per NRA already circulated the letters to districts. Beneficiaries are not willing to demolish it as some of have been using for storage, some have emotional attachments and some of have lack of money to pay for it.	Local Bodies, wards, Rural/municipality should take initiation for this issue. Local bodies and technical team should conduct orientation and awareness program to highlight the risk of using damaged house and provide knowledge on safety and disaster preparedness.		Ward office, Municipality office, Political, social local leaders Engineers	

Photos



Beneficiary name: Chhabilal Adhikari, KhadgaBhanjyang, ward no 3, Bidur Municipality, Nuwakot. 2 storey 3 roomed Reinforced Cement Concrete Framed Building (RCC) structure with 9"X12" column. The structure was found to be unsafe by the structural analysis. So, it is on process to forward in the list of the non-compliance houses which



Beneficiary name: Shalikram Ghimire, Khadga Bhanjyang, Ward no 3, Bidur Municipality. A damaged 3 storey SMM house is still used for kitchen and storage though beneficiary have reconstructed a house and have received all the tranches of housing

were constructed immediately after EQ and before publication of the NRA guideline and deployment of the technical staffs.

grant. Such damaged structures are still in use and have not been demolished in the fields.

Field Visit Reports (Nuwakot)

Visit 3

Date	Location	Participants
04-Jun-19	Bahundanda, Jiling ward no.8, Gairaghar, Nalagaun ward no. 9, BelkotGadhi Municipality	- Prabhu Ram Pokherel, M/E consultant-CLPIU - Rajendra Chilwal, DSE, DLPIU-building, Nuwakot - Samir K.C., Engineer, DLPIU-Building, Belkotgadhi N.P. - 8 - Kamal Kuwar, Sub-Engineer, DLPIU-Building, Belkotgadhi N.P.-8 - Sandip Marahattha, Engineer, DLPIU-Building, Belkotgadhi N.P.- 9 - Govinda Yadav, Sub-Engineer, DLPIU-Building, Belkotgadhi N.P. - 9 - Binod Gyawali, Asst. Sub-Engineer, DLPIU-Building, Belkotgadhi N.P.- 9 - Badri Pyakurel, District Coordinator, HRRP-Nuwakot - Manisha Rai, District Information Management Officer, HRRP-Nuwakkot

Objective(s)

- To understand the factor for low progress in reconstruction
- To interact with beneficiaries to understand the reconstruction issues and challenges
- To encourage field engineers to collect third inspection (annex for completion certificate) and CS entry.
- To collect housing typology

Why was the visit carried out in this location?

HRRP Nuwakot team visited Ward no. 8 Jiling area and 9, Gairaghar area of Belkotgadhi Municipality to make interaction and meeting with ward representatives and field engineers. Further, the team also observed some non-compliant and compliant houses and interact with beneficiaries as well.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

- No. of HHs visited: 11
- No. of meetings with engineers: 2
- No. of meetings with local officials: 2

Meeting: [Meeting minutes of ward no 8](#) [Meeting minutes of ward no. 9](#)

The meeting was in both wards also with technical support Center (TSC) team of UNOPS. The main factor of low progress on reconstruction data in the Municipality because there is no technical unit for the building permit. So, as for now the third tranche is being released after the beneficiaries have paid the revenue of the new house, though reconstruction in the field is over 80 %. This municipality is shown as the lowest progressed in third tranche among all the Rrural/municipality in the district which is less than 40%, where rest of have already released third tranche by over 50%. The Key reconstruction issues of the area is related retrofitting. The beneficiaries listed on retrofitting have been waiting address of their application requesting to be beneficiaries on reconstruction.

Among the 11 observed houses, only one was found non-compliance structure which is completion phase of construction. The loadbearing BMC structure with 4 roomed of 9" wall has exceeded 6" attic height is constructed using flexible roof.

Meeting with ward chairperson and DLPIU technical staffs, in ward no. 8 and 9 separately

The main agenda and decisions were made as below.

- The pending decision for 28 houses with 9"X12" column reconstructed immediately after earthquake is decided to send the file with details to DSE ASAP for structure analysis and DSE assured to keep priority to this case.
- The case of 88 applicants of retrofitting beneficiaries requesting to be reconstruction beneficiaries is still not addressed which documents were forwarded to NRA long ago. However, most of them have reconstructed already. So, it decided to follow up again.
- M/E consultant suggested to DLPIU field engineers to speed up the third or final inspection for completion certificate. The ward chairperson is strongly agreed to engineers to fully involve on third inspection. It is targeted to a completion certificate handover program in around first week of Sawan month.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Numbers of houses reconstructed immediately after EQ with 9"X12" column are yet to forward for structure analysis.	Ward staffs should send details of the houses soon and DSE should keep it on priority.		Field engineers and DSE	Within a week
Grievances are being registered hugely during the resurvey time.	Ward representatives should play efficient role to control fake recommendations and documents.		ward representatives (Local bodies)	

Photos



Beneficiary name: Santa Bahadur Tamang, Bahundada, ward no 8, Belkotgadhi Municipality, Nuwakot. A 69 years old beneficiaries reconstructed his house up to DPC level a year ago and received second tranche. The structure up to DPC level is being used for animal shed. Since his wife died after EQ, he is living with family of son. His son is also a beneficiary and he reconstructed a hybrid 2 storey house and received 3 lakhs already. (His intention to build further could not find out since his absence in the field)



Beneficiary name: Delnath Dahal, Jiling Bahundada Ward no 8, Belkotgadhi Municipality. A family of 9 members living in EQ damaged SMM house which construction was completion phase in EQ happened. They reconstructed a BMC one roomed house opposite to the damaged house and the one roomed house is on use for grand-parent to sleep.



Meeting in ward no. 9, BelkotGadhi Municipality. Discussion over reconstruction issues and challenges with ward chairperson, ward secretary and ward engineers. The team of all 11 participants had observed some houses in the field nearby after the meeting.



Beneficiary name: Arjun Prasad Gajurel, Gairaghar ward no. 9, BelkotGadhi Municipality. Load Bearing BMC received 2nd Tranche. The structure of 9"X12" wall has exceeded 6" attic height and listed as non-compliance.

Housing Typology Report



Beneficiary name: Bhim Bahadur Majhi, Ward no 3, MajhiGaun, Bidur Municipality. 1 storey, 2 roomed load bearing BMC structure with flexible roof. The beneficiary has already received all tranches. A family having 5 members sleep in this house and the EQ damaged house is being used for kitchen.



Beneficiary name: ChakraPani Adhikari, Ward no. 3, KhadgaBhanjyang, Bidur Municipality. 1 storey, 2 roomed Loadbearing structure.



Beneficiary name: Gyan Bahadur Rai, KhadgaBhanjyang ward no. 3, Bidur Municipality. 2 storey Load Bearing Brick and Cement Mortar Masonry structure (BMC). The house was listed as non-compliance as it has missing the earthquake resistant elements such as roof band and exceeded attic height.



Beneficiary Name: Sanukanchha Tamang, KhadgaBhanjyang ward no. 3, Bidur Municipality. 2 storey hybrid structure received third tranche.
