

Fortnightly District Report

Nuwakot

1-14 February 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Field visit to Tadi-3, Kharanitar. Oxfam is supporting to the beneficiaries from Urleni. Planned for 71, 24 are completed. 20 are just started.	February 7 , 2019			dc.nuwakot@hrrpnepal.org	<i>See Detail in field visit Section</i>
Meeting with GMALI, CSRC to tackling with the case of landless, vulnerable listed by NRA.	February 8, 2018			dc.nuwakot@hrrpnepal.org	
Held orientation to the ward chair for grievance settlement/ appeal against non-beneficiaries by Gmali. 3 Palikas Tarakeshwaor, Dupcheswar and Tadi are involved.	February 12, 2019			dc.nuwakot@hrrpnepal.org	
Follow up letter and phone call to 12 Palikas for strategic planning. All palika have good response, dateline for the submission and upload to website is with this week.	February 12, 2019			dc.nuwakot@hrrpnepal.org	<i>Letter</i>
Field visit and ward level interaction meeting in Bidur Municipality ward no 2, Nuwakot durbar heritage site has 428 hh. Among them 250 has completed as per the construction rule of cultural heritage site.	February 13 , 2019	4	2	dc.nuwakot@hrrpnepal.org	<i>See Detail in field visit Section</i>

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location	Organizer	Contact Person
District Level Coordination Meeting		HRRP Nuwakot	dc.nuwakot@hrrpnepal.org /im.nuwakot@hrrpnepal.org

Tranche Status												
Rural /Municipality	Belkotgadhi NP	Bidur NP	Dupcheshwor RM	Kakani RM	Kispang RM	Likhu RM	Meghang RM	Panchkanya RM	Shivapuri RM	Suryagdhi RM	Tadi RM	Tarkeshwaor Rm
Total HHs Surveyed	9409	11203	5448	6157	1816	4003	4052	3692	5616	4197	4231	3760
Total HHs Eligible	11036	12667	5873	6916	2369	5107	4500	4226	6513	5019	4604	4353
Total HHs Enrolled	10326	11886	5639	6309	4267	4479	4244	4036	6008	4604	4450	4217
First Tranche	10326	11886	5639	6309	4267	4479	4244	4036	6008	4604	4450	4217
Second Tranche	8667	10223	5227	5451	3823	3686	3871	3653	5044	4097	4019	3718
Third Tranche	1713	5606	3593	3020	2554	2328	3040	2178	3063	2008	2630	2818
Total HH Constructed												
Grievance Registered	2271	1693	425	1389	809	1329	511	910	995	923	701	672
Grievance Addressed	1627	1464	425	759	553	1104	448	534	897	822	373	593
RF HH Eligible	256	236	35	160	25	154	141	88	63	16	23	247
RF HH Enrolled		18	1	44		9		18	1	44		9
RF 1 st Tranche		18	1	44		9		18	1	44		9

as of 29th Jan 2019.


Source : GMALI Nuwakot

Graph of Tranche Status:

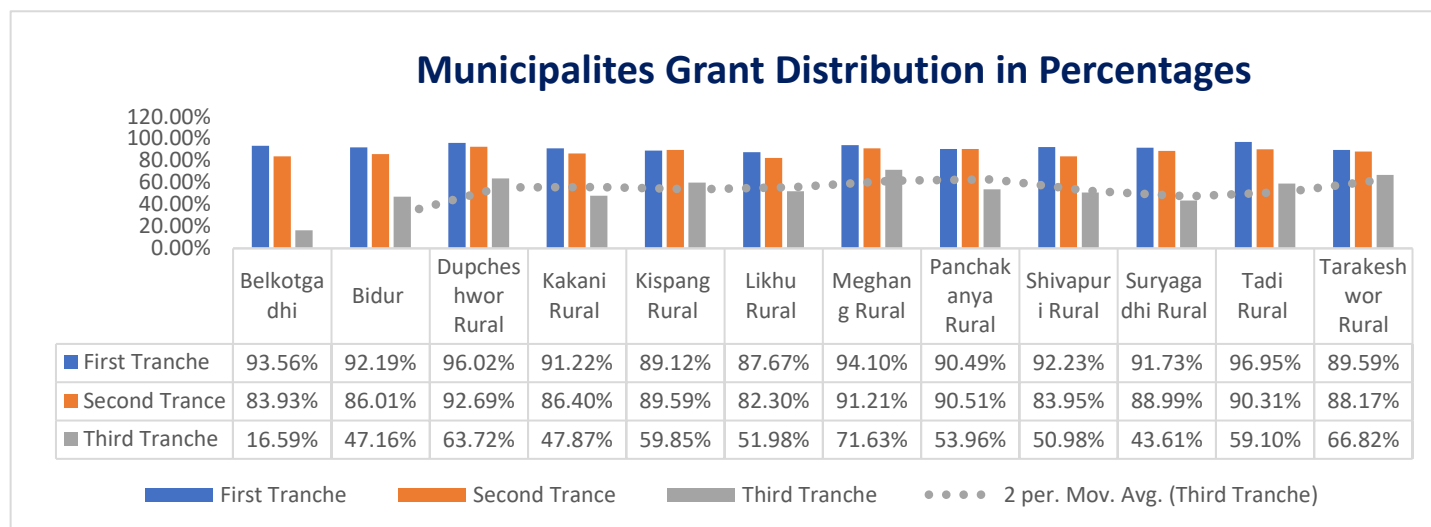

Graph for Retrofitting Status: NA

Graph for Grievance Status:

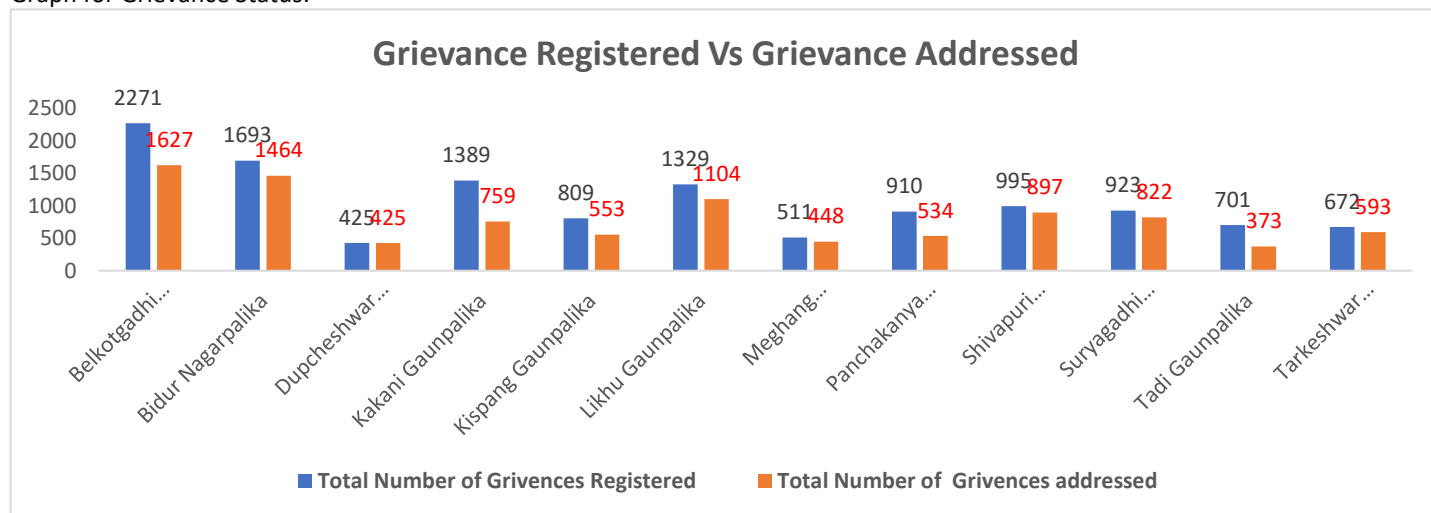

Field Visit /Joint Field Monitoring Visit Reports


Visit 1

Date	Location	Participants from HRRP and stakeholders
Feb 7, 2019	Tadi Rural Municipality ward no-3, Kharanitar	- Badri Pyakurel, DC HRRP - Bickey Lakha, Act GMALI Chief, Nuwakot

Objective(s)

- Objective 1: Monitoring the activities performed by CARDSN IP of Oxfam
- Objective 2: To know the reconstruction trend and highlighting the issues related to grant

- Objective 3: To understand the field challenges and best practice

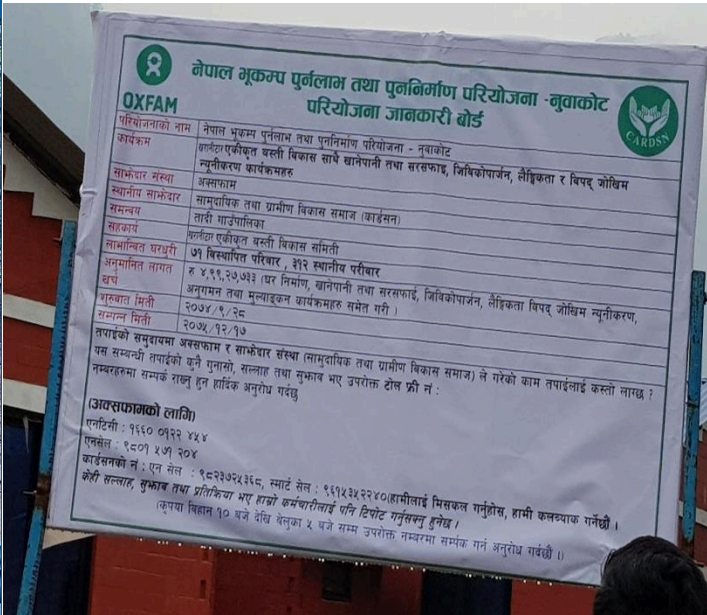Summary			
CARDSN, Implementing partner of OXAM, is working for relocated hh from Urleni VDC since 1.5 years. 71 hh are relocated from Urleni former vdc, now it is Tadi RM ward no 3. Cardsn is working for wash project in support of PURNIMA for the host community and the relocation area. It has different training program to the family from Urleni to support livelihood. Support for the private housing through the skill transfer, training to the local for CSEB construction. National Reconstruction Authority (NRA) has support to them for land purchase and all construction activities are being conducted with support from OXFAM. Among the 71, 24 families are handover to owner, 20 are just started 27 are on roofing. As per saying of Indira Adhikari, Executive director of CARDSN, they will complete the construction with in March 2019 end. Untimed rain, lacking of manpower may hinder the timeline though they are committed for completion in planned dateline.			
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Transportation of reconstruction Materials	promote to use locally available materials	POs, Ward offices	Regular
Quality of reconstruction materials	Quality assurance to local supplier	Rural Municipality	Regular
Lack of trained mason	training to local mason for retrofitting	POs and NRA	Regular
Lack of Information regarding the technical on retrofitting and correction.	Training/orientation engineers deployed in local level.	POS, NRA	As soon as possible.
Photos			
			
Fibrocement tank capacity of 14 M3 for the 71 hh. The water supply project is supported by PURNIMA (UK Aid) project, implemented by CARDSN. Monitored by Bickey Lakha Gmali Act chief and Indira Adhikari, Executive Director, CARDSN.		Display board in Project site. We can see the project cost, benefitted family, project duration and project activities are detailed in the board. The board has installed in project site.	
Visit 2:			
Date	Location	Participants from HRRP and stakeholders	
February 13, 2019	Bidur Municipality ward no 2, Nuwakot Dubar cultural heritage site.	• Badri Pyakurel, DC HRRP • Bickey Lakha, Act GMALI Chief, Nuwakot	

Objective(s)	
- Objective 1: Monitoring the construction in Cultural heritage site, its issue and challenges. - Objective 2: To know the reconstruction trend and highlighting the issues related to grant - Objective 3: To understand the field challenges and best practice	
Summary	
Nuwakot Durbar heritage site is identified as heritage site. It has an organization Nuwakot Durbar cultural heritage settlement. It is active to preserve the settlement as the historical appearance. The area has 428 identified houses to preserve. As per the saying of ward chair, Birendra Kumar Shahi, he has developed a fundamental rule for the construction of individual in this area. Community has also support to for the construction. Bidur Municipality has support to the identified hh of 40 thousand extra for heritage construction. They can't use Cement, aluminum, Concrete in front part of their construction. NRA has support program of 50 thousands per houses to the site. More than 100 houses has received 40k extra from Bidur Municipality but not received yet from NRA's extra support.	
	
Nuwakot Durbar, made at the period of Prithivi Narayan Shah, is now ruined during the Gorkha Earthquake. Reconstruction is not started	Ruined old monuments in durbar site which is endangered to passerby as well needs to reconstruct as soon as possible.
	
Construction in heritage site by using artistic wood, stone and Different kinds of brick. The house owner says, he has plan to make an exemplified one.	There is different in construction for roof, front wall and color.

Housing Typology Report



House Owner: Badri Man Shrestha
Location: Bidur-2, Nuwakot Durbar area.
Tranche Status: has received 2nd tranche and received extra support from Bidur Municipality.

Photo: Badri Pyakurel

House Owner: Rajan Khanal
Location: Bidur-2, Nuwakot Durbar area.
Tranche Status: has received 2nd tranche and received extra support from Bidur Municipality.

Photo: Badri Pyakurel



House Owner: Devendra Shrestha Location: Bidur-2, Nuwakot Durbar area. Tranche Status: has received 2nd tranche and received extra support from Bidur Municipality. <i>Photo: Badri Pyakurel</i>	House Owner: Santoshlal Shrestha Location: Bidur-2, Nuwakot Durbar area. Tranche Status: has received 2nd tranche and received extra support from Bidur Municipality. <i>Photo: Badri Pyakurel</i>
	
House Owner: Relocation integrated settlement Location: Tadi-3, Kharanitar. Tranche Status: Construction supported by Oxfam. Typology: CSEB <i>Photo: Badri Pyakurel</i>	House Owner: Relocation integrated settlement Location: Tadi-3, Kharanitar. Tranche Status: Construction supported by Oxfam. Typology: CSEB (In Pic: Bickey Lakha, Acting Chief of GMALI Nuwakot) <i>Photo: Badri Pyakurel</i>
