

Monthly District Report

Sindhupalchok

23 August - 27 September 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Sindhupalchok	Monthly Progress update	3 rd Sept	GMaLI	pradip.sharma@hrrpnepal.org	N/A
	Field visit with DLPIU GMaLI/ Building to collect the updates on Third Inspection, Completion Certificate distribution and CS Entry progress. Follow up with local level and POs on PA Scan copy	4 th - 6 th Sept	Balephi and Sunkoshi Rural municipality	pradip.sharma@hrrpnepal.org	Field visit section below
	Follow up palika profile upload, municipality survey assessment, upload housing typology	9 th - 11 th Sept	N/A	pradip.sharma@hrrpnepal.org	N/A
	Field visit with DLPIU GMaLI/ Building to collect the updates on Third Inspection, Completion Certificate distribution and CS Entry progress. Follow up with local level and POs on PA Scan copy	16 th to 19 th Sept	Indrawati and Panchpokhari Rural Municipality	pradip.sharma@hrrpnepal.org	Field visit section below
	5W Update	23 th Sept	N/A	im.kavrepalanchok@hrrpnepal.org	GD
	Prepare District Report, Meeting minutes, meal report	24 th - 26 th Sept	N/A	pradip.sharma@hrrpnepal.org	GD
	PA Form Collection Followup at Palikas and Ward	30 th Sept	N/A	pradip.sharma@hrrpnepal.org	N/A

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Field visit to Bhotekoshi and Lisankhupakhar Rural Municipality and Palika and ward level Coordination meetings Housing Typology Survey collection (including-District report, various Maps and info graphics, related to those RM) Conduct Municipal Capacity Assessment Survey	1 st to 4 th Oct 2019	HRRP Sindhupalchowk	gradip.sharma@hrrpnepal.org

Tranche Status (Sindhupalchowk)


Table of Tranche Status: As of 31th August 2019

Municipality	Reconstruction				Retrofit			Grievances	
	Eligible HHs	1st Tranche	2nd Tranche	3rd Tranche	Eligible HHs	1st Tranche	2nd Tranche	Registered	Addressed
Balefi Gaunpalika	6241	6054	5969	5966	5834	5366	91	19	12
Barhabise Nagarpalika	7988	7995	7868	7790	7438	6290	27	8	16
Bhotekoshi Gaunpalika	4438	4226	4145	4141	3578	1947	69	14	15
Chautara SangachokGadhi Nagarpalika	14580	13999	13758	13811	13365	12494	97	49	32
Helambu Gaunpalika	5732	5422	5200	5248	4810	4181	52	6	8
Indrawati Gaunpalika	8569	8389	8229	8064	7730	6591	39	23	26
Jugal Gaunpalika	5660	5666	5592	5587	5363	4821	17	6	15
Lisangkhu Pakhar Gaunpalika	4873	5376	4947	4957	4382	3205	40	8	11
Melamchi Nagarpalika	13946	13421	13142	13112	12304	9953	123	20	9
Panchpokhari Thangpal Gaunpalika	6461	7359	6903	6902	6387	4962	20	3	8
Sunkoshi Gaunpalika	5608	5749	5578	5573	5345	4060	34	10	10
Tripurasundari Gaunpalika	4512	4593	4486	4464	4332	3706	19	5	5

Graph of Tranche Status: As of 31th August 2019

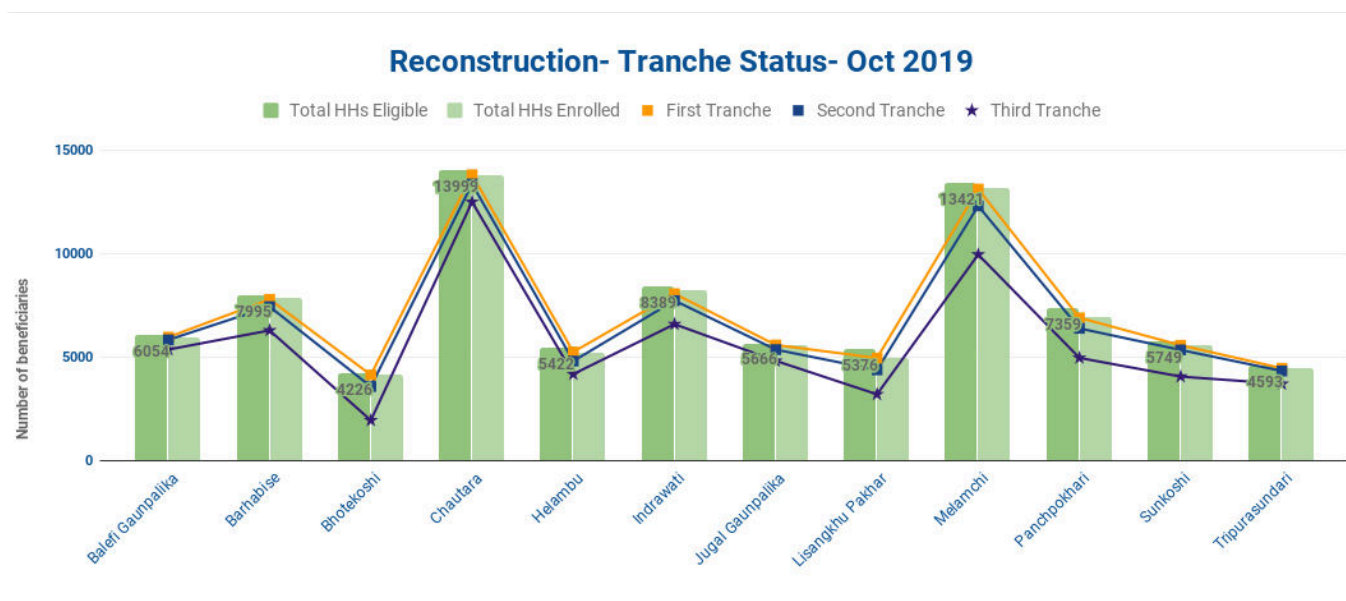

Graph for Retrofitting Status: As of 31th August 2019

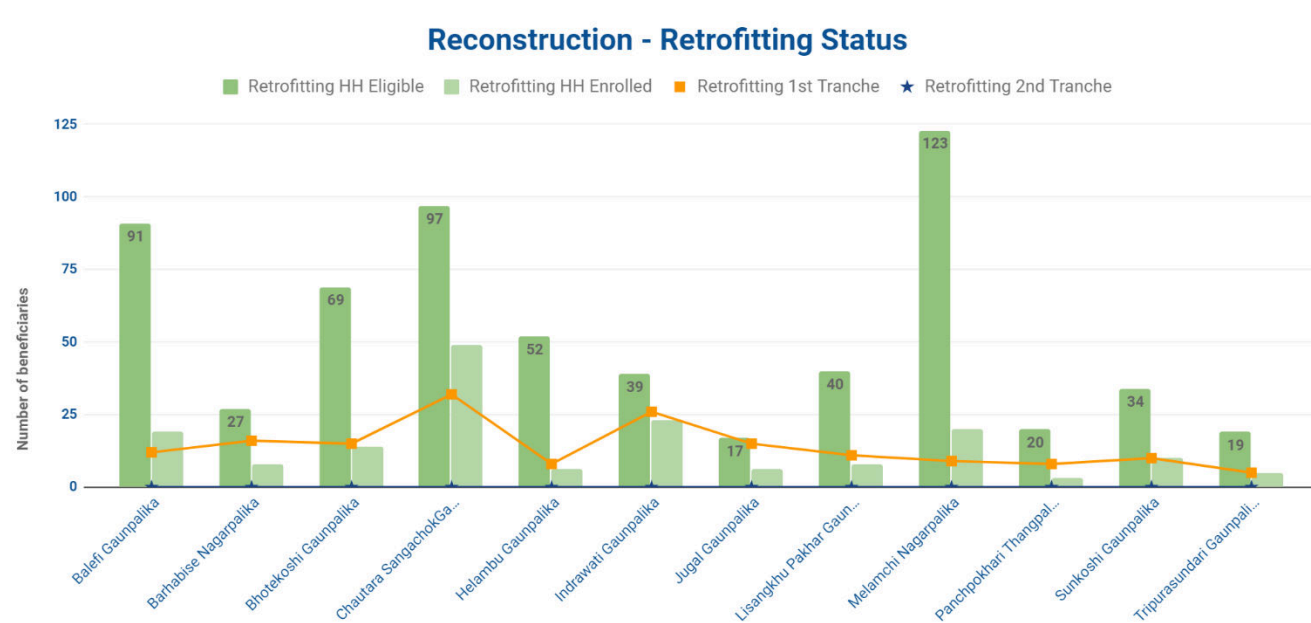

Field Visit Report (Sindhupalchowk)

Visit 1

Date	Location	Participants
4 th and 6 th September, 2019	Balephi and Sunkoshi Rural Municipality	Bishnu Paudel Seth; Chief GMaLI, Durga Regmi, GMaLI; Pradip Sharma, HRRP, Krishna Gyawali and Suman Kaphle Building and Palika/ward members
16 th to 19 th September, 2019	Indrawati and Panchpokhari Rural Municipality	Bishnu Paudel Seth; Chief GMaLI, Durga Regmi, GMaLI; Pradip Sharma, HRRP, Basanta Thapa Magar and Arjun Jaiswal Building and Palika/ward members
Objective(s) Balephi RM	- Regarding the reconstruction issue - Regarding the retrofit issue - Regarding the progress in tranche disbursement - others: - Information was provided their Ninety percent of the tranche has been forwarded in balephi rural municipality while rest are on the process. - Due to transfer of Engineers the two different beneficiaries took Third tranche by showing same house. The case is of ward-1 and name of the house owner is Mr. Anil Tamang. - As per engineer, in ward no.3, the wood band of corrected houses are not good in shape. - Due to the phased out of Save the Children (an INGO), one of the beneficiaries named Mr. Subba Tamang received first and second tranche but didn't receive third tranche as his house has already been complete and constructed. He is roaming around either thither side to get third tranche. - In ward no.7 a few houses are done simple maintenance, but beneficiaries pressurized engineers to inspect those houses as retrofitted. - Due to mistakenly entry of third tranche into second tranche of ward-8 by GMaLI, the disbursement became delayed said by ward technician. - The ward chief of ward-7, Mr. Karkel Lama is insisted and very vocal about the disbursement of all tranches of 5 houses of his ward which has constructed before engineer's deployment.	
Objective(s) Sunkoshi Rural Municipality	- Review of last meeting/meeting minute - Regarding the progress issue and challenge - Regarding the progress in tranche disbursement - others: Decisions: - Seven buildings are yet to be built in ward no.2, of which one is left in the DPC and the other is out of the beneficiary contact of the building. - Houses like ward no.3 are often abandoned and refuse to improve. - The height of the bugle in Oda No. 1 is 5 feet and will not improve - In ward number 4, there were 4 buildings left to be built and they reached outside the beneficiary contact and 12 buildings were closed out of contact by DPC. Likewise, six buildings have reached the ceiling but due to non-roofing, CS is unable to entry. 5 Ward 33 shows the various reasons for building a building and 4 building is out of touch	

	- Likewise, two beneficiaries returned the tranche - Sitaram Bhandari (23-78-3-0-11) and (23-78-3-0-49) Dil Bahadur Karki - The number seven ward does not have the land two beneficiaries to show the various reasons for the building to be built and there are no beneficiaries to build the building - the document verifying the relationship should be provided.
Objective(s) Indrawati Rural Municipality	- Review of last meeting/meeting minute - Discussion about retrofit - Discussion about the reconstruction issue, challenge and progress - Regarding the target Decisions: - Pemba Dorje Tamang at ward No. 1 is out of contact 531 beneficiary's building is completed and ready to receive the certificate of prosperity - Request for Initiative for Change if the Certificate of Affluence is Thin - In Chautara Sagachok Gadhi Municipality ward No. 13, if it is found to be a prosperity certificate, then providing one as well as - One beneficiary of land without benefit would be allowed to remain in the building. - The building of 16 beneficiaries has been completed in ward number 9, but again the beneficiary list is listed. - According to the municipality chairperson, the technician should take care of the condition of the beneficiaries of the completed building. - Built a lounge for the third installment but after the installment, the fire broke out and the fire broke out. - According to the municipality chairperson, that he was asking why the grievance survey was going to come back.
Why was the visit carried out in this location?	
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'	
NA	
Summary	- Statistics of beneficiaries at risk in Indrawati municipality decided to collect - It has been decided to accelerate the reconstruction of Indrawati municipality at a rapid pace and distribute the completed certificates to the beneficiaries. - It was decided on the 23th September 2019, that distribution of certificates of accomplishment should be made to the beneficiaries

Field Visit: - No. of HHs visited: 6 - No. of meetings with engineers: - No. of meetings with local officials: 6 Meeting: NA				
Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Photos				
				
Meeting with Palika Chairperson, Ward Chairperson, Engineers Building / GMaLI/HRRP and Pos at Balephi Rural Municipality		Meeting with Palika Chairperson, Ward Chairperson, Engineers Building / GMaLI/HRRP and Pos at Sunkoshi Rural Municipality		
				
Meeting with Palika Chairperson, Ward Chairperson, Engineers Building / GMaLI/HRRP and Pos at Indrawati Rural Municipality		Meeting with Palika Chairperson, Ward Chairperson, Engineers Building / GMaLI/HRRP and Pos at Indrawati Rural Municipality		

Photos



The house located in Sunkoshi Rural Municipality ward no.4, the house owner has received second tranche and third tranche from GoN. The house is brick and cement mortar with load bearing structure.



The house located in Sunkoshi Rural Municipality ward no.4, the house owner has received second tranche and third tranche from GoN. The house is brick and cement mortar with load bearing structure.

Housing Typology Report



The house located in Sunkoshi Rural Municipality ward no.4, the house owner has received second tranche and third tranche from GoN. The house is Stone and Mud mortar with load bearing structure.



The house located in Sunkoshi Rural Municipality ward no.4, the house owner has received second tranche and third tranche from GoN. The house is Stone and Mud mortar with load bearing structure.



Housing Typology Report

The house located in Sunkoshi Rural Municipality ward no.4, the house owner has received second tranche and third tranche from GoN. The house is Stone and Mud mortar with load bearing structure.

The house located in Sunkoshi Rural Municipality ward no.4, the house owner has received second tranche and third tranche from GoN. The house is Stone and Mud mortar with load bearing structure.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
why the grievance survey was going to come back?	Local body	GMAI/HRRP

Challenges and Way Forward

Challenge	Way Forward
the technician should take care of the condition of the beneficiaries of the completed building.	
