



Housing Recovery and Reconstruction Platform

Co-ordination Meeting District: Dhading

DATE: 28 DECEMBER 2017


Agenda :-





- Welcome & Introduction.
- HRRP Maps & Products.
- NRA, DLPIU & HRRP Updates
- District issues & Challenges
- AOB



 Mason (5 days) Training P:641R :628 VDC Covered : 11 (ChhatreDyaurali,Kalleri Goganpani,Kewalpur, Khalte, Kumpur, Maidi, Mahadevsthan, Naubise, Tasarpu, Thakre)	 Mason (7 days) Training P:860R :860 VDC Covered : 20 (Agnichok, Lapa Baseri, Budhathum,Darkha,Gumdi,Dhuwakot, Jharlang,Marpak, Mulpani, Satyadevi, Semjong, Katunje,Sertung,Phulkhark, ReeGaun,Tipling, Tripureswor, Salyankot,Salyantar)	 Mason (7 days) TrainingWith toolkit P:200R:200 Demo House- R: 6 VDC Covered : 3 (Chainpur, Jyamrung, Khari)	 Mason -7 days Training P: 184 R: 138 VDC Covered : 4 (Maidi,Dhola, Jogimara, Nalang)	 Mason (7 days) Training With toolkit P:539 R:539 Demo House P:4 R: 4 BBS Training P:2295 R:3530 VDC Covered : 6 (Aginchok, Baseri, Budhathum, Mulpani, Phulkhark, Salyantar)	 Mason : 60(10 Days) : 21(45 Days) Electrician :60(25 Days) Carpenter :60(25 Days) VDC Covered : 2 (Semjong ,Jeevanpur)																														
 Vocational : 50 days Traning (CTEVT) Mason P: 340 R: 340 Electrician P: 20 R: 20 Carpenter P: 90 R: 90 Plumber P:20 R:20 VDC Covered : 5 (Dhuwakot, Kalleri, Katunje, Khalte, Kumpur)	 Mason -7 days Training P: 120 R: 120 BBS P:20 R: 20 CD: p-2 R-1 VDC Covered : 2 (Kalleri,Katunje)	 Mason -7 days Training with toolkit P: 2250 (75 Events)R: 1603(51 Events) TOT P :288(9 Events)R:255(8 Events) Orientations: P:2000Events R:518 OJT: P 112 Mobile Technical Support: 900 Houses Covered VDC : 12(Sertung, Tipling, Darkha, Marpak, Semjong, Jyamrung, Kalleri ,Khalte,Kumpur, Nalang, .Dhuwakot. Nilkantha Na. Pa.)	 Mason -7 days Training with toolkit P: 560 R: 560 Demo House Construction P : 5 R:4 VDC Covered : 5 (Pida, Jharlang, Mahadevsthan, Lapa, ReeGaun)	 Small cottage industries Mason -45 days Training P: 158 R: 162 Electrician: P:38 R:37 VDC Covered : 8(Gumdi Baireni, Budhathum, ChhatreDyaurali,Mulpani, Jeewanpur, Salang, Nilkantha Na.Pa)																															
 Mason -7 days Training with toolkit P: 549 R: 389 CRO(TA-BBS Training) P:1800 R:450 Demo House construction- O:4 Help Desk P:2025 R:1158 Reconstruction through contractor:32-35ongoing VDC Covered : 6 (Satyadevi ,Tripureswar, Dhusaa, Benighat, Jogimara . Gaiuri)	District Activities Status (as of 25 Nov 2017) HRRP_44 Round of 4W <table><thead><tr><th>Mason Training</th><th>Electrician</th><th>Technical Assistant</th></tr></thead><tbody><tr><td>5 days :628</td><td>25 Days :60</td><td>CRO : 3990</td></tr><tr><td>7 Days :4626</td><td>45 Days :37</td><td>DTD :12464</td></tr><tr><td>10 Days:60</td><td>50 Days :20</td><td>Help Desk :1158</td></tr><tr><td>45 Days:183</td><td>Carpenter(150)</td><td>Demo House :13</td></tr><tr><td>50 Days:340</td><td>25Days :60</td><td></td></tr><tr><td>Tot :255</td><td>50 Days :90</td><td></td></tr><tr><td></td><td>Plumber: 20</td><td></td></tr><tr><td></td><td>ASF</td><td></td></tr><tr><td></td><td>DEMO-1VT-30-25 Top ups -25 p</td><td></td></tr></tbody></table>			Mason Training	Electrician	Technical Assistant	5 days :628	25 Days :60	CRO : 3990	7 Days :4626	45 Days :37	DTD :12464	10 Days:60	50 Days :20	Help Desk :1158	45 Days:183	Carpenter(150)	Demo House :13	50 Days:340	25Days :60		Tot :255	50 Days :90			Plumber: 20			ASF			DEMO-1VT-30-25 Top ups -25 p		DUDBC(Mason) 7 days :317 (Pida,Baireni,thak re,Jeewanpur,Ma lekhu,Salyantar,C hainpur,Nilkanth a,Gajuri,) ICDC(Mason) 7 days : 36 Salang	Full Form P:Planned R: Reached O:Ongoing BBS: Build Back safer OJT: On the Job Training ER: Engineer CRO: Community Reconstruction Orientation DTD: Door to door Technical Assistant DC: Demonstration Construction House CD: Community Building
Mason Training	Electrician	Technical Assistant																																	
5 days :628	25 Days :60	CRO : 3990																																	
7 Days :4626	45 Days :37	DTD :12464																																	
10 Days:60	50 Days :20	Help Desk :1158																																	
45 Days:183	Carpenter(150)	Demo House :13																																	
50 Days:340	25Days :60																																		
Tot :255	50 Days :90																																		
	Plumber: 20																																		
	ASF																																		
	DEMO-1VT-30-25 Top ups -25 p																																		

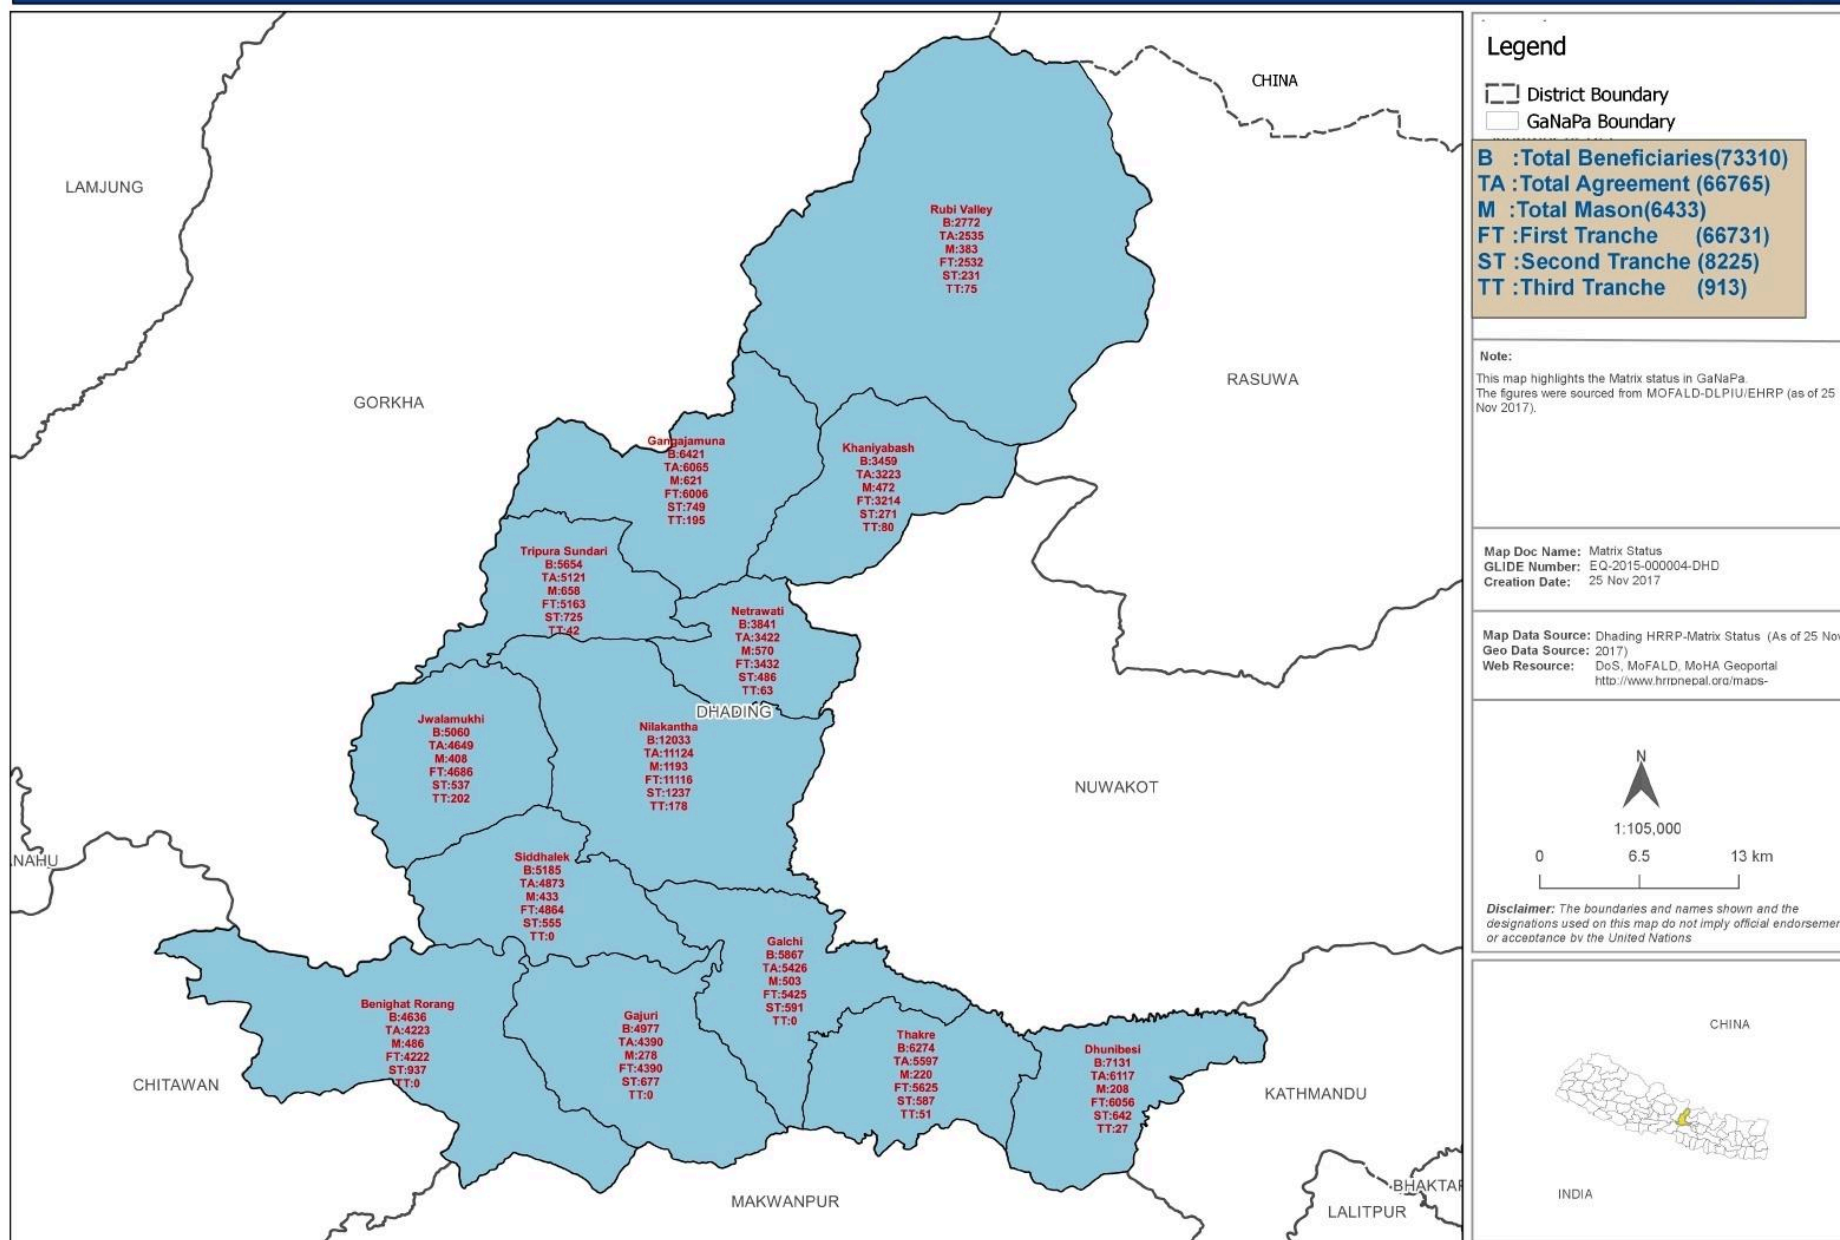

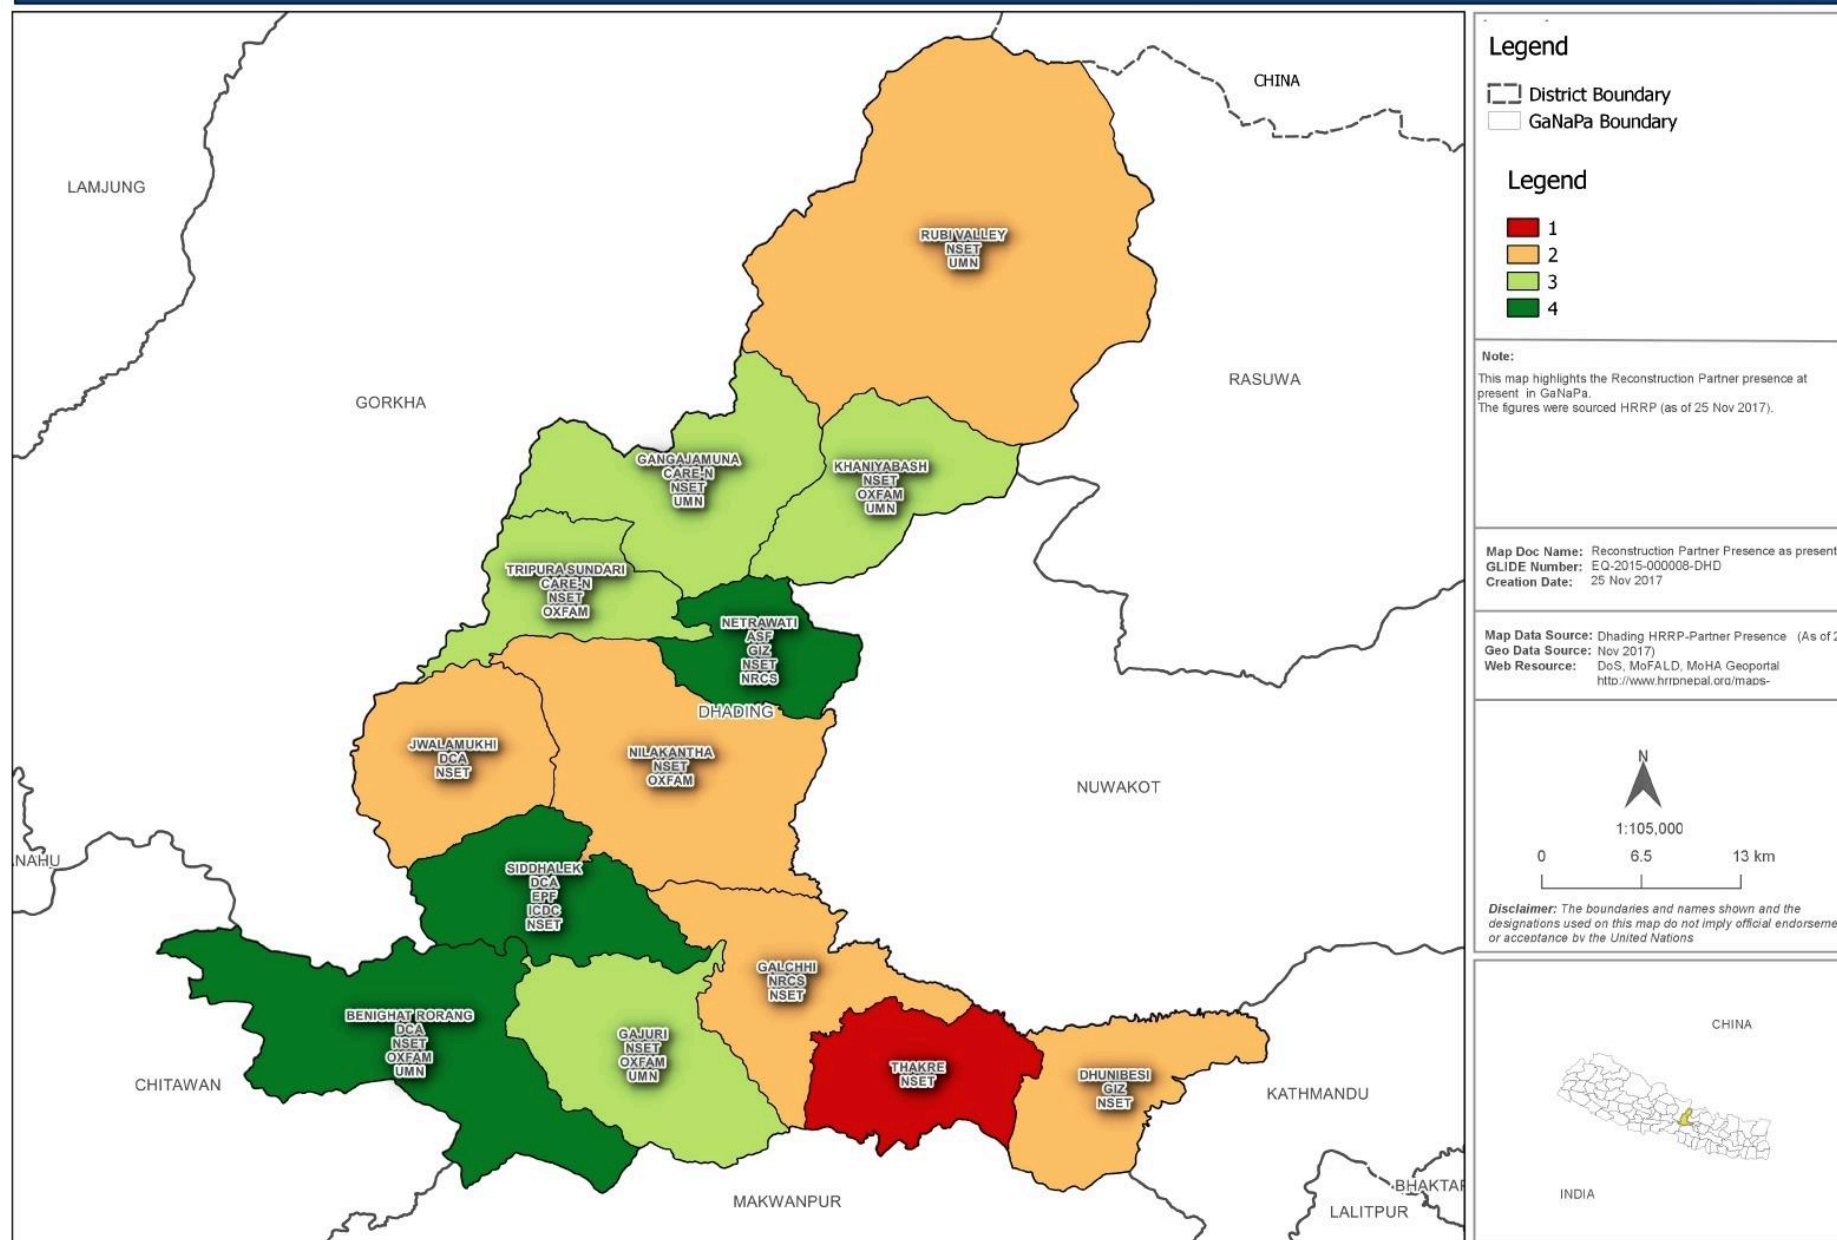

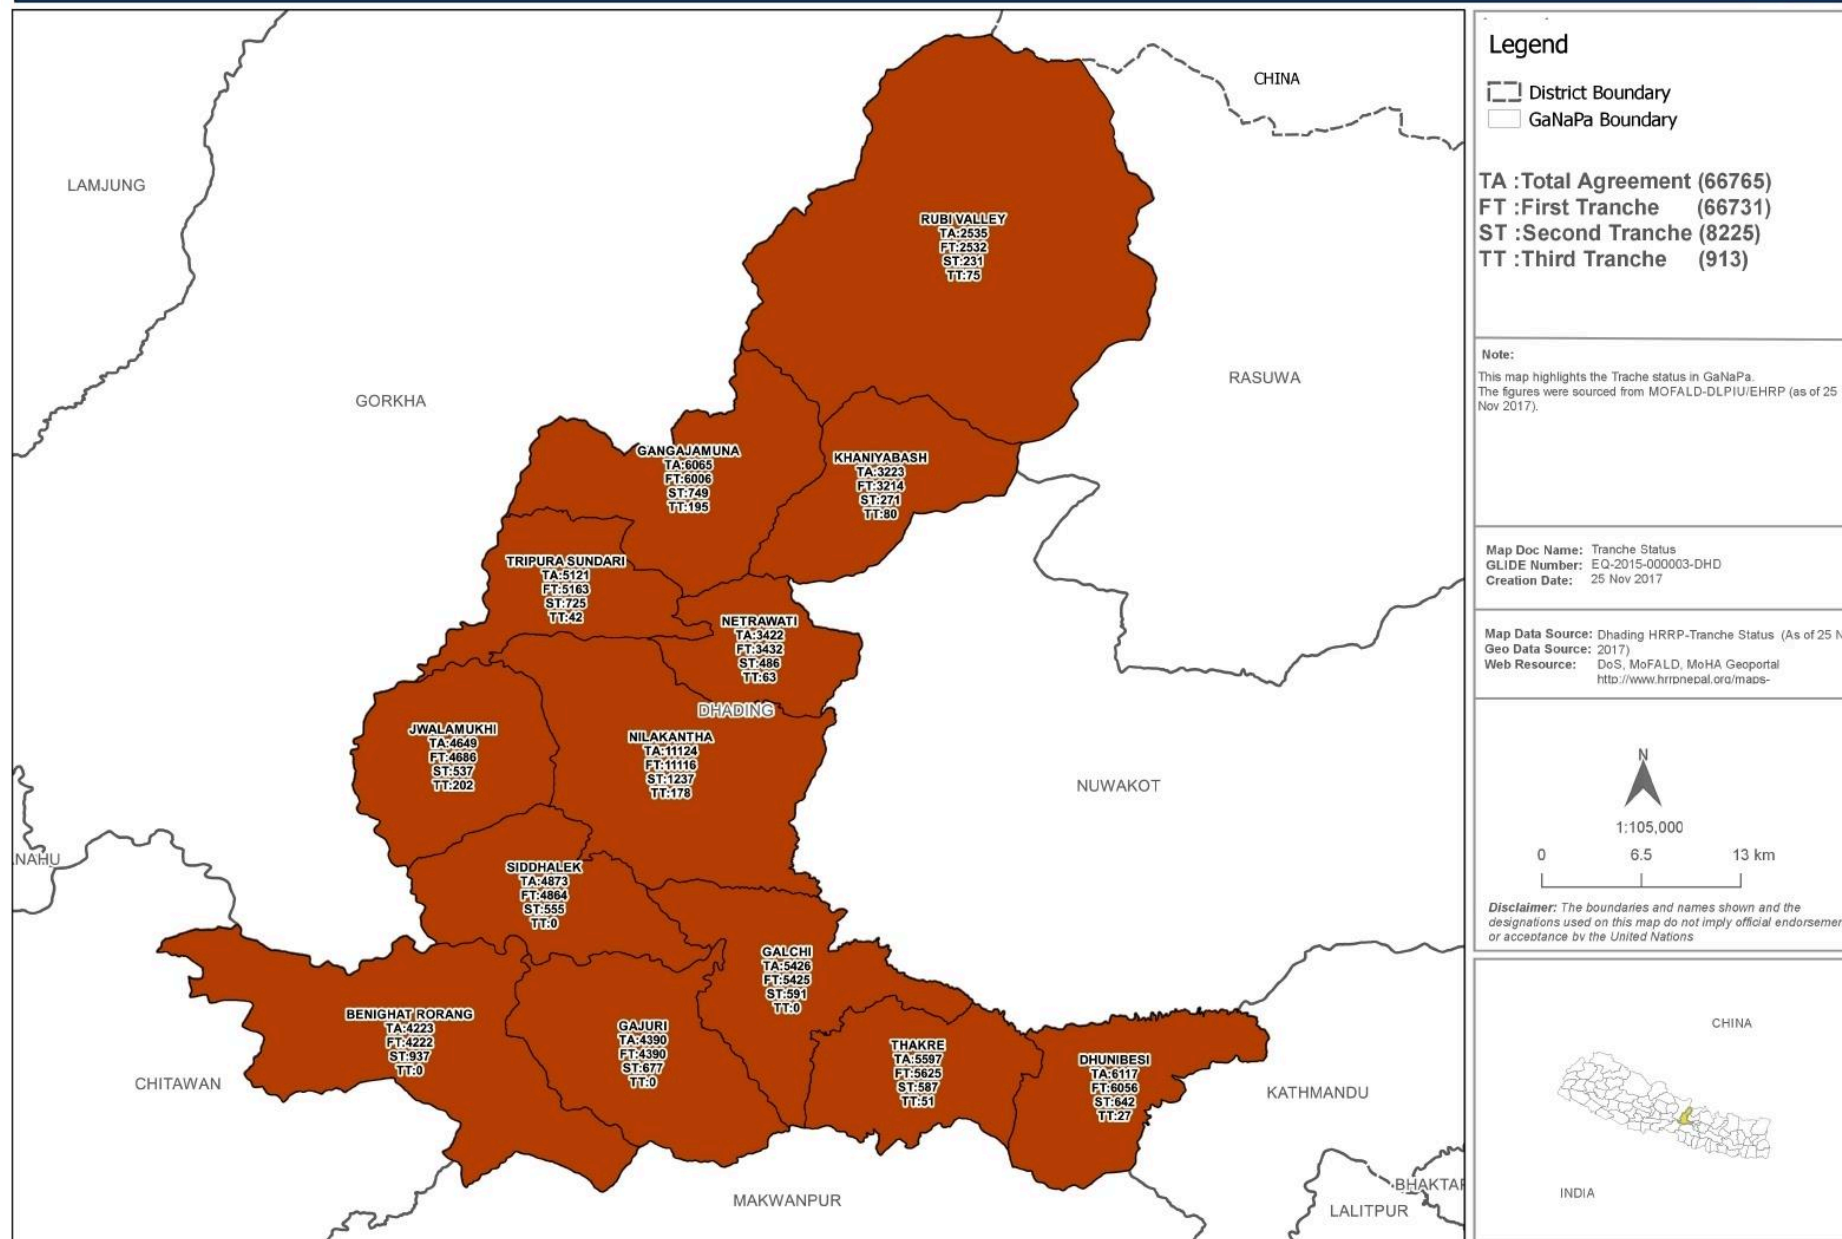

निजी आवास निर्माणको प्रगतिको अवस्था					
जिल्ला	संझौता सम्पन्न	घर निर्माण शुरु	घर निर्माण सम्पन्न	निर्माण सम्पन्न र निर्माण शुरु भएको घरको कूल संख्या	घर निर्माणमा भएकोको प्रगति प्रतिशत
१४ अति प्रभावित जिल्ला	५९५३३०	१९४१९६	७९५१४	२७३७१०	४६%

गएको ६ महिनामा झण्डै ४ गुणा बढी नयाँ घर थपिए



काँधमा काँध मिलाउनेहरु: पुनर्निर्माणमा गैर सरकारी संस्थाहरुको सहकार्य

- कार्य गर्नका लागि अनुमति लिएका संस्थाहरु: १८७
- प्रतिबद्धता गरेको रकम: रु. ४६ अर्ब ५९ करोड ९४ लाख ८५ हजार

क्र. सं.	क्षेत्र	अनुमति लिएको	सम्पन्न भएका
१	निजी आवास पुनर्निर्माण	२२७५४	८३८२
२	विद्यालयहरुको भवन पुनर्निर्माण	७५१	३५८
३	स्वास्थ्य चौकी भवन पुनर्निर्माण	८७	३७

जोखिमयुक्त स्थानबाट सुरक्षिततर्फ



भौगर्भिक अध्ययन सम्पन्न स्थान :	७९१
सुरक्षित स्थान:	३८९
सुरक्षा उपाय अवलम्बन गर्नुपर्ने:	२१२
पुर्ण वा आंशिक रूपमा असुरक्षित:	१९०
जोखिमयुक्त स्थानमा रहेका लाभग्राहीहरूको संख्या	२४९८
नुवाकोट र रसुवा जिल्लाबाट बस्ती स्थानान्तरण कार्य शुरु	
रु. २ लाख अनुदान लिइ सुरक्षित स्थानमा जग्गा व्यवस्थापन गरिसकेका लाभग्राहीको संख्या	९६

सि.नं.	पुनर्निर्माणको क्षेत्र	प्रगति प्रतिशत
१	निजी आवास निर्माण	४६%
२	शैक्षिक संस्थाहरुको पुनर्निर्माण	४९.६%
३	स्वास्थ्य संस्थाहरुको पुनर्निर्माण	४८%
४	सार्वजनिक भवनहरुको पुनर्निर्माण	३७%
५	सुरक्षा निकायका भवनहरुको पुनर्निर्माण	४८%
६	पुरात्वात्विक संपदाहरुको पुनर्निर्माण	५२%
७	खानेपानी संरचनाहरुको पुनर्निर्माण	५८%



EHRP Update - Dhading :-



■ Total no of Beneficiaries	=	73,310
■ Grant Agreement	=	67,247
■ First Tranche	=	66,731
■ Second Tranche	=	8,225
■ Third Tranche	=	913
■ Retrofitting	=	14,94

Rate of Reconstruction



District issues & Challenges





Thank You 😊
