

District Report

Kavrepalanchok

9 – 16 November 2017

Activity Summary

Activity	Contact Person	Reference Document
Contact List Update	im.kavrepalanchok@hrrpnepal.org	Google Drive/Gmail
Brief Visit to Panchkhal Municipality	reshma@hrrpnepal.org	Field Visit Report
Field Visit to SipaliChilaune	im.kavrepalanchok@hrrpnepal.org	Field Visit Report
Hollow Concrete Blocks Survey	reshma@hrrpnepal.org	Google Drive
HRRP Coordination Meeting	reshma@hrrpnepal.org	Meeting Minutes to be shared

Upcoming Events & Meetings

Event / Meeting	Date, Time, and Location	Contact Person
Field Visit to Chyamrangbesi	22 nd Nov 2017, Chyamrangbesi	Reshma Shrestha

To include details of upcoming events and meetings in the next bulletin, please share details with reshma@hrrpnepal.org by COB Wednesday of each week.

News & Updates

NRA Kavre with Central NRA conducted field assessments to Bhumlau, BoldeFediche and ChandeniMandan to assess the landslide risks of the former two areas and the possibility of proposing integrated settlement at ChandeniMandan.

Field Visit Report

Date	Location	Participants
14 th Nov 2017	Koshidkha VDC	M&E Specialist, DLPIU engineers, HRRP Kavre
Objective(s)	- Meeting with Panchkhal Municipality regarding deployment of engineers and the status of Participatory Agreement Form Collection. - Field Visit to Koshidekha to collect details on Hollow Concrete Blocks Houses. - Collect the reconstruction status of Koshidekha.	
Summary	The summary of the meeting at Panchkhal Municipality can be listed as: - The name lists of the technical persons assigned to the municipality has been received and within a couple of days, all of them will be assigned to the work stations. - An official letter has been received from MoFALD/DLPIU regarding the collection of PA Forms. Brief time will be required to get the forms collected from the respective wards. Vehicle arrangement for delivering the forms to MoFALD office would not be a problem but the main issue will be ascertaining the overall responsibility of collecting, delivering and bringing back the PA Forms. - The municipality is in discussion to waive the building permit tax for Load Bearing Masonry as per the design catalogue. This concept will be discussed in the monthly	

meeting of the municipality and actions will be taken accordingly.

Due to the long gap of technical resources at Koshidekha due to various circumstances, there is no data on the reconstruction status of the VDC. At current, technical persons have been mobilized and they are in initial stages of collecting information on the reconstruction status. Most of the constructions are Hollow Concrete Block Masonry constructed after material assistance provided from Navjyoti Center. Stone in Mud Masonry too are being constructed but compliance cannot be ascertained. Some of the constructions in Stone in Mud with Wooden Bands can be seen constructed in two storeys with attic. These households mention to have constructed in this way as they had no information on the required construction techniques.

Photos



This ongoing construction of Stone in Mud Masonry at Koshidekha initially was preparing for Plinth Level RCC Band casting with no provisions of Vertical Reinforcements. The timely visit of DLPIU engineers provided the required assistance and timely correction for the construction.

Field Visit Report

Date	Location	Participants
15 th Nov 2017	SipaliChilaune VDC	M&E Specialist, HELVETAS, HRRP Kavre
Objective(s)	Get an overview of reconstructed houses by the masons trained through Vocational Trainings by HELVETAS.	
Summary	After attending the 50 Days Vocational Training by HELVETAS, 20 houses have been reconstructed at SipaliChilaune VDC. These houses were covered during this field visit. Stone in Mud mortar with RCC bands dominated the reconstruction typology. The newly trained masons are involved into constructions under the continuous supervision of HELVETAS technical capacities. The general overview of the reconstruction status of the area too was studied during the visit. There has been a long gap of Technical Assistance by DLPIU engineers since	

Dashain, resulting the halt of verifications/inspections for Second and Third Tranche. Also, countable numbers of one roomed houses have been constructed.

Photos



A one roomed Brick in Mud Masonry with RCC Band at SipaliChilaune. The house owner Pramod Regmi has received First Tranche and awaits the inspection for the further tranches.

Housing Typology Report



House Owner: Aasha Bahadur Tamang

Location: Koshidekha VDC (Now Panchkhal Municipality)

Building Typology: Stone in Mud with Wooden Bands

This house has received Second Tranche. Due to a couple of months gap in technical assistance, none of the houses have been verified for the third tranche in the VDC.



House Owner: Tej Bahadur Tamang

Location: Koshidekha VDC (Now Panchkhal Municipality)

Building Typology: Stone in Mud with Wooden Bands

This house has received Second Tranche whereas the inspection for the third tranche is yet to be done. Hollow Concrete Blocks have been used at the corners due to difficult access to proper large stones.



House Owner: Bishnu Bahadur Tamang

Location: Koshidekha VDC (Now Panchkhal Municipality)

Building Typology: Stone in Mud with RCC Bands

This house has received Second Tranche and still awaits the inspection for the Third Tranche.



House Owner: Hem Raj Kunwar


Location: Mahendrajyoti VDC (Now Banepa Municipality)

Building Typology: Interlocking Blocks with Brick in Cement Masonry at the First Floor

This house has received First Tranche and inspection for the second has been done. As the design does not comply with the designs in design catalogue and standards do not exist for such structures, there are confusions for the process of verifying such structures for the further tranches.



House Owner: Ambika Mainalee
Location: SipaliChilaune (Now Roshi Gaupaika)
Building Typology: Stone in Mud with RCC Bands
This house has received First Tranche and still awaits the inspection for the Second Tranche.

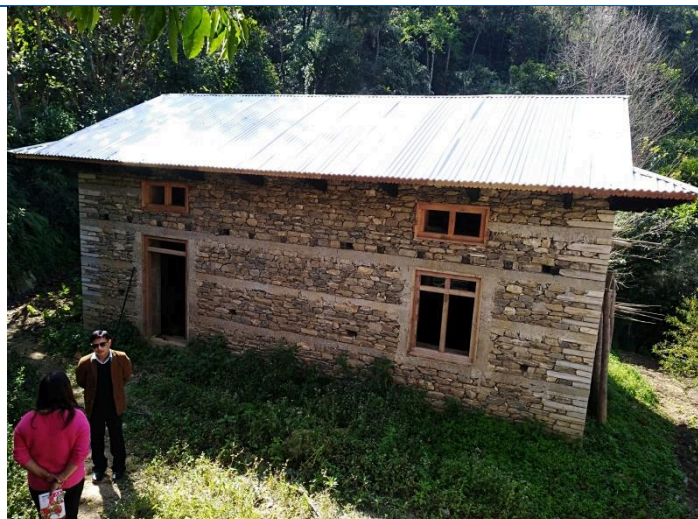

House Owner: Man Bahadur Ghalan
Location: SipaliChilaune (Now Roshi Gaupaika)
Building Typology: Stone in Cement with RCC Bands
This house has received First Tranche and still awaits the inspection for the Second Tranche.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Are Interlocking Block Houses not compliant for the Government Subsidy?	House Owner, Mahendrajyoti	For now, the designs as per the Design Catalogue II are eligible for the tranches. Further details can be collected from the DLPIU engineers assigned in the area. (HRRP Kavre)
