

[Media Digest](#) | [FAQ](#) | [Briefing Pack](#) | [Meeting & Events](#) | [4W](#) | [Housing Progress](#) | [Housing Typologies](#)

## HRRP BULLETIN

15 October 2018



*Bhubaneswari Prajuli, HRRP National Technical Coordinator, presenting on the topic of local capacity and localisation at the Shelter Centre meeting (more information [here](#)) which took place as part of the Global Shelter Cluster's annual shelter week event.*

### Highlights


- HRRP would like to wish all our partners a very happy Dasain!
- Update from HRRP participation in the Global Shelter Cluster's 'October Shelter Week'
- Number of households eligible for retrofit grant that have received the second tranche of the grant has jumped from 1 on 1 October to 359 today
- Report from Mott MacDonald Access to Finance workshop in August
- [Access to Finance Workshop Report, August 2018, Mott MacDonald Purnima Project](#)
- [Housing Reconstruction Progress Maps](#), based on Building CLPIU inspection data as of 5 October

## UPDATES & REQUESTS

### National

[NRA, CLPIU GMALI and Building, Grant Disbursement Data, as of 15 October:](#)

| Reconstruction Grant                    | 17 September | 1 October | 15 October |
|-----------------------------------------|--------------|-----------|------------|
| Total No. Eligible HHs                  | 810,196      | 810,226   | 811,857    |
| HHs Enrolled                            | 721,722      | 723,832   | 727,237    |
| HHs Received 1 <sup>st</sup> Tranche    | 716,665      | 718,057   | 723,396    |
| HHs Applied for 2 <sup>nd</sup> Tranche | 518,041      | 522,077   | 528,107    |
| HHs Received 2 <sup>nd</sup> Tranche    | 498,696      | 503,583   | 509,066    |
| HHs Applied for 3 <sup>rd</sup> Tranche | 304,940      | 314,866   | 332,540    |
| HHs Received 3 <sup>rd</sup> Tranche    | 259,477      | 267,141   | 289,862    |
|                                         |              |           |            |
| Retrofit Grant                          | 17 September | 1 October | 15 October |
| Total No. Eligible HHs                  | 50,784       | 50,787    | 53,318     |
| HHs Enrolled                            | 9,466        | 10,009    | 10,778     |
| HHs Received 1 <sup>st</sup> Tranche    | 8,473        | 8,779     | 9,640      |
| HHs Received 2 <sup>nd</sup> Tranche    | 1            | 1         | 359        |

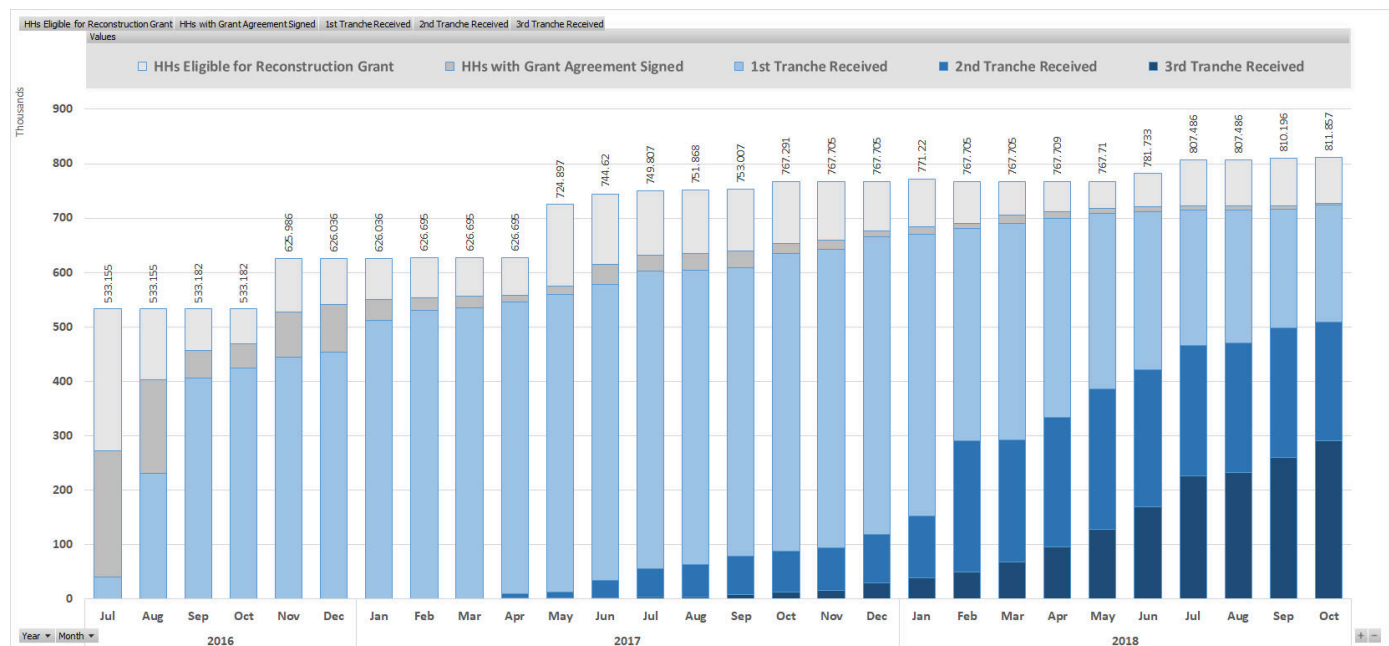

*Progress with the disbursement of the GoN housing reconstruction grant based on NRA, GMALI CLPIU, and Building CLPIU data from July 2016 to 15 October 2018.*

[Global Shelter Cluster, Annual Shelter Week, 1-5 October:](#) HRRP Nepal participated in the Global Shelter Cluster 'October Shelter Week', attending and presenting at the Cluster Coordinators Workshop, the Global Shelter Cluster Annual Meeting, and the Shelter Center Shelter Meeting. The main purpose of the week was to review and revise Shelter Cluster Coordination practices, methodologies, and tools. The workshop also focused on identifying and working to address the issues from country level clusters and IASC global level cluster-related initiatives and included a review of GSC deliverables in 2018 and discussion on how to advance the GSC 2018 – 2022 strategy. During the week HRRP shared experiences and updates on the needs and progress in Nepal, presented on the effectiveness of socio-technical assistance, the transition from the shelter cluster in Nepal, and links to recovery and challenges of the reconstruction. HRRP advocated the importance of socio-technical assistance in housing

recovery and reconstruction using examples from Nepal and emphasised that shelter / housing is a process not a product. HRRP also shared the challenges and successes of the transition from the shelter cluster to a housing recovery coordination platform. A full report will be available soon.

**Non-Resident Nepali Association's (NRNA) Global Knowledge Convention, 'Expanding Nepal's Knowledge Pool through Diaspora', 12-14 October, Kathmandu:** the NRNA organised the event, in partnership with the Government of Nepal (GoN), to bring together Non-Resident Nepalis (NRNs) with expertise in various fields of development with similar experts in Nepal. The convention was held in conjunction with the 16th NRN Day Celebrations. The event included a session on Disaster Risk Reduction in which the NRA participated. The NRNA plans to hold a knowledge convention every two years.



*NRA CEO Sushil Gyawali speaking at the NRNA Global Knowledge Convention held in Kathmandu on 12-14 October.*

**Two-day Orientation for Economic Journalists, 12 and 13 October, Dhulikhel:** the event was organised by the Society of Economic Journalists – Nepal (SEJON), in association with the NRA and with support from NDI and USAID. Journalists have an important role to play in the reconstruction and need support such as this orientation to be able to effectively take on this role.





*Participants in the orientation.*

## Districts & Municipalities

**HRRP District and Municipal Coordination Meetings, 28 September – 11 October:** during this period district coordination meetings took place in Raswua (1 October), Gorkha (11 October), and Makwanpur (11 October). Municipal level meetings took place in Bhotekoshi Rural Municipality, Sindhupalchowk (1 October), Kailash Rural Municipality, Thaha Municipality, Bhimfedi Rural Municipality, Makwanpur (3-5 October), Siddhalekh Rural Municipality, Dhading (3 October), Nilkantha Municipality, Dhading (5 October), Tamakoshi Rural Municipality, Dolakha (5 October) and Golanjar and Fikkal Rural Municipalities, Sindhuli (4-6 October). Some of the highlights from these meetings include:

- In **Rasuwa**, an update was provided on an assessment that has been completed to identify potential disasters in all five Rural Municipalities using a “vulnerable assessment form”. Identified disasters were ranked in order of their occurrence and prevalence in the district. The Disaster Preparedness and Response Plan (DPRP) Booklet was discussed during the meeting and some corrections that are required were highlighted. There was also discussion on maintaining a district relief fund in the district with support from POs working in the district. POs also shared updates on their reconstruction support in the district.
- In **Gorkha**, the 5W multi-sector information for all municipalities in the district was presented. 62% of private housing reconstruction in the district has been completed and a significant number of houses are under construction. GMALI informed that 100 households have had their grievances addressed. A notice has been published to return 50,000 NPRs (first tranche) if the household are not constructing their houses or have signed two partnership agreements. Issues regarding duplication of grant payments to households from I/NGOs and the Government were reported to have been resolved. GMALI also requested POs to provide clear information to households with language and / or literacy problems. Just one household eligible for the retrofit grant in the district has received the second tranche. The meeting

also discussed how to improve the quality of construction by working with house owners, contractors, and material vendors and producers.

- In **Makwanpur**, GMALI shared that the housing reconstruction progress in the district is lower than expected and all concerned stakeholders were requested to focus their efforts on speeding up the reconstruction in the coming months. An update from the municipal level consultation and action plan development workshop was provided during the meeting. All ten local bodies have submitted their municipal action plan.
- In **Bhotekoshi RM, Sindhupalchok**, some organisations have been implementing reconstruction activities without coordinating with the DLPIU or relevant Municipality and Ward. Some households continue to live in their old houses that have been repaired but have built a one room house in another place just to receive the tranche. There is a shortage of skilled masons. There has been quite a lot of mason trainings, but they have not been effective. People discussed during the meeting that they realise that mason training alone is not effective, and that carpenter training should be included also.
- In **Kailash RM, Bhimfedi RM and Thaha Municipality, Makwanpur**, the meeting discussed options to motivate households that have taken the first tranche to start reconstruction. There are challenges because of communication gaps between Municipalities and Wards and delays in information and paperwork passing between the two. The challenges associated with the process of taking back money from households who took the first tranche but are not willing to reconstruct were highlighted. It was decided to develop a format to collect information from the households who do not want to construct and would like to refund the first tranche of GoN housing reconstruction grant. There was also discussion on the revolving fund concept that has been implemented in Gorkha. The Ward Chairpersons suggested that they could mobilise Municipal Emergency Funds for this. For resolving the landless issue, the local representatives said they need proper guidelines and instructions from the central level. Regarding, vulnerable HHs, the Wards will complete the verification of vulnerable HHs and identification of those who has been missed.
- In **Siddhalekh RM, Dhading**, the Ward Chief raised concerns that the bank has still not been serving households as per the instruction of NRA. The banks are reported to have been creating delays in payment and acted in a biased manner with some households. Most households within the ward have to walk long distances to reach the bank. They also said the grievance registration process must be stopped once the actual victims are identified and registered as beneficiaries.
- In **Nilkantha Municipality, Dhading**, the Ward Chief said many of the households have not been counted and registered on the beneficiaries list. Some of the households damaged by the earthquake have been still left behind.
- In **Tamakoshi RM, Dolakha**, land for the construction of health post with support from DUDBC Dolakha has been approved. Representatives said the rate of reconstruction is increasing after the announcement of the deadline by NRA. However, some households are still missing from the beneficiaries list. Many houses in the area have been constructed using interlocking bricks as they are locally manufactured and cheaper. Despite these houses being constructed under the supervision of Engineers, these interlocking houses have not been approved for the final tranche due to lack of reinforcements at the corners. The Ward Chairpeople informed that 2%-3% of households will not construct their houses as some of them have migrated to other places, some are out of contact, and some are not financially strong enough to construct their houses.
- In **Golanjor and Fikkal Rural Municipalities, Sindhuli**, the high compliance rate in Tinkanya and Ratanchura of Golanjor Rural Municipality was highlighted. Some of the reasons for this are the availability of skilled and unskilled masons, awareness among households about earthquake resilient housing construction, presence of POs, and knowledge and skills of masons gained through vocational training. There are still some challenges though including a lack of monitoring of trained masons, insufficient door to door technical assistance, challenge in transportation of construction materials in most areas of Tinkanya, unavailability of DLPIU technical persons, and the lengthy grant approval process. Representatives of Fikkal Rural Municipality suggested that a joint monitoring visit in all wards should be conducted in coordination with GMALI and Building DLPIUs, Fikkal Rural Municipality, and HRRP.



[HRRP District Coordination Team Dhading, Weekly District Report, 28 Sep – 11 Oct 2018](#)



**Ward No.10, Nilkantha Municipality, Dhading:** a brick and cement mortar masonry house that was built as part of a 50 day On-the-Job training delivered by the NSET- Baliyo Ghar programme. The home owner received mason training and has been involved in construction of this house as well as other houses in the community. The home owner has received the second tranche of the Government housing reconstruction grant.

[HRRP District Coordination Team Dolakha, Weekly District Report, 28 Sep – 11 Oct 2018](#)



**Ward No.2, Tamakoshi Rural Municipality, Dolakha:** a single storey, two room, stone and mud mortar masonry house. The home owner has received the second tranche of the Government housing reconstruction grant. The tentative cost of construction is 650,000 NPR.



HRRP District Coordination Team Makwanpur, Weekly District Report, 28 Sep – 11 Oct 2018



**Ward No.3, Kailash Rural Municipality, Makwanpur:** a single storey, two room, stone and mud mortar masonry house with timber bands and flexible roof. The home owner has received the second tranche of the Government housing reconstruction grant and has been approved for the third tranche.

HRRP District Coordination Team Nuwakot, Weekly District Report, 28 Sep – 11 Oct 2018



**Ward No.5, Tarkeshor Rural Municipality, Nuwakot:** a single storey, brick in cement mortar house with fixed roof. The home owner has received all three tranches of the Government reconstruction grant. The total cost of construction is 500,000 NPRs.

HRRP District Coordination Team Sindhuli, Weekly District Report, 28 Sep – 11 Oct 2018



**Ward No.4, Golanjar Rural Municipality, Sindhuli:** a single storey, load bearing brick masonry in cement mortar house. The home owner has received all three tranches of the Government reconstruction grant. The cost of construction is approximately 800,000 NPRs.

## DOCUMENTS & PRODUCTS

### HRRP

**Housing Reconstruction Progress Maps:** based on Building CLPIU inspection data as of 5 October.

[Partnership Agreement between HHs and GoN](#)

[Construction Started](#)

[1st tranche received](#)

[Compliance rate 2nd tranche](#)

[Compliance rate 3rd tranche](#)

[Construction Completed](#)

**'The Path to Housing Recovery', Third Version, September 2018**

**Urban housing reconstruction status paper:** any comments or suggestions for improvements on the document are extremely welcome and can be sent to the HRRP National Technical Coordinator, Bhubaneswori Parajuli, [techcord.national@hrrpnepal.org](mailto:techcord.national@hrrpnepal.org).

**Housing Typologies: Earthquake Affected Districts:**

**5W Products:** prepared based on the [latest round of 5W data, as of 25 August](#).



## Partners

**[Access to Finance Workshop Report, August 2018, Mott MacDonald Purnima Project](#)**: the workshop was held on 10 and 11 August at Godavari and brought together representatives from financial institutions, construction material vendors and producers, and reconstruction actors. The way forward defined during the workshop includes the following:

- Purnima Project will engage with a small number of BFIs active in Nuwakot and Dhading district to conceptualise, refine and offer their loan products to meet the MSMEs' requirement. The project will also pilot some risk-sharing mechanisms.
- Purnima Project will support MSMEs with high growth potential to improve their financial and business literacy work.
- Purnima Project will organise follow-up meetings/dialogues with policy makers and bankers at the Nepal Rastra Bank, Nepal Bankers' Association (NBA), Ministry of Finance (MoF) and National Reconstruction Authority (NRA) to discuss further on the policy level issues raised/discussed in the workshop
- Purnima Project will share the workshop findings with potential development partners who might be interested in helping to address some of the issues raised/discussed in the workshop
- Purnima Project will set up an email list of all the workshop participants and use it as a platform for sharing updates / ideas on SME financing.
- Purnima Project will disseminate findings/learnings of the workshop to a wider audience through articles and via social media.
- The workshop participants – Banks and entrepreneurs – will take back the discussion points of the workshop to their institutions and will try to implement some of the improvements.

Please contact Rabindra Singh, [Rabindra.Singh@mottmac.com](mailto:Rabindra.Singh@mottmac.com), Private Sector Development Lead for the Purnima Project, for more information on the workshop or the way forward.

---

[Media Digest](#) | [FAQ](#) | [Briefing Pack](#) | [Meeting & Events](#) | [4W](#) | [Housing Progress](#) | [Housing Typologies](#)
