

Monthly District Report

Makwanpur, Chitwan, Nawalparasi

23 August – 27 September 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Makwanpur	To participate in the DFIDS' Reconstruction Partners meeting at Dhadingbesi.	27 th August 2019	Dhading besi	makwanpur@hrrpnepal.org	Presentation Slide click here
	District Facilitation Meeting of Reconstruction	30 th August, 2019	DCC Hall, Hetauda	makwanpur@hrrpnepal.org	Meeting Minute click here..
	District Coordination Meeting of Reconstruction	14 th Sept, 2019	DCC Hall, Hetauda	makwanpur@hrrpnepal.org	Meeting Minute click here
	Participate in the Training of trainers on "earthquake Resistant Building Construction" as an Instructor . Participants: NRA engineers from the Sindhupalchok, Kavre and Sindhuli Organizer: NRA-CLPIU-Building	16 th Sept to 22 th Sept, 2019	Dhulikel, Kavre	makwanpur@hrrpnepal.org	
	Half day orientation program for Retrofit Task Force about the retrofitting and MIS non compliance issues.	23 th Sept, 2019	Hetauda, Makwanpur	makwanpur@hrrpnepal.org	Report given Below
	Update Palika Profile data of Makwanpur	22 th Sept, 2019			
	Contact list updated in GD	25 th Sept, 2019			Contact List
Chitwan	Contact list updated in GD	25 th Sept, 2019		chitwan@hrrpnepal.org	Contact List
	Update Palika Profile data of Nawalpur	22 th Sept, 2019			Palika Profile Data
Nawalpur	Contact list updated in GD	25 th Sept, 2019		nawalparasi@hrrpnepal.org	Contact List
	Update Palika Profile data of Nawalpur	22 th Sept, 2019			Palika Profile Data

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
------------------------	---	-----------	----------------

Upcoming Events & Meetings

District Facilitation Meeting	Tentative 24 th Oct, 2019; DCC Hall, Hetauda, Makwanpur	DCC/GMaLI/HRRP	makwanpur@hrrpnepal.org
Joint Monitoring visit, targeted for retrofit task	21 th Oct to 22 th Oct, 2019	Joint Monitoring Team	makwanpur@hrrpnepal.org

News & Updates

Makwanpur, around 75% reconstruction has been completed in private housing reconstruction sector but in retrofitting no any HHs received the second tranche. There are around 6K HHs eligible for retrofitting among them around 99% received the first tranche of retrofit but anybody have not received the second tranche. Regularly we had reported after lunch the retrofitting manual and conducted orientation program at Thaha municipality with around 23 participants of ward level technicians. We clearly defined retrofitting procedure for load bearing structure and also about methodology of retrofitting such as splint and bandage and also jacketing wire mesh. After that also technicians took the retrofitting basic training with co-operative of UNOPS/BUILD Change in two shifts. Till to the date, we have not seen any retrofitting houses for second tranches. But now DIFID scale up retrofitting in Makwanpur, around 30HHs completed with 4nos. of model houses. It is a good for to us and it is just for starting. Skilled technicians are generally not involved in this type of construction, Guidance on how to carry out proper, repair and strengthening of earthquake damaged buildings are less in number No inclusion of Earthquake Resistant, Design in the curricula of civil and structural engineering. They have not developed the confidence level about retrofitting issues and challenges in field grass root level.


Tranche Status (Makwanpur)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	6039	2512	2318	2309	1646	1168	2176	1489	1489	0
Bakaiya Gaunpalika	8593	4019	2687	2687	1882	1104	1960	668	668	0
Bhimphedi Gaunpalika	5236	2698	2227	2209	1857	1684	932	608	608	0
Hetauda Upamahanagarpalika	32696	6363	4947	4705	2853	2458	2024	1076	1076	0
Indrasarowar Gaunpalika	3726	2923	2581	2572	2049	1500	254	166	166	0
Kailash Gaunpalika	4737	2614	2157	1528	1238	998	731	390	390	0
Makawanpurgadhi Gaunpalika	5516	2216	1839	1814	1328	1041	1437	949	949	0
Manahari Gaunpalika	8841	2337	1287	1287	1059	917	1487	733	733	0
Raksirang Gaunpalika	5091	1715	1580	1580	1431	1157	576	467	467	0
Thaha Nagarpalika	10519	6919	6211	5465	4283	3106	1369	693	693	0


Graph of Tranche Status:

Reconstruction- Tranche Status

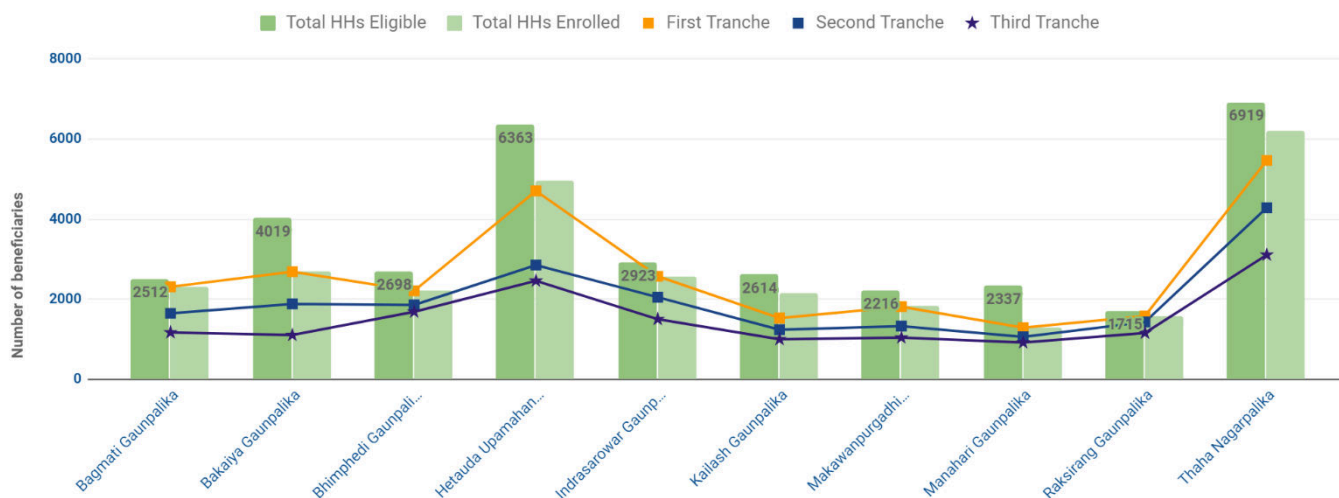

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

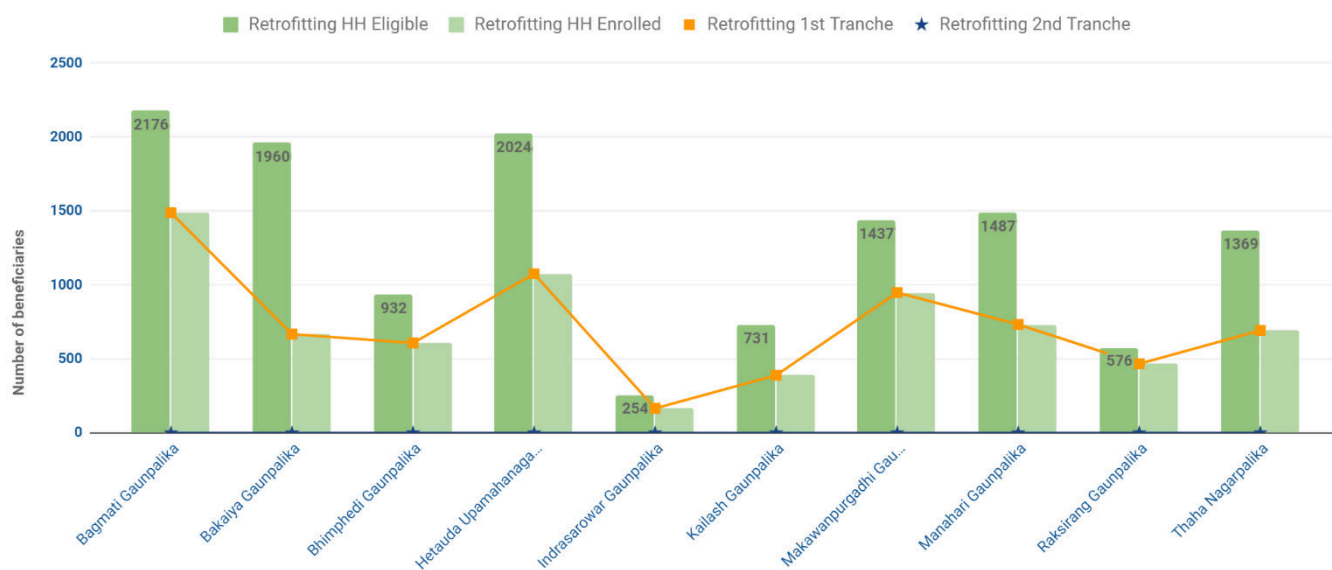


Tranche Status (Chitwan)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bharatpur Mahanagarपालिका	2087	710	660	660	387	156	38	9	9	0
Ichchhyakamana Gaunपालिका	3571	2353	2106	2106	1854	1366	248	196	196	0
Kalika Nagarpalika	2565	916	792	792	447	227	42	27	27	0
Khairahani Nagarpalika	1566	559	529	529	273	251	4	4	4	0
Madi Nagarpalika	123	23	23	23	21	16	15	13	13	0
Rapti Nagarpalika	3594	2043	1862	1862	898	578	71	18	18	0
Ratnanagar Nagarpalika	1763	731	657	657	425	381	175	164	164	0


Graph of Tranche Status:

Reconstruction- Tranche Status

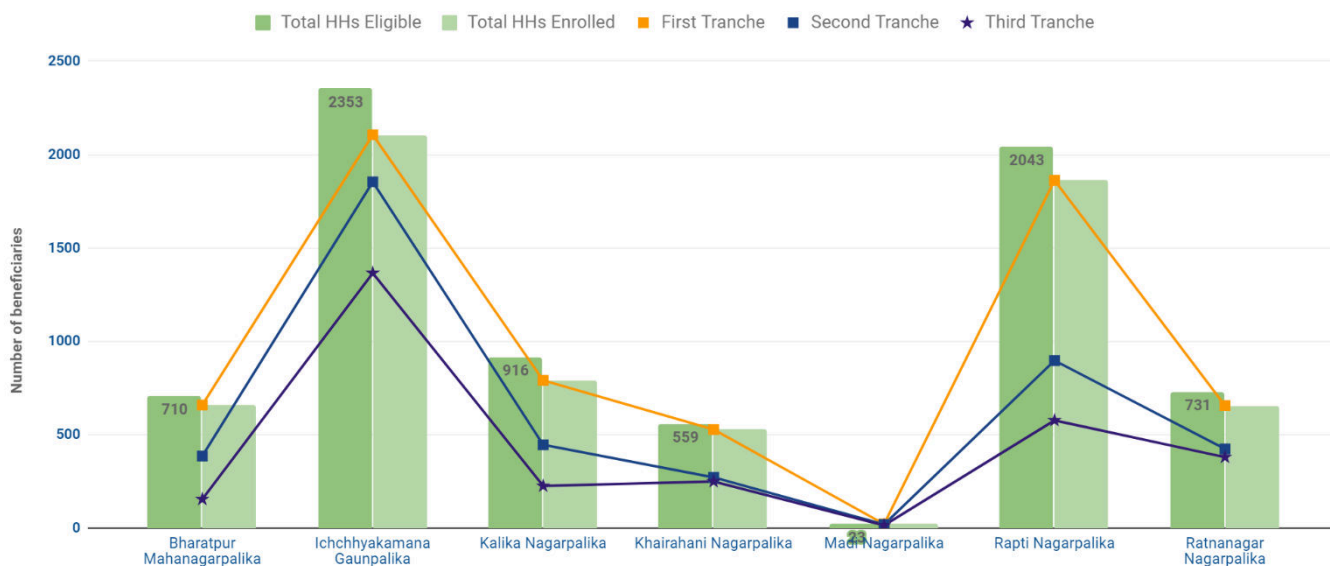

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

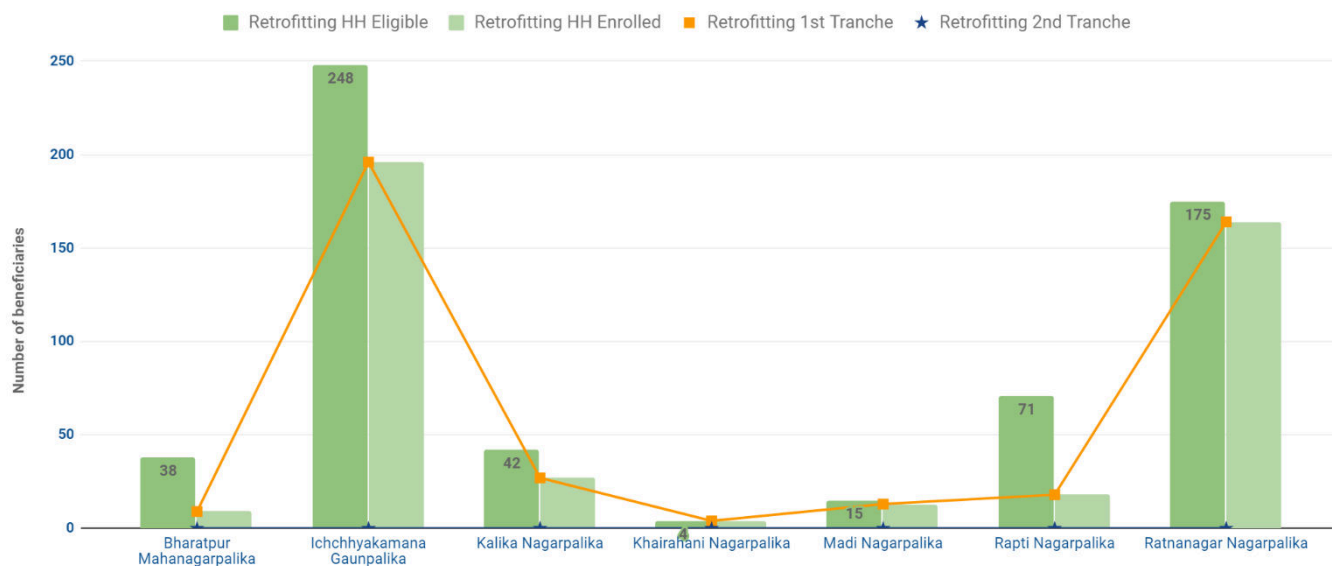


Tranche Status (Nawalparasi)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bardaghat Nagarpalika	4	4	4	4	4	3	0			
Binayee Tribeni Gaunpalika	70	66	66	65	65	56	2			
Bulingtar Gaunpalika	280	264	262	262	260	242	5			
Bungdikali Gaunpalika	133	72	72	72	67	67	1			
Devchuli Nagarpalika	177	177	177	177	171	156	1			
Gaidakot Nagarpalika	103	49	49	49	43	42	0			
Hupsekot Gaunpalika	155	139	139	139	134	108	2			
Kawasoti Nagarpalika	4	4	4	4	4	3	0			
Madhyabindu Nagarpalika	41	85	85	85	80	67	3			
Palhi Nandan Gaunpalika	1	4	4	4	3	3	0			
Pratappur Gaunpalika	6	3	3	3	3	3	0			
Ramgram Nagarpalika	3	1	0	0	0	0	0			
Sarawal Gaunpalika	4	4	3	3	2	0	0			
Sunwal Nagarpalika	2	2	2	2	2	1	0			
Susta Gaunpalika	2	3	3	3	2	1	0			

Graph of Tranche Status:

Reconstruction- Tranche Status

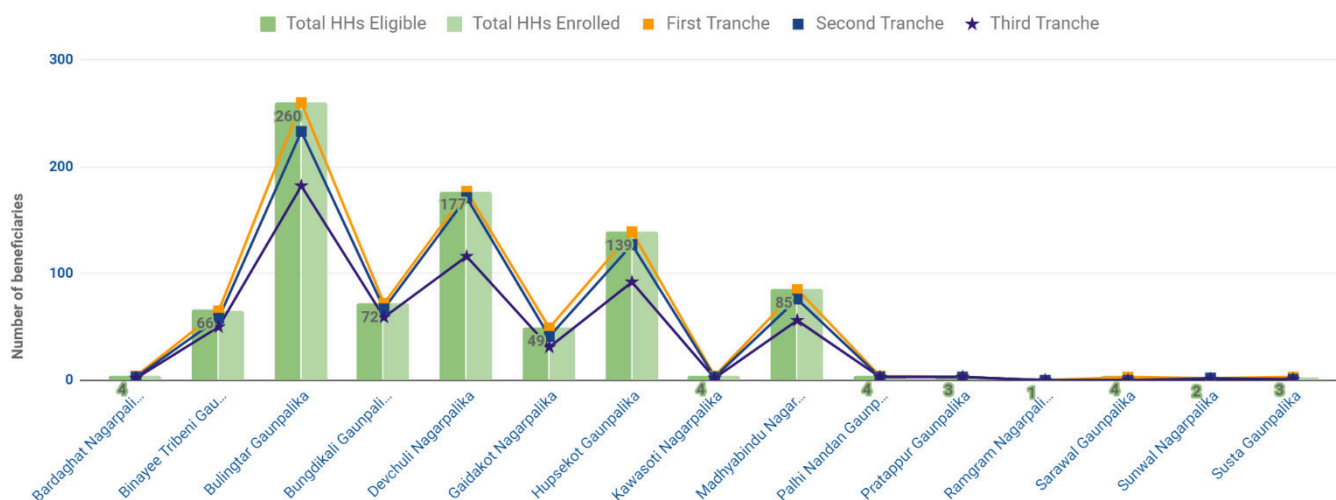

Graph for Retrofitting Status:

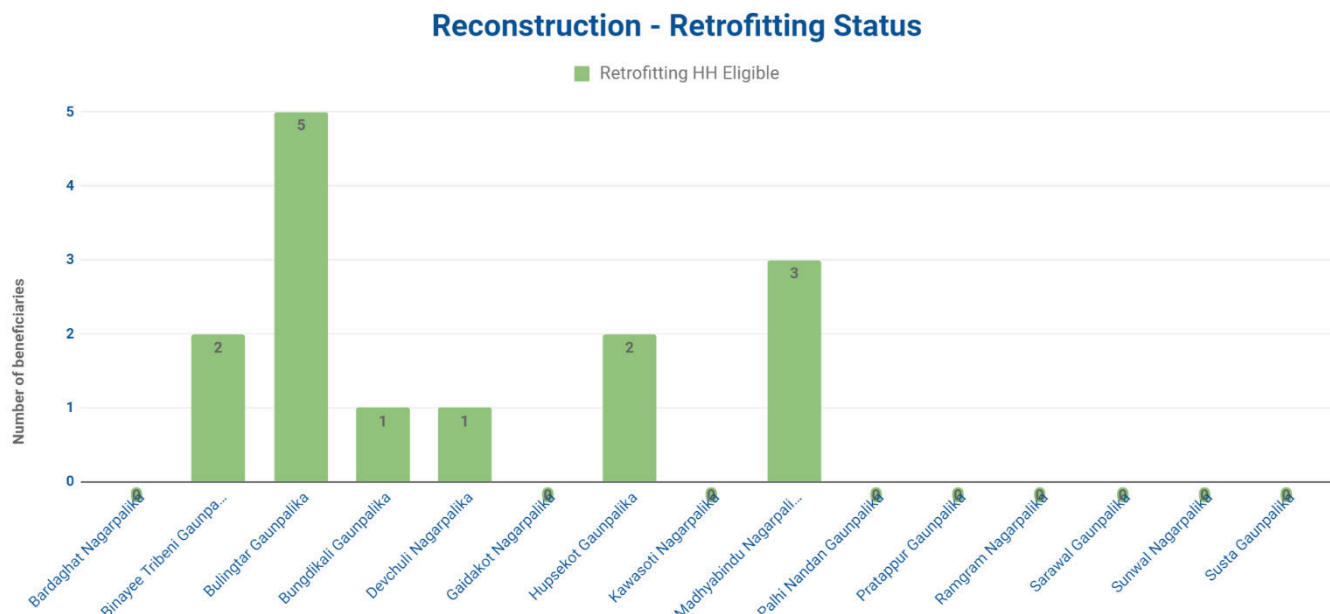

Field Visit Report

Now, we have completed the half day orientation program in district for “Retrofit Task Force” on 23th Sept, 2019 at Hetauda, Makwanpur. There were around 25 technicians participated in the event from the different rural municipalities of Makwanpur district. The orientation program was fascilitated by DLPIU Building and organized by NRA-DLPIU-GMaLI. The program was focused on retrofitting tasks and how to scaleing up and how to achieve the target with current planning schedule. There were two sessions in the event; namely Data collection, Building Typology Categorization and retrofitting Methods with power point presentation. Similarly the second session was MIS non compliance issues and its solution.

The 1st session was presented by DSE and focused on the following points;

We are regularly reporting about challenges and issues of housing reconstruction and almost issues are addressed by NRA. We are continue working in retrofit for awareness programs, interaction with focal persons and also this program supported to us for retrofitting scaleing up. The first session also focused on methods of retrofitting and retrofitting maual oriented. We concluded the following method are most suitable for our contest where materials are easily available in the market, quick access for implemented by technicians and also access for beneficiaries and skilled manpower who are working in reconstruction.

- Concrete jacketing with steel bar mesh

- Jacketing with G.I. wire mesh and cement plaster

- Splint and Bandage:** For masonry building with weak mortar like brick stone in mud building, Splint and Bandage method can be used to increase the strength of buildings and low cost materials like PP band/ gabion wire mesh jacketing can be done in remaining part to prevent local failure of masonry to make retrofit more economical.

Similarly second session was presented by DLPIU- Building MIS Specialist; He focused on how to complete the digitization with compliance. He clearly said, “ we found the maximum errors in digitization so first priority is to reduce them”.

नेपाल सरकार
राष्ट्रिय पुनर्निर्माण प्राधिकरण
केन्द्रीय आयोजना कार्यान्वयन इकाई
जिल्ला आयोजना कार्यान्वयन इकाई (भवन)
हेटौडा, मकवानपुर
प्रवलीकरण कार्यको कार्ययोजना

क्र.सं.	कार्य विवरण	समय विवरण																											
		असोज				कात्तिक				मंसिर				पुस				मार्ग				फागुन				चैत्र			
		W1	W2	W3	W4	W1	W2	W3	W4	W1	W2	W3	W4	W1	W2	W3	W4	W1	W2	W3	W4	W1	W2	W3	W4	W1	W2	W3	W4
1	Retrofit Task Force Orientation and Training																												
2	Orientation For local level Technical and elected persons																												
3	प्रवलीकरण तालिमको छनोट/अनुदान सम्झौता																												
4	Field survey/Assessment/ categorization of building typology																												
5	Retrofit Design Training for Retrofit Task Force																												
6	Retrofit design of Each typology																												
7	अनुदान छनोट तथा प्रवलीकरण सम्बन्धि तालिम																												
8	Training for Local level Technical Persons																												
9	प्रवलीकरण कार्यको शुरु र सम्पन्न																												
10	Frequent Field Visit and Monitoring																												



Fig: NRA-DLPIU Chief Bimal Kishor KP opening the half day orientation program for Retrofit Task Force.



DSE presented the session on data collection and building typology categorization and also method of retrofitting during in an event.

Retrofitting Status in Makwanpur;

DFID RETROFITTING SCALE UP model house has been constructed at four palikas of Makwanpur district namely Thaha Municipality, Bhimfedi Rural Municipality, Bakaiya Rural Municipality and Manhari Rural Municipality.

Name of Beneficiary	PA number	Palika	Ward
Jang Bahadur Jogi	R-31-9-9-0-0003	Manhari	9
Kanchi Bal	R-31-44-3-0008	Thaha	11
Man Bahadur Bal	R-31-7-4-0-0029	Bhimfedi	5
Prem Lal Ghising	R-31-5-4-0-0059	Bakaiya	4

Overall Retrofit progress, Makwanpur

Palikas	Engineers	Masons	Completed	Ongoing	Finalize to start	Total House
Manahari	10	5	1	0	0	1
Thaha	21	76	16	0	0	16
Bhimphedi	22	64	8	4	0	12
Bakaiya	11	5	0	1	0	1
Total	64	150	25	5	0	30

They have well done in retrofitting like as regular field visit; supervision, involvement of technicians and trained for masons; who have been involving in post-earthquake. We have been reporting of retrofitting while they had started the program and had suggested also for splint and bandage and also jacketing (GI wire Mesh/Steel/Wood) because of excess of technicians, retrofitting manual addressed the standards of norms and guide line and for similarities at all municipalities of district. So we request and suggestion these methods also should be implementation in grass root level.

Retrofitting Planning;

- Half day orientation program has been completed for “Retrofit Task Force” at the district. The orientation program was focused on data collection and building typology categorization and also method of retrofitting.
- To organize first round of orientation program at every R/municipality of Makwanpur district with present of beneficiaries, skilled manpower, who are working in reconstruction, ward technicians, focal person and local government.
- The main agendas of orientation program will be brief information about retrofit such as method of retrofit, how much cost for retrofit, detail about materials with tentative quantity, time period and details procedure of retrofit method by splint and bandage and jacketing with previous photos, visualize and drawing paper sheet.
- Develop the format for sure of beneficiaries and ask for each of them, are you sure for retrofit? And collection of data with help of ward level technicians and focal person of palika.
- After that regularly door to door technical assistance. It will be done by ward technicians in their respective wards.
- From the district regular monitoring and follow up them and communication follow to other areas of palikas and broadly go ahead the retrofit.
