

Monthly District Report

Makwanpur, Chitwan, Nawalpur, Parasi

12 July – 22 August 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Makwanpur	Annual Reconstruction Review Workshop	18 th June 2019	DCC Hall, Makwanpur, Hetauda Sub-Metropolitan	makwanpur@hrrpnepal.org	Report below
	Update Palika Profile data of Makwanpur	14 th August, 2019		makwanpur@hrrpnepal.org	Palika Profile Data
	Contact list updated in GD	25 th August, 2019			Contact List
Chitwan	Contact list updated in GD	26 th August, 2019		chitwan@hrrpnepal.org	Contact List
	Update Palika Profile data of Nawalpur	15 th August, 2019			Palika Profile Data
Nawalpur	Contact list updated in GD	26 th August, 2019		nawalparasi@hrrpnepal.org	Contact List
	Update Palika Profile data of Nawalpur	15 th August, 2019			Palika Profile Data
Parasi	Update Palika Profile data of Nawalpur	15 th August, 2019		nawalparasi@hrrpnepal.org	Palika Profile Data

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
District Facilitation and Coordination Meeting	Tentative 29 th August, 2019; DCC Hall, Hetauda, Makwanpur	DCC/GMaLI/HRRP	makwanpur@hrrpnepal.org
Organize orientation programs about the retrofit at all municipalities of Makwanpur	10 th Sept to 17 th Sept, 2019	Joint Monitoring Team	makwanpur@hrrpnepal.org

News & Updates

NRA-GMaLI-DLPIU, Makwanpur has been completed annual review workshop at district with presence of all municipalities and all stake holders.

[HRRP- Makwanpur Presentation Slide click here..](#)



Figure 1: Some snap of annual review program NRA-GMaLI DLPIU, Makwanpur. The program was organized in 12th July, 2019 at Puja Banquate, Makwanpur.


Tranche Status (Makwanpur)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	6039	2512	2318	2309	1646	1168	2176	1489	1489	0
Bakaiya Gaunpalika	8593	4019	2687	2687	1882	1104	1960	668	668	0
Bhimphedi Gaunpalika	5236	2698	2227	2209	1857	1684	932	608	608	0
Hetauda Upamahanagarpalika	32696	6363	4947	4705	2853	2458	2024	1076	1076	0
Indrasarowar Gaunpalika	3726	2923	2581	2572	2049	1500	254	166	166	0
Kailash Gaunpalika	4737	2614	2157	1528	1238	998	731	390	390	0
Makawanpurgadhi Gaunpalika	5516	2216	1839	1814	1328	1041	1437	949	949	0
Manahari Gaunpalika	8841	2337	1287	1287	1059	917	1487	733	733	0
Raksirang Gaunpalika	5091	1715	1580	1580	1431	1157	576	467	467	0
Thaha Nagarpalika	10519	6919	6211	5465	4283	3106	1369	693	693	0


Graph of Tranche Status:

Reconstruction- Tranche Status

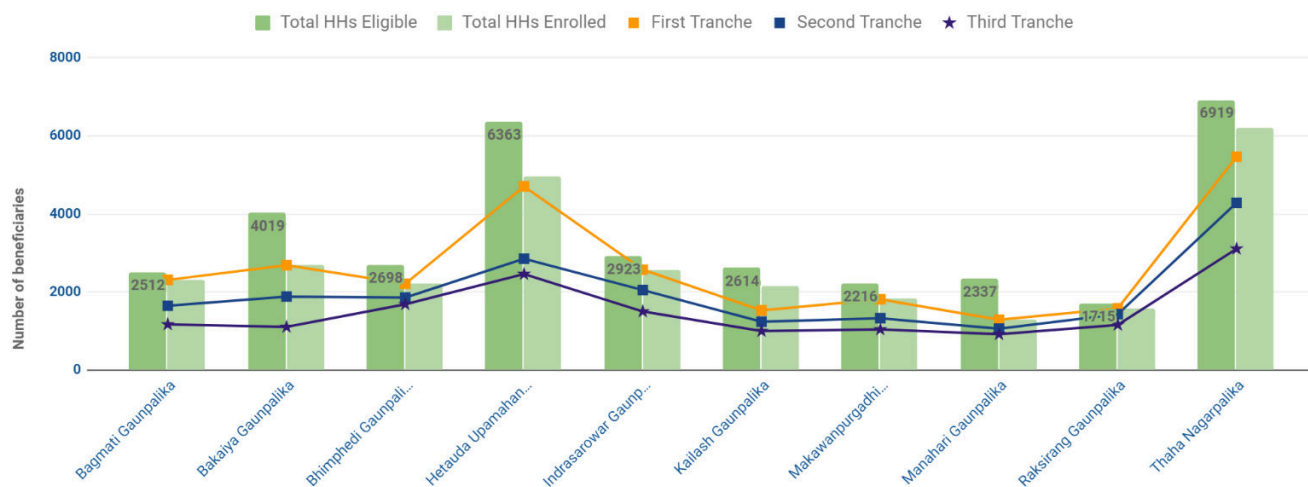

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

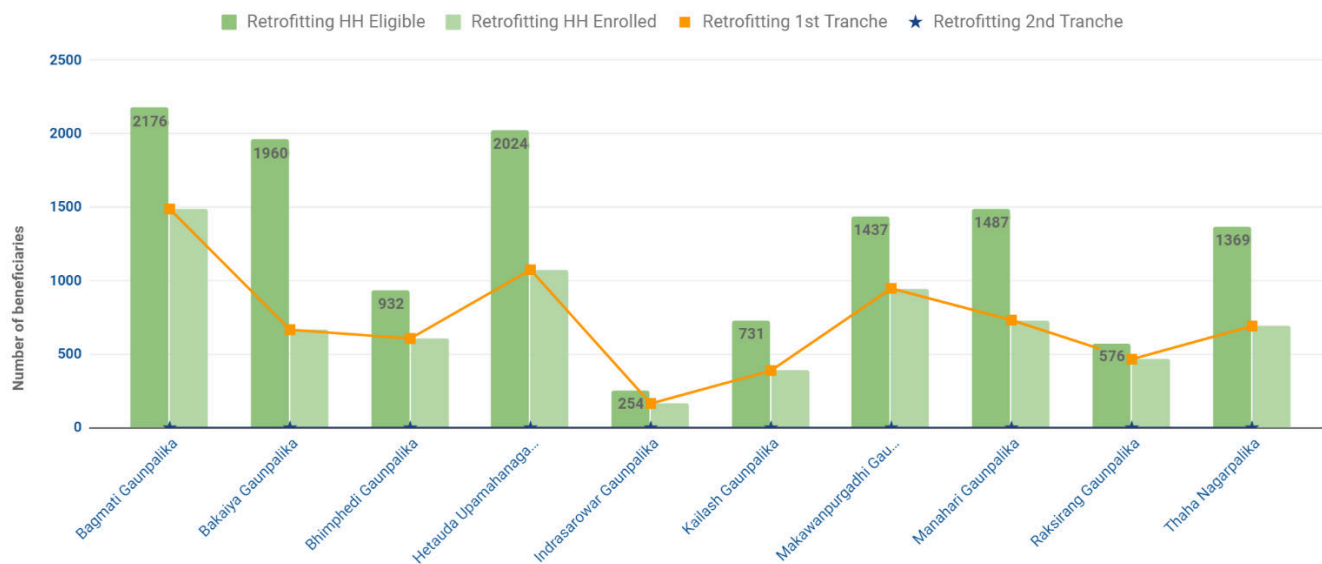


Tranche Status (Chitwan)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bharatpur Mahanagarpalika	2087	710	660	660	387	156	38	9	9	0
Ichchhyakamana Gaunpalika	3571	2353	2106	2106	1854	1366	248	196	196	0
Kalika Nagarpalika	2565	916	792	792	447	227	42	27	27	0
Khairahani Nagarpalika	1566	559	529	529	273	251	4	4	4	0
Madi Nagarpalika	123	23	23	23	21	16	15	13	13	0
Rapti Nagarpalika	3594	2043	1862	1862	898	578	71	18	18	0
Ratnanagar Nagarpalika	1763	731	657	657	425	381	175	164	164	0

Graph of Tranche Status:

Reconstruction- Tranche Status

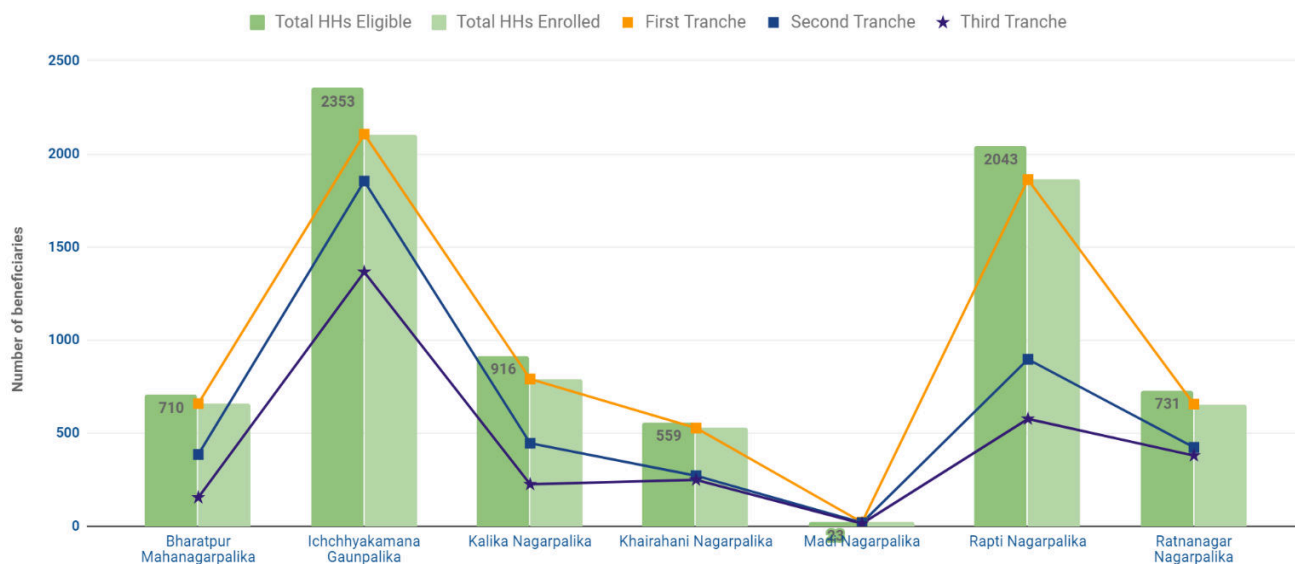

Graph for Retrofitting Status:

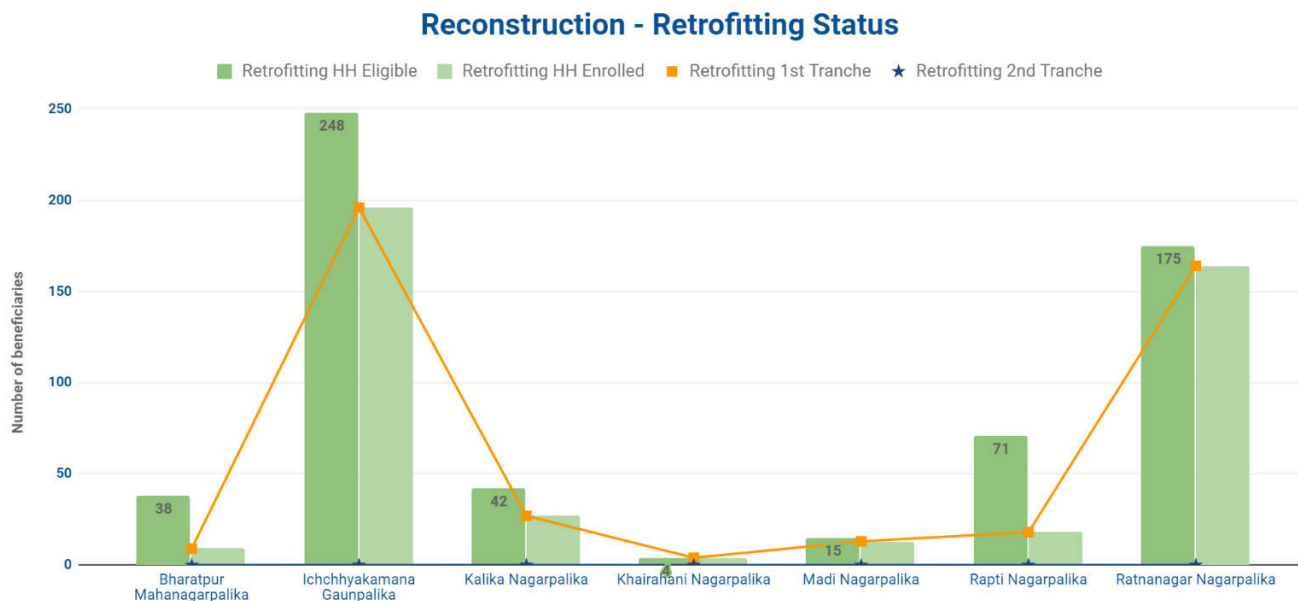


Tranche Status (Nawalparasi)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bardaghat Nagarpalika	4	4	4	4	3	2	0			
Binayee Tribeni Gaunpalika	70	66	65	65	58	50	2			
Bulingtar Gaunpalika	280	260	260	260	233	182	5			
Bungdikali Gaunpalika	133	72	72	72	67	59	1			
Devchuli Nagarpalika	177	177	177	177	171	116	1			
Gaidakot Nagarpalika	103	49	49	49	41	31	0			
Hupsekot Gaunpalika	155	139	139	139	127	92	2			
Kawasoti Nagarpalika	4	4	4	4	3	2	0			
Madhyabindu Nagarpalika	41	85	85	85	76	56	3			
Palhi Nandan Gaunpalika	1	4	4	4	3	3	0			
Pratappur Gaunpalika	6	3	3	3	3	3	0			
Ramgram Nagarpalika	3	1	0	0	0	0	0			
Sarawal Gaunpalika	4	4	3	3	0	0	0			
Sunwal Nagarpalika	2	2	2	2	2	1	0			
Susta Gaunpalika	2	3	3	3	1	1	0			

Graph of Tranche Status:

Reconstruction- Tranche Status

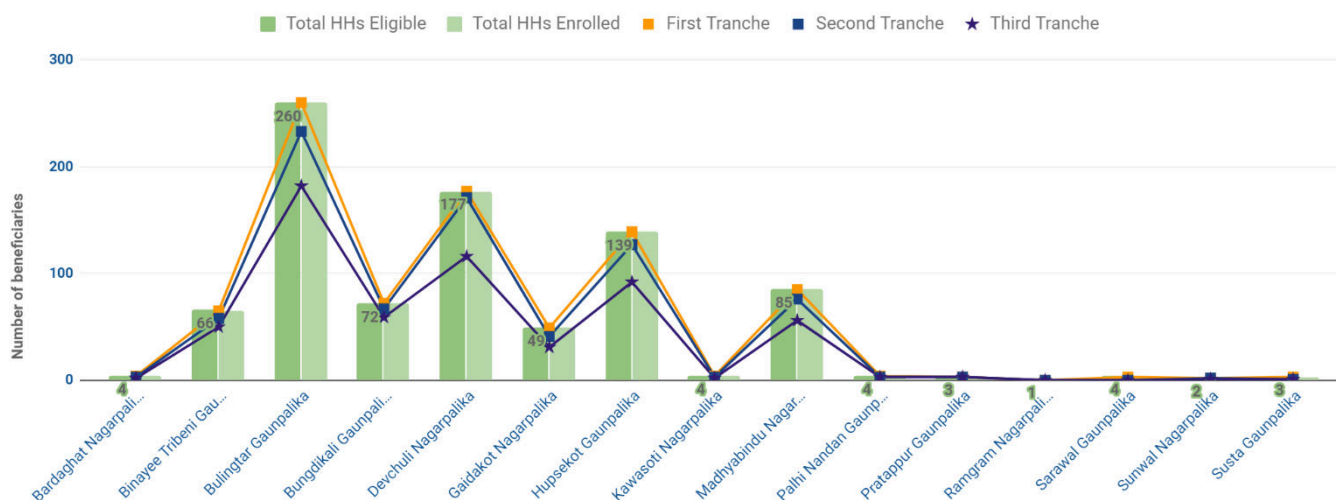

Graph for Retrofitting Status:

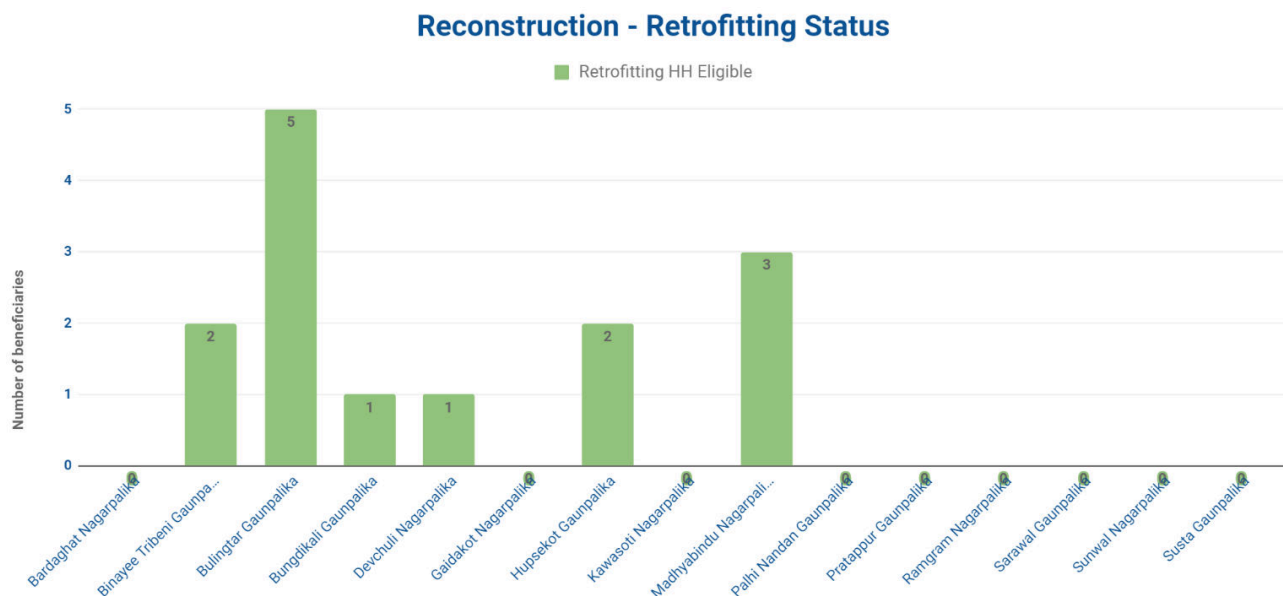

Present Scenario of Retrofitting, Makwanpur

Makwanpur, around 75% reconstruction has been completed in private housing reconstruction sector but in retrofitting no any HHs received the second tranche. There are around 6,000 HHs eligible for retrofitting among them around 99% received the first tranche of retrofit but nobody has received the second tranche. Regularly, we have been reporting the issues after the retrofitting manual orientation program was conducted at Thaha municipality with around 23 participants of ward level technicians. We clearly defined retrofitting procedure for load bearing structure and also about methodology of retrofitting such as splint and bandage and also jacketing wire mesh. After that also technicians took the retrofitting basic training conducted jointly by UNOPS/BUILD Change in two shifts. Till date, we have not seen any retrofitting houses taking second tranche. But now DIFID scale up retrofitting in Makwanpur, around 30HHs completed with four model houses. Skilled technicians are generally not involved in this type of construction. Guidance on how to carry out proper, repair and strengthening of earthquake damaged buildings are less in number. No inclusion of Earthquake Resistant, Design in the curricula of civil and structural engineering. They have not developed the confidence level about retrofitting issues and challenges in the level.

We are regularly reporting about challenges and issues of housing reconstruction and almost are addressed by NRA. We continue working in retrofit for awareness programs, interaction with focal persons, last month we conducted one event at Thaha Municipality with presence of UNOPS/BUILD Change. We concluded the following method are most suitable for our context where materials are easily available in the market, quick access for implementation by technicians and also access to beneficiaries and skilled manpower who are working in reconstruction.

- Concrete jacketing with steel bar mesh**


- Jacketing with G.I. wire mesh and cement plaster**

- Splint and Bandage:** For masonry building with weak mortar like brick stone in mud building, Splint and Bandage method can be used to increase the strength of buildings and low cost materials like PP band/ gabion wire mesh jacketing can be done in remaining part to prevent local failure of masonry to make retrofit more economic.

Current status of Reconstruction with including retrofit:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	6039	2512	2318	2309	1646	1168	2176	1489	1489	0
Bakaiya Gaunpalika	8593	4019	2687	2687	1882	1104	1960	668	668	0
Bhimphedi Gaunpalika	5236	2698	2227	2209	1857	1684	932	608	608	0
Hetauda Upamahanagarपालिका	32696	6363	4947	4705	2853	2458	2024	1076	1076	0
Indrasarowar Gaunpalika	3726	2923	2581	2572	2049	1500	254	166	166	0
Kailash Gaunpalika	4737	2614	2157	1528	1238	998	731	390	390	0
Makawanpurgadhi Gaunpalika	5516	2216	1839	1814	1328	1041	1437	949	949	0
Manahari Gaunpalika	8841	2337	1287	1287	1059	917	1487	733	733	0
Raksirang Gaunpalika	5091	1715	1580	1580	1431	1157	576	467	467	0
Thaha Nagarpalika	10519	6919	6211	5465	4283	3106	1369	693	693	0

Reconstruction - Retrofitting Status

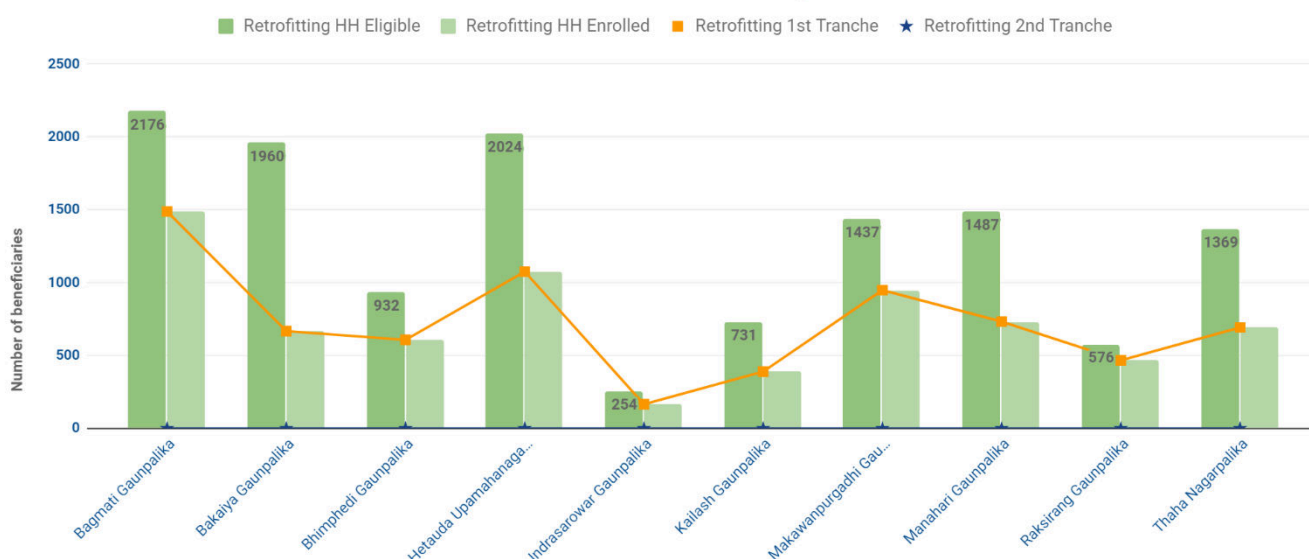

Beneficiaries view: They have not known about the difference between repair & Restoration and Retrofitting and no any ideas of retrofitting like as materials, skilled man power and how much cost. Overall they have not taken any awareness, orientations and trainings for masons etc. Almost beneficiaries are not motivated to retrofit their houses. They want to increase the government contribution fund now the guideline is 1lakh in two tranches. No any technicians, POs excess for technically helps to beneficiaries.

But for Model house, UNOPS/BUILD Change Nepal has been completed 4nos. of model house at Manhari RM, Thaha Municipality, Bhimfedi RM and Bakaiya RM.

POs view: DFID RETROFITTING SCALE UP model house has been constructed at four palikas of Makwanpur district namely Thaha Municipality, Bhimfedi Rural Municipality, Bakaiya Rural Municipality and Manhari Rural Municipality.

Name of Beneficiary	PA number	Palika	Ward
Jang Bahadur Jogi	R-31-9-9-0-0003	Manhari	9
Kanchi Bal	R-31-44-3-0008	Thaha	11
Man Bahadur Bal	R-31-7-4-0-0029	Bhimfedi	5
Prem Lal Ghising	R-31-5-4-0-0059	Bakaiya	4

Overall Retrofit progress, Makwanpur

Palikas	Engineers	Masons	Completed	Ongoing	Finalize to start	Total House
Manahari	10	5	1	0	0	1
Thaha	21	76	16	0	0	16
Bhimphedi	22	64	8	4	0	12
Bakaiya	11	5	0	1	0	1
Total	64	150	25	5	0	30

They have well done in retrofitting like as regular field visit; supervision, involvement of technicians and trained for masons; who have been involving in post-earthquake. We have been reporting of retrofitting while they had started the program and had suggested also for splint and bandage and also jacketing (GI wire Mesh/Steel/Wood) because of excess of technicians, retrofitting manual addressed the standards of norms and guide line and for similarities at all municipalities of district. So we request and suggestion these methods also should be implementation in grass root level.

Joint Monitoring View

From last one month, we are more focus on retrofit so we are conducting awareness program. Last time we have conduct in Thaha-07 and minute them. We are planning to conduct different activities after from two weeks till to date.

- Next one meeting will be conduct at the district level and formation the retrofitting team with district support engineers, focal person and others if required. (now, we have received, it has formed by central NRA-CLPIU-Building)
- To organize first round of orientation program at every R/municipality of Makwanpur district with present of beneficiaries, skilled manpower, who are working in reconstruction, ward technicians, focal person and local government.
- The main agendas of orientation program will be brief information about retrofit such as method of retrofit, how much cost for retrofit, detail about materials with tentative quantity, time period and details procedure of retrofit method by splint and bandage and jacketing with previous photos, visualize and drawing paper sheet.
- Develop the format for sure of beneficiaries and ask for each of them, are you sure for retrofit? And collection of data with help of ward level technicians and focal person of palika.
- After that regularly door to door technical assistance. It will be done by ward technicians in their respective wards.
- From the district regular monitoring and follow up them and communication follow to other areas of palikas and broadly go ahead the retrofit.

The orientation programs are going too held on following dates and respective Rural/ Municipality;

Name of R/Municipality	Program date	Remarks
Indrasarowar/Thaha Rural /Municipality	2019-09-10	
Kailash Rural Municipality	2019-09-11	
Bagmati Rural Municipality	2019-09-12	
Bakaiya Rural Municipality	2019-09-13	
Raksirang and Manhari RM	2019-09-15	
Bhimfedi Rural Municipality	2019-09-16	
Makwanpurgadhi Rural Municipality/Hetauda SM	2019-09-17	
