

District Report

Sindhuli

23 November – 6 December 2018

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Palika Level meeting and Joint Monitoring at Marin Rural Municipality.	5 th December 2018 – 8 th December 2018	19	1	1. Er. Lekhnath Paudel (DTC – Sindhuli) 2. Er. Kiran Mahat (M&E DLPIU-Building) 3. Er. Rajiv Sah (DSE DLPIU-Building) 4. Er. Pravin Thakur (DLPIU – Building Engineer)	Meeting Minutes
Support to National IM for the preparation of Palika Profiles.	23 rd November 2018 – 4 th December 2018			1. Sachin Malego (DIMO – Sindhuli) 2. Uttam Paudel (IM Manager – National IM)	Palika Profile Core Design Files
Support to National IM for the preparation of new bulletin design and layout.	23 rd November 2018 – 2 nd December 2018			1. Sachin Malego (DIMO – Sindhuli) 2. Uttam Paudel (IM Manager – National IM) 3. Siobhan Kennedy (Recovery Advisor)	Bulletin PS Design File
Support to National IM for the code review of website that is in built process.	23 rd November 2018 – 3 rd December 2018			1. Sachin Malego (DIMO – Sindhuli) 2. Uttam Paudel (IM Manager – National IM) 3. Karishma Chand Thakur (Comm. & Information Mgmt. Officer)	
Attended Municipal Orientation Program at Kavre to collect the feedbacks of the Palika Level Profile	25 th November 2018 – 26 th November 2018			1. Sachin Malego (DIMO – Sindhuli) 2. Uttam Paudel (IM Manager – National IM) 3. Karishma Chand Thakur (Comm. & Information Mgmt. Officer) 4. Yubraj Bhandari (NIMO – HRRP) 5. Monika Bajimaya Shrestha (DMT – IM) 6. Bhubaneswari Parajuli (Nat. Technical Coordinator) 7. Minar Thapa Magar (Nat. Coordination Officer) 8. Reshma Shrestha (District Coordinator Kavre) 9. Ishwor Neupane (DIMO – Kavre)	

Summary of events during this period

Workshop on Adobe InDesign and process for manual building of Palika Profiles provided to National IM, District IM and DMT IM.	4 th December 2018	7	3	1. Sachin Malego (DIMO – Sindhuli) 2. Uttam Paudel (IM Manager – National IM) 3. Yubraj Bhandari (NIMO – HRRP) 4. Resham Phuldel (IM Expert) 5. Binaya Raja Shrestha (NIMO – HRRP) 6. Karishma Chand Thakur (Comm. & Information Mgmt. Officer) 7. Monika Bajimaya Shrestha (DMT – IM) 8. Manisha Rai (DIMO – Kathmandu) 9. Buddha Singh Thakuri (DIMO – Nuwakot) 10. Jawed Mohammad (DIMO - Ramechhap)	
Attended Orientation on CRS Global Fund and Orientation to District Teams at HRRP Jwagal Office.	3 rd December 2018 – 4 th December 2018			1. Lekhnath Paudel (DTC-Sindhuli) 2. Sachin Malego (DIMO - Sindhuli)	
District support to DLPIU-Building for management of Inspection List Data of EQ affected beneficiaries as per the new governmental structure.	Ongoing from 5 th December 2018			1. Sachin Malego (DIMO – Sindhuli)	Link to Inspection Data

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location	Organizer	Contact Person
District Co-ordination Meeting with PO's, Government Agencies and other district stakeholders working in the sector of reconstruction.	25 th December 2018 (Planned)	HRRP	3. Lekhnath Paudel (DTC-Sindhuli) 4. Sachin Malego (DIMO -Sindhuli)
Municipal Level Orientation Program.	26 th – 27 th December 2018	NRZ, DLPIU-Building, GMaLI, and supported by HRRP	1. Dr. Hari Ram Parajuli (Executive Member) 2. Sanat KC (NRA) 3. Raju Neupane (CLPIU-Building) 4. Hari Prasad Sharma 5. Lekhnath Paudel (DTC-HRRP-Sindhuli)
Palika Level Meeting at Dudhauri Municipality	Planned	HRRP	1. Lekhnath Paudel (DTC-Sindhuli) 2. Sachin Malego (DIMO-Sindhuli)

Tranche Status

Tranche Status of Sindhuli as of 13th December 2018

Rural /Municipality	Kamalama i Municipality	Dudhauli Municipality	Golanjor RM	Ghanglekh RM	Tinpata n RM	Phikka l RM	Mari n RM	Sunkoshi RM	Hariharpurgadhi RM
Total HHs Surveyed	7864	4651	2779	1962	4281	2173	3340	4745	2394
Total HHs Eligible	7864	4651	2779	1962	4281	2173	3340	4745	2394
Total HHs Enrolled	7619	4368	2736	1884	4235	2164	3120	4724	2344
First Tranche	6918	4157	2707	1874	4232	2164	3120	4722	2344
Second Tranche	4588	2615	2421	1357	4109	2007	2173	4162	1916
Third Tranche	2024	855	1741	871	1579	1358	823	2697	338
Total HH Constructed	1738	612	1607	865	1352	1274	786	2344	308
Non-Compliance Registered	10	13	11	8	11	6	4	5	8
Non-Compliance Addressed	0	0	0	4	3	0	0	2	0

Graph of Tranche Status:

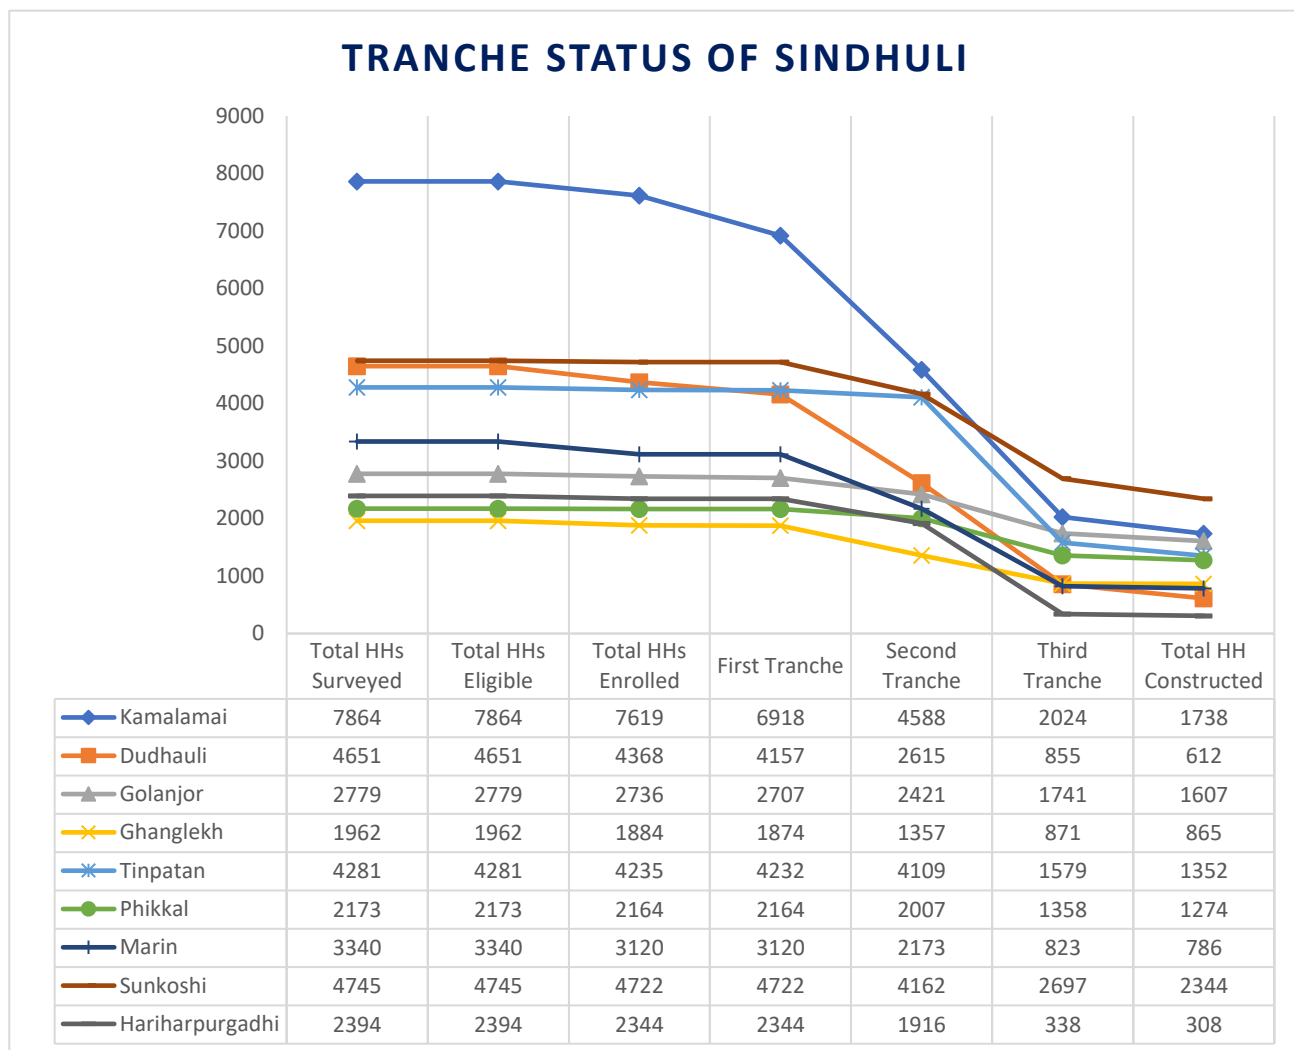

*Note: Please hover on the graph to find the exact number.



NOTE: Data for Grievances and Retrofitting has not been segregated as above by DLPIU-GMaLI, as per the conversation with EHRP-MIS Operator Mr. Barun Chaudhary. Hence, those data cannot be achieved as per desired.

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders	
5 th to 8 th December 2018	Marin Rural Municipality and wards	• Er. Lekhanath Paudel • Er. Kiran Mahat (M&E) • Er. Rajiv Shah (DSE) • Er. Pravin Thakur (DLPIU-Engineer)	
Objective(s)	• Reconstruction Update/ Housing Reconstruction Challenges • Interaction between government agencies, implementing partners and local people • Collection of Typologies of Houses		
Summary	Joint visit was conducted by HRRP Sindhuli along with NRA-CLPIU M&E (Kiran Mahat), DSE (Rajiv Sah), DLPIU-Building Engineer (Prabin Kumar Thakur). The field visit gave an opportunity to NRA-CLPIU/DLPIU and HRRP to observe, supervise and monitor ongoing construction of Houses (<i>Compliance & Non-Compliance houses</i>) at Kapilakot, Kalpabrichha, Mahadevsthan and Ratamata wards of Marin Rural Municipality. In Kapilakot ward no. 1 of Marin Rural Municipality about 244 HHs still not receiving first tranche of GON housing grant. Beneficiary with timber framed houses have not received 3rd tranche of GON housing grant. After visiting those houses DSE had advised DLPIU Engineers for the inspection of those completed timber frame houses for releasing 3rd tranche. Almost houses of Marin Rural Municipality are timber framed hybrid structure with ground floor stone/brick masonry and first floor constructed with light material, however, some houses were load bearing structures (Stone Masonry in Cement/Mud Mortar, Brick Masonry in Cement Mortar). ✓ There was no more information regarding reconstruction in the Palika, so the decision was made to submit monthly report by all the ward office in the Palika. ✓ In every month there should be at least one ward level meeting regarding reconstruction in presence of DLPIU Engineers. ✓ Most of the construction of timber framed structure houses have been completed so for releasing 3rd tranche DLPIU Engineers must start filling inspection form. The visit provided opportunities to share Information to newly elected members & DLPIU Engineers. During the visit, we advised DLPIU Engineers to make local people aware of using earthquake resilience techniques. During the meeting with Marin Rural Municipality palika members we shared the reconstruction status. All wards chairperson/ward secretariat were aware of the reconstruction and had proposed us to make regular coordination meeting in Marin Rural Municipality in coordination with DLPIU-GMaLI, DLPIU-Building, and HRRP-Nepal.		
Challenges / Issues Identified	Action Required	Responsible	Timeframe
No beneficiary who had built timber frame houses had received 3 rd tranche	Training required for timber frame structure manual	NRA, CLPIU-Building, DLPIU	As soon as possible
PA agreement in Elani land so beneficiary had not started reconstruction yet	Solid decision for the elani land issues	NRA, GON	As soon as possible

Photos

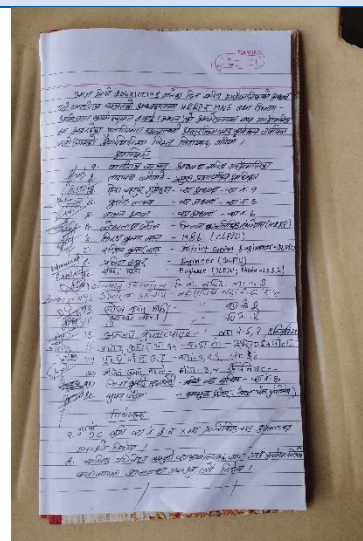

Meeting at Marin Rural Municipality. Palika chairperson Mr. Pani Raj Bamjan sharing the challenges, issues and problem regarding reconstruction in the palika.

Meeting Minutes and the decision made after the sharing session.

Housing Typology Report



The house belongs to Mr. Raj Man Moktan permanent residence of Marin Rural Municipality, ward no-06, Kapilakot



The house belongs to Mr. Dhan Bahadur Bal permanent residence of Marin Rural Municipality, ward no -06,

Sindhuli. He has received 2nd tranche of GON housing grant. The house is timber framed with hybrid structure with ground floor infill wall of stone in mud mortar and first floor light bamboo sheet. During the visit our team identified that the house was tilted in x and y direction in some angle.

Kapilakot Sindhuli. He has received 2nd tranche of GON housing grant. The house is timber framed hybrid structure with ground floor infill wall of stone in mud mortar and first floor light timber planks. During the visit our team identified that the house was tilted in x and y direction in some angle.



The house belongs to Mr. Gokul Ale Magar permanent residence of Marin Rural Municipality, ward no -02, Ratamata Sindhuli. He has received 2nd tranche of GON housing grant. The house is timber framed hybrid structure with stone in cement mortar in ground floor and light timber planks in the first floor. During the visit our team advised DLPIU Engineers and beneficiary for the correction to lager opening percentage.



The house belongs to Mr. Nara Bahadur Ale Magar permanent residence of Marin Rural Municipality, ward no -01, Kalpabrichha Sindhuli. He has received 2nd tranche of GON housing grant. The house is made using interlocking block with flexible roofing. The beneficiary he himself made theses blocks in home for the construction. Due to unavailability of testing machine for these blocks he could not receive 3rd tranche.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
When will the grievance addressed?	Chairperson ward no 01, Marin	N/A
What is the solution for PA agreement in Elani land?	All wards chairperson and palika chief	N/A

Challenges and Way Forward

Challenge	Way Forward
DLPIU Engineers cannot give solution to timber frame structure houses so beneficiary could not receive 3 rd tranche of GON housing although the construction of the houses is completed.	Training on timber framed structure manual

Case Study



Mr. Lal Bahadur Loh is a permanent resident of Marin Rural Municipality Ward No. 6, Kapliakot, Sindhuli. As per the beneficiary's statement, he lived along with the nine members of his family. On 12th Baisakh 2072, the day of the earthquake his house totally collapsed and one of his family member got injured.

After the survey team surveyed his house, he was provided with a "Nissa card" and his house was marked as totally collapsed. However, he was not able to sign the PA agreement with the Government agency for receiving tranches. Furthermore, he also filled the grievance form from NRA district secretariat and is still waiting for his grievance to be addressed by NRA so that he could then construct his home.

According to the Ward Chairperson re-survey was conducted in the ward, still none of the beneficiaries were able to sign the PA agreement. Mr. Loh is still living in a temporary shed and waiting for his voice to be heard.
