

District Report

Rasuwa

12 April – 9 May 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
We would like to update all our partners and relative stockholders that HRRP Rasuwa district team is no longer presence in district from May,2019. Nuwakot team will support Rasuwa remotely now onwards. During handover processes Rasuwa team formally hand over district activities to Nuwakot team. Theses are activities conducted during handover process: - Meeting with government bodies including CDO at DAO office, GMAli Staff at GMAli office, DLPIU staff at DLPIU(Building) respectively. - All information regarding District and technical coordination as well as information management. Rasuwa district google drive which contains full information of district team activities was handover during this process. Now onwards HRRP Rasuwa team heartily request all partners , gon stockholders , Donors and other related agency to direct communicate with Mr. Badri Pakural district coordinator for Nuwakot and Rasuwa, Mr. Sachin Sapkota district technical coordinator and Miss. Manisha Rai Information management officer for theses two district.	23-April,2019	8	1	techcord.rasuwa@hrrpnepal.org im.rasuwa@hrrpnepal.org	

9 May 2019

Summary of events during this period

Their contact number is as below: Mr. Badri Pakural: 9851154201 Mr.Sachin Sapkota: 9847621292 Miss. Manisha Rai: 9842062006					
District GMaLI organized memorial function at District headquarter Dhunche Rasuwa on the 4th anniversary of gorkha earthquake on 25th April 2019. On the chairman ship of DCC chief meeting was conducted at DCC Hall where along with chief district officer others governmental officers and partner organization were presented. Overall district update is presented by GMaLI Rasuwa during meeting. Candle march was also organized in presence of civil society activist of district at evening.	25-April,2019	16	5	techcord.rasuwa@hrrpnepal.org im.rasuwa@hrrpnepal.org	
Joint Monitoring field visit to Ammachhodingmo Rural Municipality. In the presence of M&E Mr.Prabhu Pokhral, DSE Mr. Projwal KC , DLPIU(Building) focal person Mr. Saroj kumar Yadav and HRRP Team conducted visit at Haku.	10 April 2019	5		techcord.rasuwa@hrrpnepal.org im.rasuwa@hrrpnepal.org	Field visit section below
Joint Monitoring field visit to Gosaikunda Rural Municipality. In the presence of M&E Mr.Prabhu Pokhral, DSE Mr. Projwal KC , DLPIU(Building) focal person Mr. Saroj kumar Yadav and HRRP Team conducted visit at LinLing.	11 April 2019	5		techcord.rasuwa@hrrpnepal.org im.rasuwa@hrrpnepal.org	Field visit section below
Rasuwa R10 5W has been uploaded on respective district google drive. Activities of different partners organization and governments is updated on this round of 5W.	25-April,2019	1		techcord.rasuwa@hrrpnepal.org im.rasuwa@hrrpnepal.org	For dataset (CLICK HERE)
HRRP Rasuwa district coordinator Mr. Rijan Gajurel	15-May to 21-May,2019	5	0	im.rasuwa@hrrpnepal.org	

Summary of events during this period

together with Dhading DC Mr. Prabin Gautam visited Dolakha and Ramachhap district during takeover process of district activities of these two district. Meeting with different partners and gon bodies was conducted during this visit in both district.					
Updated list of beneficiary's information on construction completion certificate along with the form pictures				techcord.rasuwa@hrrpnepal.org im.rasuwa@hrrpnepal.org	GD
Updated list of beneficiaries' information converted from retrofitting beneficiaries to reconstruction beneficiaries.				techcord.rasuwa@hrrpnepal.org im.rasuwa@hrrpnepal.org	N/A

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
District Facilitation Meeting	Location: DCC Hall Dhunche Rasuwa. Date: Not Fixed yet and will be update very shortly once finalized.	GMaLI support by HRRP	Im.rasuwa@hrrpnepal.org

News & Updates

District GMaLI organized memorial function at District headquarter Dhunche Rasuwa on the 4th anniversary of Gorkha earthquake on 25th April, 2019. On the chairman ship of DCC chief meeting was conducted at DCC Hall where along with chief district officer others governmental officers and partner organization were presented. Overall district update is presented by GMaLI Rasuwa during meeting. Candle march was also organized in presence of civil society activist of district at evening.



Photo: Appreciation certificate distribution process.
Civil
On the behalf of NRA DCC chief handover appreciation
program.
certificate to Uttaryagaya RM ward number 2.



Photo: Open session of candle light march pass.
society president Mr. Babu Lal Tamang kickoff

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date:	Location:	Participants from HRRP and stakeholders
10 April 2019	Ammachhodingmo Rural Municipality ward number -1, Haku	Biren Shah – HRRP Prabhu Pokharel – M&E, CLPIU Building Rijan Gajurel – HRRP Saroj Kumar Yadav – DLPIU Bldng Prajwal KC – DSE
11 April 2019	Gosaikunda Rural Municipality ward no-3, Ling Ling	Biren Shah – HRRP Prabhu Pokharel – M&E, CLPIU Building Rijan Gajurel – HRRP Saroj Kumar Yadav – DLPIU Bldng Prajwal K.C -DSE
23 April 2019	Ammachhodingmo Rural Municipality ward no-5, Thambuchet	Biren Shah -HRRP Rijan Gajurel-HRRP Babu Ram Fyuba-DFID Badri Pyakurel-HRRP Manisha Rai-HRRP

Objective(s)

- Update Reconstruction Progress at ward level.
- Housing Typology observation and collection.
- To discuss the issues of high rate of non-compliance, low mobilization of engineers.
- Orient on completion certificate distribution process.
- Orient technical person on MIS and CS entry.
- Interaction with ward beneficiaries on housing reconstruction issues.

Summary

HRRP team together with Monitoring and Evaluation Expert CLPIU, Building Mr. Prabhu Pokharel, DLPIU Rasuwa district focal person Mr. Saroj Kumar Yadav and district support engineer Mr. Prajwal K.C. visited Aama Chhodingmo RM ward number 1, Haku and Gosaikunda RM ward no-3, Ling Ling. One engineer and one sub-engineer are deployed in the field in Ammachhodingmo ward no-1 and two sub engineers in Gosaikunda RM ward no-3. Team conducted technical level meeting and field monitoring at field. We went to monitor the newly constructed houses and few houses which has non-compliances issue. For non-compliances houses, DSE Mr. Prajwal K.C recommended improving ideas and techniques to the house owner.

Tranche update record of Ammachhodingmo ward number 1 and Gosaikunda RM ward no-3.

Gaupalika	Total Eligible HHs	First Tranche Received HHs	Second Tranche Received HHs	Third Tranche Received HHs	Construction Completed HHs
Ammachhodingmo-1, Haku	380	376	364	310	310
Gosaikunda -3 , Ling Ling	224	207	191	160	160



Field visit at Ammachhodingmo RM, Ward no-1, Haku

Key points of discussion:

- **In completion certificate distribution process**, around 80% households already received third tranche after completion of house construction, but certificate distribution process seems slow and late. Distribution should start as soon as possible which we made the decision at meeting.
- **Information collection about house sizes and number of rooms**, HRRP district technical coordinator first illustrate the importance of collection of this information and handover the data collection templet to ward technical person.
- **Retrofitting Technical Discussion:** The methods of retrofitting in Masonary structure were discussed with the technicals and the challenges and issues of non-compliance were discussed.
- **Interaction with Beneficiaries:** Dissemination of the information regarding new deadline for first tranche were discussed along with the loan facilitation process.
- **Discussion and interaction with the technicals:** The information regarding the case-load and third inspection and to accelerate this work were disseminated to the ward technicals.

Key finding from field monitoring

- a) High rate of construction material and price inflation is a major problem.
- b) Variation in housing typologies can be seen ranging from timber structure. Hybrid structure and Load bearing BMC structure.
- c) Lack of information in the beneficiaries regarding the loan facility.
- d) Since two sub-engineers are only deployed and no engineer is deployed for Gosaikunda ward no-3 so complex issues becomes a bit harder for them to handle.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
This results in the gap of information and interaction between the beneficiaries and the technical manpower.	Coordination among the technical and beneficiaries	DLPIU Building, DLPIU GMaLI	ASAP
Common roofing multi-beneficiary house	Detach the roof as possible or by any means	DLPIU Building, DLPIU GMaLI	ASAP
The major challenge for the inspection technical is language problem.	Assistance from Social mobilizer	Partners, ward representatives	ASAP
Houses which have been under retrofit has not been started yet.	Immediate implementation of retrofitting work from the concerned authority	DLPIU Building, CLPIU, NRA	ASAP

Photos



PC: Biren Shah

Ammachhodingmo RM, Ward no-1

Name of Beneficiary: Fai Chiring Tamang

PA No-29-8-3-044

Family size -3

Length of House – 24 feet

Breadth of House -12 feet

Floor to Floor height of the room – 7 feet

Tranche update: Third received

Housing Typology: It is a two room Load bearing Stone Masonary in cement mortar structure with light CGI flexible roof, Its floor area is less than 1000 sq . ft.



PC: Biren Shah

Ammachhodingmo RM, Ward no-1

Name of Beneficiary: Buddha Tamang

PA No-29-8-3-0-70

Family size -3

Length of House – 26 feet

Breadth of House -14 feet

Floor to Floor height of the room – 8 feet

Tranche update: second received

Housing Typology: It is a two room Load bearing Stone Masonary in cement mortar structure constructed upto lintel level, Its floor area is less than 1000 sq . ft.

	
PC: Biren Shah Ammachhodingmo RM, Ward no-1, Haku Name of Beneficiary: Nima kaisang Tamang Tranche Update: Second Received Housing Typology: It is a two rooms Hybrid structure building with material used Stone with cement mortar in ground floor and light timber structure in first floor, its floor area is less than 1000 sq ft.	PC: Biren Shah Ammachhodingmo RM, Ward no-1, Haku Name of Beneficiary: Sher Chewang Tamang Tranche Update: Third Received Housing Typology: One room load bearing stone Masonary in cement mortar structure with flexible CGI sheet roofing, its floor area is less than 1000 sq ft.
	
PC: Biren Shah Ammachhodingmo RM, Ward no-1, Haku Name of Beneficiary: Rishan Tamang Tranche Update: First Received Housing Typology: It is two rooms load bearing stone Masonary in cement mortar, its floor area is less than 1000 sq ft.	PC: Biren Shah Ammachhodingmo RM, Ward no-1, Haku Name of Beneficiary: MingmarTamang Tranche Update: First Received Housing Typology: It is a one rooms load bearing stone Masonary in cement mortar with light flexible CGI roofing, its floor area is less than 1000 sq ft.



PC: Biren Shah

Ammachhodingmo RM, Ward no-1, Haku

Name of Beneficiary: Kami Dawa Tamang

Tranche Update: Second Received

Family size -2

PA No-29-8-3-0-70

Length of House – 26 feet

Breadth of House -12 feet

Floor to Floor height of the room – 8 feet

Housing Typology: It is two rooms load bearing stone Masonary in cement mortar, its floor area is less than 1000 sq ft.



PC: Biren Shah

Gosaikunda RM, Ward no-3, Ling Ling

Name of Beneficiary: Kaisang Tamang

Tranche Update: Third Received

Family size -5

PA No-29-2-1-0-5

Length of House – 36 feet

Breadth of House -12 feet

Floor to Floor height of the room – 9 feet

Housing Typology: It is two storey hybrid structure with ground floor stone Masonary in cement mortar and upper storey brick Masonary in cement mortar. It is a six rooms house constructed 12 months ago. The total cost of construction is nearly 21 lakhs. The house owner has taken loan of Rs 6 lakhs from sanima bank at an interest of 14% p.a.



PC: Biren Shah

Gosaikunda RM, Ward no-3, Ling Ling

Name of Beneficiary: Chungi Tamang

Tranche Update: Third Received

Family size -5

Length of House – 28 feet

Breadth of House -12 feet

Floor to Floor height of the room – 8 feet



PC: Biren Shah

Gosaikunda RM, Ward no-3, Ling Ling

Name of Beneficiary: Tamding Tamang

Tranche Update: Third Received

Family size -5

Length of House – 24 feet

Breadth of House -10 feet

Floor to Floor height of the room – 8 feet

Housing Typology: It is two rooms load bearing stone Masonary in cement mortar its floor area is less than 1000 sq ft.

Housing Typology: It is two rooms load bearing stone Masonary in cement mortar its floor area is less than 1000 sq ft.



PC: Rijan Gajurel

Gosaikunda RM, Ward no-3, Ling Ling

Name of Beneficiary: Chiring PalmoTamang

Tranche Update: Third Received

Family size -3

PA No-29-2-1-0-16

Before the 2015 Earthquake the family lived in a single room dry stone Masonary house with area 120 sq feet. After their house was damaged in the earthquake they constructed two rooms house.

Description of new house

Number of rooms- 2

Length of House – 30 feet

Breadth of House -12 feet

Floor to Floor height of the room – 8 feet

Housing Typology: Load bearing Stone Masonary in Cement Mortar

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Will there be additional top-up for us??	Beneficiaries	There is top up only for of 50k Rs for people who have been listed in vulnerable groups.

Challenges and Way Forward

Challenge	Way Forward
Lack of awareness in the beneficiaries about compliant construction.	Effective mason training and awareness programs must be conducted.
Lack of trained masons at present as most of the masons who have taken trainings are out of the districts in some other professions.	Tracking those masons who have taken the trainings and making them aware and providing job in the same field.
Some of the beneficiaries have constructed one room up to DPC level and are not looking up for further construction.	Follow up from DLPIU-Building, DLPIU -GMaLI about the deadline and blacklist process.

Case Story

Landless Victims Stories

Background

Displaced issued is a major problem created by Gorkha earthquake 2015. Rasuwa is one of the highly affected districts out of other 14 major affected districts. Devastating earthquake caused people not only suffer by destruction of their buildings but also made them to abandon their original land and live a life as displaced. They are living displaced life from last 3 years. Although Nepal Reconstruction authority (NRA) had made this process more flexible and easier, it is the fact that many guidelines were amended lots of times to make this process easy



to individual affected people, However the rate of reconstruction process is lagging behind as per people's expectations.

One of the major challenges for reconstruction is displaced households in Rasuwa district. Out of 12,492 eligible households for reconstruction grant 1,011 HHs are listed as displaced HHs, means that around 9 % households are displaced out of total reconstruction beneficiary. People mainly from former Haku VDC, Yarsa VDC, Dandagoun VDC, Thuman VDC and few from others VDCs were displaced. Although the number is not so high, but lack of safe lands brings bit challenges for both NRA and GMAI to address displaced HHs. Victims have been staying under temporary shelter from last 3 years. Neither the displaced people were able to find the safe land on their own nor NRA or GMAI has decided any safe land to settle them yet.


Challenges faced by Displaced HHs

Since they are living under CGI in others land from last three years, they have faced a lot of challenges during this period. The most common problem all of them faced is the difficulties caused by climate some time continuous rain for more than a week, winter is another big challenge while most of time temperature gets down below 5 degree centigrade. They are suffering from many health issue, mostly young children and old aged people are suffered from different unwanted disease like common cold, typhoid and many others. Apart from this, Other major problem is land, as they were displaced from original land and living on other lands brings many terrible situations for them. Most of them have changed their shelter sites few times, they were rejected by many host communities even they had stayed in government land during this period. Another most important fact is that, some of them are living in private land by paying land rent to landowner. Drinking water, Sanitation and Hygiene, Waste management, Livelihood, Health service, education for children are most important areas where they faced challenges every day on their daily life.

Land certificate process and Progress


As soon as NRA had published Land certificate distribution guidelines, certificate distribution process was started at district level. Out of 1,011 listed displaced households around more than half percentage of beneficiary has already received land certificate from NRA and nearly another half is left behind yet, However Rasuwa GMAI is strongly focusing for their resettlements. All the related stockholders both government and partners are showing great interest to complete the resettlement of remaining displaced people. GMAI has been getting valuable support from both rural municipalities and ward level office. Rural Municipalities office has set deadline to complete all the reconstruction process within NRA deadline which was clearly mention on their respective municipality action plan and their active participation and continuous support to GMAI shows how sincerely they are working to accomplish their plan. To speed up this process and to support victims for technical and social assistances Durable Solution project has been working from starting of this process. Both People in Need and CSRC are playing active role for the advocacy of guidelines, coordination between RM, GMAI, Public and displaced. They are also supporting GMAI during site verification process and for public in documentation process. PIN is conducting her safety orientation and training program at different sites.

Status of Land Certificate Distribution Process

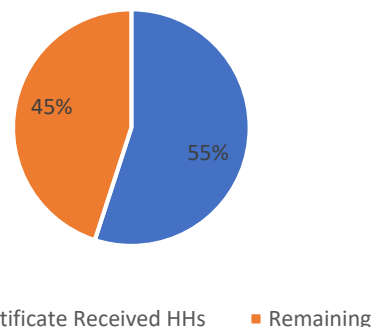



Tranche Distribution Update for displaced HHs

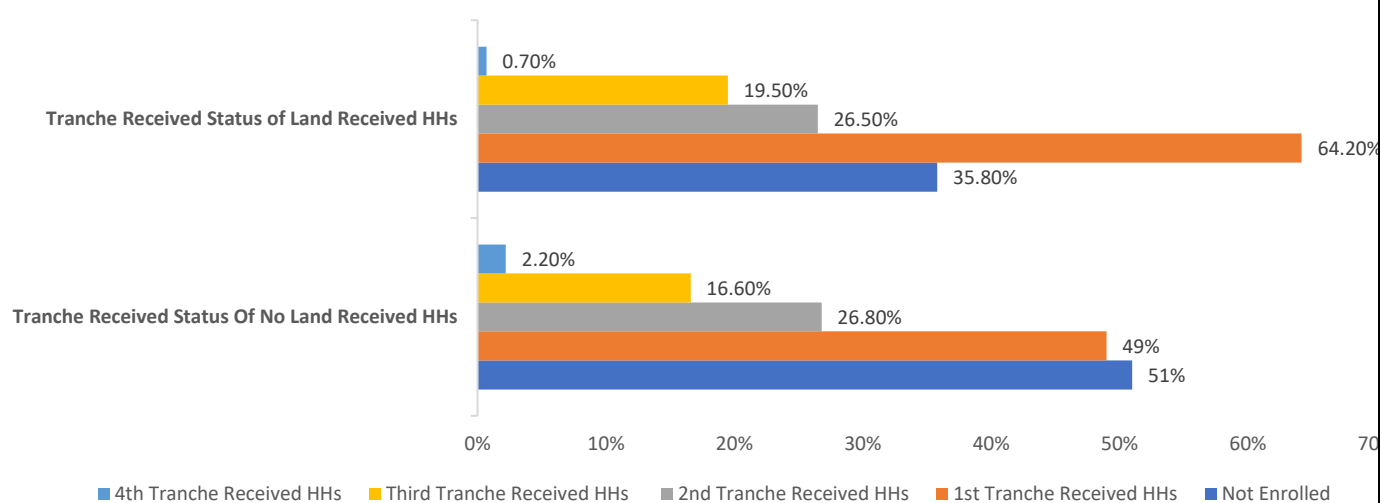

Data Source: GMaLI Rasuwa

Note: Fourth instalments refer that grant which is distribute after construction of Toilet to individual households, basically partners have implemented this approach at community level in reconstruction process.

The above bar charts illustrate tranche received status of both land certificate received and not received displaced households. In case of land certificate received households out of 559 totals, around 35.8% HHs were not enrolled yet or might be currently enrolled but first tranche payments are not made by GMaLI where 64.2% of houses has already enrolled and first tranche was already made, additionally 26.5% of HHs has received second installment or already started construction. The chart shows that 19.5% of displaced families has received third installment of reconstruction grant or they have completed construction already and 0.70 % of households were constructed by partners organization as per the GMaLI Rasuwa. The additional information which we got from GMaLI shows that around 10% land certificate received beneficiary has constructed new house at same vulnerable place.



Fig: Temporary shelters of displaced households at left and at right under construction two rooms houses by same displaced people at new safe land after receiving land from NRA.

Another side household those who have not received land certificate yet have different major serious issues, People have started construction of new houses at original vulnerable place. As per the information shows in above chart out of 452 households around 51% of displaced HHs is not enrolled yet or might be currently enrolled but first tranche payments are not made by GMaLI, around 49% has received first installment from government. Where percentage of second and third tranche received HHs is 26.76% and 16.6% respectively. Means they have constructed new houses at original vulnerable place and this issue is one of the most challenging issue in reconstruction process. 2.2% of households were constructed by partners organization as per the GMaLI Rasuwa. It was shared that around 86% of households were relocated within district, very small amount around 13.8% of beneficiary were relocated at neighborhood Nuwakot district, only a single house is relocated at Dhading district.

Role of Central and District stakeholders in relocation process:

At first the relocation process of Rasuwa district was seemed a little difficult because of limited safe land within district and the displaced communities were not accepted by host communities in many areas. The continuous follow up and coordination by ward and rural municipalities for both displaced and host communities made things possible. Also, the role of District Administration office Rasuwa, GMaLI and Durable solution project was really appreciated to solve many issues which was seen at community level. Despite of the fact that there were different challenges for relocation of displaced people both GMaLI and Durable Solution have played vital role to accomplish this achievement by supporting victims from the starting by selecting suitable safe sites for them along with doing all the necessary government documentation process. The role of central NRA especially executive members both Mr. Dhurba Parsad sharma and Chandra Shrestha has been a forefront and vital for the achievement of this progress. Their visit in the district has proved to be a boon to address the challenges and issues which arose for the resettlement of land less people.

Some Photos:



Caption: Field monitoring visit of under construction houses by displaced families in new land provided by NRA at santibazar with NRA executive member Dhurba sharma together with GMaLI Rasuwa chief and HRRP team.



Caption: Interaction meeting at Uttargaya RM office. NRA executive member Dhurba Sharma together with Uttargaya RM vice chairperson chimali Tamang, GMaLI Rasuwa team and displaced HHs interaction program.

PC: Nisha Niraula



Caption: Land certificate for displaced and cheque for landowner distribution program organized by GMaLI Rasuwa at Uttargaya RM ward number 1. GMaLI chief Bharat Kumar Thapa is distributing check and land certificate.

PC: Nisha Niraula



Caption: Her safety training program organized by Durable solution team. Nisha Niraula project coordinator of Durable solution for Rasuwa district is conducting training program.

PC: Nisha Niraula

Challenges faced for relocation program

- Before the publication of relocation related guidelines few households have already constructed new house in original vulnerable land. Now some of them have already completed construction of building and have received all the housing grant from NRA.
- Number of households seems high in respect to safe land available in district. Now, communities are migrating towards another district especially in Nuwakot. Livelihood is one the main challenges for those households.
- Displaced were not accepted in different places by host communities because of which although they have bought land, but host communities have not allowed them for the construction of houses at newly bought land.
- Khalte issue is one of the biggest challenges for the relocation process. Around 174 displaced HHs are currently living in a place called khalte at Uttargaya RM. Although different studies shown that place is not suitable for the resettlement and both NRA and rural municipalities are trying to shift people to other safe place. But those displaced households are demanding to stay at same place as the place is quite urban in respect to other area of district and people are becoming more urbanized since they are staying at same place from last 3 years.

Some photos of newly constructed building by displaced HHs after receiving land from NRA:



Caption: Displaced HHs constructed houses of timber structure after receiving grant from NRA at Gosaikunda RM ward number 1.	Caption: Displaced HHs constructed houses of stone Masonary structure after receiving grant from NRA at Gosaikunda RM ward number 6.
	
Caption: Displaced HHs constructed houses of RCC structure after receiving grant from NRA at Uttargaya RM.	Caption: Displaced HHs constructed houses of brick Masonry structure after receiving grant from NRA at Naukunda RM ward 3.
