

Monthly District Report

Lamjung, Tanahau, Kaski and Syangja

12 July – 22 August 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Lamjung	Contact list Update: NRA technical person (Ward, Palika and DLPIU office) contact list is updated in HRRP google templet.	14-July,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika Profile update and upload: Reconstruction palika profile data of all 8 palika's of Lamjung district is updated. Profile uploading process in palika website is ongoing, 6 has already uploaded out of 8 palika.	25-July,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika Level meeting: The general palika level coordination meeting of Marsyangdi Rural Municipality was organized at Marsyangdi Palika office, Lamjung district. The coordination meeting was attended by Palika Chief, engineers, representative from DLPIU Building, GMaLI, DSE and HRRP team. The main objective of this palika level meeting was to take updates of housing reconstruction and retrofitting processes in Marsyangdi Rural Municipality.	19-Aug,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Reconstruction Interaction program: HRRP team attended the interaction program organized by NRA/CLPIU team from central with DCC Chief and Palika Chief of Beshishara Municipality. The purpose of visit by NRA/CLPIU was to observe reconstruction status, take updates of resurvey and reverification works and to interact with local stakeholders of visiting districts.	24-July,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

	District Reconstruction Facilitation Meeting: Facilitation meeting was organized by GMaLI on 16-July,2019 at DCC Hall Lamjung. Meeting is chaired by DCC Chief Mr. Lokraj Panday and other facilitation committee members are presented on meeting.	16-July,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Reconstruction Interaction and feedback collection one day program: HRRP team attended one day interaction and feedback collection program organized by central NRA. Palika's chairperson, chief administrative officer and IT focal person were key participant from local level and DCC chief, CDO, DLPIUs chief were presented from district level. Program aims to collect feed back on information management capacity of local level.	13-Aug,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	MIS data update process: By the support from National IM team MIS data update process in new MIS template prepared by HRRP is completed in Lamjung district. Reconstruction grant distribution data from GMaLI and households inspection data from building is updated on newly formed template.	14-Aug,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Field visit: HRRP team conducted field visit at Marsyangdi Rural Municipality and Rainash urban municipality ward number 1. Representative from Building, GMaLI, DSE also joined HRRP team on this field visit. This visit aims to collect information on retrofitting process on these two sites, visit team interacted with retrofitting beneficiary and collected major issues and challenges they have faced on this process.	16 and 17 Aug,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Ward Level meeting: Ward level meeting is conducted on Rainash municipality ward number 1 at ward office. Meeting was focused on retrofitting status and its challenges faced by ward. After completion of meeting visit team	17-Aug,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

	together with ward chairperson conducted field visit around ward number 1 and collected suggestion and challenged faced by retrofitting beneficiaries.				
	Upload field photos in flicker			Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	https://www.flickr.com/photos/hrrp/
	Retrofit information collection for bulletin- information collection from beneficiaries, Palika ,DLPIU- Building , DLPIU-GMaLI , Field Er point of view.	17-Aug,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
Tanahau	Contact list Update: NRA technical person (Ward, Palika and DLPIU office) contact list is updated in HRRP google templet.	15-July,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika Profile update and upload: Reconstruction palika profile data of all 10 palika's of Tanahau district is updated. Profile uploading process in palika website is ongoing, 4 has already uploaded out of 10 palika.	25-July,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	MIS data update process: By the support from National IM team MIS data update process in new MIS template prepared by HRRP is ongoing in Tanahau district. Reconstruction grant distribution data from GMaLI and households inspection data from building is updated on newly formed template.	15-Aug,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Ward wise Segregated non-compliance data sharing with Tanahun DSE	28-July,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
Kaski	Contact list Update: NRA technical person (Ward, Palika and DLPIU office) contact list is updated in HRRP google templet.	16-July,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

Summary of events during this period

Syangja	Palika Profile update and upload: Reconstruction palika profile data of all 5 palika's of Kaski district is updated. Profile uploading process in palika website is ongoing, 4 has already uploaded out of 5 palika.	25- July,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Contact list Update: NRA technical person (Ward, Palika and DLPIU office) contact list is updated in HRRP google templet.	17- July,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	
	Palika Profile update and upload: Reconstruction palika profile data of all 11 palika's of Syangja district is updated. Profile uploading process in palika website is ongoing. Out of 11 Palika's 9 has uploaded profile on their respective palika website.	25- July,2019		Rijan.gajurel@hrrpnepal.org Biren.shah@hrrpnepal.org	

News & Updates

Lamjung

Reconstruction Interaction program:

HRRP team attended the interaction program organized by NRA/CLPIU team from central with DCC Chief and Palika Chief of Beshishara Municipality. The purpose of visit by NRA/CLPIU was to observe reconstruction status, take updates of resurvey and reverification, reconstruction update and its challenges and to interact with local stakeholders of visiting districts.

Reconstruction Interaction and feedback collection one day program: HRRP team attended one day interaction and feedback collection program organized by central NRA. Palika's chairperson, chief administrative officer and IT focal person were key participant from local level and DCC chief, CDO, DLPIUs chief were presented from district level. Program aims to collect feedback on information management capacity of local level.

Syangja


Reconstruction Interaction and feedback collection one day program: HRRP team attended one day interaction and feedback collection program organized by central NRA. Palika's chairperson, chief administrative officer and IT focal person were key participant from local level and DCC chief, CDO, DLPIUs chief were presented from district level. Program aims to collect feedback on information management capacity of local level.

Tranche Status (Lamjung)


Tranche Status Table: 22- Aug,2019

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Besishahar Nagarpalika	2851	1308	1257	1259	1815	452	11	6	6	0
Dordi Gaunpalika	3375	2238	2206	2206	373	278	25	3	3	0
Dudhpokhari Gaunpalika	2667	2437	2361	2367	109	65	6	4	4	0
Kwholasothar Gaunpalika	740	314	271	272	869	300	72	0	0	0
MadhyaNepal Nagarpalika	2346	1505	1448	1449	671	466	54	0	0	0
Marsyangdi Gaunpalika	1936	911	877	880	1359	849	176	158	158	0
Rainas Nagarpalika	4362	2989	2947	2951	2079	825	105	99	99	0
Sundarbazar Nagarpalika	4084	2257	2157	2158	708	220	90	19	19	0

Graph of Tranche Status: 22-Aug,2019

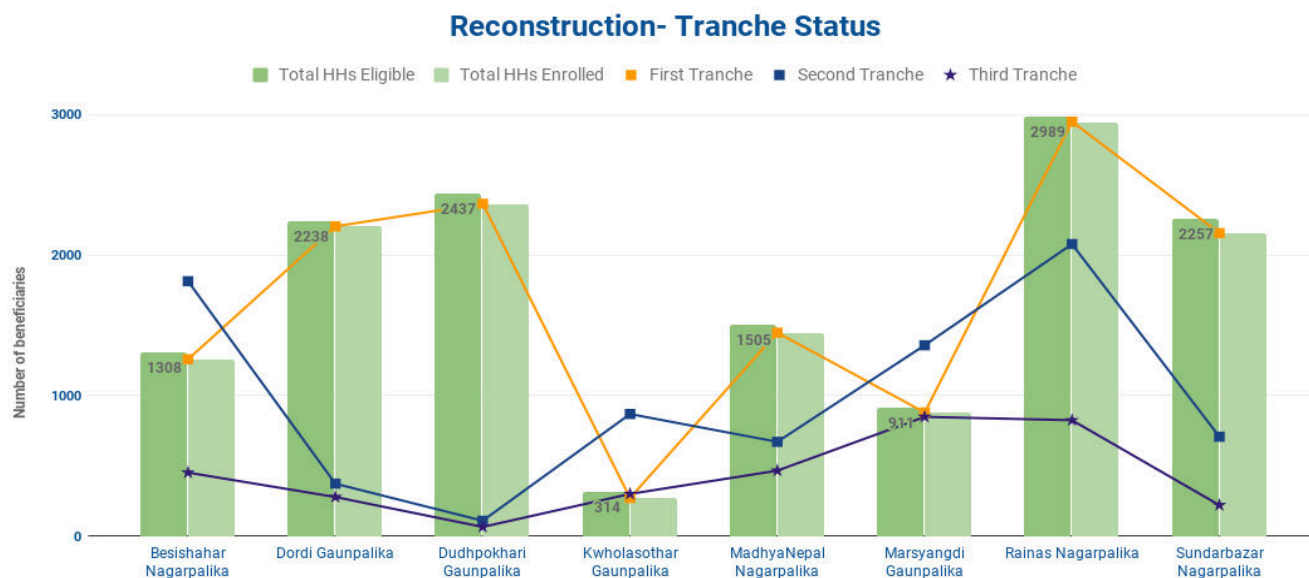

Graph for Retrofitting Status: 22-Aug,2019

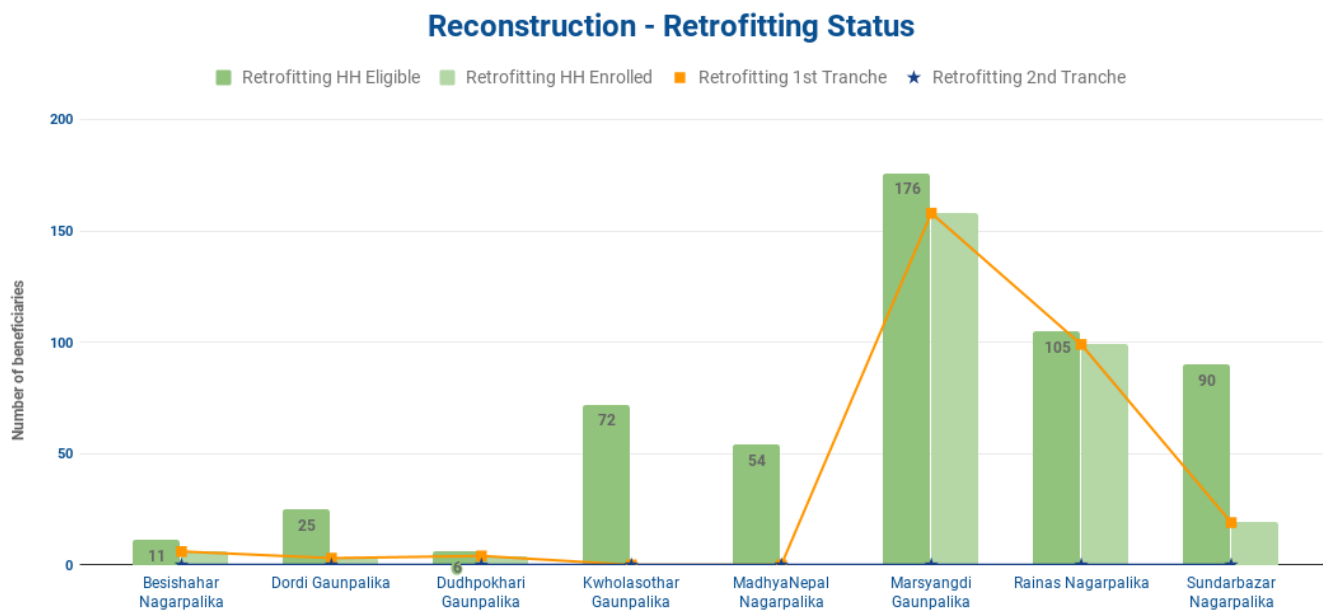


Tranche Status (Tanahau)

Tranche Status Table: 22-Aug,2019


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Anbukhaireni Gaunpalika	1050	710	705	705	477	400	21	5	5	0
Bandipur Gaunpalika	1226	609	1055	590	298	234	33	32	32	0
Bhanu Nagarpalika	7540	4219	4147	4198	2433	1579	75	12	12	0
Bhimad Nagarpalika	2680	987	974	975	512	190	46	0	0	0
Byas Nagarpalika	4626	2486	1981	2401	1439	988	163	180	180	0
Devghat Gaunpalika	960	725	499	499	328	127	32	8	8	0
Ghiring Gaunpalika	969	254	232	232	120	80	0	0	0	0
Myagde Gaunpalika	1877	1292	1065	1066	653	417	38	33	33	0
Rhishing Gaunpalika	1771	680	473	473	283	170	34	0	0	0
Shuklagandaki Nagarpalika	2837	1859	1740	1742	981	519	24	1	1	0

Graph of Tranche Status: 22-Aug,2019

Reconstruction- Tranche Status

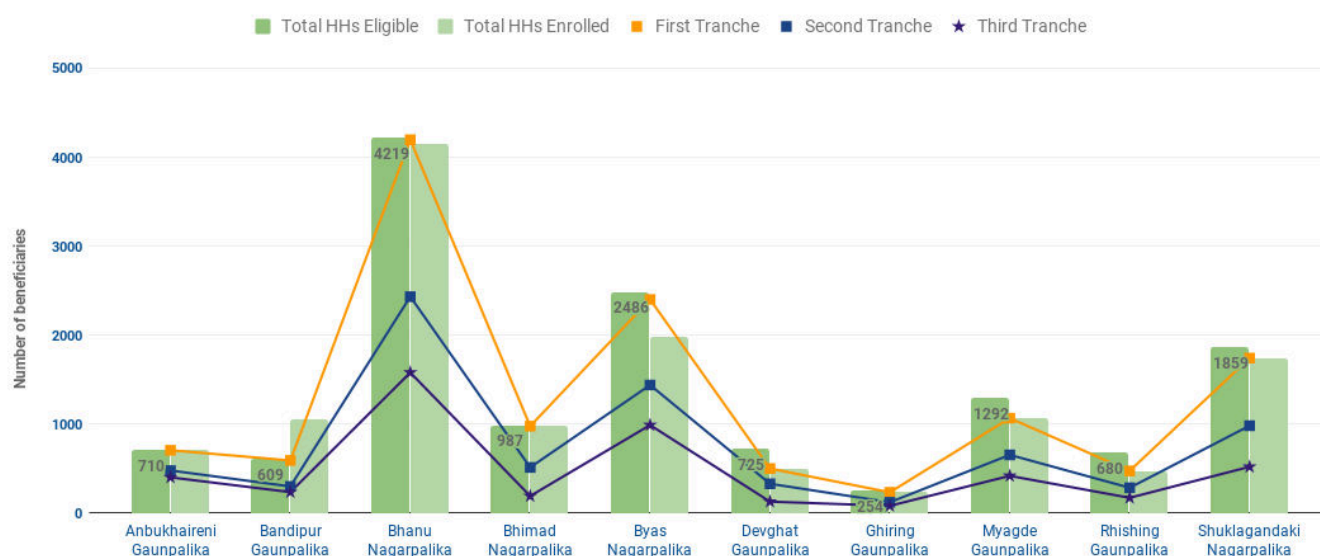

Graph for Retrofitting Status: 22-Aug,2019

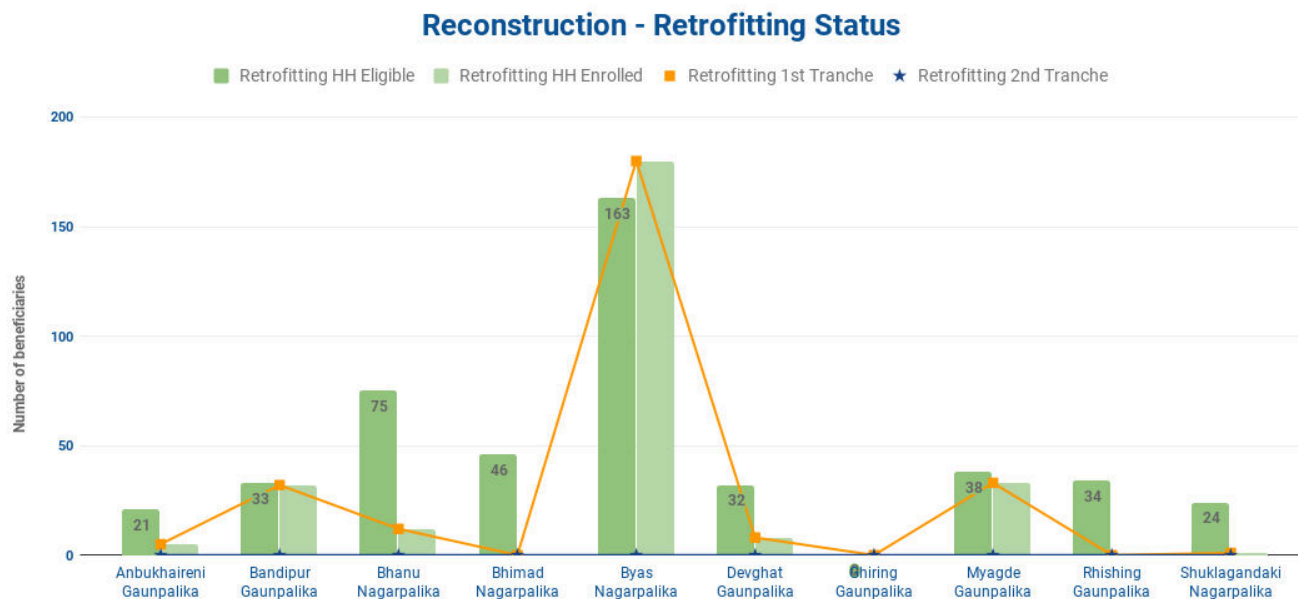


Tranche Status (Kaski)


Tranche Status Table: 22-Aug,2019

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Annapurna Gaunpalika	667	395	395	395	179	74	19	12	12	0
Machhapuchchhre Gaunpalika	781	427	427	427	265	34	30	5	5	0
Madi Gaunpalika	2296	1160	1160	1160	512	97	40	12	12	0
Pokhara Lekhnath Mahanagarpalika	5276	2774	2421	2421	1153	281	111	84	84	0
Rupa Gaunpalika	2054	1270	1222	1222	455	238	42	26	26	0

Graph of Tranche Status: 22-Aug,2019

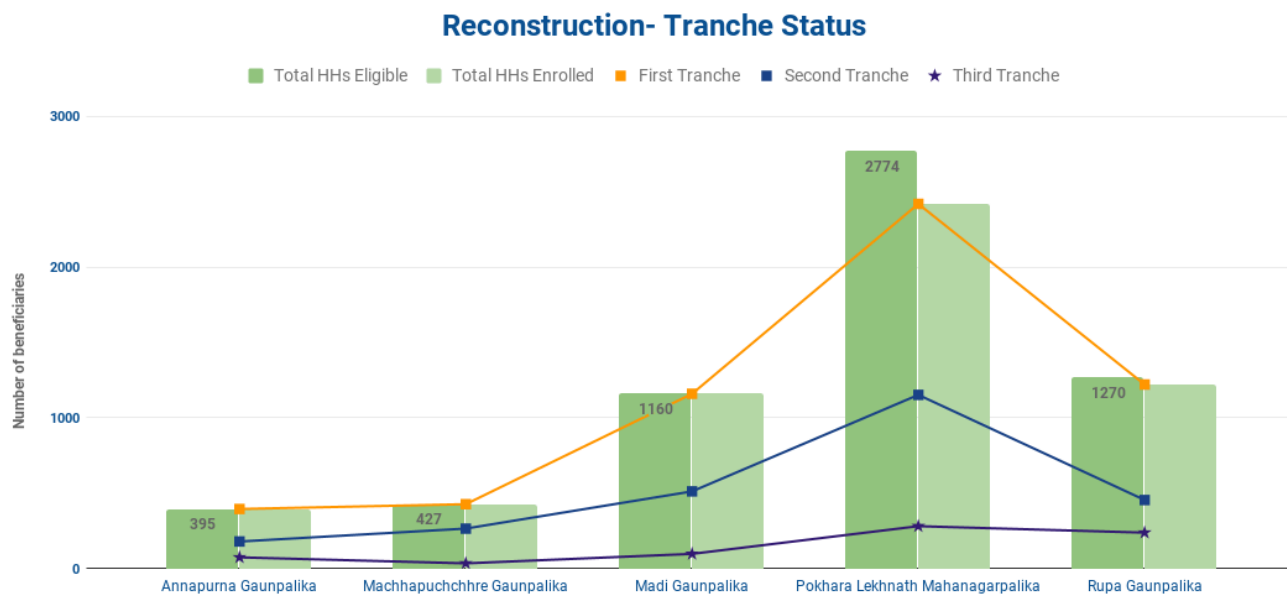

Graph for Retrofitting Status: 22-Aug,2019

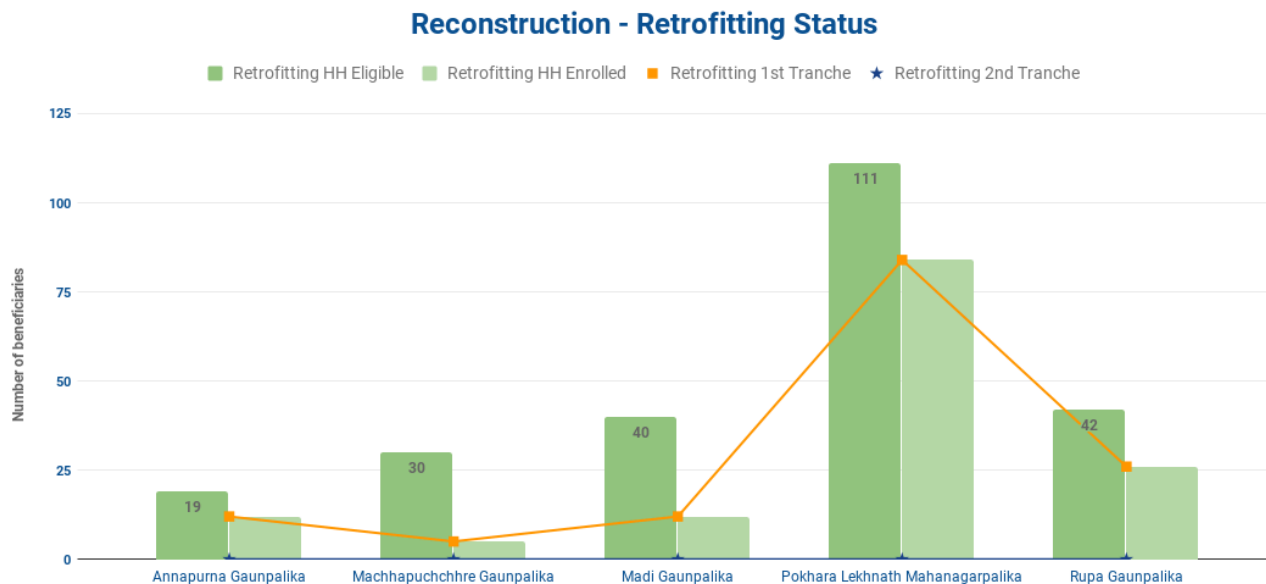


Tranche Status (Syangja)

Tranche Status Table: 22-Aug,2019


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Aandhikhola Gaunpalika	1515	843	820	820	369	83	72	34	34	0
Arjunchaupari Gaunpalika	803	509	470	470	248	164	65	46	46	0
Bhirkot Nagarpalika	2099	1041	992	992	299	73	26	24	24	0
Biruwa Gaunpalika	1024	638	609	609	166	81	40	9	9	0
Chapakot Nagarpalika	1815	804	797	797	411	58	12	3	3	0
Galyang Nagarpalika	1294	634	621	621	311	105	101	99	99	0
Harinas Gaunpalika	912	435	398	398	157	32	1	0	0	0
Kaligandagi Gaunpalika	752	493	397	397	152	95	2	0	0	0
Phedikhola Gaunpalika	403	278	266	266	111	55	10	7	7	0
Putalibazar Nagarpalika	2798	1471	1458	1458	736	313	321	294	294	0
Waling Nagarpalika	2696	1671	1605	1605	708	198	54	32	32	0

Graph of Tranche Status: 22-Aug,2019

Reconstruction- Tranche Status

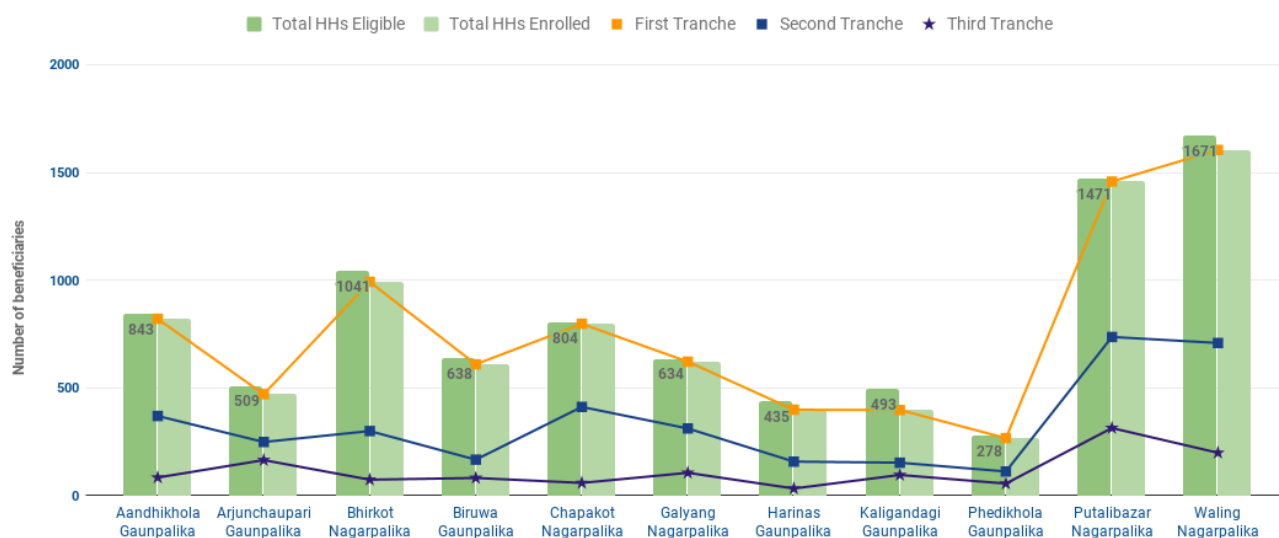

Graph for Retrofitting Status: 22-Aug,2019

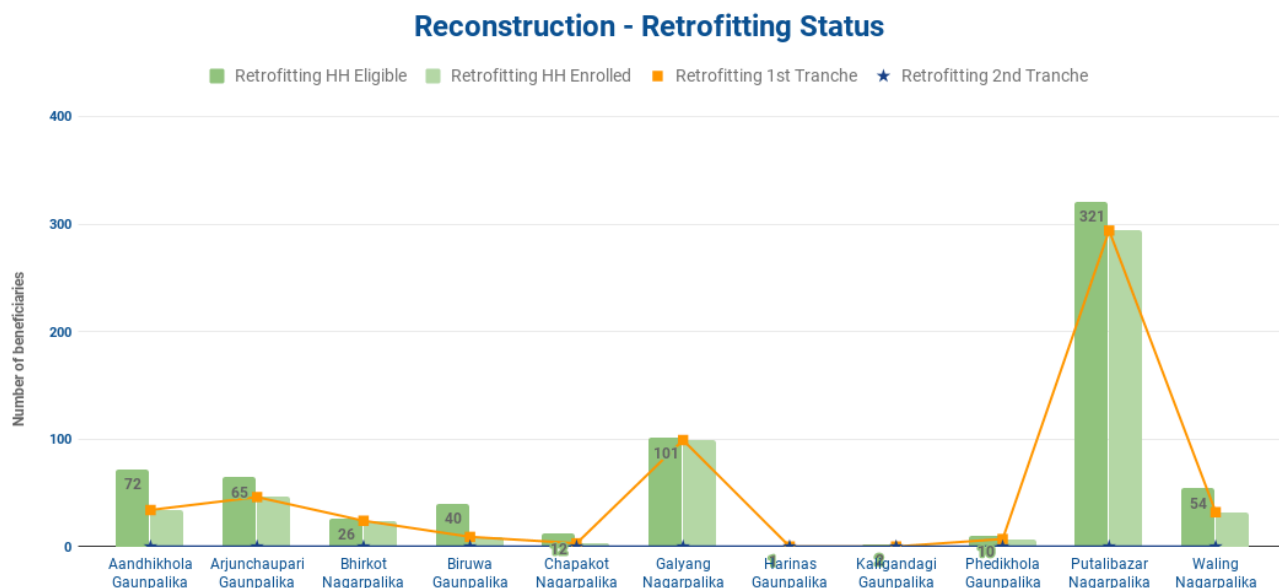

Field Visit Reports (Lamjung)

Visit 1

Date	Location	Participants
19-August, 2019	Ward no-5, Marsyangdi RM	- Biren Shah, DTC, HRRP - Rijan Gajurel, DC, HRRP - Umesh Dangol, DSE, NRA - Shittal Babu Lohani, Focal Er, DLPIU-Building - Binayak Dawadi, GMAI
20-August, 2019	Ward no-1, Rainas Nagarpalika	- Biren Shah, DTC, HRRP - Rijan Gajurel, DC, HRRP - Umesh Dangol, DSE, NRA - Shittal Babu Lohani, Focal Er, DLPIU-Building - Binayak Dawadi, GMAI
Objective(s)	- To conduct Palika level meeting at Nagarpalika. - Update the reconstruction progress at Nagarpalika level. - Discuss the problems and issues faced by the Nagarpalika elected officials and Engineers regarding reconstruction. - Information collection on Retrofit.	

Why was the visit carried out in this location?

The progress in retrofitting after 4 years of earthquake is less compared to the reconstruction progress. There has been a huge ambiguity among the stakeholders especially the beneficiaries on the benefit of retrofitting of the house compared to the reconstruction. Lack of communication to the community on the retrofitting and its contribution in making the houses as resilient and strong as that of reconstructed house has been the major factor hindering the retrofitting speed. Apart from the selected POs providing the retrofitting training to the mason/engineers and retrofitting the houses (model house) as part of the training, there are very few cases of retrofitting in the field with the free will of the beneficiaries. The slow pace of retrofit has a diversified reasons and dimensions to be looked from.

Collection of the reasons why retrofit has not taken its pace from the grass-root level can help us to identify the problems and a way forward can be probably given making various strategies from the government level. The perception of slow pace of retrofitting from different groups are different. The beneficiaries have various problem

regarding retro and its initiation. The stakeholders, technical persons have different views on this regard. Also built change a Partner organization has retrofitted a house in this Palika using strong back concept. So, in order to study the effectiveness of this model to the other beneficiaries this field was conducted.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

Field Summary:

HRRP Lamjung along with DSE, DLPIU-GMaLI, DLPIU-Building and technical staffs from DLPIU Building conducted joint field monitoring at Ward no 5, Marsyangdi RM and Ward no-1, Rainas Municipality of Lamjung district. The field visit was mainly focused on the interaction and meeting with Palika representatives regarding retrofitting. The progress in retrofitting after 4 years of earthquake is less compared to the reconstruction progress. There has been a huge ambiguity among the stakeholders especially the beneficiaries on the benefit of retrofitting of the house compared to the reconstruction. Lack of communication to the community on the retrofitting and its contribution in making the houses as resilient and strong as that of reconstructed house has been the major factor hindering the retrofitting speed. Apart from the selected POs providing the retrofitting training to the mason/engineers and retrofitting the houses (model house) as part of the training, there are very few cases of retrofitting in the field with the free will of the beneficiaries. Majority of the beneficiaries wants to get converted into the reconstruction beneficiaries from retrofit beneficiaries due to lack of awareness and difficulty in applying retro to their houses. Some of the beneficiaries also wants to return the first tranche of the retrofitting as they do not want to retrofit their houses due to the misleading concept on retro.

The beneficiaries are not satisfied for retrofitting and has also applied for conversion from retro to recon beneficiary. They say that "They are not satisfied with the government evaluation right now and if they could be converted to reconstruction beneficiaries. Also, there is no masons and technical support yet so this could be tedious and long process for them.

- No. of HHs visited:7
- No. of meetings with engineers:1
- No. of meetings with local officials:2

The knowledge and perception of retrofitting in various levels (Beneficiary, DLPIUs, Palika, etc.) are different. So, during this field visit we captured some views of different related authorities regarding retrofitting:

From	Links
Palika Representative	Click
Beneficiaries	Click1 Click2
DLPIU-GMaLI	Click
DLPIU-Building	Click

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
The technicals of the municipality have no proper knowledge on retro and, they have not been able to convince the beneficiaries regarding technical and cost parameters of retro. There are no masons specialized in retro work, not even one as a result of which if any beneficiaries are interested in retro, they cannot find trained masons for retrofitting their houses. The beneficiaries are likely	Practically implemented training to the technicals along with mason training in retrofitting	Not yet	DLPIUs, Palika, ward	ASAP

to get converted into recon from retro due to these causes.				
Lack of reporting from the technicals to the Palika representatives regarding reconstruction challenges, issues and updates.	Weekly reporting and involvement of technicals in reconstruction related meetings with update.	Weekly or bi-monthly reporting to the Palika representatives regarding reconstruction challenges, issues and updates.	DLPIU Building technicals	ASAP
Lack of knowledge among the beneficiaries regarding retrofitting resulting in tendency to get converted from retro to reconstruction beneficiaries.	Orientation program in ward and palika level related to retrofit must be implemented asap.	Not yet	DLPIU-GMaLI, DLPIU-Building, Palika stakeholders, Pos,	ASAP

Photos



Image: Palika level meeting in progress at Ward no. 5, Marsyangdi RM. The meeting was attended by Palika Chief, Focal Engineer (DLPIU Building Lamjung), District Support Engineer and engineers of DLPIU Building Lamjung, HRRP Lamjung team and reconstruction engineers deployed at Marsyangdi Rural Municipality



Ward No. 5, Marsyangdi Rural Municipality, Lamjung: Demo retrofit house carried out as part of the DFID funded retrofit project implemented by a consortium of UNOPS and Build Change. Five masons and nine Engineers are trained under the Retrofit Program. The retrofitting was started on 19th April, 2019 and Finished on 14th June, 2019.



Front view



Back view

Talaborang, ward no-1, Rainas Municipality, Lamjung

Name of the beneficiaries: Shakuntala Adhikari

Description of house: Two storey – two rooms Stone Masonary in mud mortar house in which the they have done animal husbandry in lower floor and are living in the upper floor. Small hair line cracks and shear cracks are seen with large openings. Walls on the two eaves only and the remaining two sides are open.



Name of the beneficiary: Daya Ram Neupane

Description of house: Two storey – two rooms with attic Stone Masonary in mud mortar house. Already plastered the house which has already cost them nearly 20-30k. Now they are not financially able to retrofit as it will cost more than the support granted by the GON.



Name of Beneficiary: Laxmi Kanta Dawadi

Description of house: Two storey – three rooms with attic Stone Masonary in mud mortar house. As he wants to get converted to reconstruction beneficiary and reconstruct a new house as per his need he has field to get converted. If he is not converted, then he has planned to refund the first tranche of retro grant to the government and construct a new house by dismantling the old one.

	
Name of Beneficiary: Aas Maya Gurung Description of House: Two storey plus attic house, Stone in mud mortar Masonary. Hair lines and shear cracks in all walls. The beneficiary is interested in retrofitting but due to lack of technical support and trained masons she has not been able to retrofit her house and receive the second tranche.	

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Will there be any additional top-up for retrofitting beneficiary?	Beneficiaries	There are not any decisions made regarding additional top-up, but it has been a subject of discussion in NRA for now we could only say its not increased.

Challenges and Way Forward

Challenge	Way Forward
Most of the retrofitting beneficiaries wants to get converted to reconstruction.	Awareness and orientation program to the beneficiaries regarding the advantages, and cost parameters of retro.
Lack of masons who can implement the retro process in the district.	Mason training on retrofitting focusing those masons who have already taken training on EQ resilient housing construction.
Lack of technicals in the field for the implementation of retro.	One ward one technical (Engineer) must be implemented and these technicals must be trained on practical implementation of retrofitting.
People are not ready to adopt the concept of strong back as they feel this more costly and tedious.	Other simplified methods such as wire meshing, splint and bandage must be implemented.

Case Story:

From the Beneficiaries Perspective

Please mention the district/municipalities and ward you have collected the Case stories of beneficiaries:
[Talaborang, ward no-1, Rainas Municipality, Lamjung](#)
Name of the beneficiaries [Shakuntala Adhikari](#)

- Description of house: [Two storey – two rooms](#)
[Stone Masonary in mud mortar house in](#)
[which the they have done animal husbandry](#)
[in lower floor and are living in the upper floor.](#)
[Small hair line cracks and shear cracks are](#)
[seen with large openings. Walls on the two](#)
[eaves only and the remaining two sides are](#)
[open.](#) Front view



- Issues and challenges, they have faced/facing:
The beneficiary is not satisfied for retrofitting and has also applied for conversion from retro to recon beneficiary. She says that “I am not satisfied with the government evaluation right now and if I could be converted, I will make new house as per my requirement. The process of retrofitting will be costly and, I would not get the house as per my occupancy. Also, there is no masons and technical support yet so this could be tedious and long process for me.
- what types of support they are expecting?

They are hoping to get converted into recon beneficiary. Also, if its not possible for conversion than it would be helpful if technical and mason support for the process of retro would be provided from government side.

- Are they motivated to retrofit their houses?

No, they are not motivated for retro. They have been waiting for long and haven't got any technical support and there is not even a single mason who is familiar with this process.

- What they understand about retrofitting and what is their view

Once the Palika engineer told her that her house needs to get differently treated and strengthened using several methods making a lot of holes in their house and right now since the government is focusing on recon so the engineer will also ask in the district about this during his visit at that time.

- Their suggestions? What they think about how retro can be improved, and other beneficiaries can be motivated to retro their houses

Demonstration house using applicable and simple techniques which can be easily implemented must be done. Only after then retro can be boosted. Doing orientation and social debate can't solve this issue unless practically seen by the beneficiaries in demo house.

- Have they talked with their ward/Palika representatives? What they said?

We have talked but they said that a team will come and will start the process.

- Do they know the availability of technical HR, like Masons? Engineers?

They know about engineers but not about trained masons in retro

- Are they connected with engineers to retro their houses? What engineers say about it?

No, they are not connected with the engineers who can implemented the retro process. The engineers have just theoretical knowledge on retro. According to them the strong back concept of retro is the only one process they have seen practically in one Palika demo house, but this method is very hard and cannot be implemented for the beneficiaries. The need some more practical knowledge on process of retro (implementation) using other easy methods.

- What NRA/Government should do to complete retro houses?

- Add Top up from 1lakh so that it could be easier for beneficiaries to start the process financially.
Also provide technical assistance and masons who are trained for retrofitting.

- what would motivate them to undergo retrofitting (try to probe more on social, cultural, economic, political, personal influencing factors)

If the government provide additional top-up, technical assistance and masons they are ready. Demonstration house using easy and applicable method must be implemented to scale up retro. Also, orientation programmes from Palika level regarding retro. Masons are the most important parameter in this process as we cannot find even one masons who knows retro. So, Mason training must be implemented regarding retrofit.

