

Fortnightly District Report

Dolakha

18 – 31 January 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
DGCM concluded in Dolakha: District General Coordination Meeting concluded in Dolakha. Key decisions taken in the meeting were survey data of POs should be tallied with GMaLI Dolakha's data and tracking the data. The other decision was data of vulnerable beneficiaries (over 65 years single women; over 70 years senior citizens; below 16 years orphan children; People with disability who have red and blue card only provided by Nepal government) should be updated and collect data of their houses construction status in respective palika/wards.	31 Jan 2019	10	1	Ms. Rita Lamsal, Section/Information Officer, GMaLI, Dolakha, Cell: 9846075504, Email: ritalamsal@gmail.com	
Chief Minister Observed Integrated Settlement in Jilu: Mr. Dormani Poudel, Chief Minister, Province No. 3 observed progress of Dihi Phasibhai Model Integrated Settlement in Bhimeshwar-4 Jilu, Dolakha. During the visit, the chief minister Mr. Poudel; Bhimeshwar municipality mayor Mr. Bharat KC, chair of settlement Mr. Arjun Chaulagain, ward chair Mr. Haribansha Chaulagain and other stakeholders, beneficiaries assured that they will complete the settlement in time. Fifty percent of the settlement works already has been completed so far. 183 private houses will be completed till Chaitra 2075(April 2019). Total budget of the settlement is NRs 7 crore 32 lakhs. In settlement, solar electricity and community building will be constructed. NRA will provide 4 lakhs for each house to construct their houses.	26 Jan 2019	47	39	Mr. Haribansha Chaulagain, Ward Chair, Bhimeshwar Municipality-4, Dolakha, Cell: 9851194360	

News & Updates

<http://annapurnapost.com/news/118119> 50 percent completed Jilu's Integrated Settlement construction, Rabindra Gautam, Dolakha, Jan 19, 2019(5 Magh, 2075) Annapurna Post National Daily,

44,000 Private houses have been constructed in Dolakha(*Dolakhama 44,000 niji aawas bane*),


[https://www.nayapatrikadaily.com/news-details/4030/2019-01-](https://www.nayapatrikadaily.com/news-details/4030/2019-01-23?fbclid=IwAR2LolVUIFRmfiXAvIbFT1e3zKDP_HbCkhVIJbUzroPbOueNARzjt-CIQ4)

[23?fbclid=IwAR2LolVUIFRmfiXAvIbFT1e3zKDP_HbCkhVIJbUzroPbOueNARzjt-CIQ4](https://www.nayapatrikadaily.com/news-details/4030/2019-01-23?fbclid=IwAR2LolVUIFRmfiXAvIbFT1e3zKDP_HbCkhVIJbUzroPbOueNARzjt-CIQ4) Shyam Khatiwada, Charikot, Naya Patrika National daily, January 23,2019(Magh 9, 2075)


Tranche Status

Rural /Municipality	Baiteshwor	Bhimeshwor	Bigu	Gaurishankar	Jiri	Kalinchowk	Melung	Sailung	Tamakoshi
Total HHs Surveyed	8550	13693	6799	6656	5991	9062	8067	8524	7537
Total HHs Eligible	8308	12394	6699	6762	5805	8866	7474	8110	7428
Total HHs Enrolled	8204	11147	6257	6541	5644	8395	6935	6979	6827
First Tranche	7701	10976	6189	6439	4839	8388	6534	6831	6819
Second Tranche	6713	7756	5209	5179	3708	7375	5673	5302	5822
Third Tranche	6013	6006	4557	4831	2769	6808	4643	4021	5134
Total HH Constructed	6025	6014	4564	4841	2775	6816	4657	4037	5149
Grievance Registered	248	546	132	123	222	378	1191	226	84
Grievance Addressed	1795	2235	719	760	961	1238	1100	1257	828
RF HH Eligible	339	348	34	74	153	32	402	746	110
RF HH Enrolled	4	101	4	25	20	1	8	20	9
RF 1 st Tranche	4	101	4	25	20	1	8	20	9
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	1875 (9 Palikas in total)								
Non-Compliance Addressed	1518 (9 Palikas in total)								


Graph of Tranche Status:

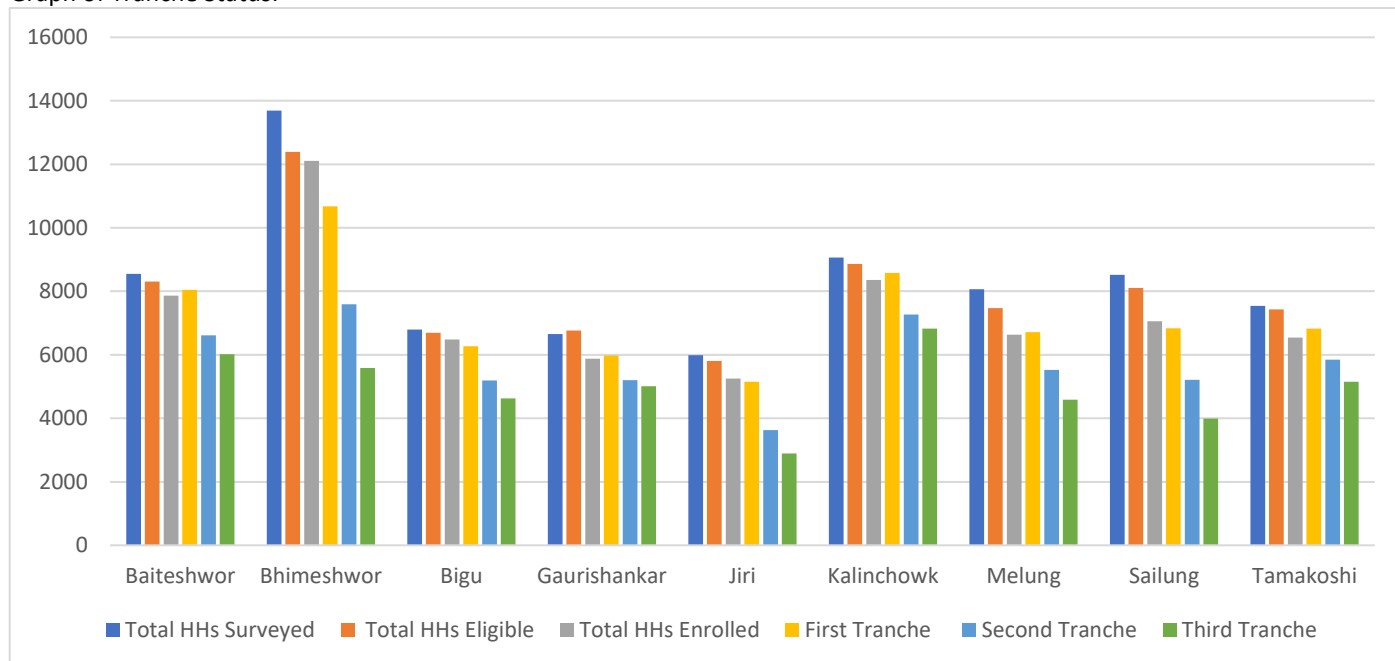

Graph for Retrofitting Status:

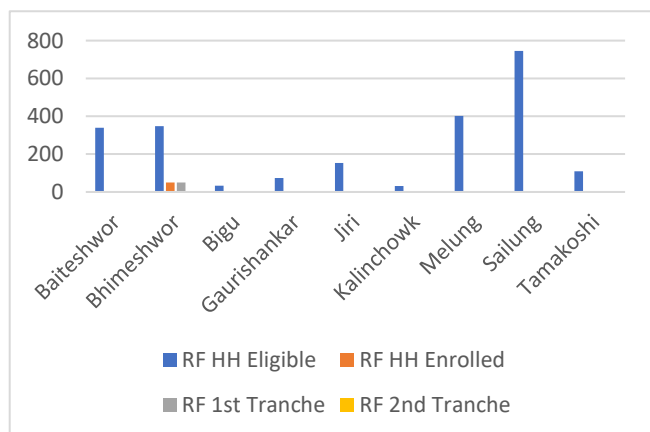

Graph for Grievance Status:

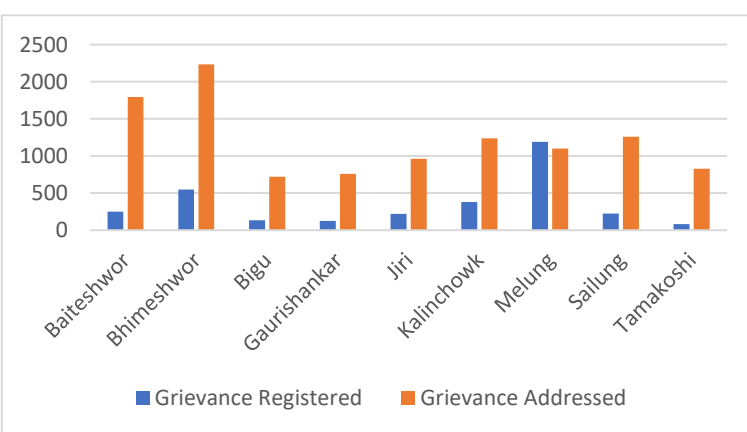

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
24 th Jan 2019	Tamakoshi Rural Municipality-3, Jhule, Dolakha	- Binod Kalauni - Kamal B Mahat - Nirmal Darshan Acharya, Unit chief, GMaLI, Dolakha - Mr. Arjun Tamang, Unit chief, DLPIU (Building) - Ms Rita Lamsal, Section/Information Officer, GMaLI, Dolakha - Janak Raj Joshi (M&E) Officer - Bhogendra Kr Sah (DLPIU/Focal Person)

Objective(s)
- To conduct palika level coordination meeting - To observe construction of buildings - To collect housing typology

Summary
Mr. Ishwor Chandra Pokharel, Chairperson of Tamakoshi Rural Municipality remembered casualties done by the earthquake in Tamakoshi Rural Municipality. 274 people were died which is the second largest casualty in the Dolakha among other Palika's. He expressed his heartfelt condolence to the victims of the quake. Further, chairperson was seen quite excited with the reconstruction rate at Tamakoshi Rural Municipality. He told that people has named reconstructed house as "Bhukampa Ko Ghar" (house constructed only to get tranche purpose) because it has been constructed for receiving 3 lakh reconstruction grants. This has created dominant buildings of two roomed which is not satisfying the need of the family which has results addition of light or heavy structure above after receiving third tranche. This has made much vulnerable towards earthquake and other disasters. Reconstruction of houses without analyzing the family needed is the major shortcomings of this reconstruction, chairperson told. Regarding the presence of the technical staff of NRA most of them not present at field which is delaying construction and file forwarding. He informed that where technical staff are available all the time construction quality and progress is good but where not quality and progress is low. Further, he added that if all the authority is given to local levels then within one year they will accomplish reconstruction work.

During the meeting, GMaLI chief Mr. Nirmal Darshan Acharya requested all to cooperate with them to speed up reconstruction. He further told that if anybody is facing problems regarding reconstruction can meet him at office time for discussion on which he will do his best from his side.

Acting Chief of DLPIU/Building Mr. Arjun Tamang told that everybody must be aware about the quality of the construction to minimize the risk in future. Further, he informed that few houses have been found non-compliance such files have been sent to CLPIU for further analysis which needs detail analysis for making them eligible for tranche. Therefore, he requested to take suggestions before going for construction from technical team of NRA regarding technical knowledge useful for the construction of earthquake resistant construction.

Photos



Figure 1: People participating in the coordination meeting at Tamakoshi Rural Municipality, in front of the RM office 03 ward of Jhule. Pc = Binod Kalauni





Figure 2: Meeting minute. Pc = Binod Kalauni

Housing Typology Report

Photo

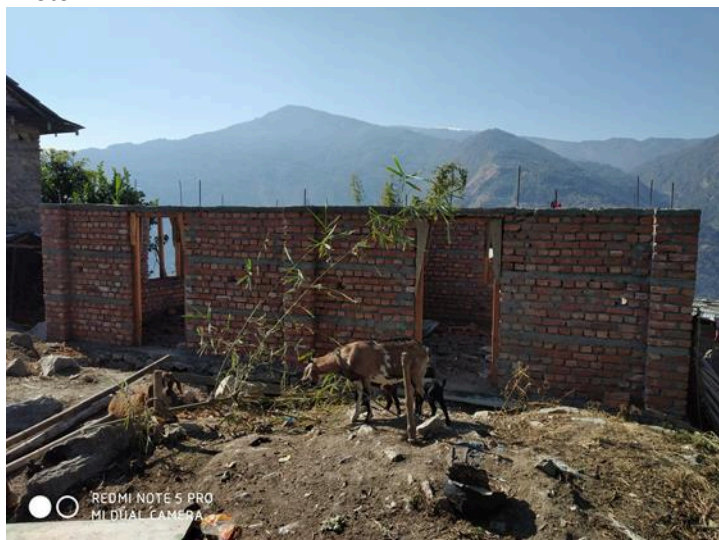

One Story load bearing and brick in cement mortar building has been constructed in 03-Jhule, Tamakoshi RM. Mr. Pardum Pokharel is the house owner and he has received second tranche. Pc = Binod Kalauni

Photo



Load bearing and brick in cement mortar building has been constructed in 03-Jhule, Tamakoshi RM. Mr. Om Dhakal is the house owner and he received first tranche till date. This building is situated at road side which is steep and road side earth is retained by retaining wall. Pc = Binod Kalauni

Case Story

First tranche returnee happy with her house constructed by RDTA/SCI

Mrs. Bimala Bishwakarma, Baiteshwor-8, Chhetrapa returned first tranche (NRs 50,000) to government. She told me in recent phone interview, 'I am living happily in my house which Rural Development Tuki Association (RDTA)/Save the Children International (SCI) constructed after the earthquake. In her house husband and wife and daughter have been living. Further, she told me, 'I had been living in temporary makeshift with facing lots of hardship.'

RDTA/SCI supported to construct her house with the support of Save the Children International Nepal. She had been supported by the project entitled 'Technical support to National Reconstruction Authority on Private housing in Baiteshwor Gaunpalika'. The project was launched in all 8 wards of Baiteshwor Gaunpalika. Total 450 earthquake beneficiaries had been supported by this project.

Technicians had been mobilized for the quality construction work intensely. Social mobilization was also crucial part of the project. WASH, rural road construction had been also conducted as project activities.

Significantly, 79 vulnerable households have been supported by providing extra NRs 45,000 each which had been extra than NRs 3,00,000 provided by NRA to the earthquake beneficiaries.

RDTA/SCI also facilitated on banking process to release/ease the tranche in time and without hassle. Moreover. Some of the houses also received the housing/building completion certificate.

She told me that she was so happy with the two-room house constructed by RDTA/SCI where she had contributed to making snacks to masons.
