

Monthly District Report

Gorkha, Dhading

9 May - 13 June 2019

Summary of events during this period					
Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Gorkha	District Reconstruction Facilitation Meeting. The detail agenda can be accessed in HRRP website, and meeting minute can be found in the link provided.	20 th May 2019	Gorkha	chandra.gurung@hrrpnepal.org , rsa.laxmi@gmail.com	Meeting minute
	NRA CEO's visit to Gorkha; handover school building at Barpak and observed NRNA's integrated settlement of Gupsipakha, Laprak, Dharche Rural Municipality.	5 th June 2019	Gorkha	chandra.gurung@hrrpnepal.org	
	MEAL report of May submitted.	6 th June 2019	Gorkha	chandra.gurung@hrrpnepal.org	Click here
	Palika wise technical staff's information, and PO's staff's information of the district updated.	7 th June 2019	Gorkha	chandra.gurung@hrrpnepal.org	Click here
	Materials and labor costs= of district finalized and updated based on district rate	7 th June 2019	Gorkha	chandra.gurung@hrrpnepal.org	Click here
Dhading	District Reconstruction Facilitation Meeting was conducted, organized by GMALI. The detail agenda can be accessed in HRRP website, and meeting minute can be found in the link provided.	22 nd May 2019	Dhading	chandra.gurung@hrrpnepal.org , sachin.sapkota@hrrpnepal.org	Meeting Minute

Summary of events during this period

	Joint Monitoring Field Visit	28 th – 31 st May 2019	Salyantar, Tripurasundari Rural Municipality	sachin.sapkota@hrrpnepal.org	See details in field visit report section
	Meeting with CLPIU Deputy director at Dhading	28 th May 2019	Dhading	sachin.sapkota@hrrpnepal.org	Meeting Minute
	Public Hearing program organized by GMALI, Dhading	9 th June 2019	Galchi Rural Municipality	chandra.gurung@hrrpnepal.org	Meeting Minute
	Public Hearing program organized by GMALI, Dhading	10 th June 2019	District Coordination Committee, Dhading	chandra.gurung@hrrpnepal.org	Meeting Minute
	MEAL report for the month of May submitted	6 th June 2019	Dhading	chandra.gurung@hrrpnepal.org , sachin.sapkota@hrrpnepal.org	Click here
	HRRP had short meeting with DFID senior level team at Dhading & discussed HRRP support provided NRA, GMALI and overall reconstruction status in the district	11 th June 2019	Dhading	chandra.gurung@hrrpnepal.org ,	
	Palika wise technical staff's information, and PO's staff's information of the district updated	6 th June 2019	Dhading	chandra.gurung@hrrpnepal.org , sachin.sapkota@hrrpnepal.org	Click here
	Materials and labor costs of district finalized and updated based on district rate	7 th June 2019	Dhading	chandra.gurung@hrrpnepal.org , sachin.sapkota@hrrpnepal.org	Click here
Palpa	Tranche data updated	12 th June 2019	Palpa	chandra.gurung@hrrpnepa.org	
Gulmi	Tranche data updated	12 th June 2019	Gulmi	chandra.gurung@hrrpnepa.org	
Arghakhachi	Tranche data updated	12 th June 2019	Arghakhachi	chandra.gurung@hrrpnepa.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Field visit to support for reconstruction facilitation in Palpa	27 – 30, June 2019 (Palpa – Tansen Urban Municipality)	HRRP/GMALI	palpa@hrrpnepal.org
Field visit to supportfor reconstruction facilitation in Gulmi	1 – 4 July 2019 (Gulmi – Musikot Urban Municipality)	HRRP/GMALI	gulmi@hrrpnepa.org
Field visit to support reconstruction facilitation in Arghakhachi	5 – 9, July 2019 (Arghakhachi – Bhumekasthan Urban Municipality)	HRRP/GMALI	arghakhachi@hrrpnepal.org

News & Updates

- ✓ NRA CEO visit Gorkha, handed over school building supported by JICA, and observed NRNA's ongoing integrated settlement of Laprak
- ✓ The work of Earthquake Memorial Park will be commenced from August 2019 -



बारपाकमा भूकम्प स्मृति पार्कको काम साउनबाट सुरु हुने

Published On : ३० जेष्ठ २०७६, बिहीबार ०८:३२

By : Daraundi Daily

On : देश, मुख्य खबर, राजनीति, समाचार, समाज

अनुपमा खनाल :

राष्ट्रिय पुनर्निर्माण प्राधिकरणले गोर्खाको बारपाकमा 'भूकम्प स्मारक(पार्क)' बनाउने काम आउँदो आर्थिक वर्षबाट सुरु गर्ने जनाएको छ । २०७२ सालमा गएको विनाशकारी भूकम्पको केन्द्रविन्दु रहेको बारपाकमा भूकम्प स्मारक बनाउने काम आउँदो आर्थिक वर्षबाट सुरु गर्नेगरी बजेटको व्यवस्था गरिएको जानकारी प्राधिकरणका प्रमुख कार्यकारी निर्देशक सुशील ज्ञवालीले दिए ।

तत्पश्चात् संघीय संसदको टिगो विकास तथा सशासन समितिको बैठकमा बोल्दै उनले यसका लागि आवश्यक पानी ताटो पाटीपौता लगायतका


<https://daraundi.com/main-news/15996/>

गुप्सी पाखामा बन्यो मनमोहक वस्ती — <http://www.gorkhasamachar.com/2019/06/06/35177>


Rural /Municipality	Aarughat	Ajirkot	Bhimsen	Chumnubri	Dharche	Gandaki	Gorkha	Palungtar	SahidLakhan	Siranchoik	Sulikot
Total HHs Surveyed	6925	4126	6836	2275	4169	5619	10217	9798	7065	6835	7202
Total HHs Eligible	6925	4126	6836	2275	4169	5619	10217	9798	7065	6835	7202
Total HHs Enrolled	6659	3955	6635	1812	3731	4815	9133	8309	6082	5922	6856
First Tranche	6656	3961	6615	1943	3794	4842	9356	8685	6087	5872	6848
Second Tranche	6290	3820	6336	1619	3367	4266	8193	7149	5551	5578	6688
Third Tranche	5562	3462	5170	1404	3067	3173	7574	5775	4854	4773	6302
Total HH Constructed	5562	3462	5170	1404	3067	3173	7574	5775	4854	4773	6302
Grievance Registered						16622 (Total)					
Grievance Addressed	967	452	941	279	1121	1390	2496	3770	2282	2023	901
RF HH Eligible	171	63	168	49	280	441	1079	1038	836	904	177
RF HH Enrolled	171	63	168	49	280	441	1079	1038	836	904	177
RF 1st Tranche	32	3	35	1	85	29	559	442	31	29	2

Tranche Status (Gorkha)

Tranche Received Update #Gorkha

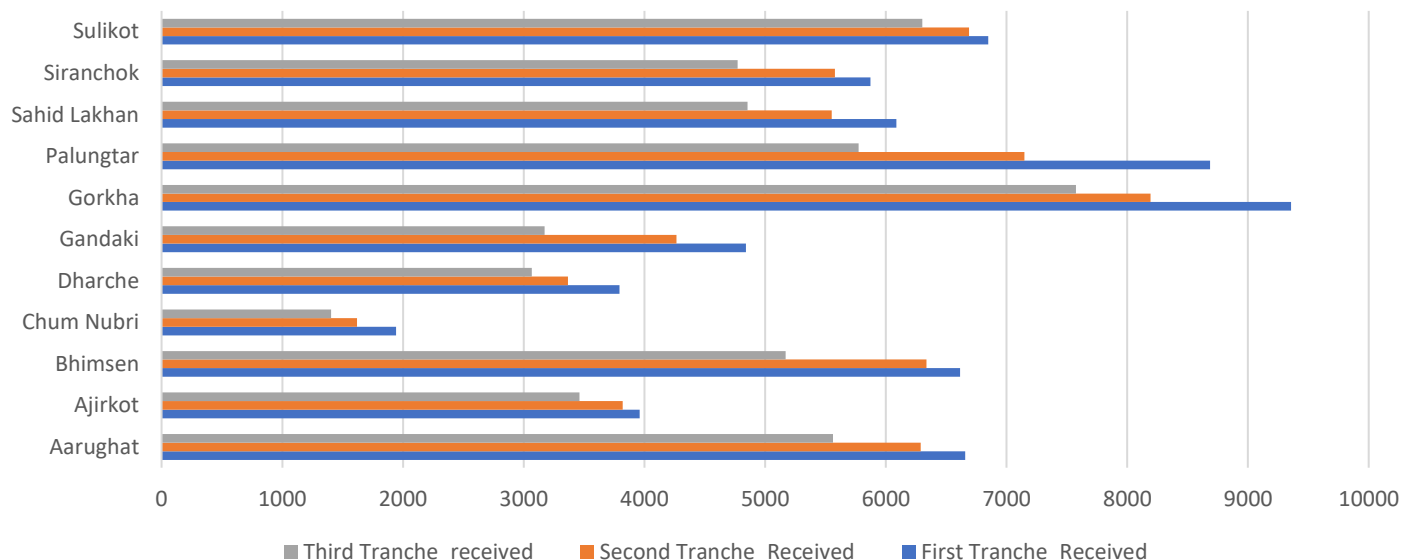

Retrofitting #Gorkha

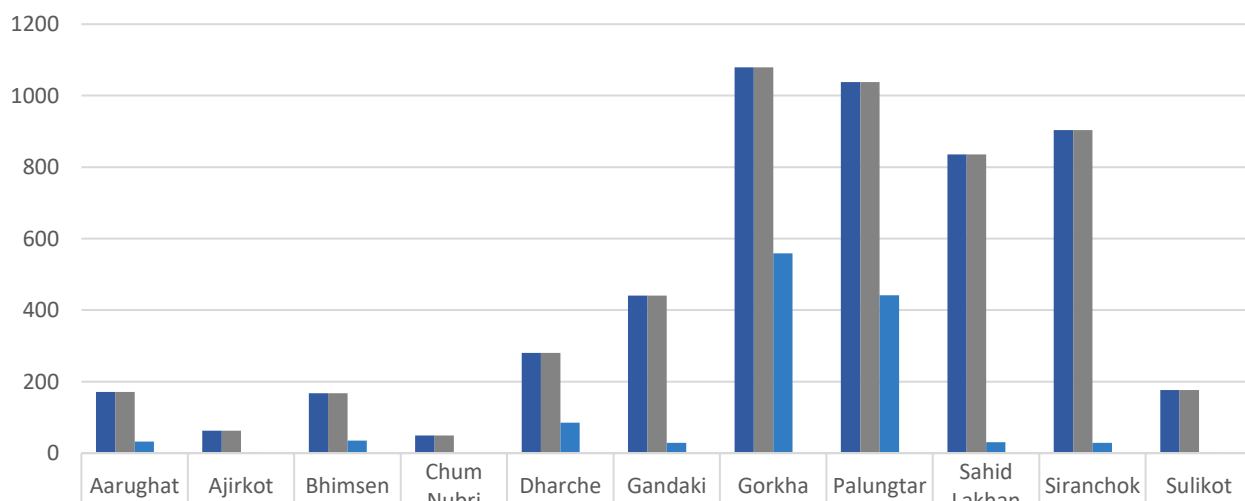


	Aarughat	Ajirkot	Bhimsen	Chum Nubri	Dharche	Gandaki	Gorkha	Palungtar	Sahid Lakhan	Siranchok	Sulikot
RF HH Eligible	171	63	168	49	280	441	1079	1038	836	904	177
RF HH Enrolled	171	63	168	49	280	441	1079	1038	836	904	177
RF 1st Tranche	32	3	35	1	85	29	559	442	31	29	2
RF 2nd Tranche											

Tranche Status (Dhading)


Tranche Status Table

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Benighat Rorang Gaunpalika	7010	5538	4685	4685	3894	3087	647	647	0	0
Dhunibesi Nagarpalika	8212	7580	6810	6810	5277	3726	109	109	9	0
Gajuri Gaunpalika	6480	5735	4969	4969	4269	3275	520	520	45	0
Galchi Gaunpalika	6661	6746	6041	6041	5330	3674	327	327	36	0
Gangajamuna Gaunpalika	6532	6743	6600	6600	5983	5221	42	42	2	0
Jwalamukhi Gaunpalika	7255	6552	5199	5199	4093	3365	1110	1110	35	0
Khaniyabash Gaunpalika	3485	3633	3552	3552	3142	2482	12	12	0	0
Netrawati Gaunpalika	4122	4057	3848	3848	3506	3131	57	57	1	0
Nilakantha Nagarpalika	15239	13618	12353	12353	10580	8899	640	640	53	0
Rubi Valley Gaunpalika	3164	3270	3046	3046	2469	2091	187	187	43	0
Siddhalek Gaunpalika	6277	6194	5325	5325	4590	3896	538	538	0	0
Thakre Gaunpalika	8017	6780	6256	6256	5325	3792	274	274	10	0
Tripura Sundari Gaunpalika	6668	6567	6035	6035	5130	3915	248	248	10	0

Graph of Tranche Status

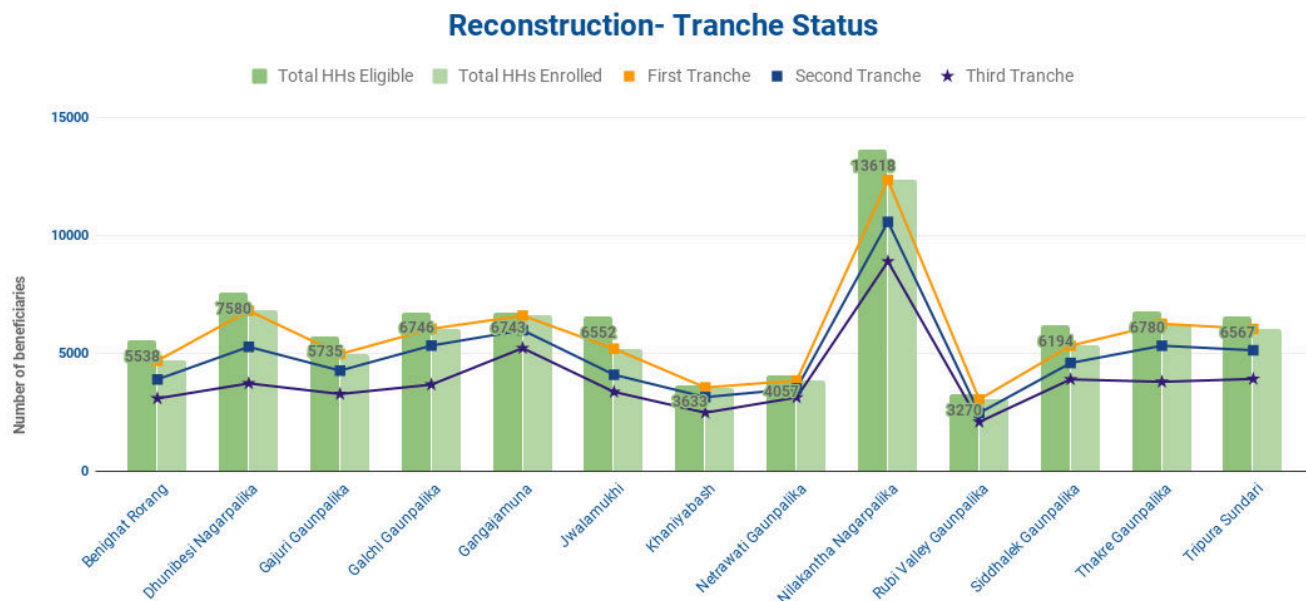

Graph for Retrofitting Status:

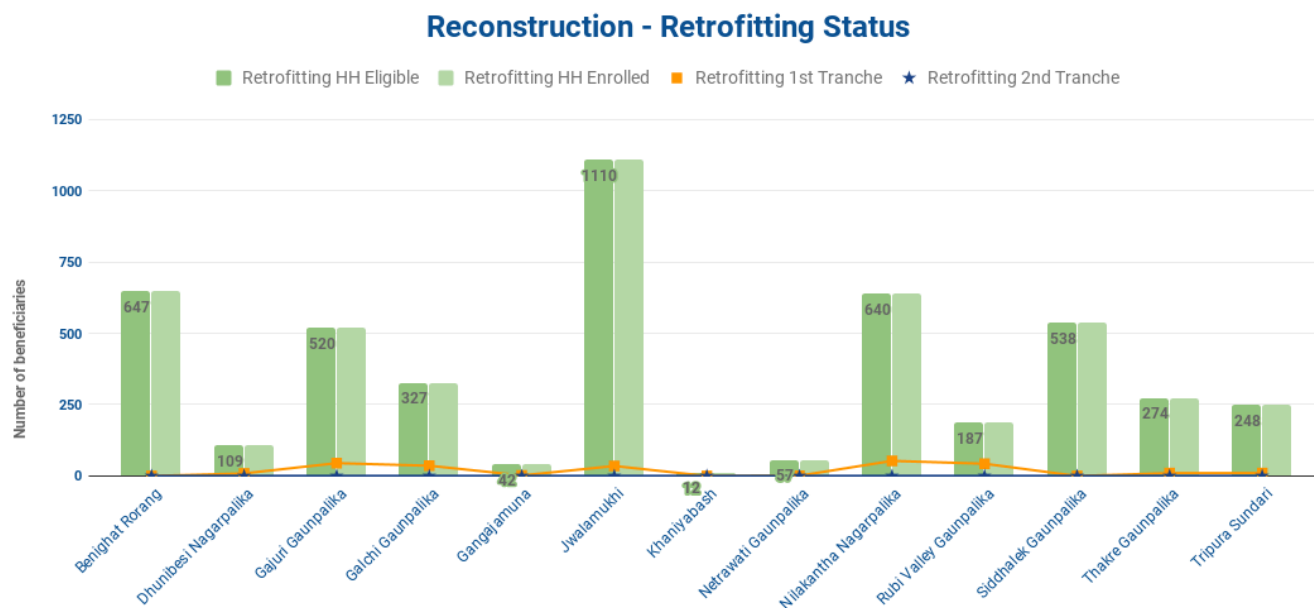


Tranche Status (Palpa)

Tranche Status Table

Palpa	Tranche
Total HHs surveyed	10727
Total HHs Eligible	4652
Total HHs Enrolled	4100
1st Tranche	4042
2nd Tranche	1832
3rd Tranche	1126
Retrofit beneficiaries	2375

Graph of Tranche Status

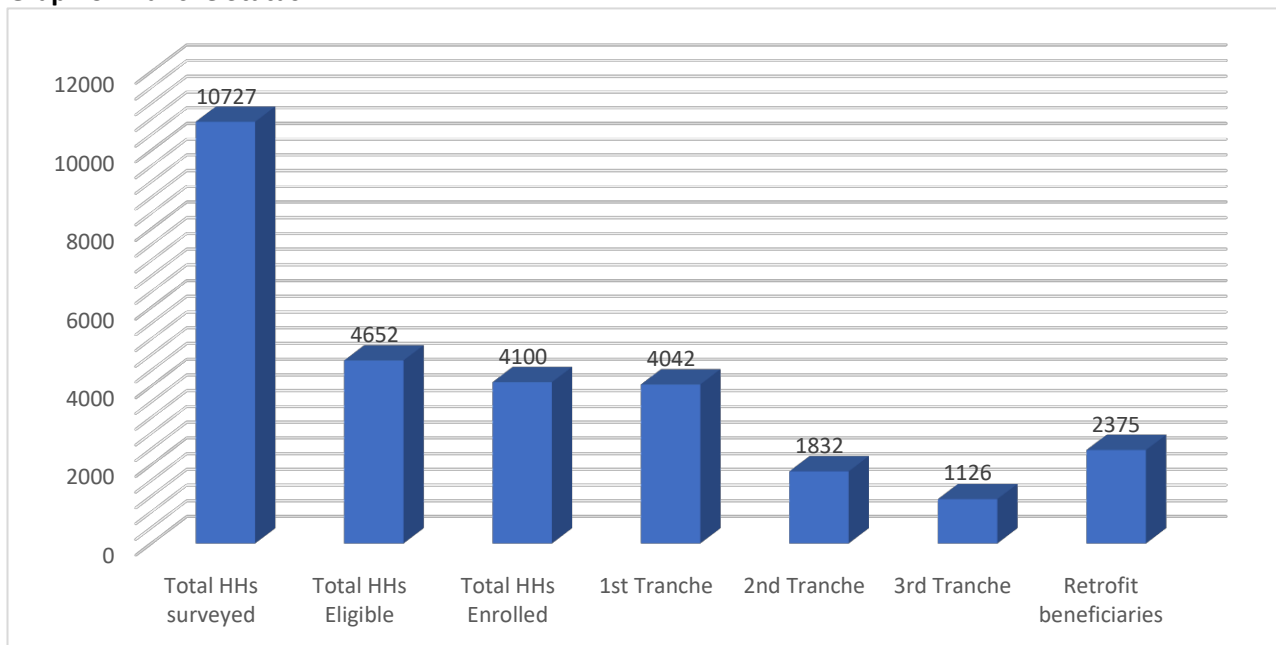


Tranche Status (Gulmi)

Tranche Status Table

Gulmi	Tranche
Total HHs surveyed	7050
Total HHs Eligible	4144
Total HHs Enrolled	3956
First Tranche	3956
Second Tranche	2382
Third Tranche	1200
Retrofit beneficiaries	2363

Graph of Tranche Status

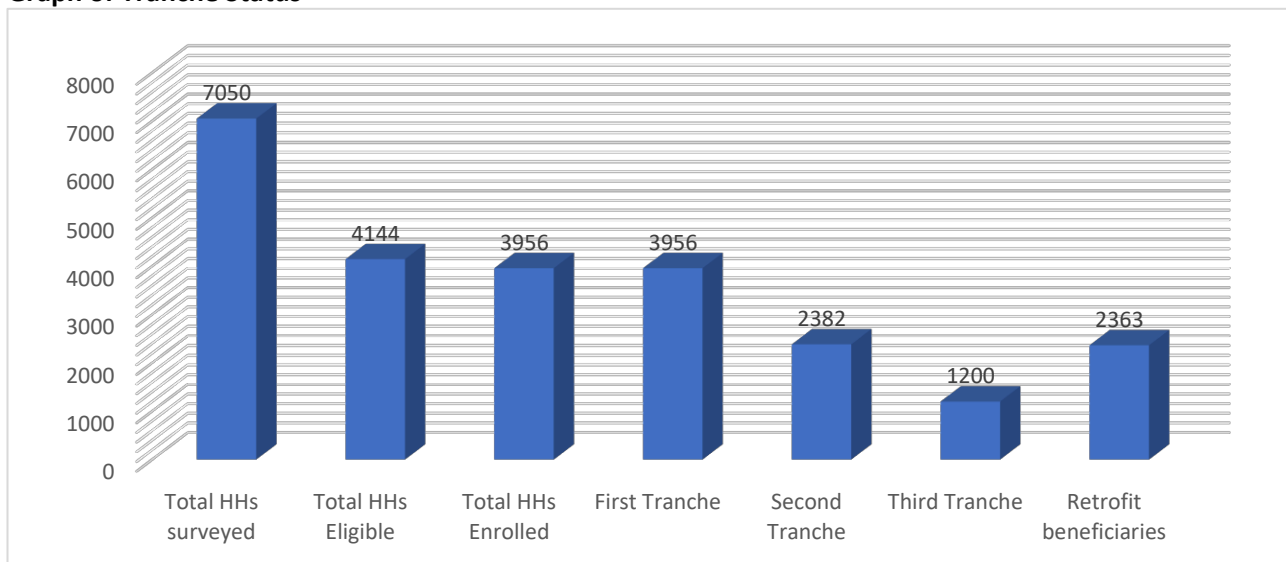


Tranche Status (Arghakhachi)

Tranche Status Table

Arghakhachi	Tranche
Total HHs surveyed	1648
Total HHs Eligible	1038
Total HHs Enrolled	949
First Tranche	949
Second Tranche	416
Third Tranche	295
Retrofit beneficiaries	2345

Graph of Tranche Status

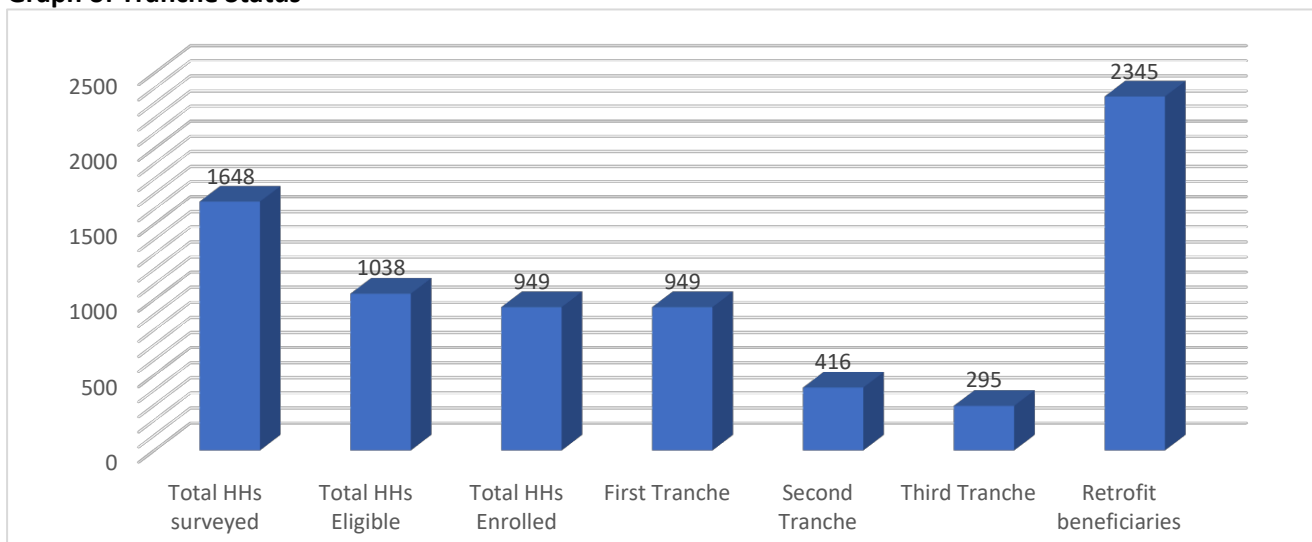

Field Visit Reports (Dhading)

Visit 1

Date		Location	Participants		
28 – 31 May 2019		Ward 2, Tripurasundari Rural Municipality, Dhading	• Sachin Sapkota (HRRP-DTC) • Khagendra Awasti (CLPIU/building-M&E) • Ananda Raj Pandey (GMAI) • Rajesh K. Shrestha (NRA-DSE) - Naresh Chandra Bhatta (DLPIU-Building, Focal Person)		
Objective(s)		✓ Discussion on status of reconstruction. ✓ Identification of fake beneficiaries. ✓ Re-survey, Re verification status ✓ Palika Level Meeting			
Why was the visit carried out in this location?					
✓ To identify the real scenario on finding the fake beneficiaries, who already received tranche without fulfilling the required compliant standards of CLPIU-Building. ✓ Receive Tranche without construction ✓ Receive Tranche by repairing old House or Receive tranche by showing noncompliance house or cattle pen. ✓ Double benefited beneficiary					
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'					
There was no previous visit in the sites.					
Summary					
Field Visit: • No. of HHs visited: total 39 HHs had been visited and observed by the joint monitoring team • A team of joint monitoring consisting of HRRP, DLPIU-DSE, M&E consultant, GMAI Financial Management Specialist visited to Salyantar of Tripurasundari Rural Municipality of Dhading. The joint monitoring team visited a total 39 HHs. • The team observed the housing reconstruction reportedly received the grants without fulfilling the compliant standards of technical guidelines • The Joint monitoring team also prepared some case studies and presented in GMAI and respective government line agencies for the correction and recommendation					
Challenges / Issues Identified		Solutions Provided	Decision Taken	Responsible	Timeframe
39 HHs have received the tranche by showing their old houses		Either those HHs should return the tranche or build new houses	Case studies prepared and submitted for the decision	Rural Municipality, GMAI and respective GoN line agencies	As soon as possible
Re-survey and reverification issues		All grievant information has been collecting and will be forwarded for the final decision	N/A	NRA	Within July 2019
Remove names of beneficiaries not		Need to collect the names of those beneficiaries who are	N/A	As soon as possible	Ward offices, municipalities and GMAI

willing to reconstruct their homes from reconstruction list	not willing to reconstruct their home due to various reasons and forward it to GMALI with all the relevant documents for name removal			
---	---	--	--	--

Photos



Joint Monitoring team observing the houses



Joint Monitoring team observing the houses

Housing Typology Report



Name: -Kul Devi Upadhy
Place: Salyantar, Tripurasundari Rural Municipality



Name: -Maika Kumal
Place: Salyantar, Tripurasundari Rural Municipality



Name: -Padam Bahadur Thapaliya
Place: Salyantar, Tripurasundar Rura Municipality



Name: Dil Bahdur Kumal
Place: Salyantar, Tripurasundari Rural Municipality

Questions Collected		
Question	Who Asked the Question?	Response Provided (By Whom)
Technical support to beneficiaries regarding retrofitting is required for beneficiaries to carry out retrofitting in their house. How can we give technical support to beneficiaries?	Beneficiaries	DLPIU engineers based in ward offices of urban/rural municipalities have received training on seismic retrofitting. So, beneficiaries can contact them, and they will provide technical support to beneficiaries regarding retrofitting. (DLPIU Building)
Where can beneficiaries get the information regarding returning the first tranche money?	Beneficiaries	Beneficiaries can get the information from the GMALI office in the district or contact the NRA hotline number for the information regarding how to return the tranche money. (GMALI)

Challenges and Way Forward	
Challenge	Way Forward
Distribution of second tranche to retrofitting beneficiaries	The beneficiaries can consult with the engineer's based in the field for retrofitting measures to be implemented. Then after completion of measures recommended by engineer, the technical team will inspect the house and recommend for tranche payment.
Distribution of construction completion certificate	Final inspection to be carried out by DLPIU engineers and issuing construction completion certificate to beneficiary through ward offices

Case Stories

A Case study of Til Bahadur Thapa Magar

Til Bahadur Thapa Magar, 72 old man who belongs from the ethnic community is living with his wife of sixty-seven years old at Gandaki rural municipality ward -6 Debisthan in a poor economic condition. Beside his poor financial condition, he is very weak and also struggling with his physical disability, but his name is not in the list of vulnerable beneficiaries. His house was completely collapsed in Gorkha earthquake 2015 so he was obligated to shift into tent with his family in his old age.

Life was not easy for Til Bahadur inside the tent in the freezing winter and thundering summer. So, he decided to construct the house from the grant provided by government as he had received the first tranche of 50000. He constructed his house up to DPC level and proceed for the 2nd tranche process. As per the rule of NRA, He contacted the engineer from ward palika and finalized the document for the second tranche.



While Til Bahadur started dreaming of staying his remaining life in an earthquake resilient house by receiving the 2nd tranche for the remaining construction work. His dream not reached so long far because he compelled to hear the message that his son had been missing with the amount of second tranche.



An old, disable and poor Til bahadur have not alternative solution to continue his construction so he was waiting for the arrival of his missing son. He used to come with his situation and dream with an insipid face in every toll level meeting but Without the require money, nobody was ready to support him.

Finally, Nepal Housing Reconstruction Project (NHRP) Gandaki cluster took responsibility to shift the Til bahadur into the new earthquake resilience house. For this, with the collaboration of cluster level and district level team, required documents such as supporting documents, design, estimation and drawing etc. had been prepared. As per the suggestion of ward and district level, decision to construct the CR technology house for Mr. Magar. Was made.

Decision had been made but implementation part of the construction was not easy. Because almost two lakh amounts had already finished but house was in only DPC level. We made proper plan specially for this house and mobilized the cluster level team to execute the construction work. Two number of ANS are deputed to raise the work. Except this, some number

of training have been conducting for progress of work. Beside this, frequent supervision and monitoring work have been going on from the cluster level staff such as TC, Engineer, Sub engineer and CF.

With this, and addition support of non-local materials equal to amount of Nrs. 50000 (Fifty Thousand) by project as a support for the vulnerable HHs, the house construction work has reached to roof level. With the progress of construction and support of NHRP Gandaki, Mr. Magar is very happy.

“I am confident that I am going to get a new and model house with the support from the team of NHRP and Government of India. I am happy and many of the people nearby come to see this house. I am happy to get such a resilient house and frequent support from the technical person. All the thanks to the team.” Say Til Bahadur.



Story courtesy: Government of India supported Nepal Housing Reconstruction Project – NHRP, Gorkha
