

Monthly District Report

Dolakha, Ramechhap, Sindhuli

14 June – 14 July 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Dolakha	District Facilitation and Coordination meeting.	20-June-2019	DCC office, Charikot, Dolakha	prabin.gautam@hrrpnepal.org	Meeting minute available Here
	District POs (UNOPS, USAID and Build Change) meeting with GMaLI & HRRP	21-June-2019	GMaLI office, Dolakha.	prabin.gautam@hrrpnepal.org	Meeting minute available Here
	Municipality Annual Assembly Meeting on Annual budget, Policy and programs of Bhimeshwor Municipality.	25-June-2019	Bhimeshwor Municipality	prabin.gautam@hrrpnepal.org	Refer to News & Update section
	Ward level coordination meeting on reconstruction.	26-June-2019	Melung Gaupalika ward no.: 5 & 6, Dolakha.	prabin.gautam@hrrpnepal.org	Refer to Field visit section1 and Minute
	Ward level coordination meeting on reconstruction.	28-June-2019	Bhimeshwor Municipality, ward no.: 9	prabin.gautam@hrrpnepal.org	Meeting minute available Here
	GMaLI/HRRP coordination meeting with district facilitation and coordination committee members and POs.	4-July-2019	DCC office, Charikot, Dolakha	prabin.gautam@hrrpnepal.org	Meeting minute available Here
	DLPIU/Building organized government building handover program chaired by CLPIU/Building Chief Mr. Nawaraj Pyakurel with NRA CEO Susil Gyawali.	5-July-2019	DFO office Building, Charikot, Dolakha.	prabin.gautam@hrrpnepal.org	Refer to News & Update section
Ramechhap	District Facilitation Committee Meeting	25 th June 2019	Ramechhap, Manthali	Pranjal Bhandari	Meeting Minutes
	Conflict-Mitigation Coordination Meeting.	26 th June 2019	Ramechhap, Manthali	Pranjal Bhandari	Meeting Minutes

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Review coordination meeting on reconstruction	18 th July 2019 at GMaLI, Charikot, Dolakha.	NSET-Dolakha	pranavdahal@nset.org.np
Joint monitoring field visit with GMaLI, DLPIU/Building and CLPIU-M&E.	15 - 19 July 2019 at Tamakoshi RM, Baiteshwor RM and Jiri Municipality.	HRRP-Dolakha	prabin.gautam@hrrpnepal.org
Field Visit to Ramechhap Municipality	17-19 July, Ramechhap, Ramechhap Municipality	HRRP	Pranjal Bhandari

News & Updates

Bhimeswor municipality organized annual coordination meeting along with each ward chiefs and ward members, GMAI Chief, representatives from DLPIU-education, DLPIU-building, district forest office, journalist, representatives of I/NGOs and HRRP on 25 June 2019, Dolakha.



Photo: Bhimeswor Municipality Annual Assembly Meeting on annual budget, Policy and programs, Dolakha.

The meeting was mainly focused on

1. Forecasting budget for fiscal year 2067/2077 B.S. ([Link](#) to budget file)
2. Prioritize activities on education, livelihood, agriculture, public buildings, DRR, protection of cultural heritages, industrial development, drinking water supply per household, maintain rule of law with good governance, implementation of GESI, protection/support to elders.
3. Development of tourism, stop youths for foreign employment encouraging to work at locality through establishment of local industries.
4. Development of well-planned urban areas within municipality with adequate urban facilities in lined with current reconstruction activities.

DLPIU/Building organized government building handover program chaired by CLPIU/Building Chief Mr. Nawaraj Pyakurel with NRA CEO Susil Gyawali on 5 July 2019, DFO Dolakha.



Photo: NRA CEO Sushil Gyawali as chief guest at building handover program, DFO office, Dolakha .

Here all relevant district government office authorities along with journalist and POs are attending this event.

Ramechhap, DLPIU-Building organized a meeting to orient the DLPIU field engineers on the resurvey and reverification. This was done as some of the engineers who had received the orientation and were involved in the resurvey and reverification had left the job. A need was realized to orient all the field engineers such that they could be mobilized as per the need.




Tranche Status (Dolakha)


Graph of Tranche Status:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Baiteshwor Gaunpalika	6392	8359	8204	7754	7230	6754	342	15	15	0
Bhimeshwor Nagarpalika	10796	12515	11524	11180	8838	7404	353	113	113	0
Bigu Gaunpalika	5758	6733	6356	6276	5698	5285	35	6	6	0
Gaurishankar Gaunpalika	5405	6876	6674	6554	5716	5445	134	41	41	0
Jiri Nagarpalika	4764	5850	5665	5086	4265	3557	171	43	43	0
Kalinchok Gaunpalika	7527	8916	8514	8486	7979	7638	32	21	21	0
Melung Gaunpalika	7006	7685	7179	6825	6077	5520	476	102	102	0
Sailung Gaunpalika	6800	8424	7133	7059	6079	5017	918	60	60	0
Tamakoshi Gaunpalika	6191	7461	6897	6886	6441	5879	115	9	9	0

Graph of Tranche Status:

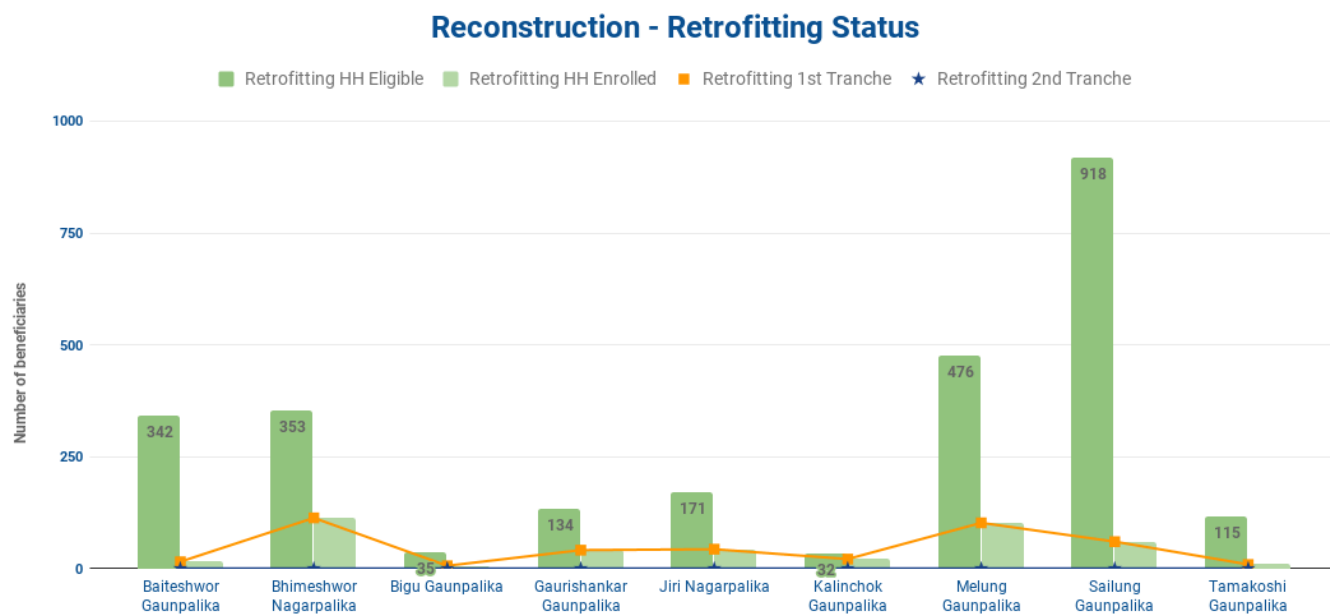

Graph for Retrofitting Status:

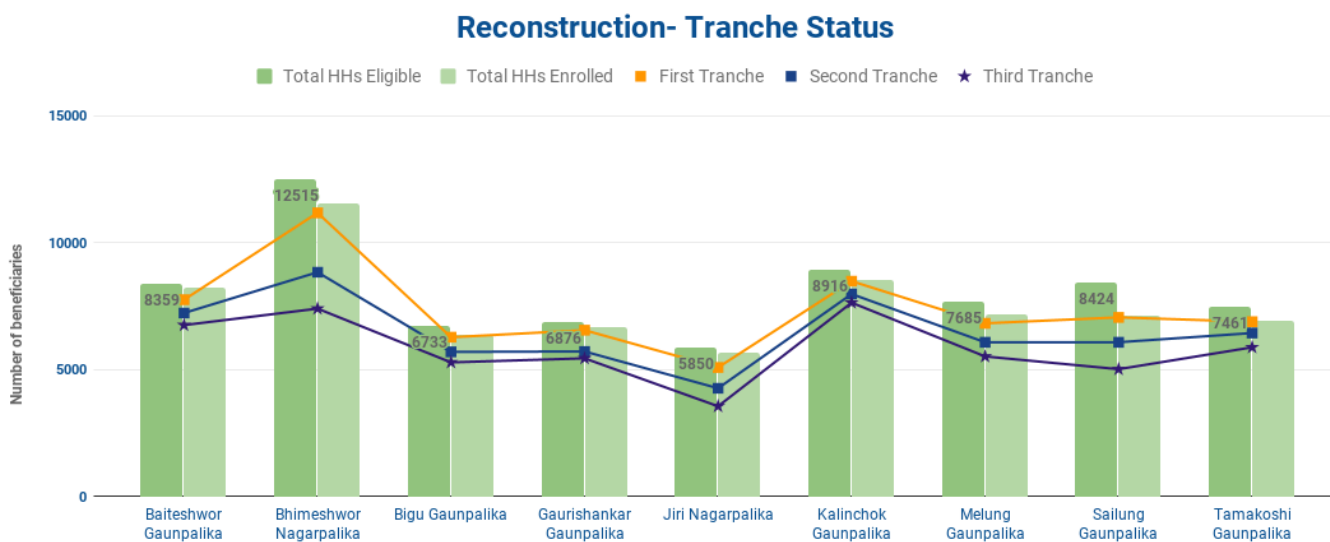


Tranche Status (Sindhuli)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Dudhouli Nagarpalika	15002	5179	4692	4692	2275	842	3531		804	0
Ghanglekh Gaunpalika	3032	2244	2139	2139	1662	1148	530		118	0
Golanjor Gaunpalika	4835	3231	2992	2992	2372	1774	667		97	0
Hariharpurgadhi Gaunpalika	5176	2601	2296	2296	1746	326	1538		0	0
Kamalamai Nagarpalika	15659	8537	7799	7799	4528	2610	1788		376	0
Marin Gaunpalika	5717	3720	3192	3192	2084	830	1266		138	0
Phikkal Gaunpalika	4072	2666	2171	2171	2005	1699	932		8	0
Sunkoshi Gaunpalika	6393	5032	4858	4858	3554	1685	327		0	0
Tinpatan Gaunpalika	8863	4701	4671	4671	3986	3234	2499		543	0

Graph of Tranche Status:

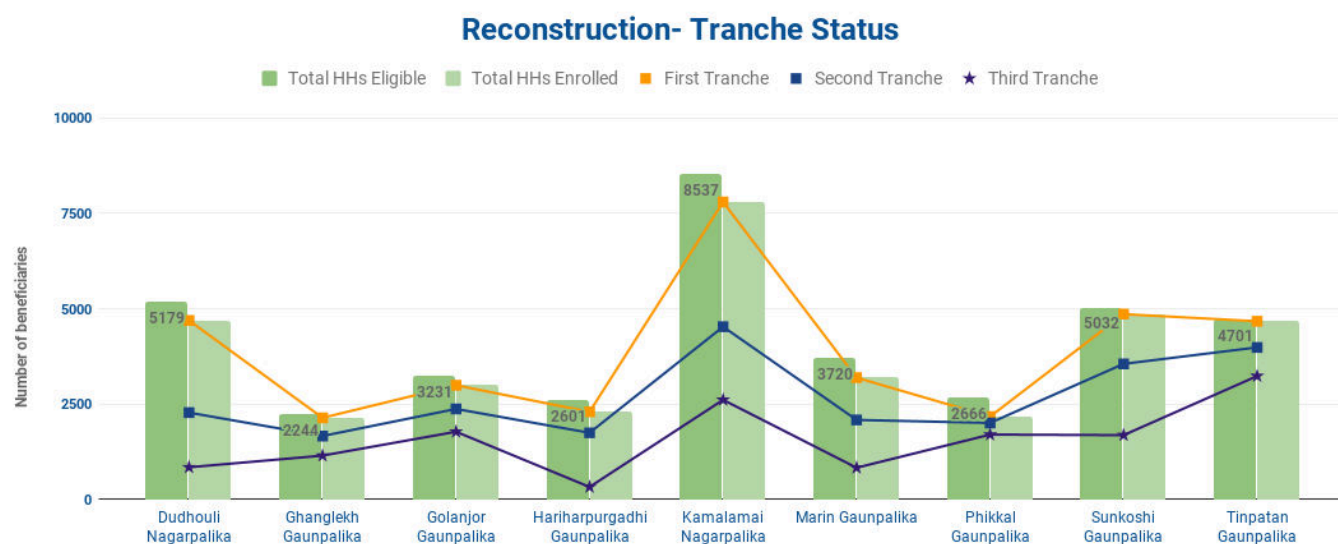

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

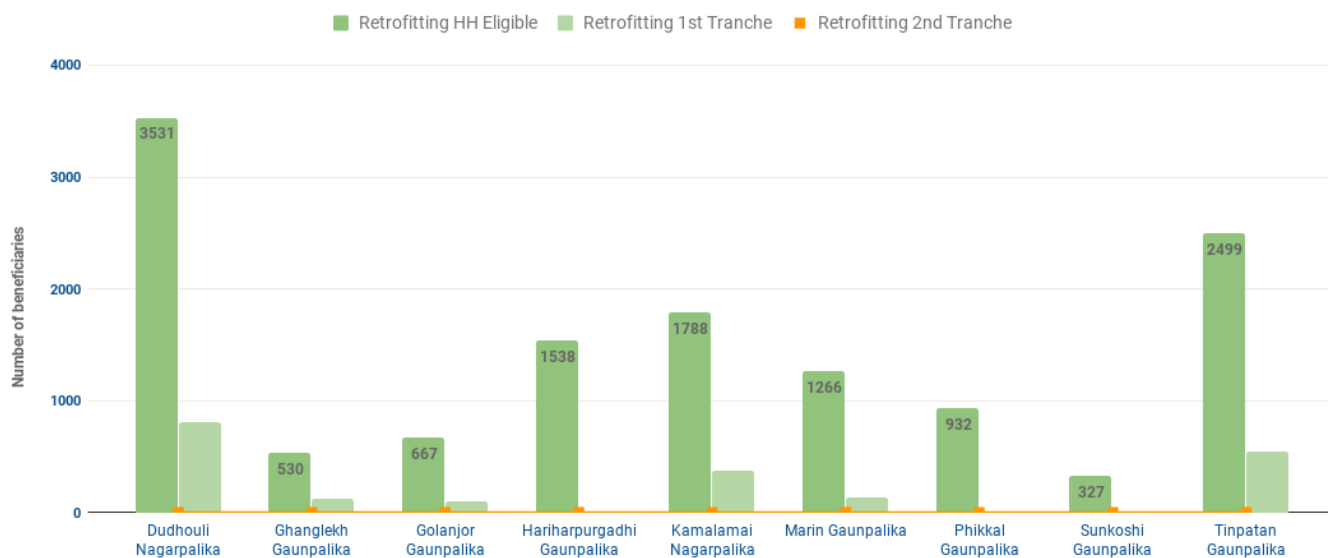


Tranche Status (Ramechhap)


Tranche Status Table:

Palika Name	Eligible HHs	PA Agreement Signed	Tranche I	Tranche II	Tranche III	Eligible HHs RF	PA Agreement RF	Tranche I RF	Tranche II RF
Doramba Gaunpalika	5252	4716	4708	3968	2932	1076	47	47	0
Gokulganga Gaunpalika	6343	6075	6066	5203	4294	347	1	1	0
Khadadevi Gaunpalika	5212	5215	5121	4769	4105	1317	222	222	0
Likhu Gaunpalika	5686	5545	5544	5123	4494	1010	16	16	0
Manthali Nagarpalika	11077	10758	10756	9700	8170	1271	39	39	0
Ramechhap Nagarpalika	6554	6416	6412	5708	5131	960	6	6	0
Sunapati Gaunpalika	3671	3555	3550	3148	2240	821	20	20	0
Umakunda Gaunpalika	4984	4566	4566	4087	2858	343	5	5	0

Graph of Tranche Status:

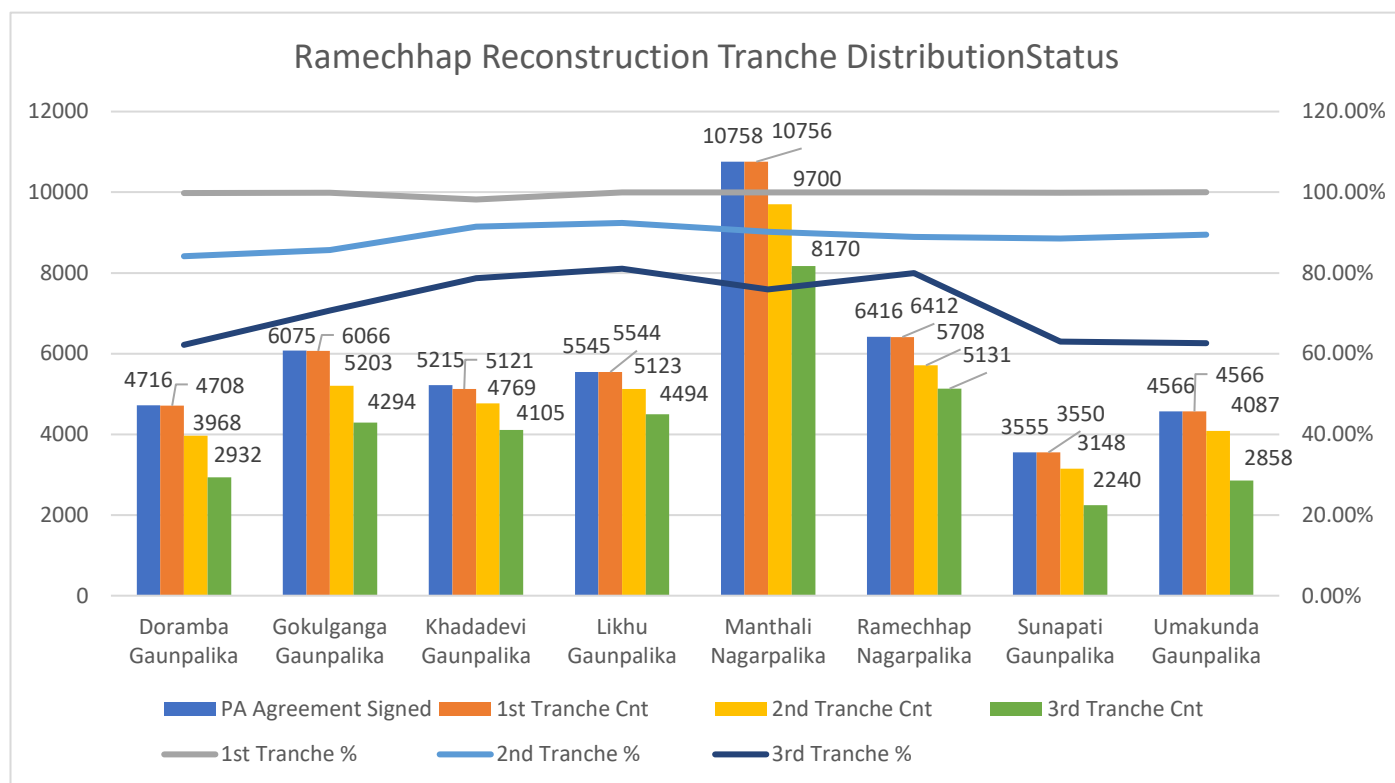

Graph for Retrofitting Status:

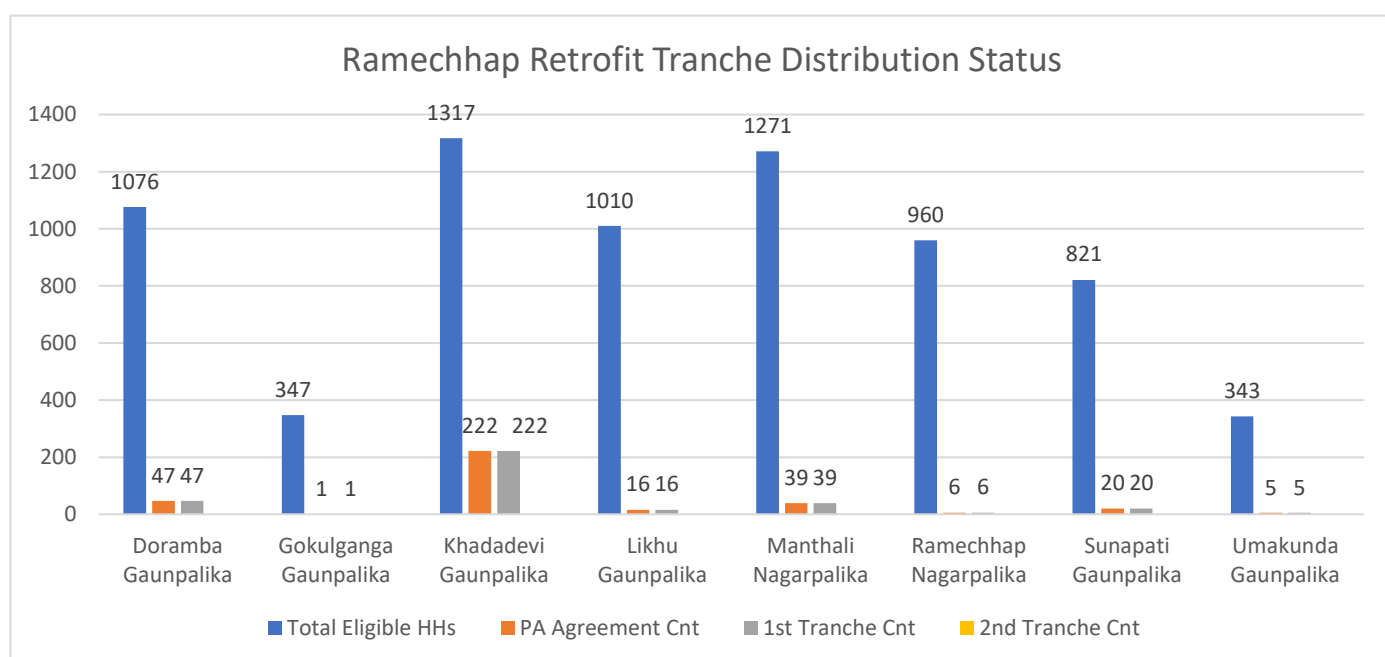

Field Visit Reports (Dolakha)

Visit 1

Date	Location	Participants
(25 – 28) June 2019	Melung RM, ward no.: 5 & 6 and Bhimeshwor municipality ward no.: 9.	- Bhogendra Sha (DLPIU/building-Focal person) - Tika Joshi (GMaLI) - Prabin Gautam (Cluster-10, DC)
Objective(s)	- Palika level coordination meetings - Ward level reconstruction coordination meetings. - Housing Typology HRRP Survey collection - Ward level coordination meeting	

Why was the visit carried out in this location?

The field visit was conducted to find out the current situation of reconstruction at palika level.
To support DLPIU/building engineers for completion of resurvey and reverification task with final inspection process.
Monitoring POs activities on reconstruction at Palika.
Collect list of vulnerable beneficiaries from palika in coordination with wards.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

- All together 7 Households were visited at Melung RM ward no.: 5 & 6 and Bhimeshwor municipality, ward no.: 9.
- Ward level meetings were conducted at ward offices of Melung RM and Bhimeshwor municipality where one engineers and focal person attended it.

A close coordination meeting and discussion was conducted with representatives of ward, technical staffs of DLPIU/building at Melung rural municipalities ward office 5 and 6.

Also, Ward level meeting was conducted at Bhimeshwor municipality, ward no.: 9 on 28 June in presence of ward chief, ward member, DLPIU engineer, district focal person.

The main points of the meeting/discussion were as follows:

- Convey message for Non-beneficiaries that they can file claim against NRA in court if they are not satisfied with the result from NRA. To do so, they were suggested to put file against NRA in court through the help of ward office.
- Discussion to support retrofit beneficiaries for repair and retrofit of houses within deadline.
- Ward members were given step-by-step suggestions on how beneficiaries from RTB who are needed to convert to RCB was provided.
- Beneficiaries from all wards who have received 3rd tranche to be inspected for certificate of completion. A case load is prepared by DLPIU/building-Dolakha and on the basis of it, the last inspection needs to be completed on time.
- During the last inspection, technical support will be provided through DLPIU/building in coordination with ward office in order to conduct last inspection of “non-complicance and incomplete roofings” will not be carried out. If the beneficiary house construction is not completed at all, the PA number with the reason for the incompleteness need to be submitted at DLPIU/building office.
- After the 1st and 2nd inspection digitalization is completed then only 3rd inspection need to be checked and uploaded at EHRP portal.

Meeting: Meeting minute [Here](#) Melung RM, ward no.: 5 & 6.

Meeting: Meeting minute [Here](#) Bhimeshwor Municipality, ward no.: 9

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Palika focused on providing all grant supports to those beneficiaries who have not followed NRA guidelines and built non-compliance houses.	Prolicy level orientation needed for palika officials.	--	NRA engineers and Palika officials	
RM officers have less understandings with NRA engineers and did not respond positively with the team.	Common understanding is required from both sides.	--	NRA engineers and Palika officials	
Beneficiaries claim that they have registered grievance more than two times but, yet no result/solutions have come out.	Reapply on resurvey and reverification process.	--	Beneficiaries, local officials and NRA engineers	
Difficulty of road has raised cost of materials for construction.	Road maintenance shall be carried out by Palika and ward office.	--	Palika and ward office.	

Photos



Photo: Ward level meeting at Melung RM, ward no.: 6



Photo: Ward level meeting at Melung RM, ward no.: 5

Housing Typology Report



Name: - Chandra Bahadur Magar
Location: - Meung rural Municipality, ward no.: 5, Dolakha.
It is double storey built using stone in mud mortar with RCC bands. The cost of construction is 10 Lakhs. The beneficiary has received all tranche of government grants.



Name: - Baal Kumari Shrestha
Location: - Meung rural Municipality, ward no.:6, Dolakha.
The beneficiary is single women and her house is single storey stone in mud mortar with RCC bands. The cost of construction is 2.5 Lakhs. She has received all tranches of government grants.



The house is situated at Gumdel, Umakunda RM-1, Ramechhap.
The owner of the house is Janaki Devi Basnet. The house is a two roomed SMM structure. The owner has received all three tranches from the government. The estimated cost of house is 6 lakhs according to the owner.



The house belongs to Babulal Shrestha and is situated at Umakunda RM-4 Lapchane, Ramechhap.
The house is a SMM structure but three storied. The house is a non-compliant. The owner has received the first and second tranches from the government. the estimated cost of the house is 19 lakhs according to the owner
