

Monthly District Report

Dolakha, Sindhuli

23 August - 27 September 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Dolakha	Palika Level Coordination Meeting on Reconstruction	23-Aug-2019	Tamakoshi RM	prabin.gautam@hrrpnepal.org	GD link
	Palika profile link upload at Palika website	till 26-Aug-2019	District-palikas	prabin.gautam@hrrpnepal.org	8 out of 9 completed. Link
	Updated palika profile.	26 Aug & 25 Sept, 2019	-	prabin.gautam@hrrpnepal.org	GD link
	Updated RTB to RCB conversion data and vice-versa, DLPIU staff detail with caseload.	9-13 Sept. 2019	-	prabin.gautam@hrrpnepal.org	
	Completion certificate distribution, ward meeting and field visit.	16 – 18 Sept. 2019	Bhimeshwar Mun & Bigu RM.	prabin.gautam@hrrpnepal.org	Refer to field visit section - 1
	Support GMAI for compilation of INGOs tranche released detail	24 Sept. 2019	-	prabin.gautam@hrrpnepal.org	
	Field visit, cross-verification of tranche received from POs/GoN with any duplication.	25 – 27 Sept. 2019	Bhimeshwar Mun, Baiteshwar RM.	prabin.gautam@hrrpnepal.org	Refer to field visit section - 2
Sindhuli	Joint Monitoring field visit to Dudhauli Municipality	11 th Sept 2019	Dudhauli Municipality	Tulasi Ram Lamichhane; tulasi.lamichhane@hrrpnepal.org	Click Here for Minutes
	Coordination Meeting in Kamalamai Municipality	19 th Sept 2019	Kamalamai Municipality	Tulasi Ram Lamichhane; tulasi.lamichhane@hrrpnepal.org	Click Here for Minutes
	Support GMAI and DLPIU Building in preparation of action plan in the event organized by CLPIU	15 th Sept 2019	Sindhuli	Tulasi Ram Lamichhane; tulasi.lamichhane@hrrpnepal.org	Click Here
	Palika Profile upload in palika website		Sindhuli	Tulasi Ram Lamichhane; tulasi.lamichhane@hrrpnepal.org	Click Here

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Joint monitoring field visit plan	22 – 25 October 2019, Dolakha.	HRRP	prabin.gautam@hrrpnepal.org

News & Updates

Dolakha:

- A program was organized by PIN at Dolakha on 12 Sept. 2019 regarding “Use of Map for identification of Landslide area” of each palika. PIN is working at Dolakha to support vulnerable(displaced) households for distribution of land and housing grant from the government.



Photo: Participants observing Map of Landslide at each Palika of Dolakha.

- NRA/GMaI organized a program “Judicial Interaction” with all palika representatives by Punarabedan Committee, NRA on 14 Sept. 2019 at DCC hall, Charikot, Dolakha.



Photo: Participants at Judicial Interaction program organized by NRA.


Sindhuli:

- CLPIU-GMALI organized a full day workshop on preparation of action plan to complete the reconstruction in allocated time in Sindhuli on 15th September 2019. The program was chaired by DCC Chairperson Shankar Raj Burma Tiwari. Member of province parliament Pradip Katuwal was the chief guest of the program. The guests were CDO of Sindhuli Mr. Janardan Gautam, DCO of Sindhuli Mr. Dik Bahadur Karki. The mayor, executive officer and focal person from each palika were available in the program. The program started with the interaction with the people's representatives from each palika. The program proceeded with the preparation of the action plan to speed up the reconstruction in the allocated timeframe of NRA.
- HRRP Sindhuli have supported to finalise the list of beneficiares who have received the tranche. It was done by reviewing the files at DTCO office.


Tranche Status (Dolakha)

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Baiteshwor Gaunpalika	6392	8359	8204	7826	7333	6995	342	54	54	0
Bhimeshwor Nagarpalika	10796	12515	11617	11371	9121	8074	353	179	179	0
Bigu Gaunpalika	5758	6733	6358	6303	5862	5585	35	8	8	0
Gaurishankar Gaunpalika	5405	6876	6697	6604	5866	5691	134	51	51	0
Jiri Nagarpalika	4764	5850	5665	5177	4368	3805	171	77	77	0
Kalinchok Gaunpalika	7527	8916	8534	8513	8085	7803	32	21	21	0
Melung Gaunpalika	7006	7685	7207	6922	6170	5800	476	262	262	0
Sailung Gaunpalika	6800	8424	7308	7293	6297	5611	918	213	213	0
Tamakoshi Gaunpalika	6191	7461	6979	6981	6525	6130	115	41	41	0

Reconstruction- Tranche Status

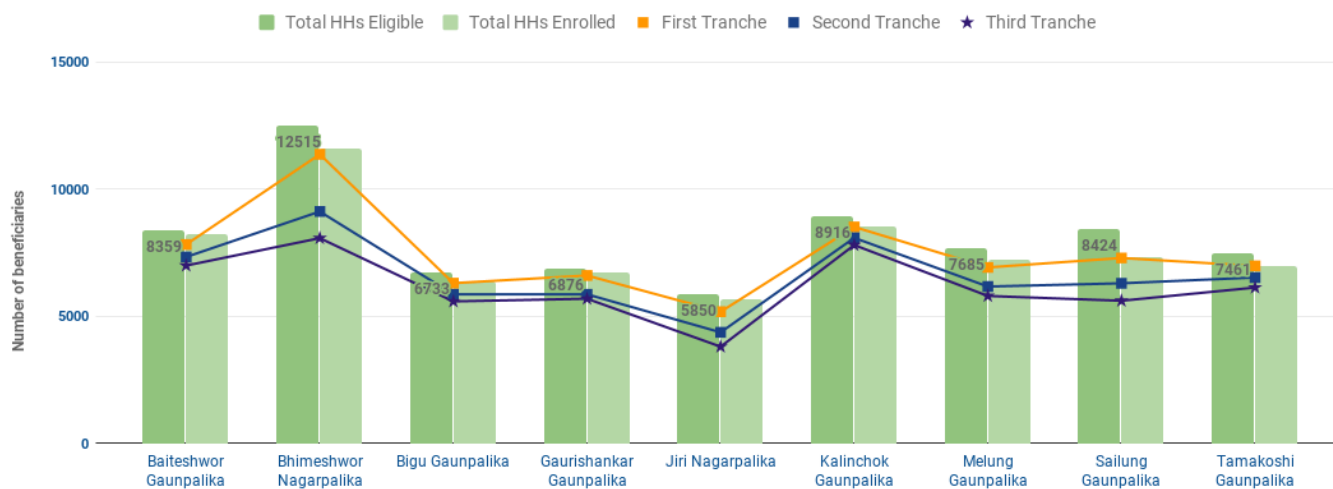

Reconstruction - Retrofitting Status

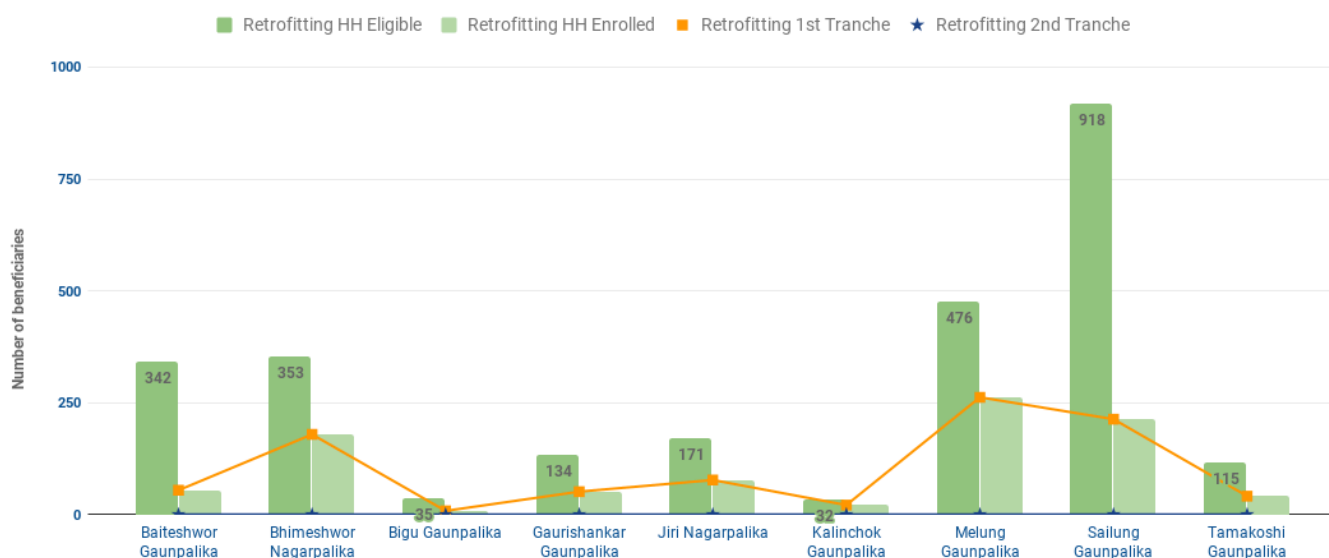


Tranche Status (Sindhuli)

Tranche update:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Dudhouli Nagarpalika	15002	5203	5203	4494	2698	1213	3910		2480	0
Ghanglekh Gaunpalika	3032	2247	2247	2135	1879	1500	533		406	0
Golanjor Gaunpalika	4835	3235	3235	3116	2818	2481	683		234	0
Hariharpurgadhi Gaunpalika	5176	2632	2632	2511	1991	629	1786		1104	0
Kamalamai Nagarpalika	15659	8578	8578	8043	5465	3748	2042		1331	0
Marin Gaunpalika	5717	3773	3773	3450	2446	1282	1371		972	0
Phikkal Gaunpalika	4072	2669	2669	2571	2230	1984	928		161	0
Sunkoshi Gaunpalika	6393	5058	5058	4821	4420	3656	343		35	0
Tinpatan Gaunpalika	8863	4719	4719	4606	4142	2778	2513		2132	0

Graph of Tranche Status:

Reconstruction - Retrofitting Status

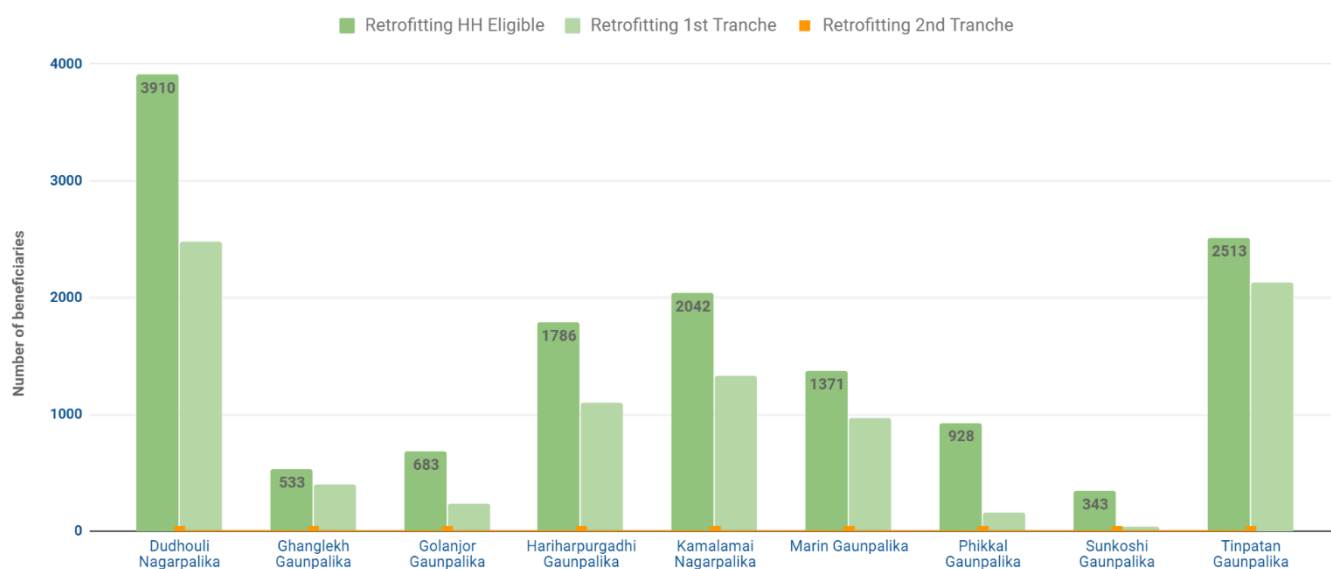

Graph for Retrofitting Status:

Reconstruction- Tranche Status



Field Visit Reports (Dolakha)

Visit 1

Visit 1		
Date	Location	Participants
(16 – 18) September 2019	• Bigu RM and Bhimeshwar Municipality.	• Ganesh Aryal (GMAI-Chief) • Prabin Gautam (HRRP) • Ashok Kafle (GMAI) • Lalbabu Ray (GMAI)
Objective(s)	• Distribution of completion certificate to mentioned wards beneficiaries. • Ward level coordination meeting and completion certificate distribution program. • Conduct palika capacity assessment survey. • Housing Typology Survey collection.	
Why was the visit carried out in this location?		
The house completion certificate distribution program is scheduled at Smriti Bhavan, Bigu RM – 6 (Aalampu) and Bhimeshwar municipality, ward no.: 1.		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		

Summary		
Field Visit:		
• No. of HHs visited:3 • No. of meetings with engineers: 1 • No. of meetings with local officials: 1		
During the field visit of Bhimeshwar municipality, ward no.: 1 and Bigu rural municipality, ward no.: 6, a program was organized to certify the households/beneficiaries who have completed the construction of house as per the norms of NRA. 335 households of Bigu RM received the completion certificate from NRA/GMAI, Dolakha. It has encouraged other beneficiaries to complete construction of house and receive the certificate as soon as possible. Moving gradually from ward no.: 6 of Bigu RM, the similar program is being planned by other wards of Bigu RM.		
Similarly, completion certificate distribution program was organized at Bhimeshwar municipality, ward no.: 1 where 20 households/beneficiaries received the certificate from NRA/GMAI, Dolakha.		

In both of the visits, a major concern was raised on retrofit beneficiaries that with a limited support of government grant it is unaffordable to carry out the retrofit of traditional houses at village. Due to deadline on tranche, some of the beneficiaries who could not process to receive first tranche of government grant are left behind and thus, they were curious on how, when and what should be done to proceed forward?

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
What will happen after receiving house completion certificate?	.		Beneficiary, NRA, Plaika/Ward and NRA/GMaLI	
When will the resurvey and reverification task result be publish from NRA?		Orientation on retrofit technique should be provided.	NRA/GMaLI and DLPIU/Building	
How will be retrofit beneficiary be supported technically from NRA?	RTB beneficiary can be converted to RCB only through recommendation of NRA field engineers and palika/ward officials to central NRA.			

Photos



Photo: Dolakha-Gmali chief distributing completion certificate at Bigu RM.



Photo: Vice-chief of Bigu rural municipality Mr.Sanjiv Oli at meeting with certificate distribution program.

Field Visit Reports (Dolakha)

Visit 2

Date	Location	Participants
(25 – 27) September 2019	Bhimeshwor Municipality and Baiteshwor rural municipality.	- Prabin Gautam (HRRP) - Tika Shrestha (GMAI) - Minmar Lama (DLPIU/building)
Objective(s)	- Cross verification of tranche distributed from POs at Dolakha. - Ward level coordination meetings on duplication of tranche. - Conduct palika capacity assessment survey, if any. - Housing Typology Survey collection - Reimbursement of duplication of tranche if found any.	

Why was the visit carried out in this location?

The field visit was focused on reimbursement of any duplication of tranche either from POs or GoN.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

- No. of HHs visited:4
- No. of meetings with engineers: 1
- No. of meetings with local officials: 2

During the field visit of Bhimeshwor municipality, ward no.: 9 which was carried out on 25 Sept 2019; following points were some of the main discussion points:

- Beneficiaries who are supported by SOS will not receive any further tranches of government grant. Furthermore, it may require returning of the first tranche received by those HHs.
- SOS supported HHs have not received completion certificate due to technical errors on building of beneficiaries.
- As per ward member, some beneficiaries (14 to 16) who have PA cards but could not receive 1st tranche due to unavailability at ward or some other reasons. Thus, they were curious on how, when and what should be done to process forward?

On 26 Sept 2019, field visit was carried out at Baiteshwor rural municipality, ward no.: 3, Yarsa village. Following were some of the main discussion points:

- Out of 110 beneficiaries identified as HHs supported by YLF, some of the beneficiaries have received dual support from both sides; PO and GoN.
- HHs were oriented about how the completion certificate is received and its benefits for them. Ward secretary Mr. Amrit Tamang had supported on the process.
- Field visit helped GMAI to compile a complete list of YLF supported HHs of Yarsa village.

Following are the minutes of the program:

- [Bhimeshwor Municipality-9, ward level meeting and completion certification distribution 190925](#)
- [Baiteshwor Rural Municipality-3, ward level meeting and completion certification distribution 190926](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
What will happen after receiving house completion certificate?	.		Beneficiary, NRA, Plaika/Ward and POs	
When will the resurvey and reverification task result be publish from NRA?		Orientation on retrofit technique should be provided.	NRA and POs	
How will be retrofit beneficiary be supported technically from NRA?	RTB beneficiary can be converted to RCB only through recommendation of NRA field			

	engineers and palika/ward officials to central NRA.			
Photos				
				
Photo: FGD with YLF supported households/beneficiaries of Yarsa village, Baiteshwor RM – 3, Dolakha.		Photo: Meeting with ward member of Bhimeshwor municipality, ward no.: 9, Dandapakhar village.		

Field Visit Reports (Sindhuli)

Visit 1

Visit 1		
Date	Location	Participants
11 th Sept 2019	Dudhauri Municipality Health Post Hall	• Surya Bista, Act. Chief GMALI • Pramod Kr. Sah, Focal Person DLPIU Building • Dinesh Sanjel,DSE • Kiran Kr. Mahat, M&E Consultant • Hem Karki, CO GMALI • Tulasi Ram Lamichhane, DTC HRRP
Objective(s)	• Status of Reconstruction in Palika. • Challenges the Rural Municipality is facing in reconstruction. • Updating of the Palika Profile links to the Palika Websites. • Information regarding Retrofitting	
Why was the visit carried out in this location?		
•		
'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'		
N/A		
Summary		

Field Visit:

- No. of HHs visited: 4
- No. of meetings with engineers: 1
- No. of meetings with local officials: 1

The program was chaired by the mayor of Dudhauri Municipality Ghanshyam Raut. Ex member of parliament, GMALI Chief, Under secretary from NRA, DSE, DLPIU Focal Person were the guests in the program. The program was facilitated by Hem Karki, computer operator of GMALI.

- GMALI Chief updated the reconstruction status of ward level of Dudhauri Municipality.

वडा नं.	पुनर्निर्माण तर्फ				प्रबलीकरण तर्फ		जम्मा लाभग्राही
	लाभग्राही संख्या	पहिलो किस्ता लिने	दोस्रो किस्ता लिने	तेस्रो किस्ता लिने	लाभग्राही संख्या	पहिलो किस्ता लिने	
१	६४५	५१९	३२३	११४	१००	७५	७४५
२	३०२	२३३	१८२	८५	३९१	३१३	६९३
३	२९८	२७६	८	३	३५२	२५७	६५०
४	३२८	२५६	१५८	९६	४९७	३४३	८४५
५	३५७	३०७	२१३	१०९	३२८	२५१	६८५
६	१३०	८२	३१	१६	४४८	२८१	५७८
७	६४७	१६२	४४	२४	२८२	१४४	९२९
८	४२२	७७१	३०९	१२८	२२४	१६०	६४६
९	८१	६४	११	३	२५७	२३९	३३८
१०	२०८	७६	५३	३२	२६	२५	२३४
११	४२८	४८३	२२८	१२१	२३६	१८०	६६४
१२	२५९	२२७	२१०	१७३	३५३	२८५	६१२
१३	७२९	७१५	६३३	२२७	३९८	२८७	११२७
१४	३६९	३२३	२९५	८२	१८	०	३८७
जम्मा	5203	4494	2698	1213	3910	2840	9113

- He also stated that the several reasons delay in reconstruction in the district. He stated that the number of retrofitting beneficiaries in the district is about 22% of the total retrofitting beneficiaries of the earthquake affected districts and the guidelines and training programs have been just introduced. So, the retrofitting status has not been started in the district. Also, he stated the problem of people residing in the *ailani* land has been solved in large number in the district and they have just started reconstructing the house has also slowed the reconstruction. Also, the availability of the guidelines regarding timber structures have also slowed the reconstruction in the district. He also stated that about 816 beneficiaries who lived in the *ailani* land have been permitted to reconstruct the house in the existing land.
- Focal person of DLPIU Building stated that a task force for retrofitting has been formed in the palika and district level whose responsibility is to boost the retrofitting in the district. The coordinator of the task force

is DSE in the district and focal person of the palika in palika level. He also requested the ward chairperson to motivate the beneficiaries for retrofitting.

- GMALI chief also requested the ward chairperson for the PA book collection for digitization. He also requested the ward chairperson to support the PA collectors for collecting the PA Books. The collected books will be digitized in the district.

S.No.	No.	Remaining PA book to collect
1	1	72
2	2	64
3	3	13
4	4	120
5	5	61
6	6	48
7	7	567
8	8	284
9	9	22
10	10	180
11	11	210
12	12	38
13	13	51
14	14	93

- District Technical Coordinator of HRRP distributed the info packs of HRRP. He also stated that the palika profile is the document showing the status of reconstruction of the palika. He requested the mayor of the palika for stepping the necessary process for the upload in the palika profile. He stated the palika profile is being generated in monthly basis.
- Chairperson of ward no 2 requested GMALI to organize the mobile team to make necessary amendment on the issues in the ward level. He also requested to make the regular communication between ward engineer and DLPIU in order to update the ward engineers with the latest updates. He also mentioned that the banks are not releasing the fund after the cash transaction approved from GMALI. They are releasing the cash after few days.
- Mayor of Dudhauri Municipality gave the closing remarks. He committed all the support from the palika to complete the reconstruction in time.

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
The bank has not giving the cash in the day when the transaction has been made from district level	An interaction with banks will be made in district level in chairmanship of CDO	GMALI Chief	GMALI and district stakeholders	ASAP
The timber houses constructed are not complying with the building code	Some corrections should be provided as suggested by DSE	DSE	DLPIU Building and house owner	ASAP
There are people residing in <i>ailani</i> land and have <i>numberi</i> land nearby the river which is vulnerable to construct house.	First the list of such beneficiaries should be provided for geological study. If the land is	GMALI	GMALI, NRA, Cabinet	ASAP

	considered as vulnerable, then the house owner can leave the current land and get 2 lakhs to reside in new land. If the owner is willing to reside in the current land a decision from cabinet must be made			

Photos



Act. Chief of GMALI Surya Prakash Bista updating the status of reconstruction of Dudhauli Muicpality



Focal Person of DLPIU Building Pramod Kr. Sah giving information regading reconstruction and retrofitting

Housing Typology Report



Write caption here:

The house of Shyam Prasad Ghimire, resident of Dudhauli Municipality ward no. 7 have constructed the house. He has received all three tranche of reconstruction grant. The house is constructed using brick in cement mortar. RC bands have been provided in the house. The house is provided with Rigid roof. The house owner provided with shutter in the house previously which was removed after recommendation from DSE to receive the third tranche.



Write caption here:

The house of Kopila Ghimire, resident of Dudhauli Municipality ward no. 7 have constructed the house. She has received all three tranche of reconstruction grant. The house is constructed using stone in mud mortar. RC bands have been provided in the house. The house is provided with flexible roof.



Name: - Mitthu Bahadur Sapkota(Beneficiary)

Location: - Bhimeshwor Municipality, ward no.: 3, Dolakha.

It is three and a half storey RCC building made using brick in cement mortar with RCC bands. The beneficiary has received all tranche of government grants.

He has 4 members in his family with his wife Mrs. Padam Kumari Khatri and 2 children.



Name: - Gyanendra Bahadur Khadka

Location: - Baiteshwor RM, ward no.: 3, Yarsa village.

The beneficiary has a single storey interlocking brick in cement mortar with RCC bands. The house is constructed by Young Living Foundation (YLF).

The beneficiary has also received 1st tranche of government grant.
