

[FAQs](#) | [Briefing Pack](#) | [Meeting & Events](#) | [5W](#) | [Housing Progress](#) | [Housing Typologies](#)



Left: a hybrid structure with a steel frame and stone masonry infill in Annapurna Rural Municipality-6, Myagdi which was rebuilt four months after the earthquake. Right: a non-compliant house in Bhirkot Municipality-5, Syangja that was built before the inspection engineers were deployed in the field. Both of these houses will fall under the National Reconstruction Authority's new guidelines for disbursement of the second and third tranches of the housing reconstruction grant to households that completed reconstruction before the inspection engineers were deployed. Field engineers across earthquake affected areas will now be responsible for collecting information on all households that rebuilt before technical staff were deployed and the local authority will then make the recommendation for the tranche disbursement.

Transition to HRRP4

HRRP3, which started in March 2017, is finishing at the end of July 2019. The platform will be continuing into a fourth phase (HRRP4) which starts on 1 August 2019 and will run for two years. There will continue to be eleven District Coordination Teams (DCTs) covering clusters of districts and the coordination activities and services provided by HRRP, including this monthly bulletin, will continue into the fourth phase. Funding from DFID and CRS has been confirmed for HRRP4. Further funding is being sought which would enable the platform to scale up geographical coverage of coordination services and to implement additional activities. It is expected that the transition from HRRP3 to HRRP4 will be smooth and there will be no disruption to coordination services. Please feel free to raise any questions or suggestions regarding HRRP4 with Minar Thapa, Deputy National Coordinator (minar@hrrpnepal.org).

Featured Technical Staff Person



Angdawa Sherpa
Assistant Sub Engineer, Bhojpur municipality

This month's featured technical staff person is Angdawa Sherpa. He has been working as an assistant sub-engineer in Bhojpur Municipality for a year and is also from Bhojpur. The experience has been challenging because he did not receive any training or orientation before he was deployed and there are only three technical staff working on reconstruction and this is not sufficient. This has held up the resurvey process as they have only been able to get to 150 out of the 1,400 houses that need to be resurveyed.

Angdawa feels that it has been positive to be working in the place that he is from. He has also learnt a lot from his field experience to date which has helped him to overcome the challenges associated with being deployed without prior training or orientation.

Highlights

- Flooding and heavy rainfall have affected 28 districts, with more than 30,000 people affected. The Disaster Risk Management Executive Committee has activated the 13 clusters at national level to support the immediate response. Contact details for the clusters are available [here](#)
 - The NRA has published new [guidelines on the disbursement of the full housing reconstruction grant to households who rebuilt before technical staff were deployed](#)
 - 322 households, across eight districts, have switched from the retrofitting grant to the reconstruction grant
 - More than 450,000 households, 55% of eligible households, have received the third tranche of the housing reconstruction grant
 - [HRRP Round 5 Partner Satisfaction Survey](#): the HRRP team is pleased to invite all partners to take part in the latest round of the partner satisfaction survey and help to improve the platform's services.
-

Flood Response

Heavy rains since 11 July have caused flooding across 28 districts of Nepal. To date, the flooding has killed 64 people with a further 31 people missing. Thirty-two people were injured, and more than 2,500 people have been rescued. The Ministry of Home Affairs has issued a press statement which states that 33,113 people have been affected by the flooding. The 13 July meeting of the Disaster Risk Reduction and Management Executive Committee, in coordination with the National Emergency Operations Centre (NEOC), decided to activate the thirteen national clusters to support the immediate response required. Contact details for the clusters are available [here](#). Updates and situation reports are available on the [Government of Nepal Disaster Risk Reduction Portal](#).



*A man carries his bicycle along a flooded road following heavy rainfall in Biratnagar, on Monday, 15 July 2019.
Photo credit: Skanda Gautam/The Himalayan Times.*




Nepali army officer carrying a child through a flooded colony in Kathmandu, on Friday, 12 July. Photo credit: Reuters.

National Updates

NRA, CLPIU GMALI and Building, Grant Disbursement Data, as of 15 July:

Reconstruction Grant	13 May	17 June	15 July
Total No. Eligible HHs	825,633	826,333	826,634
HHs Enrolled	763,598	766,316	768,192
HHs Received 1 st Tranche	759,138	761,542	763,470
HHs Applied for 2 nd Tranche	585,529	598,295	607,597
HHs Received 2 nd Tranche	573,974	584,516	590,542
Non-compliant at 2 nd Tranche	4,405	4,287	4277
HHs Applied for 3 rd Tranche	429,951	458,715	479,811
HHs Received 3 rd Tranche	418,417	436,272	453,354
Non-compliant at 3 rd Tranche	2,355	2,222	2005
Houses Completed	386,527	417,395	418,760
HHs with Completion Certificate	9,008	16,027	24,361
Retrofit Grant	13 May	17 June	15 July
Total No. Eligible HHs	65,977	66,664	71,358
HHs Enrolled	20,291	21,587	21,984
HHs Received 1 st Tranche	19,528	20,877	21,583
HHs Received 2 nd Tranche	41	41	45

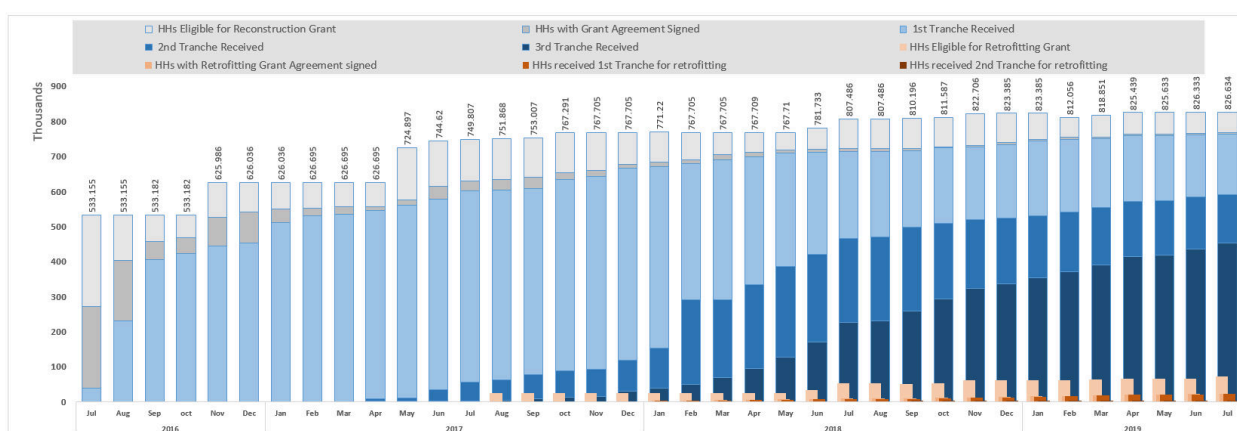

Progress with the disbursement of the GoN housing reconstruction and retrofit grants based on NRA, GMALI CLPIU, and Building CLPIU data from July 2016 to 15 July 2019.

NRA Executive Committee Meeting, 25 June: the main outcome of the meeting was the approval of [guidelines for the disbursement of the housing reconstruction grant to households who rebuilt their houses before the Government of Nepal technical staff were deployed in the field](#). Building and GMALI CLPIUs have been notified and will begin implementation of the guideline after collecting information on these households, as per Annex 1 of the guidelines. The inspection engineers are the focal persons for the collection of this information which will then be passed to the local authority (ward chief and municipal chief) who will make the recommendations for tranche disbursement. Based on conversations that the HRRP team have had with various local officials, it seems that in the Kathmandu Valley there is less awareness about this guideline but there is a commitment from local officials to work with the engineers and households so that houses are only approved once they meet the minimum standards. This will require technical support for applying corrections and will require households to invest in applying those corrections. Outside of the Kathmandu Valley, many municipalities are already collecting the lists of households that rebuilt before the technical staff were deployed. The local officials plan to sit with the engineers once the final list is prepared to discuss any technical concerns and will also visit the houses if required.

HRRP Rapid Municipal Capacity Assessment: on September 2018, NRA started the transfer of responsibilities related to post earthquake reconstruction and recovery to municipalities by signing an MoU ([Nepali](#), [Unofficial English Translation](#)) with all 282 earthquake affected municipalities. To better understand municipal capacity following the signing of the MoU, HRRP has started a rapid capacity assessment of municipalities in earthquake affected districts. HRRP district teams will be responsible for the data collection. The survey covers four main areas:

- Physical infrastructure
- Human resources (numbers)
- Knowledge and capacity of human resources on reconstruction policies, procedures and guidelines.
- Attitude and receptiveness of the municipality in terms of accepting external support and leading the reconstruction process.

The identified gaps will support the HRRP team for strategic planning in supporting the municipality to strengthen its capacity to perform its activities.

Retrofitting Sharing Session 21 June, Building CLPIU: during the session organised by Building CLPIU, UNOPS, UNDP, NSET, and ASF shared details of challenges and opportunities in relation to retrofitting. A person whose house was retrofitted also shared his experience during the session. Building CLPIU provided an overview of the GoN's plan to identify households who are willing to retrofit their house and to develop a strategic support plan and package for them. Everyone present at the session was requested to circulate this information in their working areas. Building CLPIU also urged Partner Organisations to get any designs/guidelines approved by the relevant GoN entities and to share these with Building CLPIU so that they can compile all approved designs and guidelines for reference.

Multi-Stakeholder Dialogue on Localisation of Humanitarian Aid and Actions, 28 June, MoFAGA: the objective of the event, which was co-organized with ALtP Consortium, UNRCO, CBDRR Platform, IFRC, and ICVA, was to discuss on practical issues and priorities for the localization of disaster response and the implications for the humanitarian community. The participants discussed opportunities and challenges based on the localization performance measurement frameworks and a task force was formed, led by MoFAGA, to draw out recommendations on implementation options for localizing disaster response.

MIS Orientation for MIS Consultants and Computer Operators, 21-24 June, NRA: the objective of the event was to discuss the major issues and challenges faced at district level and provide solutions to address these. The most common issue that came up was the need for a uniform MIS throughout different departments so that the required information can be readily available.

EPICentre Encounters “Recent advances and perspectives in multi-hazard risk and resilience” 2 and 3 July: EPICentre at University College London (UCL) is an interdisciplinary research centre that investigates the risk to society, the built and natural environment from natural hazards. This two-day knowledge exchange event in London brought together researchers, academics, practitioners and industry partners working at the nexus between risk, environmental hazards and the built environment. The conference discussed on varied topics ranging from Methods for multi-hazard risk assessment and resilience, Transformative technologies for improved decision making, Innovation in disaster risk reduction and resilience and Community resilience. The HRRP National Coordinator took part in the conference and shared the experience of Nepal's housing recovery after the Gorkha earthquake 2015 in a session on “methods of multi hazard risk assessment and resilience”. The presentation is available [here](#).

District & Municipal Updates

Number of households switching grant type: this data has been collected from the DLPIU offices by the HRRP District Coordination Teams. It will be updated as more information is received.

District	No. of HHs changed from Retrofitting to Reconstruction	No. of HHs changed from Reconstruction to Retrofitting
Dhading	6	0
Dolakha	27	0
Gorkha	71	0
Gulmi	0	0
Kavrepalanchok	154	5
Kathmandu	1	5
Rasuwa	39	0
Sindhupalchok	24	0
Total	322	10

Access to Finance Program Launch in Gorkha, 1 July, Sakcham: the program mainly focused on facilitating access to soft / concessional loans for households who have received the first tranche of the GoN housing reconstruction grant but have not been able to build their house due to financial constraints. The launch program was attended by representatives from central level NRA, HRRP District Team Dhading, GMAI, DCC, DFID and other district stakeholders. For more information on the Sakcham programme please contact Udhav R Subedi District Level Coordinator - Housing Reconstruction Project, usubedi@sakcham.com.np.

HRRP District Coordination Meetings, 14 June – 14 July 2019: HRRP District and Municipal Coordination Meetings, 14 June – 14 July 2019: during this period district coordination meetings took place in Dhading (18 June), Makwanpur (18 June), Sindhupalchok (26 June), Nuwakot (26 June & 12 July), Ramechhap (26 June), Lalitpur (2 July), Dolakha (4 July), Kathmandu (12 July), Baglung (20 June), Chitwan (26 June), Arghakhanchi (9 July) and Gulmi (14 July). Some of the highlights from these meetings include:

- In **Dhading**, Partner Organizations (POs) shared updates on their activities in reconstruction in the district. GMAI also requested all the POs to submit their monthly progress report to GMAI regularly on time.
- In **Makwanpur**, it was noted that the housing as well as school reconstruction is going well in the district. The meeting decided to coordinate with all concerned stakeholders in the district, issue public notice to inform the households who have not signed partnership agreement (PA) by 6 July 2019 and get the first tranche by 16 July 2019. Land purchase investigation committee shared the report on land purchasing for landless households, TI Nepal also monitored the sites and found that the process was transparent. Finally, land purchase for 14 landless households will be forwarded to GMAI.
- In **Sindhupalchok**, it was reported that 80% of reconstruction has been completed in the district. A huge gap in PA digitization was reported. About 21,000 copies of PA have not been digitized and this has been communicated to all municipalities and concerned stakeholders for the collection in their respective wards. The meeting discussed on the issue of the 171 landless households that acquired land with consent from the landowners and reconstructed houses, but they do not have legal landownership document.
- In **Nuwakot**, POs updated on their activities in the district. Mott MacDonald has planned to extend its activities to other four Municipalities. DLPIU Building shared that 613 non-compliant houses built before the establishment of NRA and mobilization of technical staffs have been sent to CLPIU Building. It was also noted that the progress with PA digitization, third and final inspection of houses is increasing as this has been the priority for the field staffs. DLPIU Building requested POs to support during the final inspection of the houses in their respective working areas. 238 displaced households in the district have been relocated

to five different integrated settlements. The meeting decided to request for geo-hazard report from NRA and requested POs to coordinate with local authorities for coming fiscal year planning.

- In **Ramechhap**, meeting discussed on carrying out the resurvey and reverification process in an effective manner adhering to NRA guideline and complete within the timeframe. However, if any difficulties are encountered during the survey, request would be made to NRA for additional time. It was decided to coordinate with all municipalities to ensure that households who have not done the PA to do within 6 July 2019 and those who have not received first tranche receive by 16 July 2019. A detail of 720 houses built immediately after the 2015 earthquake, before the mobilization of engineers have been forwarded to NRA for further action and decision.
- In **Lalitpur**, the meeting was attended by 12 Partner Organizations (POs) such as Maya Foundation, Himalayan Dana Foundation, Rotary Club of Jawalakhel Manjushree & Shangrila Orphanage Home that have completed housing reconstruction project. There were concerns regarding the duplication in the grants provided to the households in the areas supported by these POs. Thus, POs were requested to support NRA to get the tranche back from the households that received tranche from the Government and the POs. GMaLI Chief also requested the POs to inform/submit proposal to NRA to be registered officially. With regards to the challenges faced by UN Habitat in housing reconstruction in Bungmati, GMaLI noted to have a separate discussion with NRA.
- In **Dolakha**, meeting discussed on the activities of Partner Organizations (POs), speeding up the reconstruction process and recovery of the first tranche if households are not willing to build houses. Many of the POs have completed the activities in the district but there has been no coordination with the Government stakeholders on their exit plan. Thus, GMaLI Chief emphasized on the proper exit strategy plan by POs working in the district. POs were requested to provide details of the activities carried out in the district, coverage areas, coordination with municipal and ward authorities, evaluation report of the project including recommendation to GMaLI after the completion of the project.
- In **Kathmandu**, yearly review meeting of the private housing reconstruction of Kathmandu was held on 12 July 2019. The meeting discussed on the status of the reconstruction in Kathmandu district along with the issues and challenges. The DLPIU chief presented the reconstruction status of the district and highlighted on the NRA deadline for the housing reconstruction grant. DLPIU chief requested all the representative of the municipality to facilitate on timely flow of the information of the deadlines to ward offices and households. Dr. Chandra Bahadur Shrestha, NRA executive member highlighted on the NRA policies to facilitate the reconstruction in the valley including the house pooling concept. He further highlighted that with the joint effort of the NRA, DLPIUs and local elected representatives the reconstruction can be successful, and a safer community and a safer nation can be build.
- In **Baglung**, meeting discussed on the 25 schools that have been selected for the construction of toilets. The schools have been selected based on damage, number of students and the technical reports from technical staffs. This list would be forwarded to NRA in accordance with the schools' reconstruction procedure, 2075.
- In **Chitwan (26 June)**, meeting decided that landless households if want to construct houses in the area they have been living for generation can do so in accordance with NRA and District Coordination Committee.
- In **Arghakhanchi**, the meeting discussed on the on progress of housing reconstruction, local infrastructure, schools, health facilities building including issues and challenges in the district. HRRP shared the achievements, learnings and findings from the field visit of some municipalities. The meeting decided that all sectors support DLPIU for timely completion of reconstruction as stipulated by NRA. The decided to re submit the request of the decision made by the meeting held on 22 April 2019 to NRA for making necessary arrangements for reconstructing the physical infrastructures in the district.
- In **Gulmi**, out of the total 4,144 eligible households, 3,981 have received first tranche, 2,432 have received second tranche and 1,413 have received third tranche. The meeting shared the progress in other sectors and discussed on issues related to grievances, landless, retrofitting and CS Entry and completion certificate

distribution to the households that have completed reconstruction. The meeting decided to coordinate with all local authorities to update the vulnerable households as per the decision made by NRA.

Municipal level meetings took place in municipalities and wards across 14 severely earthquake affected districts Bhaktapur, Dolakha, Kathmandu, Kavrepalanchok, Rasuwa, Sindhuli, Sindhupalchok and 18 moderately affected districts Lamjung, Khotang, Baglung, Parbat, Myagdi, Bhojpur, Dhankuta, Arghakhanchi, Gulmi Chitwan and Nawalpur.

- In **Bhaktapur, Ward 3, Changunarayan Municipality (19 June 2019)**, reconstruction has progressed well in ward 3 after some of the issues related to reconstruction have been solved through proper documentation and public inquiry deed process. However, few households have not been able to move forward in getting the tranches as they have not received building permit from the Municipality due to landownership issues. The major non-compliance cases are larger room size than specified in the building guideline, missing bands and houses not per the design. In **Wards 2,3,4 & 8, Suryabinayak Municipality (20 – 21 June 2019)**, land ownership issues due to multiple beneficiaries, issues between tenant and land owners and family disputes have caused delay in reconstruction process. The Ward offices said households need technical support and regular supervision during reconstruction. Ward offices have decided to issue public notice to inform households that have not signed PA of the deadline to do PA and request them to start reconstruction.
- In **Kathmandu, Ward 10, Chandragiri Municipality, (20 June 2019)**, the main issues in the ward are small land parcel after the property division and households are not able to reconstruct in such lands, lack of land ownership documents and road extension program have impacted on the households to sign the partnership agreement and start reconstruction. Some other issues in the ward are non-compliant houses constructed before the NRA guidelines were published such as 9"X12" column, missing of earthquake resistant elements in load bearing structure
- In **Rasuwa, Wards 2, Uttargaya Rural Municipality (20 June 2019)**, reconstruction progress was discussed, and field engineers were suggested to prioritize CS Entry work and inspection of houses for third tranche release.
- In **Kavrepalanchok**, meetings took place in **Wards 8 & 9, Namobuddha Municipality (28 June 2019)**, in **ward 8**, the major challenge in reconstruction is the water scarcity which has delayed reconstruction and even led to migration. 44 families have migrated to Bhakundebesi and 4 to Banepa. People also buy water at the cost of 2 NPRs per litre. Most houses constructed in the ward are two room brick in cement mortar structures. Most families are using the old damaged houses for storage purposes while new houses are being used for bedrooms and kitchen. In **ward 9**, due to the NRA new notice on tranche deadline, 16 households have enrolled to get the Government financial assistance to start reconstruction. The households along the main road in Dapcha Bazar are reluctant to reconstruct as they need to follow new road bylaws which will leave them with small plots of land. A discussion was also held on conserving the traditional Dapcha Bazar for which the letter has been sent to Namobuddha Municipality. Most households are living in the old damaged houses after minor repairs, they also have not done the PA with the Government. In **Ward 7, Roshi Rural Municipality (3 July 2019)**, the major issue is with retrofitting. 86 households identified as eligible for retrofit grant, none of them have done the partnership agreement as they wish to switch to the full reconstruction grant. The ward office is planning to distribute completion certificate to the households that have completed reconstruction. In **Ward 11, Dhulikhel Municipality (3 July 2019)**, of the 48 households included in retrofit grant, 19 have applied to switch to be on full reconstruction grant. Being an urban area, many households intend to build RCC and BMC structures which are comparatively expensive. One of the challenges in such area is convincing people to build stone in mud mortar houses that are strong enough. The ward has not implemented the policy of building permit to apply for the tranche thinking it will slow down the tranche distribution process. However, it will implement the policy before distributing the completion certificate. In **Ward 8, Bhumlu Rural Municipality (4 July 2019)**, of the 80 households included in retrofit grant, 3 have applied to switch to be on full reconstruction grant. Among the 16 households identified under hazard risk area, 11 households have received 200,000 NPRs for purchasing land in safe places. Two out of them have

acquired land with the consent from the landowners and reconstructed but have not moved as they are waiting for legal documentation to be done with the landowners who is abroad.

- In **Dolakha, Wards 5 & 6, Melung Rural Municipality (26 June 2019), Ward 9, Bhimeshor Municipality (28 June 2019)**: in both meetings, discussion focused on supporting the households in retrofit grant to retrofit their houses within the deadline. Ward offices were requested to prepare for final inspection of houses that have received third tranche for completion certificate distribution. DLPIU Building based on the caseload will provide technical support to the wards during final inspection. Ward offices were also given information on the procedure for converting households from retrofit to full reconstruction grant. Additionally, if any households are not satisfied with the result of NRA can appeal through the support of ward offices. Finally, technical persons were requested to do the third inspection only after the first and second inspection have been digitized and upload in EHRP portal.
- In **Sindhupalchok, Melamchi Municipality (19 June 2019), ChautaraSagachokgadhi Municipality (20 June 2019), Ward 6, Balephi Rural Municipality (1 July 2019) and Bhotekoshi Rural Municipality (2 July 2019)**: the most common concerns were delay in addressing the grievances by NRA even after months doing the resurvey and reverification, delay in tranche processing and lack of file tracking mechanism as local authorities have to spend lot of time to track the files. Despite masons' trainings conducted, there is shortage of masons, most of the masons working are from western part of the country with no trainings. This has led to construction of non-compliant houses that do not meet building standard. In Bhoekoshi RM, there are 317 vulnerable households that have not started reconstruction due to lack of manpower and poor economic condition. In Melamchi Municipality a farewell was given to HELVETAS Sindhupalchok on completion of their program. DLPIU GMaLI requested to recheck and reverify the tranche duplication data of HELVETAS and the Government and requested engineers to support the final inspection and certificate distribution by HELVETAS. Municipal office noted that trained masons have not been involved in reconstruing and requested POs and stakeholders to monitor and motivate them to be engaged in reconstruction.
- In **Sindhuli, Dudhauri Municipality (27 June 2019), Tinpatan Rural Municipality (29 June 2019)**, both municipalities assured to complete the resurvey and reverification within the deadline set by NRA. Municipalities were requested to revise the vulnerable households list shared by NRA and submit to DLPIU GMaLI.
- In **Khotang, Ward 5, Ruapakot Majhuwagadhi Municipality (26 June 2019)**, there are 75 households in the ward and 70% have received third tranche. Some households that have completed new construction have not received third tranche as they have not demolished old damaged houses. There is lack of trained masons. Engineers said the time for resurvey and reverification was not enough and they found it hard to categorize the damage level for some houses and those houses had been repaired.
- In **Lamjung, Dudhpokhari Rural Municipality (21 June 2019)**, main discussion was on the non-compliant houses constructed by Gorkha Welfare Relief (GWR), 82 houses in ward 3 and 39 houses in ward 6 on Dudhpohari RM were constructed without any coordination with NRA. There is also tranche duplication in households supported by GWR. 39 households from ward 3 and 12 households from ward 6 have signed the partnership agreement with the Government and received the reconstruction grant. Municipal Chairperson requested to address this problem for better reconstruction progress in the Municipality.
- In **Chitwan, Kalika Municipality (26 June 2019)**, it was reported that 50% of housing reconstruction has been completed, reconstruction rate is increasing however not retrofitting. Households are not convinced of the cost, quality, materials and the manpower for doing retrofitting. Most houses were built before the deployment of field technical persons. NRA recent guideline will help these households to move ahead with the remaining tranches. There is a gap in the households receiving first and second tranche. It was reported that there are still households submitting grievances.

- In **Nawalpur, Hupsekot Rural Municipality (27 June 2019)**, reconstruction in Hupsekot is almost at the end of completion. However, retrofitting and completion certificate distribution have not started. Technical persons were requested to make a final inspection, do the CS Entry and coordinate with municipality to plan for completion certificate distribution.
- In **Dhankuta, Chhatarjorpati Rural Municipality (2 July 2019)**, main concern raised was the non-compliant houses built immediately after the earthquake. Some of the RCC structures were found to be unsafe after the structural analysis because of which the households have not got the tranche. There is lack of trained manpower to construct earthquake resilient buildings as well as to do retrofitting. So, many buildings that need to be retrofitted have not been done so. Third tranche of some households have been stopped as they have not demolished the old damaged houses. There are also households who have received first tranche and do not intend to reconstruct.
- In **Ward 12, Bhojpur Municipality (8 July 2019)**, resurvey and reverification has not been completed in some wards. One of the issues was the duplication in Name and PA number. It was reported that municipality is facing pressure from the people to approve their houses constructed immediately after the 2015 earthquake and are non-compliant. The common houses built are two storey, brick in mud mortar.
- In **Baglung, Kathekhola Rural Municipality (7 July 2019)**, majority of the houses were constructed immediately after the 2015 earthquake, they do not meet the building code requirement, so the households have not progressed to receive second and third tranches. A recent NRA decision on providing reconstruction grant to the families who built before the mobilization of engineers has created confusion among communities regarding minimum requirement and grant disbursement mechanism. Till date, no completion certificate has been provided, even to the households that have received third tranche. It was reported that many single room houses have been built just for the sake of getting the Government grant. These houses have been mostly used as cowsheds or as store rooms.
- In **Parbat**, meetings took place in **Modi Rural Municipality (8 July 2019)** and **Painyu Rural Municipality, (9 July 2019)**. In both Municipalities, most of the houses were built immediately after the earthquake and are non-compliant that lack corner stitches, sill and lintel bands. These households have not progressed beyond first tranche, showing a huge gap in accessing first, second and third tranches by the households. Households are also facing financial challenges in applying correction measures to the houses even after recommendation from engineers. There are significant number of households in retrofit grant list, but they have only applied minor repairs to the damaged houses, not proper retrofitting. Completion certificate has not been provided to anyone, even to the households that have received third tranche. In some wards of **Modi RM**, resurvey of grievances is still going on. It was reported that **ward 2 of Modi RM** office with its own resources had undertaken a geological survey in upper belts where landslides and land degradation had caused earthquake affected families to move to lower belts. In **Painyu RM**, two roomed houses built being not enough for larger families have been using damaged houses for other purposes without demolishing them.
- In **Myagdi, Myagdi Municipality (12 July 2019)**, there are nearly 14 households in retrofit grant that have taken first tranche, but no retrofitting work has been carried out. Local masons are available in Beni Municipality but due to lack of proper mason training, they are not confident to build earthquake resilient houses. Resurvey and reverification of beneficiaries have been completed in all wards of Beni Municipality.
- In **Arghakhanchi, Malarani Rural Municipality (7 July 2019)** and **Chatradev Rural Municipality (8 July 2019)**, discussion was on reconstruction progress, issues with non-compliant cases, issues with retrofitting, grievances and resurvey and reverification done by NRA and current directive of NRA on providing reconstruction grant to houses built immediately after the earthquake, before the technical persons were in the field. The meeting also decided to monitor the non-compliant houses and encourage the households to apply correction measures to move forward with the remaining tranches. Meeting in Malarani RM also decided to send letter to DLPIU GMAI for conducting resurvey of health posts.
- In **Gulmi, Chatrakot Rural Municipality (12 July 2019)**, discussion focused on the NRA notice and guideline released regarding houses built before the deployment of engineers. For the households who have

received second tranche but not the third, the meeting decided to motivate those households to apply correction measures to move forward in getting the remaining tranche. Issues regarding resurvey and reverification and grievances were also raised, grievances have been forwarded to DLPU GMAI. No progress has been made in retrofitting, engineers requested for the retrofitting training for the technical staffs in the field. In **Musikot Municipality (14 July 2019)**, 165 houses were built before the mobilization of engineers in the field. There are 16 households that have not signed the partnership agreement. 140 households have completed reconstruction and 280 are under construction. The Municipality is planning to distribute completion certificate to households that have completed reconstruction.

[HRRP District Coordination Team Bhaktapur and Lalitpur, Monthly Report, 14 June – 14 July 2019](#)



Ward 8, Changunarayn Municipality, Bhaktapur: single storey, brick and cement mortar masonry, wall system house with flexible roof with a shutter in the front. The homeowner has received the first tranche of the GoN housing reconstruction grant. The house does not have roof bands, so the homeowner needs to apply corrections by jacketing with wire mesh above the lintel level.

[HRRP District Coordination Team Kathmandu, Monthly Report, 14 June – 14 July 2019](#)



Ward 12, Chandragiri Municipality, Kathmandu: two storey, load bearing brick and cement mortar masonry house. The house is considered non-compliant due to the size of the openings. The homeowner has received the first tranche of the GoN housing reconstruction grant and is planning to keep the rolling shutter on the ground floor.

[HRRP District Coordination Team Kavrepalanchok & Sindhupalchok, Monthly Report, 14 June – 14 July 2019](#)



Ward 11, Panchkhal Municipality, Kavrepalanchok: two room, hollow concrete block structure. The homeowner is an elderly woman looking after two young grandchildren. The house has been constructed with vulnerable to up support of 50,000 NPRs and technical assistance from ASF Nepal/Habitat for Humanity.

[HRRP District Coordination Team Dhading, Gorkha, Arghakhanchi, Gulmi & Palpa Monthly Report, 14 June – 14 July 2019](#)



Ward 5, Chhatradev Rural Municipality, Arghakhanchi: single storey, two room, stone and mud mortar masonry house with RCC bands and flexible roof. The homeowner has received all three tranches of the GoN housing reconstruction grant.

[HRRP District Coordination Team Dolakha, Ramechhap, and Sindhuli Monthly Report, 14 June – 14 July 2019](#)



Ward 4, Umakunda Rural Municipality, Ramechhap: three storey, stone and mud mortar masonry structure. The house is non-compliant since it is three storeys. The house was constructed immediately after the 2015 earthquake, before the deployment of NRA technical persons. The homeowner has received the second tranche of the Government housing reconstruction grant. The total cost of construction was 1,900,000 NPRs.

[HRRP District Coordination Team Makwanpur, Chitwan, and Nawalparasi, Monthly Report, 14 June–14 July 2019](#)



Ward 4, Hupsekot Rural Municipality, Nawalpur: single storey, two room, load bearing brick and cement mortar masonry house with flexible roof. The homeowner has received all three tranches of the GoN housing reconstruction grant. The total cost of construction was 1,200,000 NPRs.

[HRRP District Coordination Team Nuwakot and Rasuwa, Monthly Report, 14 June – 14 July 2019](#)



Ward 2, Uttargaya Rural Municipality, Rasuwa: single storey, two room, stone and cement mortar masonry house with rigid roof. The homeowner has received all three tranches of the GoN housing reconstruction grant.

[HRRP District Coordination Team Lamjung, Tanahun, Kaski, and Syangja, Monthly Report, 14 June – 14 July 2019](#)



Ward 6, Dudhpokhari Rural Municipality, Lamjung: single storey, three room load bearing structure. The house is constructed using stone and mud mortar masonry up to 3 feet, with no DPC bands, and above this with CGI sheets connected to vertical steel square pipe of 2"x2". The thickness of the wall from ground level to 2 feet height is 18" and the remaining 1 foot is 16". The roof trusses are not connected along the length. This type of house is built with support from the Gorkha Welfare Society. During a recent municipal coordination meeting in Dudhpokhari these non-compliant houses constructed by Gorkha Welfare Society was a major topic of discussion. The organisation has built 82 houses in ward 3 and 39 houses in ward 6 without any coordination with NRA and the houses are non-compliant. There has also tranche duplication in households supported by Gorkha Welfare Society with 39 households from ward 3 and 12 households from ward 6 having signed the partnership agreement with the Government and received the reconstruction grant from the government as well as from Gorkha Welfare Society.

HRRP District Coordination Team Parbat, Baglung, and Myagdi, Monthly Report, 14 June – 14 July 2019



Ward 5, Kathekhola Rural Municipality, Baglung: single storey, two room stone and mud mortar masonry house. The homeowner has received all three tranches of the GoN housing reconstruction grant. The cost of construction was 330,000 NPRs

HRRP district coordination team Khotang, Okhaldhunga, Solukhumbu, Bhojpur, Dhankuta and Sankhuwasabha,
Monthly Report, 14 June – 14 July 2019



Ward 12, Bhojpur Municipality, Bhojpur: two storey, stone in cement mortar house with RCC bands. There are three rooms in ground floor and four rooms in the first floor. The home owner has received all three tranches of the GoN housing reconstruction grant. The cost of construction is 11,00,000 NPRs.

Case Studies

Featured Technical Staff Person, Aangdawa Sherpa: this month's featured technical staff person is Aangdawa Sherpa. He has been working as an assistant sub-engineer in Bhojpur Municipality for a year and is also from Bhojpur. The experience has been challenging because he did not receive any training or orientation before he was deployed and there are only three technical staff working on reconstruction and this is not sufficient. This has held up the resurvey process as they have only been able to get to 150 out of the 1,400 houses that need to be resurveyed. The technical staff have been under huge pressure from GMALI to complete the resurvey, but it has not been possible. Aangdawa hopes that the GoN will push back the deadline for completing the resurvey or deploy more human resources so that they can get it finished on time. Aangdawa is worried that there will be households left out if they cannot finish the resurvey and that the technical staff will face a lot of negative feedback from households and local officials if this happens. He has also found the resurvey process difficult from a technical perspective as it has been very difficult to categorize the damage to houses more than four years after the earthquake. As there is no District Support Engineer (DSE) in the district, Aangdawa is responsible for non-compliance checks but has found this very difficult because he has not received any orientation or training on non-compliances or the corrections and exceptions manual. Aangdawa feels that it has been positive to be working in the place that he is from. He has also learnt a lot from his field experience to date which has helped him to overcome the challenges associated with being deployed without prior training or orientation.

Handover of retrofitted houses, Siddhalekh Rural Municipality, Nalang, Dhading, 4 July: the NRA CEO, Sushil Gyewali, handed over six houses that were retrofitted as part of trainings under the NSET Baliyo Ghar programme to the home owners in a ceremony in Dhading. The 25 days training programme provided masons (six worked on each house) the opportunity to build new skills and knowledge on implementing retrofitting.



Left: retrofitted house in Nalang Village, Shiddhalekh RM, Dhading. The retrofiting has been carried out by NSET under the Baliyo Ghar programme. NSET Baliyo Ghar provided the labour costs (25 days of 6 masons paid 800 NPRs / day) and in-kind material support of around 25,000 NPR. Right: NRA CEO, Sushil Gyewali, handing over 6 houses retrofitted under NSET-Baliyo Ghar.

Enabling Social Support System via Community Forest User Group at Maskichap, Sahid Laxhan Rural Municipality, Gorkha:

Sandhan Besauni Community Forest User Group (CFUG) was established in 2056 BS under the 1993 Forest Act (provision relating to formation of CFUG). There are 76 households who are members of the CFUG. To support recovery from the 2015 earthquake, the CFUG is supporting earthquake affected families by providing low cost timber for the construction of houses. The CFUG charges 680 NPRs for one cubic feet of untreated timber, which is approximately 1,500 NPRs cheaper than the market price. The CFUG has also formed a saving and credit cooperative which now holds more than 500,000 NPRs in savings. The saving and credit cooperative is using this to provide low interest loans for vulnerable and poor families to support with their reconstruction and livelihood recovery.




Requests for Partner Support

HRRP Round 5 Partner Satisfaction Survey: the HRRP team is pleased to invite all partners to take part in the latest round of the partner satisfaction survey and help to improve the platform's services. The survey is an opportunity for HRRP to be evaluated by all stakeholder in the earthquake recovery and reconstruction effort based on our service delivery. Your feedback will guide and shape us for more effective coordination in coming days. The survey should take approximately 10 to 15 minutes to complete but will take longer if you choose to provide more detailed feedback in the open answer questions and can be conducted in Nepali or English. The survey will be open until COB 19 July. More detailed feedback on the HRRP can be also be sent at any time to info@hrrpnepal.org. The results of the previous rounds of the Partner Satisfaction Survey can be accessed here [Round One](#), [Round Two](#), [Round Three](#), [Round Four](#). Many thanks to all those who provided input in the last round, it was very valuable and has helped adjust our activities.

NRA Newsletter, June 2019

Municipal Profiles: HRRP has developed reconstruction and recovery profiles for all 282 earthquake affected municipalities. The municipalities are responsible for updating the profiles on a monthly basis with support from HRRP. Some municipalities have also made the profiles available on their own websites, for example [Sandhikharka Municipality](#) in Arghakhanchi.

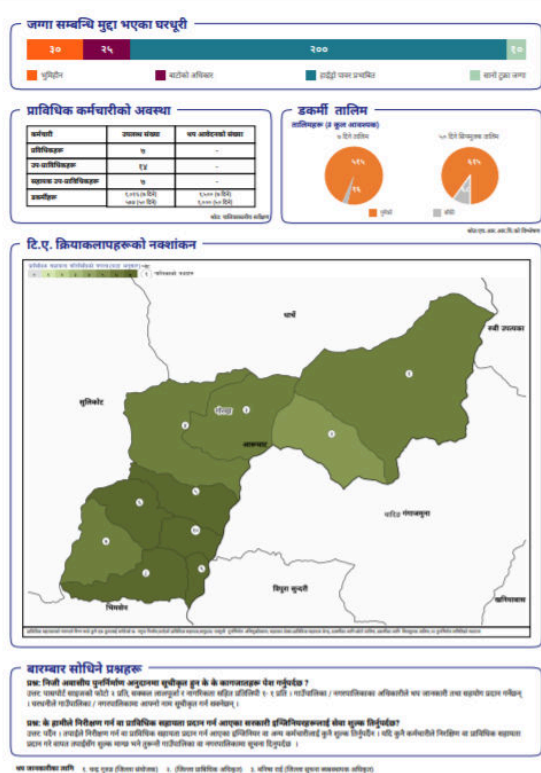

Citizen Insider, Issue No. 19

ASF Nepal, Newsletter #28, May 2019

[Baliyo Ghar TV, Episode 152](#) this episode highlights the ten major points to consider while retrofitting the Stone Masonry or BMC Buildings using GI Wire. A detailed presentation from Mr. Ranjan Dhungel, Program Manager, NSET-Baliyo Ghar Program.



KathaMaala Radio Drama Episode 1: this radio drama is produced by Radio Nepal and BBC Media Action with financial support from DFID. The first episode of the drama discusses retrofitting. Two little girls, Seema and Kala, are playing together in the front yard of Seema's newly built house. They soon get into an argument about the score of their *chungu* game. Seema tells Kala to go back to her "damaged house" and says she would never come to her house to play, because it is damaged. The incident scars Kala and she begins to sleep talk about the condition of the house. This prompts her parents to start to retrofit their house. After retrofitting, Kala's house is safe and the story ends with the two friends reconciling and playing together again.

[FAQs](#) | [Briefing Pack](#) | [Meeting & Events](#) | [5W](#) | [Housing Progress](#) | [Housing Typologies](#)



CONTACT US

HRRP Nepal Office

Jawagal, Lalitpur, Nepal

Tel: (+977) - 01 - 5544149

Email: info@hrrpnepal.org
