

District Report

Sindhuli

15 February - 14 March 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
1. Joint Monitoring and Field Visit to Sindhuli, Dudhouli Municipality Ward no. 1 & 2 (Hatpate, Nipane, Sirthouli)	19 th February 2019			Kiran Mahat (M&E- CLPIU - Building), Dinesh Sanjel (DSE-NRA), Pravin Thakur (Engineer-DLPIU/Building), Lekhanath Paudel (DTC-HRRP), Sachin Malego (DIMO-HRRP)	
2. Ward Level Meeting in Sindhuli, Dudhouli Municipality Ward no. 1	19 th February 2019	22	5	Kiran Mahat (M&E- CLPIU - Building), Dinesh Sanjel (DSE-NRA), Pravin Thakur (Engineer-DLPIU/Building), Lekhanath Paudel (DTC-HRRP), Sachin Malego (DIMO-HRRP)	Meeting Minutes
3. Joint Monitoring and Field Visit to Sindhuli, Dudhouli Municipality Ward no. 2 (Hatpate, Nipane, Sirthouli)	19 th February 2019			Kiran Mahat (M&E- CLPIU - Building), Dinesh Sanjel (DSE-NRA), Pravin Thakur (Engineer-DLPIU/Building), Lekhanath Paudel (DTC-HRRP), Sachin Malego (DIMO-HRRP)	
4. Ward Level Meeting in Sindhuli, Dudhouli Municipality Ward no. 2	19 th February 2019	11	0	Kiran Mahat (M&E- CLPIU - Building), Dinesh Sanjel (DSE-NRA), Pravin Thakur (Engineer-DLPIU/Building), Lekhanath Paudel (DTC-HRRP), Sachin Malego (DIMO-HRRP)	Meeting Minutes

Summary of events during this period

5. Joint Monitoring and Field Visit to Sindhuli, Tinpatan R M, ward no. 1, 2 & 3 (Belghari, Bhimasthan)	20 th February 2019			Kiran Mahat (M&E- CLPIU - Building), Dinesh Sanjel (DSE-NRA), Pravin Thakur (Engineer-DLPIU/Building), Lekhanath Paudel (DTC-HRRP), Sachin Malego (DIMO-HRRP)	
6. Ward Level Meeting in Sindhuli, Tinpatan R M, Ward no. 2	21 st February 2019	22	0	Kiran Mahat (M&E- CLPIU - Building), Dinesh Sanjel (DSE-NRA), Pravin Thakur (Engineer-DLPIU/Building), Lekhanath Paudel (DTC-HRRP), Sachin Malego (DIMO-HRRP)	Meeting Minutes
7. Joint Monitoring and Field Visit to Sindhuli, Tinpatan R M, Ward no. 9 & 10 (Lampantar, Chakmake)	21 st February 2019			Kiran Mahat (M&E- CLPIU - Building), Dinesh Sanjel (DSE-NRA), Pravin Thakur (Engineer-DLPIU/Building), Lekhanath Paudel (DTC-HRRP), Sachin Malego (DIMO-HRRP)	
8. Joint Monitoring and Field Visit to Sindhuli, Tinpatan R M, ward no. 8 & 11 (Lampantar)	22 nd February 2019			Kiran Mahat (M&E- CLPIU - Building), Dinesh Sanjel (DSE-NRA), Pravin Thakur (Engineer-DLPIU/Building), Lekhanath Paudel (DTC-HRRP), Sachin Malego (DIMO-HRRP)	
9. Ward Level Meeting in Sindhuli, Tinpatan R M, Ward no. 11	22 nd February 2019	10	2	Kiran Mahat (M&E- CLPIU - Building), Dinesh Sanjel (DSE-NRA), Pravin Thakur (Engineer-DLPIU/Building), Lekhanath Paudel (DTC-HRRP),	Meeting Minutes

Summary of events during this period

				Sachin Malego (DIMO-HRRP)	
10. Support to DLPIU-GMaLI for dissemination and segregation of data at KO-LE-NI-KA Sindhuli from the year 73-74 and 74-75 regarding first and second tranche	Ongoing since January 2019			Lekhnath Paudel Sachin Malego	
11. Training Database Entry of 45+ events and 450+ participants from HELVETAS to EHRP MIS	1 st March 2019 and onwards			Lekhnath Paudel Sachin Malego	
12. Joint Monitoring and Inspection of non-compliance houses and recommend corrections and Conduct Ward Level Meeting in Hariharpurgadhi Rural Municipality	5 th March – 6 th March 2019			Kiran Mahat (M&E- CLPIU - Building) Lekhnath Paudel Sachin Malego	
13. Ward level meeting in Sindhuli, Hariharpurgadhi R M ward no. 8	6 th March 2019	14	0	Kiran Mahat (M&E- CLPIU - Building) Lekhnath Paudel Sachin Malego	Meeting Minutes
14. Ward level meeting in Sindhuli, Kamalamai Municipality ward no. 11	7 th March 2019	13		Kiran Mahat (M&E- CLPIU - Building) Lekhnath Paudel Sachin Malego	Meeting Minutes
15. Joint Monitoring and Inspection of non-compliance houses and recommend corrections and Conduct Ward Level Meeting in Ranichuri and Jarayotar of Kamalamai Municipality	7 th March 2019			Kiran Mahat (M&E- CLPIU - Building) Lekhnath Paudel Sachin Malego	
16. Engineers training on Light Timber/Steel Frame Structure Manual	13 th and 14 th March 2019	37	5	Lekhnath Paudel Sachin Malego	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
1. Orientation on Hollow Concrete Block (HCB) Manual	15 th March 2019	HRRP	Lekhnath Paudel Sachin Malego

News & Updates



Er. Lekhnath Paudel (DTC, HRRP-Sindhuli) presenting to the participants in the session of Light Timber/Steel Frame Structure Manual a two days training to engineers in Sindhuli.




Mr. Subas Ghimire (Swisscontact) welcoming the participants in the training of Light/Timber Frame Structure Manual.




Mr. Dev Narayan Prasad Yadav (Acting Planning Chief – GMALI, Sindhuli) presenting a key note speech as Chief Guest in the program of Engineer's Training on Light Timber/Steel Frame Structure Manual in Sindhuli.

Tranche Status									
Rural / Municipality	Dudhauri Municipality	Ghanglekh RM	Golanjor RM	Hariharpurgadhi RM	Kamalamai Municipality	Marin RM	Phikkal RM	Sunkoshi RM	Tinpatan RM
Total HHs Surveyed	14607	2834	4330	5046	15479	5465	3474	5745	7935
Total HHs Eligible	4650	2068	2992	2394	8150	3340	2173	4723	4855
Total HHs Enrolled	4646	2068	2992	2394	8150	3340	2173	4723	4855
First Tranche	4646	2109	2992	2344	8150	3335	2164	4722	4855
Second Tranche	2755	1448	2873	2157	5058	2288	2033	4299	4187
Third Tranche	1257	1202	2173	556	2927	1143	1699	3448	2163
Total HH Constructed	1240	882	1764	363	2000	507	1402	2669	1655
Grievance Registered	11157	785	1614	2531	7018	2303	1294	1067	5491
Grievance Addressed	9449	781	1598	2487	6831	2235	1292	1045	4827
RF HH Eligible	3493	530	667	1538	1768	1266	923	327	2499
RF HH Enrolled	288	97	95	0	278	59	6	0	316
RF 1 st Tranche	288	97	95	0	278	59	6	0	316
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	52	16	16	20	38	9	22	13	16
Non-Compliance Addressed	0	4	0	0	0	0	0	2	3


Graph of Tranche Status:

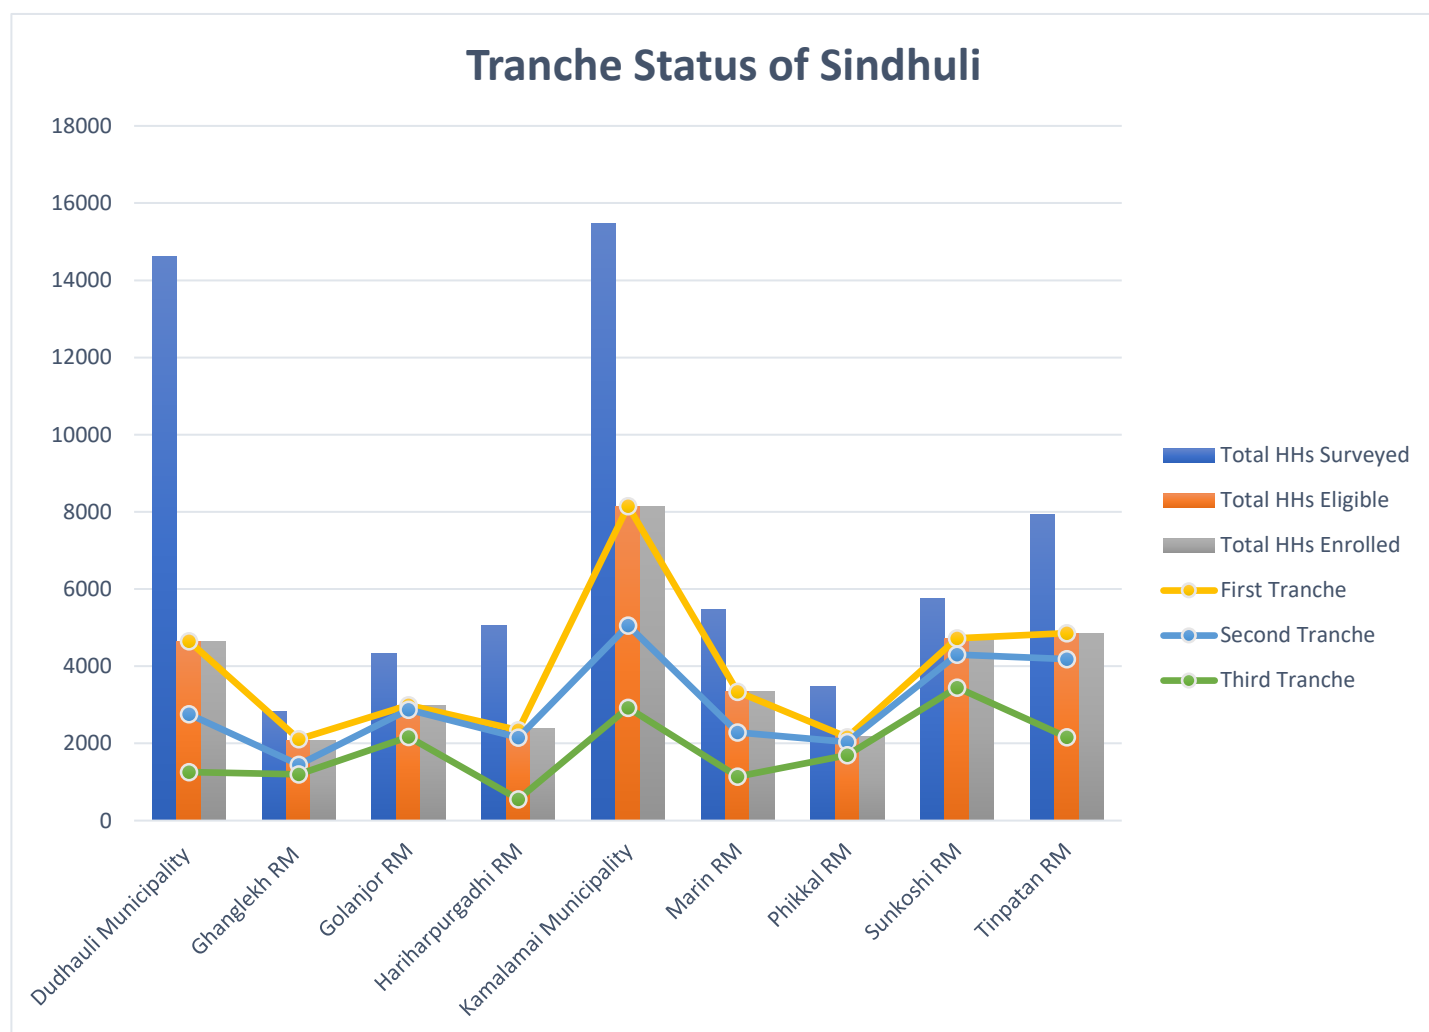

Graph for Retrofitting Status:

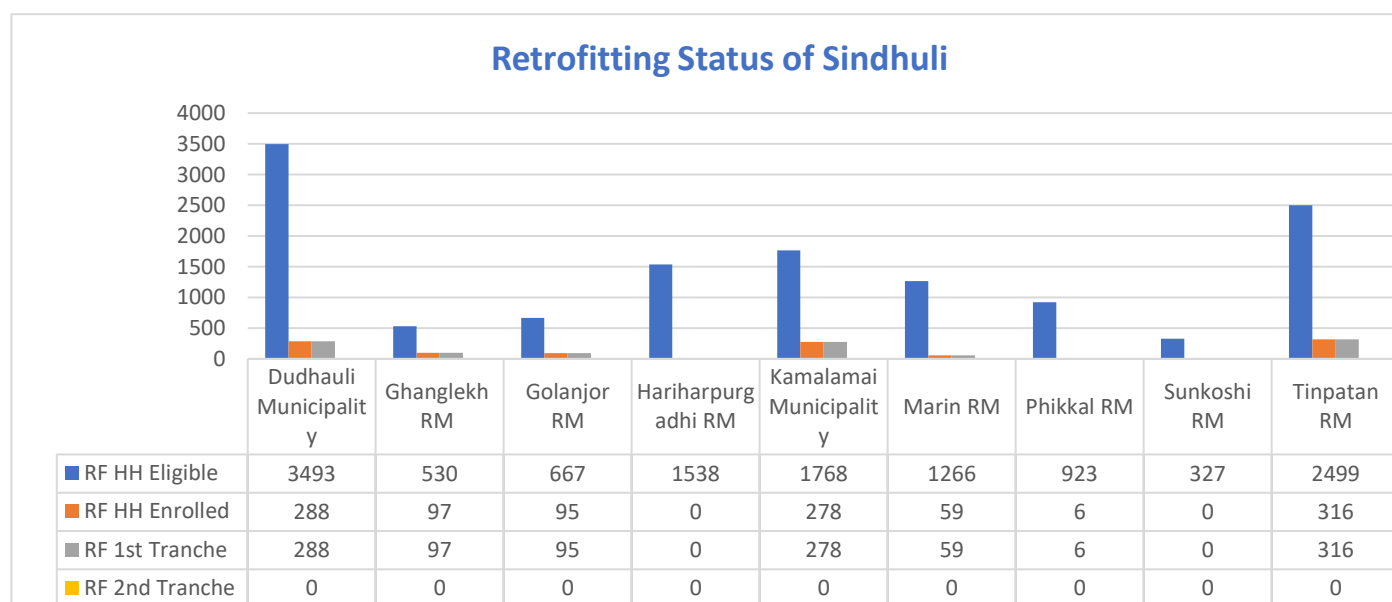

Graph for Grievance Status:

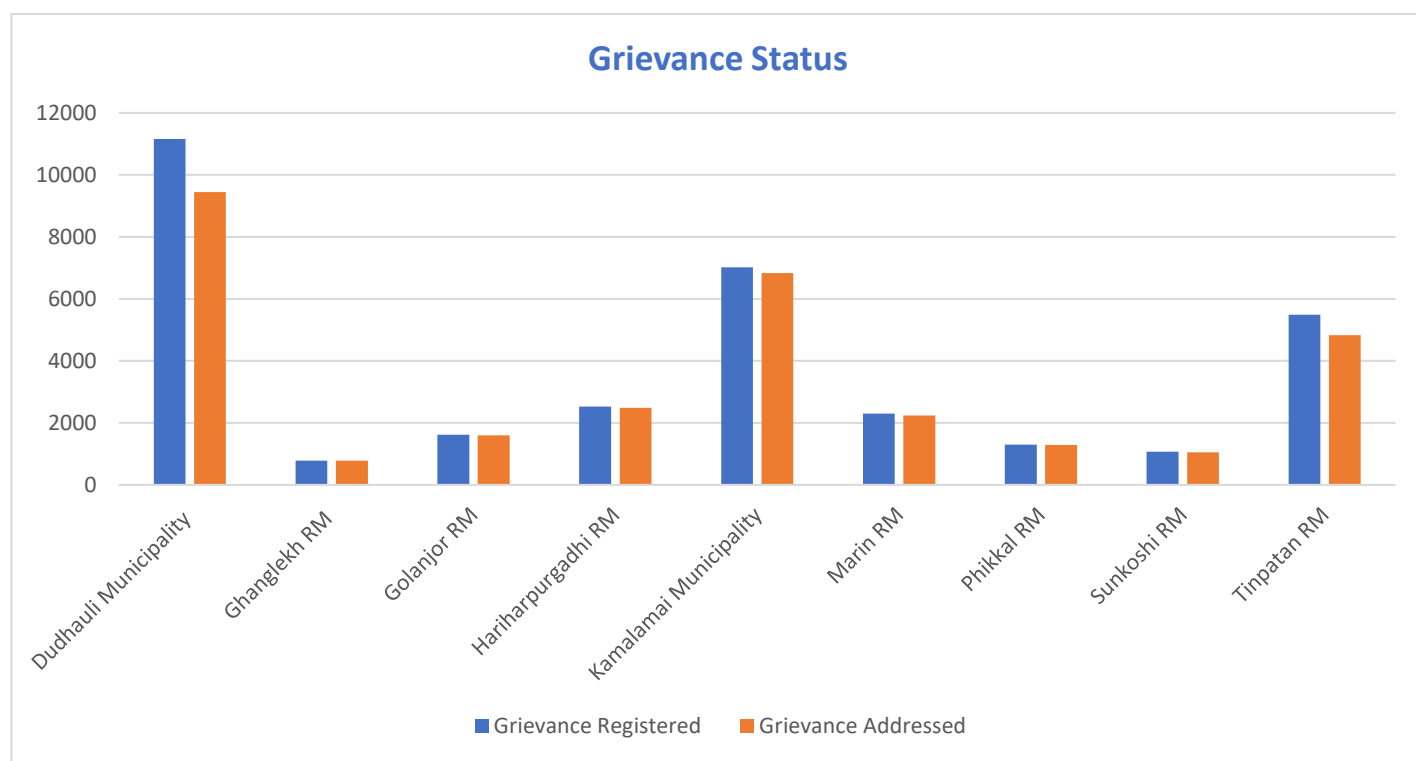

Field Visit /Joint Field Monitoring Visit Reports

Visit: Tinpatan Rural Municipality, Dudhouli Municipality, Hariharpurgadhi Rural Municipality, Kamalamai Municipality

Date	Location	Participants from HRRP and stakeholders
19 th – 23 rd Feb 2019	Dudhouli Municipality, ward no. 1 & 2 Tinpatan Rural Municipality ward no. 2 & 11	Er. Kiran Mahat Er. Lekhanath Paudel Mr. Sachin Malego
5 th – 8 th March 2019	Hariharpurgadhi Rural Municipality, ward no. 6,7 & 8 Kamalamai Municipality, ward no. 11 & 12	Er. Kiran Mahat Er. Lekhanath Paudel Mr. Sachin Malego

Objective(s)

- **Reconstruction Update/ Housing Reconstruction Challenges**
- **Interaction between government agencies, implementing partners and local people**
- **Collection of Typologies of Houses**

Summary

Joint Monitoring field visit was conducted by HRRP Sindhuli along with NRA-CLPIU M&E (Kiran Mahat), DSE (Dinesh Sanjel) and DLPIU-Building Engineer (Prabin Kumar Thakur). The field visit gave an opportunity to NRA-CLPIU/DLPIU and HRRP to observe, supervise and monitor ongoing construction of Houses (*Compliance & Non-Compliance houses*) at Harshahi, Nipane, Lampantar, Bhimasthan, Hariharpurgadhi, Kyaneshwor and Ranichuri wards of Dudhouli, Kamalamai Municipality, Tinpatan and Hariharpurgadhi, Rural Municipality, Sindhuli. In Kyaneshwor, ward no. 08 of Hariharpurgadhi Rural Municipality most of the beneficiaries wants to change their agreement from retrofitting to reconstruction, but due to lengthy process they are in dilemma. After visiting the constructed compliant houses, our team advised DLPIU Engineers for the inspection of those completed timber frame houses for releasing 3rd tranche.

Almost houses of Hariharpurgadhi and Tinpatan Rural Municipality are timber framed hybrid structure with ground floor stone/brick masonry and first floor constructed with light material, however, some houses were load bearing structures (Stone Masonry in Cement/Mud Mortar, Brick Masonry in Cement Mortar).

- ❖ **On 19th Feb 2019 the ward level meeting was conducted in Hatpate, ward no. 02, Dudhouli Municipality, Sindhuli.**
 - Almost houses are constructed using timber structure with brick masonry in the ground floor and light structure in the first floor.
 - Although, construction of the houses is completed but are non-compliance due to late design approval of timber structure manual.
 - Re-survey was done only in limited area and could not addressed all the households, so beneficiaries are waiting for grievance address.
 - However, availability of timber is plenty in this area beneficiaries could not construct timber structure houses due to lack of knowledge on construction process.
- ❖ **On 19th Feb 2019 the ward level meeting was conducted in Harshahi, Nipane, ward no. 01, Dudhouli Municipality, Sindhuli.**
 - During re-survey technical staff could not cover all the area, so beneficiaries are waiting for grievance to be addressed.
 - Due to Elani land problem some beneficiaries could not start reconstruction yet.
 - Beneficiaries had constructed houses using timber structure but could not receive 3rd tranche yet.
 - Beneficiaries waiting for banking loan, but banks are not ready to serve loan process.

- Some houses were constructed before the deployment of DLPIU Engineers, which are non-compliance and according to them they could not correct those houses, NRA needs to address these types of problems.
- ❖ **On 21st Feb 2019 the ward level meeting was conducted in Bhimasthan, ward no. 02, Tinpatan Rural Municipality, Sindhuli.**
 - Due to plenty of availability of timber, beneficiaries are interested to construct timber frames structure houses.
 - Most of the beneficiaries wants to change from retrofitting to reconstruction, although they are unknown about the procedure.
 - About 75% beneficiaries are listed in retrofitting from the grievance list but are not ready retrofit their houses due that no exact retrofitting model.
- ❖ **On 22nd Feb 2019 the ward level meeting was conducted in Lampantar, ward no. 11, Tinpatan Rural Municipality, Sindhuli.**
 - Due to plenty of availability of timber, beneficiaries are interested to construct timber frames structure houses.
 - More than 40% houses are constructed using timber frame structure.
 - Some beneficiaries constructed their houses using timber structure but in traditional practice, now these houses are not included in the timber structure manual, so they are waiting to receive GON grant.
- ❖ **On 5th March 2019 the Palika level meeting was conducted in Hariharpurgadhi Rural Municipality.**
 - Seems lack of coordination between Palika members and technical staff regarding reconstruction
 - Palika action plan and district profile was uploaded to their website after the meeting
 - Grievance list not received yet, although few beneficiaries have signed the PA agreement
 - Beneficiaries are in big trouble due to banking process, banks are not giving priority for GON reconstruction grant
- ❖ **On 6th March 2019 the ward level meeting was conducted in Kyaneshwor, ward no. 08, Hariharpurgadhi Rural Municipality, Sindhuli.**
 - Beneficiaries are willing to change the agreement ie. Retrofitting to Reconstruction but technical staffs could not provide good coordination about the procedure
 - Very poor coordination between ward level and palika level
 - Mobility of technical staff in the field seems poor
 - Elani land problem, beneficiaries could not start the reconstruction yet
 - Beneficiaries have constructed their houses using timber structure but could not receive 3rd tranche
- ❖ **On 7th March 2019 the ward level meeting was conducted in Ranichuri, ward no. 11, Kamalamai Municipality, Sindhuli.**
 - Among 621 total beneficiaries 610 had received 2nd tranche and 375 beneficiaries had received 3rd tranche of GON housing grant
 - 11 household could not start the reconstruction yet due to topographical problem and inaccessible to transportation facility
 - 3 household of landless people were sent one year before from ward office to the NRA for granting land, but still could not address any solution
 - Beneficiaries are constructing their houses using timber frame structure, so progress status of receiving 3rd tranche seems slower

- Among 222 beneficiaries 206 were listed in grievance list, in which 51 HHs are in reconstruction and 155 HHs are in retrofitting

Housing Typology Report



The house belongs to Mrs. Laxmi Maya Pahadi, permanent residence of Hatpate, ward no. 02, Dudhouli Municipality, Sindhuli. She has received 2nd tranche of GON housing grant. The house is constructed using timber frame structure with 5-inch Brick in Cement Masonry (BMC) wall and light timber planks in first floor. The house is non-compliance, since there seems no adequate bracing between timber post and joists. Recommended for correction.



The house belongs to Mr. Netra Hari Bhandari, permanent residence of Nipane, ward no. 01, Dudhouli Municipality, Sindhuli. He has received 1st tranche of GON housing grant. The house is constructed using timber frame structure with 5-inch Brick in Cement Masonry (BMC) wall and light timber planks in first floor. The house was constructed before the deployment of DLPIU Engineers and is non-compliance due to L-shape.



The house belongs to Mrs. Hari Maya Sijali, permanent residence of Lampantar, ward no. 11, Tinpatan Rural Municipality, Sindhuli. She has received 2nd tranche of GON housing grant. The house is constructed using timber frame structure with 9-inch Brick in



The house belongs to Mr. Sitaram Ghimire, permanent residence of Bhimasthan, ward no. 02, Tinpatan Rural Municipality, Sindhuli. He has received 3rd tranche of GON housing grant. Construction of the house is completed and

Cement Masonry (BMC) wall and first floor is in under-construction. The house is L-shape and is recommended for correction to be eligible for receiving 3rd tranche.



The house belongs to Mr. Chandra Man Bholan, permanent residence of Chisapani, ward no. 01, Hariharpurgadhi Rural Municipality, Sindhuli. He has received 2nd tranche of GON housing grant. The house is constructed using timber frame structure with 14-inch Stone in Mud Mortar (SMM) wall. The house is in under construction.

after receiving 3rd tranche beneficiary modified his house by adding roof truss in the first floor without adequate support to vertical member.



The house belongs to Mr. Prem Bahadur Ghising, permanent residence of Chisapani, ward no. 01, Hariharpurgadhi Rural Municipality, Sindhuli. He has received 2nd tranche of GON housing grant. Construction of the house is completed using timber frame structure with Hollow Concrete Block (HCB) Masonry structure in ground floor. The house is non-compliance due to improper lacing and bracing of vertical post and horizontal joists.



The house belongs to Mr. Dip Kumar Ghising, permanent residence of Chisapani, ward no. 01, Hariharpurgadhi Rural Municipality, Sindhuli. He has received 2nd tranche of GON housing grant. Construction of the house is completed using timber frame structure with Stone in Cement Mortar (SMC) in ground floor and light timber planks in first floor. The house owner was advised to add cross bracing to make eligible for receiving 3rd tranche.



The house belongs to Mr. Chandra Prasad Pahadi, permanent residence of Hatpate, ward no. 02, Dudhouli Municipality, Sindhuli. He has received 2nd tranche of GON housing grant. Construction of the house is completed using timber frame structure with 5-inch Brick in Cement Mortar (BMC) wall in ground floor and first floor. The house is non-compliant due to heavy wall in first floor and was recommended for correction.

Case Story

CASE STORY

Dhansingh shifted into new house

Dhansingh Syangba (*grant agreement #20-36-8-0-12*) is very happy nowadays because his new house construction has been completed. Till the construction time, he was living in goat shed with his wife. He is permanent residence of Sunkoshi Rural Municipality Ward No. 7 locally known as Chalise Pokhari. The house was badly damaged by 2072 earthquake and demolished before constructing new house. He had constructed up to plinth level before SERVE project intervention.

When the technical team of SERVE visited his house, he was living in his old damaged house. He was not able to complete the newly constructed house due to elder. He was then informed about SERVE Project and top up support from Mercy Corps, then he agreed to complete the construction of new house. Also, he was informed about the governments housing grant and its timeframe.

He started constructing his house by technical support from Mercy corps. Dhansing also demolished the old house and used the stone and other materials to construct his new house. After completion, they have shifted into new house and had planned to use one room as kitchen and another as bed room. Mercy Corps (SERVE project) provided NPR 50,000/- top up support to Dhansingh to complete the construction.

