

Monthly District Report

Lalitpur, Bhaktapur

27 September - 21 October 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Lalitpur	General coordination meeting of POs working in Lalitpur district was organised by DLPIU GMALI Lalitpur office. The meeting was attended by Undersecretary Mr. Shiva Ram Gelal, Project Chief of DLPIU GMALI Lalitpur, subject specialist team of EHRP/GMALI Lalitpur, representatives of POs such as CIUD, Satya Sai Kendra, PIN/Durable Solutions, Love Green Nepal and Maya Foundation. Reconstruction initiatives forwarded by these POs was discussed in the coordination meeting.	30 Sept. 2019	DLPIU GMALI Office, Manbhawan, Lalitpur district	Mr. Yamnath Giri M & E Specialist DLPIU GMALI Lalitpur Manbhawan, Lalitpur Contact: 9851239785, yamnathgiri2014@gmail.com	Meeting minute
	DLPIU GMALI Lalitpur organized an interaction program on preparing action plan to track the reasons of delays in accessing 2 nd tranche and 3 rd tranche by beneficiaries of Bhaktapur district further. The program was attended by NRA CEO, elected local heads, heads and heads of CLPIUs (Building and GMALI), DLPIU Building, focal engineers and media personnel.	18 Oct. 2019	Entrance Café, Pulchowk	Mr. Yamnath Giri M & E Specialist DLPIU GMALI Lalitpur Manbhawan, Lalitpur Contact: 9851239785, yamnathgiri2014@gmail.com	
	HRRP Lalitpur district team joined NRA DLPIU GMALI Lalitpur in Joint M & E visit at Ward no 9 (Chyasal) and Ward no 17 (Lukhusi), Lalitpur Metropolitan City, Lalitpur district. Ward coordination meeting was organised with Ward Chief of Ward no 9 & 17 where issues of delays in accessing 2 nd and 3 rd tranche by beneficiaries was discussed. The team also observed reconstruction status of 4 houses in Ward no 17.	21 Oct. 2019	Ward no 9 & 17, Lalitpur Metropolitan City, Lalitpur district	Mr. Yamnath Giri M & E Specialist DLPIU GMALI Lalitpur Manbhawan, Lalitpur Contact: 9851239785, yamnathgiri2014@gmail.com	field visit section, ward-level meeting minute
	Tranche status of Lalitpur updated to GD sheet in Palika Profile	21 Oct. 2019		Sachin Malego IM Officer, HRRP	
	Preparation of Ward wise GIS maps of Ward no 9 & 17, Lalitpur Metropolitan City	21 Oct. 2019			
	Contact list update, 5 W update, upload of shelter photos	18 Oct. 2019		Sachin Malego IM Officer, HRRP Ms. Ambika Amatya District Coordinator	
	Tranche Maps Prepared of Lalitpur	21 Oct. 2019		Sachin Malego IM Officer, HRRP	

Summary of events during this period

	Palika Profile Updated Lalitpur	24 Sept. 2019		Sachin Malego IM Officer, HRRP	
				Ms. Ambika Amatya District Coordinator	
Bhaktapur	Contact list update, 5 W update, upload of shelter photos	21 Oct. 2019		Sachin Malego IM Officer, HRRP	
				Ms. Ambika Amatya District Coordinator	
	Tranche Maps Prepared of Bhaktapur	21 Oct. 2019		Sachin Malego IM Officer, HRRP	
	Palika Profile Updated Bhaktapur	18 Oct. 2019		Sachin Malego IM Officer, HRRP	
				Ms. Ambika Amatya District Coordinator	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Joint M & E visit to observe reconstruction efforts of beneficiaries in Bhaktapur and Lalitpur districts	November 2019/ Various wards of Municipalities of Lalitpur and Bhaktapur district	DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team	District Coordinator HRRP Lalitpur and Bhaktapur Cluster
General Palika level and Ward level meeting and consultation with elected ward officials over the reconstruction progress and status of the visited wards of Bhaktapur and Lalitpur district	November 2019/ Various wards of Municipalities of Lalitpur and Bhaktapur district	DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team	

News & Updates


- DLPIU Building Bhaktapur and Lalitpur are engrossed in providing orientation and information on suitable retrofitting measures to beneficiaries in retrofitting list. Retrofitting task force has been formed under lead of District Support Engineers in each district to provide relevant orientation and information dissemination on retrofitting measures. The task force are also involved in observing damage status of houses in retrofitting list.
- DLPIUs (GMALI and Building) Bhaktapur and Lalitpur are involved in tracking reasons of delays in accessing 2nd tranche and 3rd tranche by beneficiaries who are enrolled in partnership agreement with NRA and those who have taken 1st tranche. Further, DLPIU Building are also tracking reasons of delaying in rebuilding of houses by beneficiaries who have accessed 1st tranche only.

Tranche Status (Lalitpur)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	3361	3370	3138	3127	2642	2126	252	197	180	0
Godawari Nagarpalika	10950	9604	8062	7999	2868	2365	323	136	133	0
Konjyosom Gaunpalika	2580	2156	2086	2082	1947	1448	372	328	319	0
Lalitpur Mahanagarpalika	6594	7408	6357	6338	1374	887	275	125	120	0
Mahalaxmi Nagarpalika	4409	3669	3132	3105	1056	903	83	53	50	0
Mahankal Gaunpalika	2451	2271	2239	2238	1837	1260	61	58	57	0

Graph of Tranche Status:

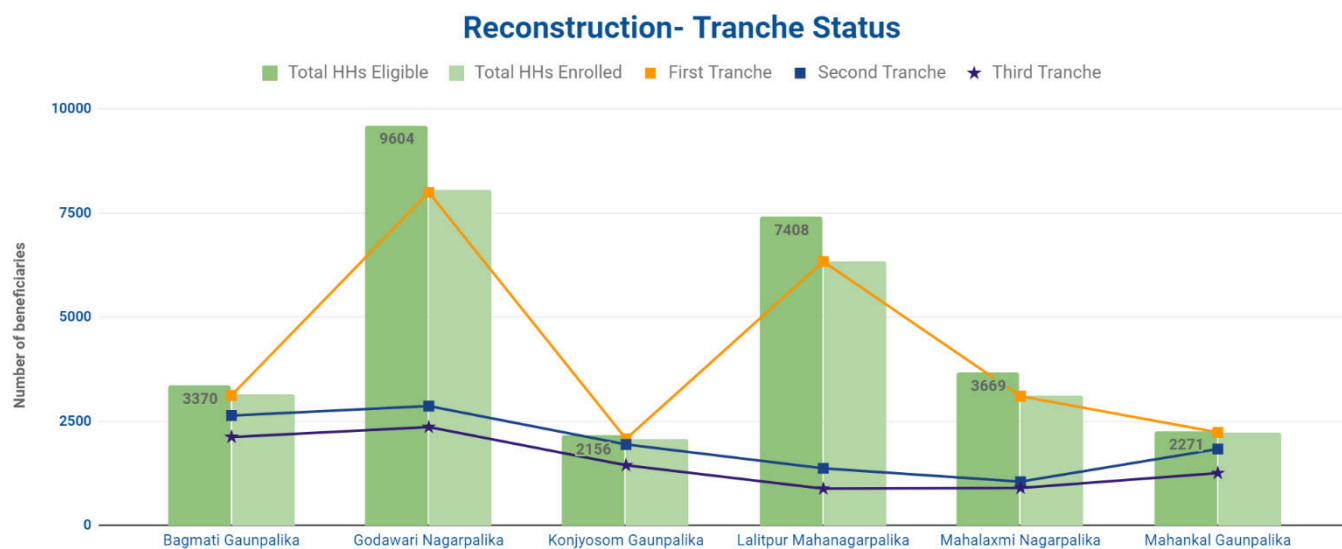

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

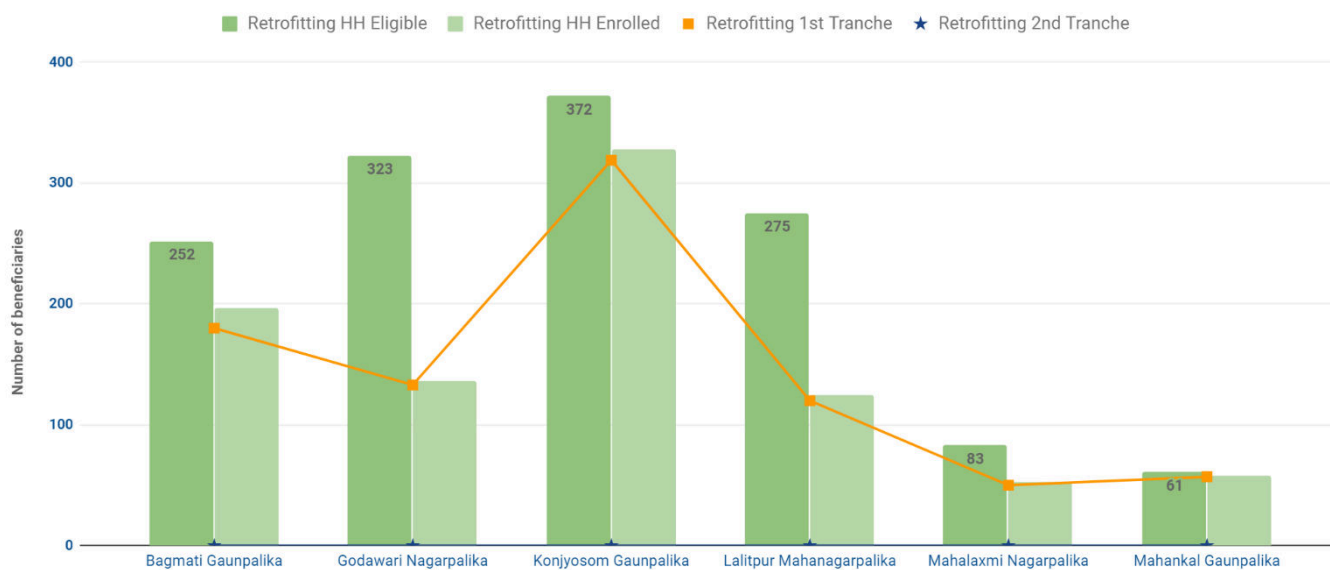

Tranche Status (Bhaktapur)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bhaktapur Nagarpalika	8175	7656	5637	5637	1822	1634	161	43	43	0
Changunarayan Nagarpalika	11059	11000	9826	9826	3788	3660	212	109	109	0
Madhyapur Thimi Nagarpalika	3015	2333	2080	2080	727	706	95	61	61	0
Suryabinayak Nagarpalika	7948	7425	6998	6998	2982	2818	234	105	105	0


Graph of Tranche Status:

Reconstruction- Tranche Status



Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

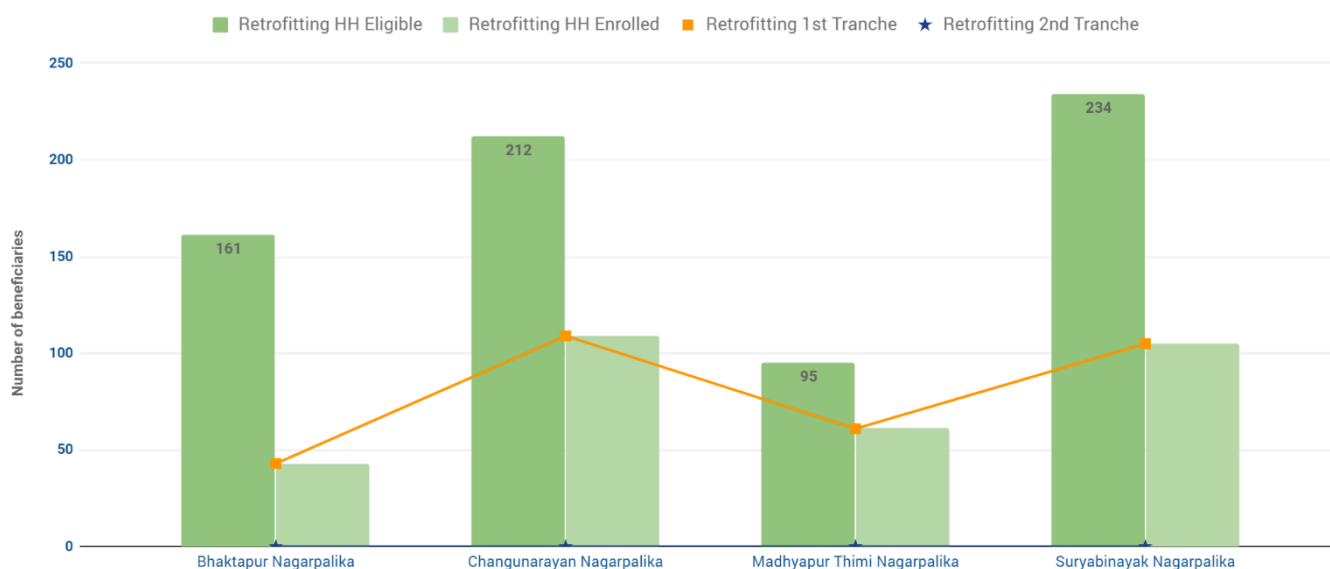

Field Visit Reports (Lalitpur)

Visit 1

Date	Location	Participants
21 October 2019	Ward no. 9 & 17, Lalitpur Metropolitan City Municipality, Lalitpur district	- Ambika Amatya, District Coordinator, HRRP Lalitpur Cluster - Sabi Shrestha, Focal Engineer, DLPIU Building Lalitpur - Sudha Ghimire, Engineer, Lalitpur Metropolitan City - Jyoti Bastola, Engineer, Lalitpur Metropolitan City - Krishna Chalauni, Engineer, DLPIU Building Lalitpur - Sneha Malani, Urban Reconstruction Volunteer, HRRP
Objective(s)	- To discuss on reconstruction progress, issues and challenges in Ward no 9 & 17, LMC - To observe reconstruction status and progresses of beneficiaries in Ward no 9 & 17, LMC	

- To provide feedbacks and way forward to Ward about reconstruction initiatives taking place in Ward no 9 & 17.

Summary

HRRP Lalitpur Coordination Team along with representatives of DLPIU Building Lalitpur and NRA Engineers of Lalitpur Metropolitan City conducted joint field visit in Ward no 17. The field visit team observed nearly 4 houses in total. All of the observed houses are made with RCC technology and above 4 storeys.

Meeting with Ward Chief, Ward no 9, Chyasal, Lalitpur Metropolitan City

Total Beneficiaries	267
PA enrolled	245
1st tranche	245
2nd tranche	83
3rd tranche	33
Retrofitting	9
Retrofitting- enrolled beneficiary	3
Retrofitting 1 st tranche	3

The Ward no 9 has 245 beneficiaries under full reconstruction however only 83 of them have accessed 2nd tranche and 3rd tranche were taken by 33 beneficiaries. The key reconstruction issues persisted in Ward no 9 is related with small parcel land holdings, multiple beneficiaries belonging to same houses, family disputes as well as disputes with neighbours (eccentric footing of quake damaged & non-quake damaged houses), difficulty in transportation of removing rubbles and poor economic financial condition of beneficiaries. The non compliance issues of houses in Ward no 9 is related with addition of storeys after accessing 3rd tranche, houses are rebuilt not as per the drawing and have not followed minimum requirements properly.

To address the small parcel land holdings, ward office has requested for need of proper guidelines for houses with very small plot size – 1 *paisa jagga* (such as in 85.5 square feet). The visit team stressed Ward Chair to track exact reasons of delays in reconstruction by beneficiaries who have accessed 1st tranche only.

Meeting with Ward Chief, Ward no 17, Lukhusi, Lalitpur Metropolitan City

Total Beneficiaries	161
PA enrolled	154
1st tranche	153
2nd tranche	57
3rd tranche	33
Retrofitting	14
Retrofitting- enrolled beneficiary	5
Retrofitting 1 st tranche	3

The Ward no. 17 has 161 beneficiaries under full reconstruction however only 57 of them have accessed 2nd tranche and 3rd tranche were taken by 33 beneficiaries. Ward Chief revealed there is good rate of reconstruction of houses in the Ward as majority of houses that were fully damaged by earthquake 2015 have been reconstructed. The houses that are left out in reconstruction are partially damaged houses, houses that are undergoing issues of multiple beneficiaries with land ownership issues, eccentric footing of quake damaged houses and the vulnerability posed to non-quake damaged houses and disputes among family members. Majority of beneficiaries have reconstructed their houses by selling their family property (land) and very few had taken banking loans in regular interest rates.

Ward Chief revealed that beneficiaries in retrofitting list are uninteresting to retrofit their houses as proper information on suitable retrofitting measures have not been reached to them. Further, beneficiaries prefer full reconstruction of their houses instead of conducting retrofitting.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Challenges / Issues Identified	Solutions Provided
Advantages of retrofitting processes have not been sufficiently reached to beneficiaries' level (ground level).	There is need of adequate orientation and information dissemination on retrofitting process among beneficiaries and in communities as a whole.	Retrofitting task force by DLPIU Building office have targeted orientation and site visits for disseminating key messages of retrofitting procedures.	Advantages of retrofitting processes have not been sufficiently reached to beneficiaries.	There is need of adequate orientation and information dissemination on retrofitting process among beneficiaries and in communities as a whole.

Photos

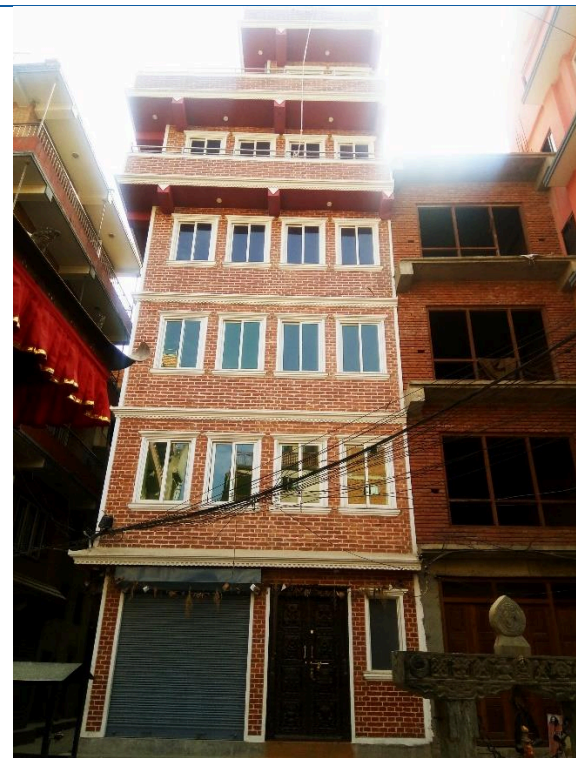


Image: Mr. Bagacha Maharjan, Ward no 17, Lukhusi, Lalitpur Metropolitan City. 5 ½ storey RCC framed structure house has received all three tranches from government. However after accessing 3rd tranche, the owner has added extra storeys (1.5 storeys). The engineer advised that the house will not receive construction completion certificate.



Image: Ward no 17, Lukhusi, Lalitpur Metropolitan City. 5 ½ storey RCC framed structure house has received upto 2nd tranche. The owner has added extra storeys which was not mentioned in building permit (not as per drawing), further 1 room has been added in cantilever side.

a

Housing Typology Report (Max 4 Photos, Select best photos from each district)



Beneficiary name: Santa Bishunke, Ward no 3, Changunarayan Municipality has non compliance structure of 9"x12" column which came out unsafe during analysis. The structure was completed immediately after earthquake.



Beneficiary name: Shyam Krishna Nepal, Ward no 7, Changunarayan Municipality has structure of confined masonry. The house was terms non compliance as the structure is not as per the building drawing. The beneficiary is still using the damaged house after repair and maintenance.



Beneficiary Name: Surya Bahadur Gole, Ward no 4, Kaleshwor, Mahankal Rural Municipality. One storey plus attic SMM structure with RC bands has cemented front finishing



Beneficiary Name: Hari Prasad Dahal, Kaleshwor, Ward no 4, Mahankal Rural Municipality. One story plus attic SMM structure with RC bands has received upto 2nd tranche. The owner has requested for 3rd tranche during the time of inspection.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Disputes among family members for division of land ownership is the key reasons of delays in reconstruction of houses by interested beneficiaries. How such land issues can be solved?	PO representative	NRA has solved many kinds of land related cases therefore methods documentation or as -built recording system (<i>abhilekhikaran</i>) and community/public inquiry deed (<i>sarjamin</i>) is among the key process to address land issues that has triggered delays in reconstruction and division of family property from ages. Ward offices are also responsible to forward relevant discussion among family members for land issues. (M & E Specialist, DLPIU GMALI)

Challenges and Way Forward

Challenge	Way Forward
Addition of extra storeys after accessing 3 rd tranche has in fact raised question over resiliency of houses.	Building permit approval and number of needful storeys are provided on the basis of size of land. Any addition in the storeys in fact increases risk of the rebuild houses. Ward offices should be responsible in disseminating key messages of risks and threats of adding extra storeys other than mentioned in the building drawing. Concerned ward office and municipality office should properly disseminate information of abiding by the building bylaws. The key messages of constructing resilient structures should be the highlighted in information sharing sessions by Ward office.
