

Activity Report

Joint Monitoring Field Visit to Sunkoshi Rural Municipality Sindhuli 15th May 2019

Background:

Housing Recovery and Reconstruction Platform (HRRP) Nepal has been working in the 32 districts which were highly and moderately affected by the devastating Gorkha earthquake of April 2015. HRRP has been providing coordination support services to the NRA in the national Level and DLPIU-GMALI and DLPIU-Building in the district level. To observe the status of reconstruction and provide necessary solutions in the local level HRRP has initiated the joint monitoring field visit in the Rural Municipalities where the problems are high regarding the reconstruction. The joint monitoring team comprises of the district stakeholders which are related to private housing reconstruction (DLPIU-GMALI and DLPIU Building), M&E consultant, DSE, POs and other stakeholders when required.

Objective:

- To observe the reconstruction status of the Rural Municipality
- To interact with the local authorities regarding the reconstruction
- To discuss regarding the pending caseload
- To appoint the focal person of the Rural Municipality
- To discuss regarding the resurvey and reverification
- To collect housing typology

Team involved in visit:

S.No.	Name	Designation	Organization
1	Prabhakar Lal Karn	Project Chief	DLPIU-Building
2	Kiran Mahat	M&E Consultant	CLPIU-Building
3	Dinesh Sanjel	District Support Engineer	DLPIU-Building
4	Pramod Kumar Sah	Focal Person	DLPIU-Building
5	Tulasi Ram Lamichhane	District Technical Coordinator	HRRP

Highlights of visit:

The field visit to Sunkoshi Gaupalika was organized in 15th May 2019 to identify the status of reconstruction, issues and challenges of reconstruction, interaction with the ward chairpersons, palika chief and Pos regarding private housing reconstruction. The meeting was conducted in the meeting hall of the Rural Municipality. The meeting was chaired by the Chairperson of the Rural Municipality Ms Dipa Bohora. The program was facilitated by focal person of DLPIU Building Mr. Pramod Kumar Sah. The program started with the introduction of the participants. After then the issues were discussed on the ward level. The ward chairperson and the ward representatives talked about the status of their respective wards.

• Ward No. 1:

- The genuine beneficiaries are still missing in the beneficiaries list.
- Very few grievances have been addressed
- The previous grievances are still not still solved.

• Ward No. 2:

- 2 Households were constructed before the arrival of the technical persons
- Still the process for conversion to beneficiaries from retrofitting has not been solved despite of sending the letter for central NRA long time past.
- **Ward No. 3:**
 - 25 Households were constructed before arrival of the technical persons
 - Houses expanded in height after receiving the third tranche
 - Confusion in the right of way allocated by Rural Municipality and the Nepal Government.
 - With same typologies one is provided with tranche and next is not.
 - Updates regarding the reconstruction must be provided on timely basis.
- **Ward No. 4:**
 - 2 houses constructed before arrival of technical persons
 - 2 houses with excess attic height
 - Vulnerable houses have been constructed by Mercy Corps
 - 2 house owners have died before receiving the 3rd tranche whose nominees are in beneficiaries list.
 - 2 house owners have migrated from neighboring districts but the gaupalikas are attached with sunkoshi gaupalika. They are the beneficairees of the previous gaupalika and want to reconstruct in sunkoshi gaupalika
- **Ward No. 5:**
 - 38 real beneficiaries missing in the beneficiaries list
 - 3 retrofitting beneficiaries have applied for beneficiary's conversion
- **Ward No. 6:**
 - NRCS have provided STA and financial support in the reconstruction
 - 9 households have not received the tranche due to right of way
 - 4 house owners have applied for appellate against the decision of having another house
 - No proper correction provided to the 5 households
 - Tranche of Bhakta Bahadur Karki has been halted due to the excess opening
- **Ward No. 7:**
 - No detail information regarding the new grievance has been provided via radio

Discussion of resurvey and Reverification

- The house owners who have been involved in previous grievances are not eligible for this resurvey and reverification
- This will be the final round of resurvey and reverification
- The number of engineers involved in the resurvey and reverification is limited by resources and persons which is difficult to conduct. So, the resource and number of engineers must be added.

Case Load

The project Chief of DLPIU directed the engineers no to hold the case load and process them as soon as possible. The DLPIU Building will provide necessary action for the case load support if required.

Focal Person Assignment


Pujan Raj Shrestha has been assigned as the focal person for the Sunkoshi Gaupalika.

Closing Remarks from Palika Chairperson

- Resurvey and Reverification engineers will be provided with some support from Rural Municipality
- Engineers and Ward elected members both must work for public welfare

- Sharing program between Gaupalika and technical persons will be conducted periodically
- Involvement of ward chairperson in resurvey group to minimize the errors
- Uniformity of guidelines within the district

Reconstruction Status:

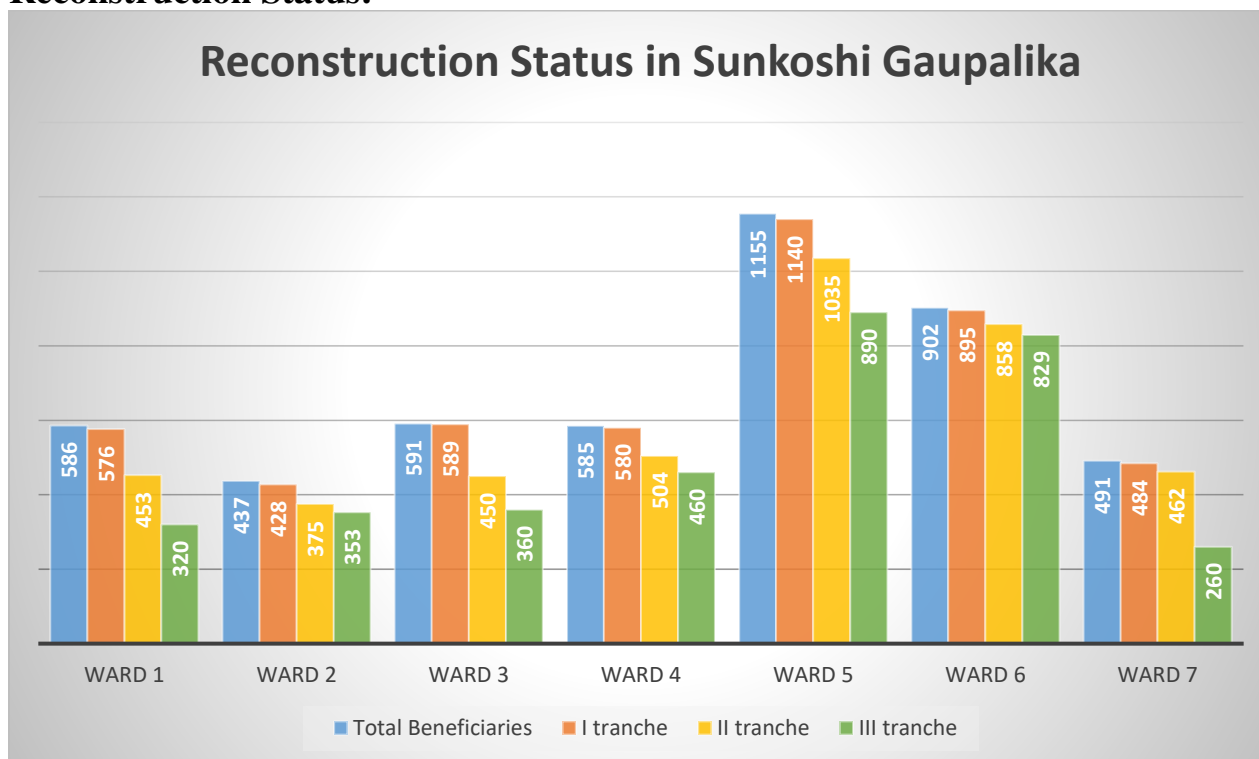

S.No.	Ward No	Total Beneficiaries	I tranche	I tranche %	II tranche	II tranche %	III tranche	III tranche %
1	1	586	576	98.29	453	77.3	320	54.61
2	2	437	428	97.94	375	85.81	353	80.78
3	3	591	589	99.66	450	76.14	360	60.91
4	4	585	580	99.15	504	86.15	460	78.63
5	5	1155	1140	98.70	1035	89.61	890	77.06
6	6	902	895	99.22	858	95.12	829	91.91
7	7	491	484	98.57	462	94.09	260	52.95
Average				98.79		86.32		70.98

Attendees:

S.No.	Name	Organization	Designation	Gender	Contact No.	Email
1	Deepa Bohora	Sunkoshi RM	Chairperson	F	9844082014	dipabohora2018@gmail.com
2	Dirba Singh Moktan	Sunkoshi RM	Vice Chairperson	M	9841230660	dsmuktan2018@gmail.com
3	Prabhakar Lal Karn	DLPIU Building	Project Chief	M	9854041543	maxplk26@gmail.com
4	Krishna Raj Dahal	Sunkoshi RM-5	Ward Chairperson	M	9841416364	krishnaraj@gmail.com
5	Sapna Pradhan	Mercy Corps	SPO	F	9851163960	sapradhan@mercy Corps.org
6	Khil Prasad Chaulagain	Sunkoshi RM-4	Ward Secretary	M	9864029241	
7	Dipesh Karki	DLPIU Building	Engineer	M	9827793050	dipeshkarki477@gmail.com

8	Prabin Siwakoti	DLPIU Building	Sub Engineer	M	9849791177	prawinme2050@gmail.com
9	Bikash Yadav	DLPIU Building	Engineer	M	9844030170	bikashy51@gmail.com
10	Rajpati Yadav	DLPIU Building	Engineer	M	9660801888	rajcee09@gmail.com
11	Sunil Kumar Yadav	DLPIU Building	Sub Engineer	M	9863433357	Sunilpky49@gmail.com
12	Bhuwan Kumar Singh	DLPIU Building	Asst. Sub Engineer	M	9842859930	
13	Kiran Kumar Mahat	CLPIU Building	M&E Consultant	M	9841500163	kiranmahat@hotmail.com
14	Dinesh Sanjel	DLPIU Building	DSE	M	9803179520	dinesh_olg@yahoo.com
15	Shankar Jargha	Sunkoshi RM		M	9869626660	
16	Ramchandra Acharya	Sunkoshi RM	Ward Chairperson	M	9864029440	
17	Lal Bahadur Gole	Sunkoshi RM-7	Ward Chairperson	M	9844177612	
18	Kumar Bhandari	CDP Sindhuli	Program Coordinator	M	9851257333	cdpsnepal@gmail.com
19	Gorakh Khadka	Sunkoshi RM-6	Ward Secretary	M	9844254080	
20	Rhaghvendra Kumar Sah	DLPIU Building	Sub Engineer	M	9807716117	raghbendrasah30@gmail.com
21	Binod Poudel	DLPIU Building	Asst. Sub Engineer	M	9844228610	bpmanthali@gmail.com
22	Indrakala Thapa	DLPIU Building	Asst. Sub Engineer	F	9842245226	
23	Rama Khadka	DLPIU Building	Asst. Sub Engineer	F	9861527881	
24	Ronal Adhikari	DLPIU Building	Engineer	M	9849042021	adhikarironal@gmail.com
25	Bhawesh Gajurel	DLPIU Building	Engineer	M	9849149247	gajurel44@gmail.com
26	Khagendra Prasad Joshi	DLPIU Building	Asst. Sub Engineer	M	9846541305	Khagendrajoshi98765@gmail.com
27	Uddhav Raj Chaulagain	Sunkoshi RM-3	Ward Secretary	M	9754202240	
28	Rudra Bahadur Bhandari	Sunkoshi RM-7	Ward Secretary	M	9844019868	
29	Tulasi Ram Lamichhane	HRRP	DTC	M	9851213610	techcord.ramechhap@hrrpnepal.org
30	Pujan Raj Shrestha	DLPIU Building	Engineer	M		
31	Pramod Kumar Sah	DLPIU Building	Focal Person	M	9849205849	pujan_93@hotmail.com

Housing Typology



The house of Dirgha Raj Puri, resident of Sunkoshi Rural Municipality-3, Jhangajhuli has constructed his house. The house is constructed using brick in cement mortar. The RC bands have been provided to the house. The house is provided with the RC Slab. There are two rooms in the house. The house has been constructed under the technical support of Mercy Corps. The house owner has received second tranche of reconstruction grant. The house owner is one of the beneficiaries of vulnerable group.



The house of Saraswati Kafle Puri, resident of Sunkoshi Rural Municipality-3, Jhangajhuli has constructed his house. The house is constructed using stone in mud mortar. The RC bands have been provided to the house. The house is provided with the flexible Slab. There are two rooms in the house. The house owner has received all three tranches of reconstruction grant.



The house of Sukumaya Majhi, resident of Sunkoshi Rural Municipality-3, Majhi Tole has constructed his house. The house is constructed using brick in cement mortar. The RC bands have been provided to the house. The house is provided with the flexible roof. There is single room in the house. The house has been constructed under the technical support of Mercy Corps. The house owner has received second tranche of reconstruction grant. The house owner is one of the beneficiaries of vulnerable group.



The house of Shyam Kumar Majhi, resident of Sunkoshi Rural Municipality-3, Majhi Tole has constructed his house. The house is constructed using brick in cement mortar. The RC bands have been provided to the house. The house is provided with the RC Slab. There are two rooms in the house. The house owner has received second tranche of reconstruction grant.

Photos:



Meeting being conducted in the premises of Sunkoshi Rural Municipality



Project Chief of DLPIU Building addressing the questionnaires raised by the ward chairperson.

Issues and Challenges:

- The house owners are expanding their houses in vertical direction after receiving the third tranche.
- As the number of grievances is higher, the number of engineers assigned for the resurvey and reverification process is too low so that the resurvey and reverification will not be completed in allocated time.
- The grievance management has not been completed in time which make the confusion in the new resurvey and reverification.
- The conversion decision from retrofitting to reconstruction beneficiaries has not been provided leaving the people living in vulnerable houses
- The conflict between Central Government and local government regarding the right of way of BP highway is prevailed. The National government has allocated 25 meters right of way from center while the local government has decided it to be 15 meters from center and forwarded those houses for construction.
