

Monthly District Report

Dhading, Gorkha, Arghakhanchi, Gulmi, Palpa

14 June - 14 July 2019

Summary of events during this period					
Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Gorkha	Access to Finance – Sakchayam launched its project activities in Gorkha in presence of GMALI, HRRP, POs and district level stakeholders. Click here for details.	2 nd July 2019	Gorkha	chandra.gurung@hrrpnepal.org , manisha.rai@hrrpnepal.org	Key points
	NRA/CLPIU visit to Gorkha and had interaction meeting with GMALI and DLPIUs was held. Click here for details.	10 th July 2019	Gorkha	gorkha@hrrpnepal.org ; badri.pyakurel@hrrpnepal.org	Key points and minute
	HRRP visited district level POs: DFID, Mott MacDonald/Purnima, JICA/EHRP & GoI/NHRP.	3 rd July 2019	Gorkha	chandra.gurung@hrrpnepal.org , manisha.rai@hrrpnepal.org	Key points
Dhading	GMALI/HRRP NGO coordination meeting is held in Dhading. Click here for details.	18 June 2019	Dhading	chandra.gurung@hrrpnepal.org , dhading@hrrpnepal.org	Key points and meeting minute
	NSET observed its 26 th anniversary by organizing an stakeholders meeting	18 June 2019	Dhading	chandra.gurung@hrrpnepal.org , dhading@hrrpnepal.org	
	MEAL report for the month of June submitted	8 th July 2019	Dhading	chandra.gurung@hrrpnepal.org ,	
Gulmi	Palika level coordination meeting conducted at Chatrakot Rural	12 th July 2019	Gulmi	chandra.gurung@hrrpnepal.org ; ishor.neupane@hrrpnepal.org	Field visit section & meeting minute

Summary of events during this period

	Municipality. Click here for details				
	Municipal level coordination meeting conducted at Musikot Urban Municipality. Click here for details.	14 th July 2019	Gulmi	chandra.gurung@hrrpnepa.org ; ishor.neupane@hrrpnepal.org	Field visit section & meeting minute
	District Reconstruction Coordination & Facilitation Meeting was held in DCC, Gulmi. Click here for details.	14 th July 2019	Gulmi	chandra.gurung@hrrpnepa.org ; ishor.neupane@hrrpnepal.org	Key points and meeting minutes
Arghakhachi	Palika level coordination meeting conducted at Malarani Rural Municipality. Click here for details.	7 th July 2019	Arghakhachi	chandra.gurung@hrrpnepa.org ; ishor.neupane@hrrpnepal.org	Field visit section & minute
	Palika level coordination meeting conducted at Chhatradev Rural Municipality. Click here for details.	8 th July 2019	Arghakhachi	chandra.gurung@hrrpnepa.org ; ishor.neupane@hrrpnepal.org	Field visit section & minute
	Interaction meeting with Shandikharkha Urban Municipality. Click here for details.	9 th July 2019	Arghakhachi	chandra.gurung@hrrpnepa.org ; ishor.neupane@hrrpnepal.org	Key points
	District Reconstruction Coordination and Facilitation Meeting completed at DCC, Hall. Click here for details.	9 th July 2019	Arghakhachi	chandra.gurung@hrrpnepa.org ; ishor.neupane@hrrpnepal.org	Key points & meeting minute

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Palika level coordination meeting at Gulmi Durbar Rural Municipality	15 July 2019	HRRP/GMALI	chandra.gurung@hrrpnepal.org , ishor.neupane@hrrpnepal.org


Palika level coordination meeting and joint monitoring field visit to RuRu Rural Municipality	16 July 2019	HRRP/GMALI	chandra.gurung@hrrpnepal.org , ishor.neupane@hrrpnepal.org
Field visit to support reconstruction facilitation in Palpa	18 – 22 July 2019	HRRP/GMALI	chandra.gurung@hrrpnepal.org , ishor.neupane@hrrpnepal.org

Tranche Status (Gorkha)


Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche
Aarughat Gaunpalika	7188	6748	6603	6603	6348	5678	168	67	71
Ajirkot Gaunpalika	4175	4087	3959	3959	3842	3582	62	2	3
Bhimsen Gaunpalika	6758	6669	6583	6583	6347	5208	167	35	35
Chum Nubri Gaunpalika	2750	2268	1944	1944	1626	1459	49	7	7
Dharche Gaunpalika	3683	3894	3713	3713	3399	3158	280	89	86
Gandaki Gaunpalika	6281	5176	4810	4810	4313	3356	443	43	42
Gorkha Nagarpalika	13107	9108	8724	8724	8255	7819	1097	706	680
Palungtar Nagarpalika	11726	8700	8156	8156	7288	6194	1100	567	546
Sahid Lakhani Gaunpalika	7901	6227	6063	6063	5606	5034	831	28	31
Siranchok Gaunpalika	7203	5924	5840	5840	5643	5108	911	39	42
Sulikot Gaunpalika	7302	7021	6851	6851	6712	6464	181	2	2

Graph of Tranche Status:

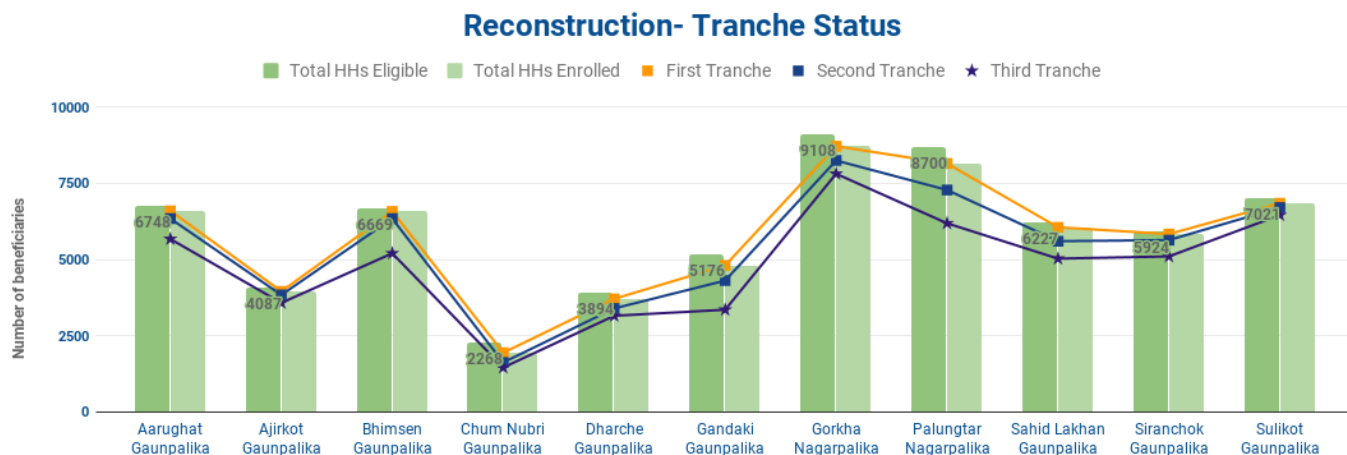

Graph for Retrofitting Status:

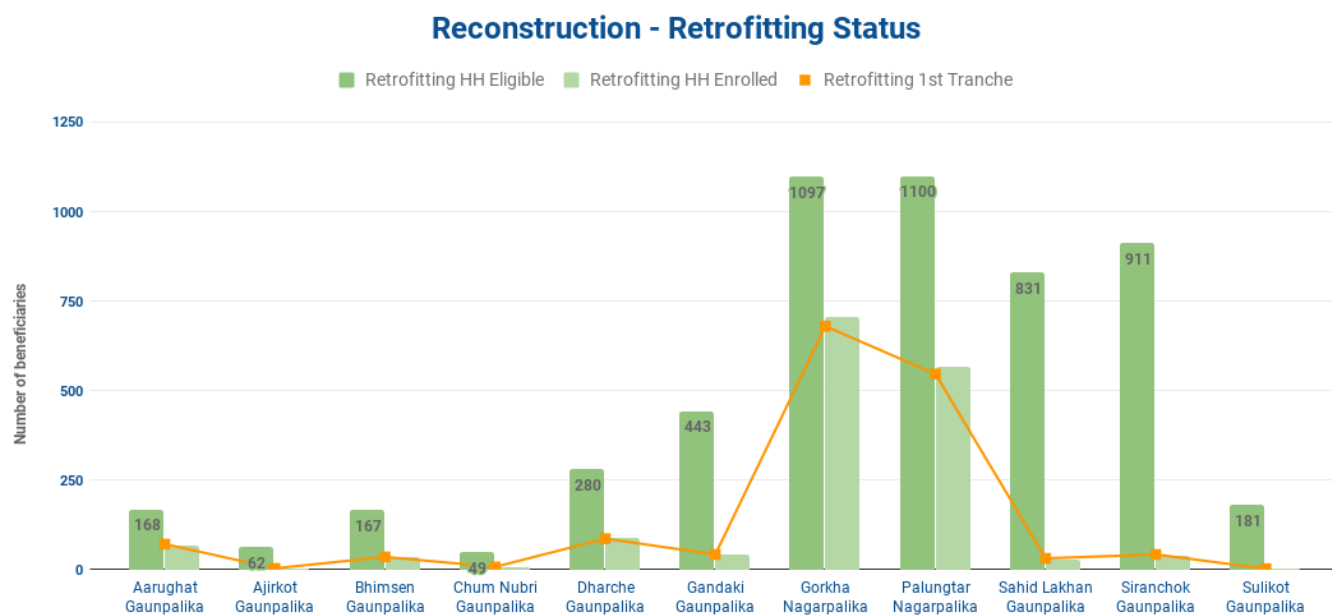


Tranche Status (Dhading)


Tranche Status Table

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Benighat Rorang Gaunpalika	7010	4891	4586	4586	3942	3114	647	107	107	0
Dhunibesi Nagarpalika	8212	7471	6893	6893	5431	4344	109	30	30	0
Gajuri Gaunpalika	6480	5215	4858	4858	4367	3417	520	115	115	0
Galchi Gaunpalika	6661	6419	6076	6076	5376	3859	327	67	67	0
Gangajamuna Gaunpalika	6532	6701	6595	6595	6056	5269	42	6	6	0
Jwalamukhi Gaunpalika	7255	5442	5176	5176	4525	3466	1110	96	96	0
Khaniyabash Gaunpalika	3485	3621	3545	3545	3216	2484	12	10	10	0
Netrawati Gaunpalika	4122	4000	3841	3841	3568	3148	57	14	14	0
Nilakantha Nagarpalika	15239	12978	12317	12317	10889	9041	640	92	92	0
Rubi Valley Gaunpalika	3164	3083	2971	2971	2476	2092	187	103	103	0
Siddhalek Gaunpalika	6277	5656	5326	5326	4679	3930	538	26	26	0
Thakre Gaunpalika	8017	6506	6198	6198	5507	4415	274	66	66	0
Tripura Sundari Gaunpalika	6668	6319	6120	6120	5264	3950	248	99	99	0

Graph of Tranche Status

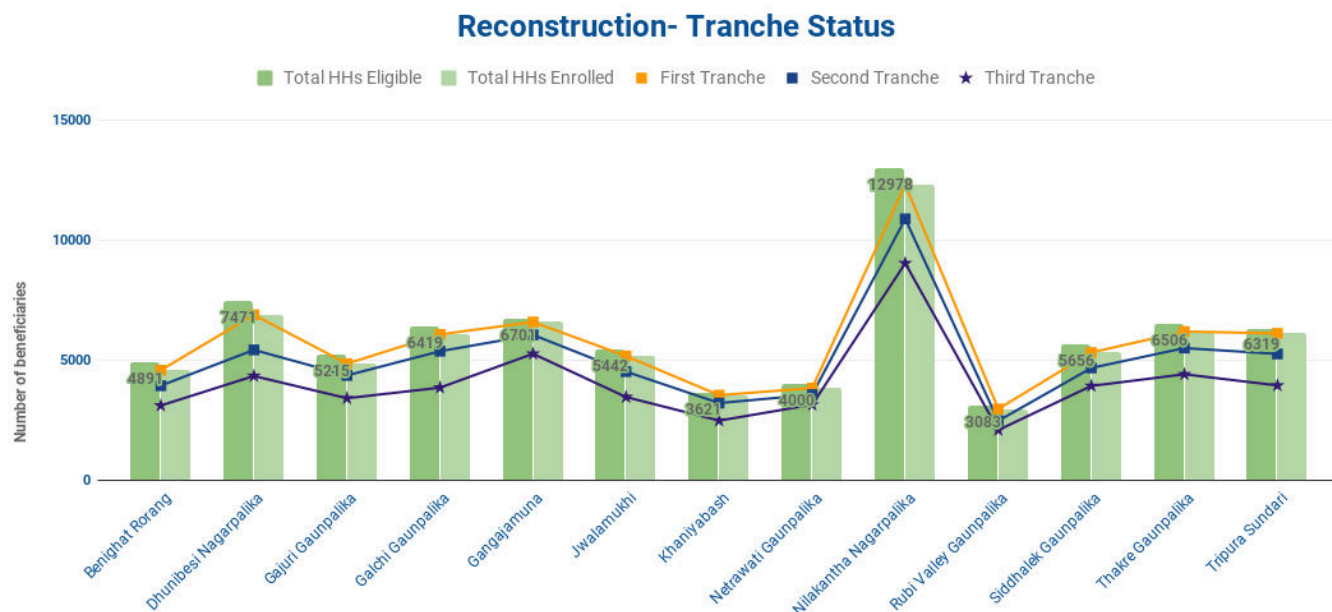

Graph for Retrofitting Status:

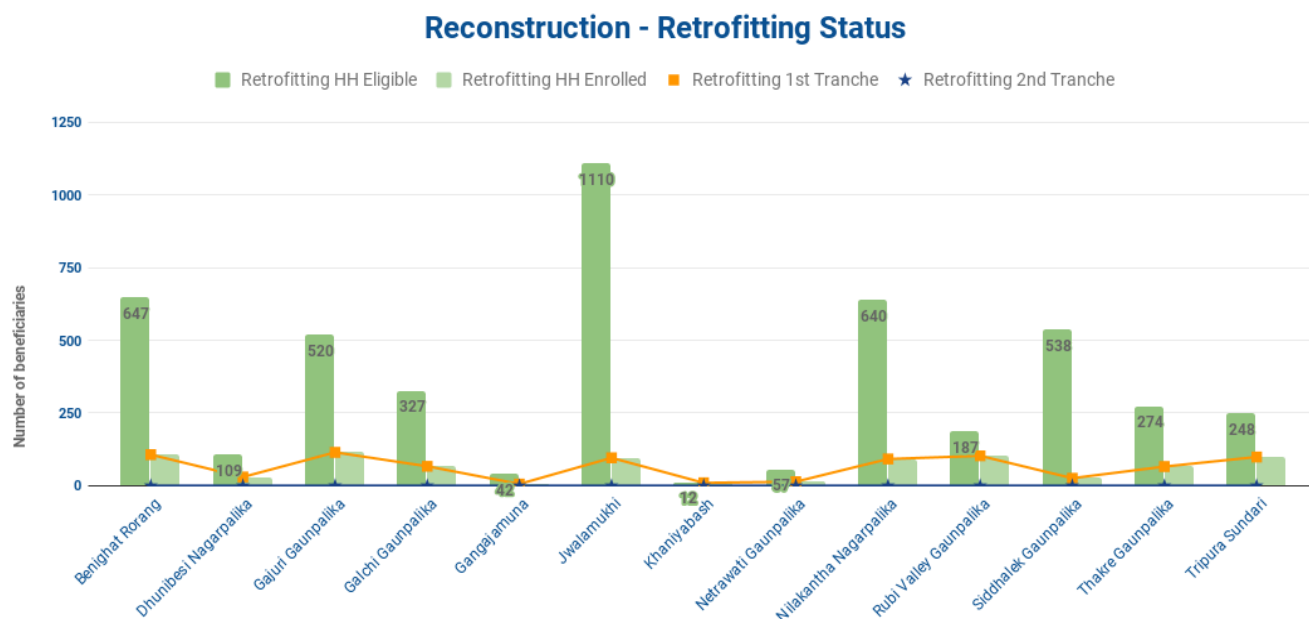


Tranche Status (Gulmi)

Tranche Status Table

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	1 st Tranche	2 nd Tranche	3 rd Tranche	Ret HH Eligible
Chandrakot Gaunpalika	359	289	238	222	61	46	32
Chatrakot Gaunpalika	297	213	213	208	132	70	60
Dhurkot Gaunpalika	1047	475	450	450	266	60	33
Gulmidarbar Gaunpalika	271	166	172	157	113	61	20
Isma Gaunpalika	138	111	111	111	66	19	1
Kaligandaki Gaunpalika	1823	1070	1036	1036	817	537	101
Madane Gaunpalika	257	123	123	123	109	71	1
Malika Gaunpalika	103	77	73	73	46	27	0
Musikot Nagarpalika	1168	754	712	694	263	150	14
Resunga Nagarpalika	306	178	174	174	154	68	2
Ruru Gaunpalika	439	289	289	279	166	131	7
Satyawati Gaunpalika	842	556	556	434	239	173	23

Graph of Tranche Status

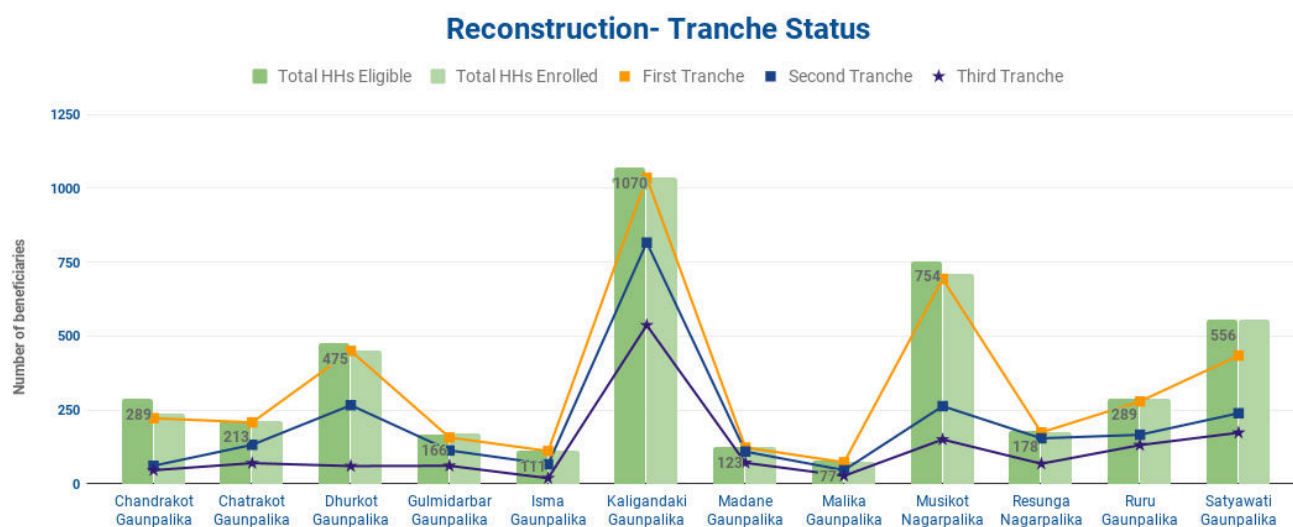


Tranche Status (Arghakhachi)

Tranche Status Table

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	1 st Tranche	2 nd Tranche	3 rd Tranche	Ret HH Eligible	Ret HH Enrolled	Ret 1 st Tranche
Bhumekasthan Nagarpalika	230	148	123	131	45	39	24	10	10
Chhatradev Gaunpalika	391	208	202	193	77	76	9	4	4
Malarani Gaunpalika	312	245	210	191	112	31	3		
Panini Gaunpalika	331	241	220	220	49	26	6		
Sandhikharka Nagarpalika	207	64	80	78	36	31	34	21	21
Sitganga Nagarpalika	177	139	77	131	64	64	6		

Reconstruction- Tranche Status

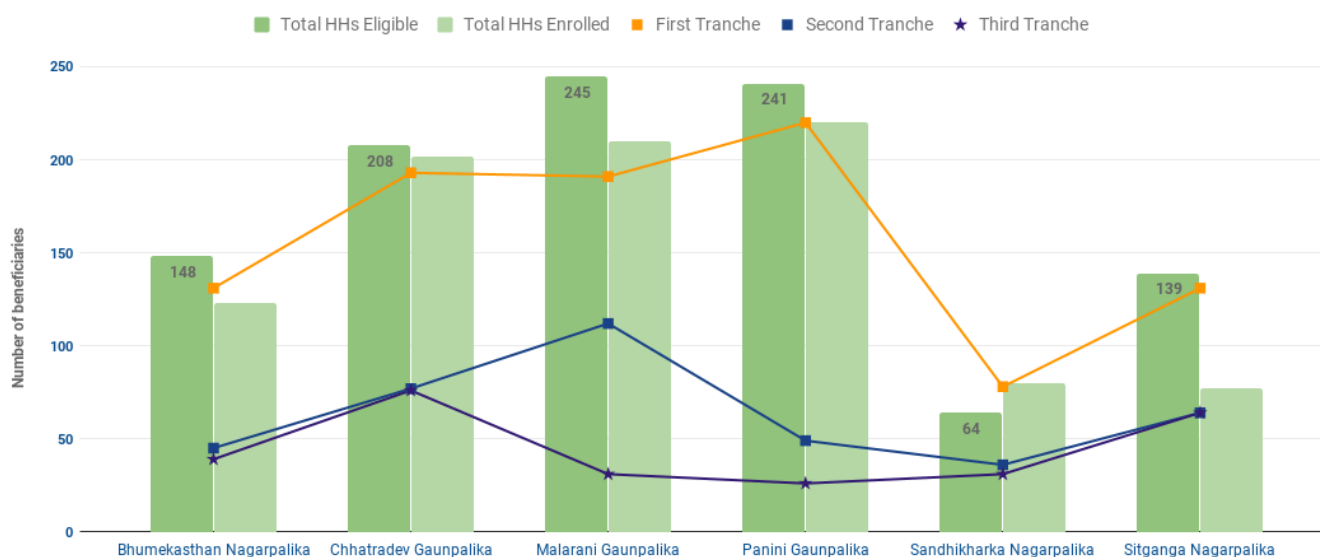

Field Visit Reports (Arghakhachi)

Visit 1

Date	Location	Participants
7 th July 2019	Mala Rani Rural Municipality, Arghakhachi	1. Mr. Chandra Gurung – DC – HRRP 2. Mr. Ishor Neupane – IMO – HRRP 3. Mr. Srawan KC – Focal Engineer, DLPIU Building 4. Mr. Mukesh Kumar Yadav – DLPIU Engineer, Mala Rani RM 5. Mr. Sarju Shrestha – DLPIU Engineer, Sandhikhar UM
Objective(s)	✓ Identifying the current situation and status of reconstruction. ✓ Palika level coordination meeting. ✓ Housing typology collection ✓ Municipal capacity assessment	

Why was the visit carried out in this location?

- ✓ To identify the real situation of housing reconstruction status, grievances and beneficiaries' interest in housing reconstruction and how DLPIU engineers are providing technical support to beneficiaries
- ✓ Palika level coordination meeting to know about the perspective of local representative and approaches to facilitate the issues occurred in housing reconstruction by local representative
- ✓ Housing typology collection.
- ✓ Municipal capacity assessment and palika profile updates and uploaded in palika's website

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

N/A

Summary

Field Visit:

DLPIUs of Arghakhachi and HRRP conducted joint monitoring field visit to Mala Rani Rural Municipality, Arghakhachi. The team conducted palika level coordination meeting with palika chairperson and chief executive officer; and discussed the progress status, issues, challenges, compliant and non-compliance issues, current directives of grievances regarding re-survey and reverification by NRA, retrofitting issues, of housing reconstruction in the palika. The joint monitoring team includes focal engineer of DLPIU-Building, Focal engineer of Mala Rani RM, HRRP, and engineer of Sadhikharka RM.

The joint monitoring team also observed the compliant house owned by Mrs. Basanta Gharti, who received all tranches of GoN, in ward no. 6, Ratanmare, Malarani RM.

In the visit, municipal capacity assessment was also carried out and reconstruction data of palika was updated to upload in the website.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Houses constructed before mobilizing engineers	A decision to provide grant to those beneficiaries were made by NRA	Guidelines were released	Rural Municipalities, Engineers, GMALI	As soon as possible
Re-survey and reverification issues	Engineers completed collecting grievances and forward to NRA through GMALI.	The files were forwarded to NRA through GMALI	GMALI & NRA	By November end 2019
Issues of receiving 2 nd tranche and not able to receive 3 rd tranche	Beneficiaries need to improve and correct their houses as the	N/A	As soon as possible	Beneficiaries, Engineers, and

	technical guidance provided by DSE, and Engineer			District Support Engineer
--	--	--	--	------------------------------

Photos



Joint Monitoring team had meeting with Mr. Bak Krishna Acharya – Chairperson of Malarani Rural Municipality, Arghakhachi



The team observing the houses owned by Mrs. Basanta Gharti Magar, who received all the tranches of government grant at Ratanmare – 6, Malarani Rural Municipality, Arghakhachi

Field Visit Reports (Arghakhachi)

Visit 2

Date	Location	Participants
8 th July 2019	Chhatradev Rural Municipality, Arghakhachi	6. Mr. Chandra Gurung – DC – HRRP 7. Mr. Ishor Neupane – IMO – HRRP 8. Mr. Srawan KC – Focal Engineer, DLPIU Building 9. Mr. Santosh Pokhrel – DLPIU Sub-Engineer, Chhatradev RM

Objective(s)	✓ Identifying the current situation and status of reconstruction. ✓ Palika level coordination meeting. ✓ Housing typology collection ✓ Municipal capacity assessment
--------------	---

Why was the visit carried out in this location?

- ✓ To identify the real situation of housing reconstruction status, grievances and beneficiaries' interest in housing reconstruction and how DLPIU engineers are providing technical support to beneficiaries
- ✓ Palika level coordination meeting to know about the perspective of local representative and approaches to facilitate the issues occurred in housing reconstruction by local representative
- ✓ Housing typology collection.
- ✓ Municipal capacity assessment and palika profile updates and uploaded in palika's website

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

N/A

Summary

Field Visit:

DLPIUs of Arghakhachi and HRRP conducted joint monitoring field visit to Chhatradev Rural Municipality, Arghakhachi on 8th July 2019. The team conducted palika level coordination meeting in presence of Palika Chairperson Mr. Lekhnath Pokhrel and Mr. Khadananda Bhusal – Chief Administrative Officer, and discussed the progress status, issues, challenges, compliant and non-compliance issues, current directives of grievances regarding re-survey and reverification by NRA, retrofitting issues, private housing reconstruction in the palika. The joint monitoring team includes focal engineer of DLPIU-Building, Focal engineer of Chhatradev RM, and HRRP. The joint monitoring team also observed three different houses in the palika, including a vulnerable beneficiary, who received all tranches of GoN, two houses in ward no. 5, Khaireni of Chhatradev & one vulnerable beneficiary house in ward no. 7 Shivalayatole of Chhatradev RM. In the visit, municipal capacity assessment was also carried out and data reconstruction data of palika was updated to upload in the website.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Houses constructed before mobilizing engineers	A decision to provide grant to those beneficiaries were made by NRA	Guidelines were released	Rural Municipalities, Engineers, GMALI	As soon as possible
Re-survey and reverification issues	Engineers completed collecting grievances and forward to NRA through GMALI.	The files were forwarded to NRA through GMALI	GMALI & NRA	By November end 2019
Issues of receiving 2 nd tranche and not able to receive 3 rd tranche	Beneficiaries need to improve and correct their houses as the technical guidance	N/A	As soon as possible	Beneficiaries, Engineers, and District Support Engineer

	provided by DSE, and Engineer			
--	----------------------------------	--	--	--

Photos



Joint Monitoring team had meeting with Mr. Lekhnath Pokhrel– Chairperson of Chhatradev Rural Municipality, Arghakhachi



The team observing the houses owned by Mr. Netra Prasad Pokhrel, who received all the tranches of government grant at Khaireni – 5, Chhatradev Rural Municipality, Arghakhachi

Field Visit Reports (Gulmi)

Visit 1

Date	Location	Participants
12 July 2019	Chatrakot Rural Municipality, Gulmi	10. Mr. Chandra Gurung – DC – HRRP 11. Mr. Ishor Neupane – IMO – HRRP 12. Mr. Atit Shrestha – District Support Engineer, DLPIU Building
Objective(s)	✓ Identifying the current situation and status of reconstruction. ✓ Palika level coordination meeting. ✓ Housing typology collection ✓ Municipal capacity assessment	

Why was the visit carried out in this location?

- ✓ To identify the real situation of housing reconstruction status, grievances and beneficiaries' interest in housing reconstruction and how DLPIU engineers are providing technical support to beneficiaries
- ✓ Palika level coordination meeting to know about the perspective of local representative and approaches to facilitate the issues occurred in housing reconstruction by local representative
- ✓ Housing typology collection.
- ✓ Municipal capacity assessment and palika profile updates and uploaded in palika's website

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

N/A

Summary

Field Visit:

HRRP team and district support engineer had joint monitoring field visit to Chatrakot Rural Municipality on 12 July 2019. The team had palika level coordination meeting in presence of palika chairperson, palika deputy chairperson, ward chairperson of ward no. 1, 2, 3 & 6, member of rural municipal executive and palika based DLPIU's engineers. The team visit to Chatrakot rural municipality had very fruitful meeting particularly focused on private housing reconstruction issues and challenges. The key points of the meeting were:

- those houses which were constructed before engineers mobilized and responded accordingly based on the recent decision of NRA executive committee and guidelines released by NRA.
- Issues regarding beneficiaries who got 2nd tranche but not able to receive 3rd tranche were also discussed and concluded to motivate the beneficiaries to apply correction measures to access the 3rd tranche by following the technical direction by engineers
- Issues regarding re-survey and re-verification and grievances were also discussed and all the registered grievances were forwarded to GMALI
- Engineers raised the issues of providing retrofitting training to the engineers mobilized in the field

In the visit, municipal capacity assessment was also carried out; and reconstruction data of palika updated for palika profile to upload in the website.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Houses constructed before mobilizing engineers	A decision to provide grant to those beneficiaries were made by NRA	Guidelines were released	Rural Municipalities, Engineers, GMALI	As soon as possible
Re-survey and re-verification issues	Engineers completed collecting grievances and forward to NRA through GMALI.	The files were forwarded to NRA through GMALI	GMALI & NRA	By November end 2019

Issues of receiving 2 nd tranche and not able to receive 3 rd tranche	Beneficiaries need to improve and correct their houses as the technical guidance provided by DSE, and Engineer	N/A	As soon as possible	Beneficiaries, Engineers, and District Support Engineer
Issues regarding retrofitting – zero progress in retrofitting houses & also no retrofitting training has been provided to engineers yet,	The concern will be reported to NRA/CLPIU	N/A	N/A	Engineers, beneficiaries
No training mason are available	Mason training should be provided in the community	N/A	As soon as possible	NRA, DLPIU- Building

Photos



HRRP team & DSE from DLPIU, Gulmi had meeting with ward chairperson of ward no. 1,2, 3 & 6, member of rural municipal executive, deputy palika chairperson, chief administrative officer, and DLPIU engineers in presence of Mr. Madhu Krishna Panta – Chairperson of Chhatrakot Rural Municipality, Gulmi



HRRP team & DSE from DLPIU, Gulmi had meeting with ward chairperson of ward no. 1,2, 3 & 6, member of rural municipal executive, deputy palika chairperson, chief administrative officer, and DLPIU engineers in presence of Mr. Madhu Krishna Panta – Chairperson of Chhatrakot Rural Municipality, Gulmi

Field Visit Reports (Gulmi)

Visit 2

Date	Location	Participants
14 July 2019	Musikot Urban Municipality, Gulmi	13. Mr. Chandra Gurung – DC – HRRP 14. Mr. Ishor Neupane – IMO – HRRP 15. Mr. Atit Shrestha – District Support Engineer, DLPIU Building
Objective(s)	✓ Identifying the current situation and status of reconstruction. ✓ municipal level coordination meeting with local representatives and NRA engineers. ✓ Housing typology collection ✓ Municipal capacity assessment	

Why was the visit carried out in this location?

- ✓ To identify the real situation of housing reconstruction status, grievances and beneficiaries' interest in housing reconstruction and how DLPIU engineers are providing technical support to beneficiaries
- ✓ municipal level coordination meeting to know about the perspective of local representative and approaches to facilitate the issues occurred in housing reconstruction by local representative
- ✓ Housing typology collection and monitoring of some houses constructed and under-construction.
- ✓ Municipal capacity assessment and palika profile updates and uploaded in palika's website

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

N/A

Summary

Field Visit:

HRRP team and district support engineer had joint monitoring field visit to Musikot Urban Municipality on 14 July 2019. The team had municipal level coordination meeting in presence of mayor, deputy mayor, ward chairperson and palika based DLPIU's engineers. The team had municipal meeting focusing on private housing reconstruction issues and challenges. The discussion points of the meeting were:

- i. 165 houses built before engineers mobilized in the field
- ii. Houses constructed with technical error – problem with attic
- iii. 16 HHs have not made PA agreement yet
- iv. 201 grievances enlisted
- v. Beneficiaries wants to change to retrofitting beneficiaries
- vi. 140 HHs completed construction, and 280 HHs are under construction
- vii. Planning to distribute completion certificate to those who completed their house reconstruction
- viii. Plan to provide refresher training to mason
- ix. Some beneficiaries want to return the tranche to GoN

The team also observed some houses constructed in the field. In the visit, municipal capacity assessment was also carried out; and reconstruction data of palika updated for palika profile to upload in the website.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Houses constructed before mobilizing engineers	A decision to provide grant to those beneficiaries were made by NRA	Guidelines were released	Rural Municipalities, Engineers, GMALI	As soon as possible
Re-survey and reverification issues	Engineers completed collecting grievances and forward to NRA through GMALI.	The files were forwarded to NRA through GMALI	GMALI & NRA	By November end 2019

Issues of receiving 2 nd tranche and not able to receive 3 rd tranche	Beneficiaries need to improve and correct their houses as the technical guidance provided by DSE, and Engineer	N/A	As soon as possible	Beneficiaries, Engineers, and District Support Engineer
Issues regarding retrofitting – zero progress in retrofitting houses & also no retrofitting training has been provided to engineers yet,	The concern will be reported to NRA/CLPIU	N/A	N/A	Engineers, beneficiaries

Photos



HRRP team & DSE from DLPIU, Gulmi had meeting deputy mayor, ward chairperson, chief administrative officer, and DLPIU engineers in presence of Mr. Somnath Sapkota – Mayor of Musikot Urban Municipality, Gulmi



District Reconstruction Facilitation Meeting of Gulmi presence of Mr. Laxman Parajuli – Chief of DCC, Gulmi, & deputy chief of DCC, CDO, other members of the committee & HRRP

Housing Typology Report (Max 4 Photos, Select best photos from each district)



Name: -Basanta Gharti Magar
Place: Ratanmare – 6, Malarani Rural Municipality,
Arghakhachi
Typology: SMM with cemented band of two rooms
Tranche: received all



Name: -Bhup Narayan Acharya
Place: Shivalayatole - 7, Chhatradev Rural Municipality,
Arghakhachi
Typology: SMM with cemented band of two rooms
Tranche: received all



Name: -Narayan Prasad Pokhrel
Place: Khairani - 5, Chhatradev Rura Municipality,
Arghakhachi
Typology: SMM with cemented band of two rooms
Tranche: received all



Name: Netra Prasad Pokhrel
Place: Khairani -5, Chhatradev Rural Municipality,
Arghakhachi
Typology: RCC with four rooms
Tranche: received al



Name: Bed Prasad Pandey
Typology: RCC structure with 2.5 stories
Place: Resunga Municipality – 10, Gulmi,
Tranche: received all



Name: Bhimi Sunar
Typology: RCC structure with 4 room single story
Place: Resunga Municipality – 9, Gulmi
Tranche: received all



Name: Lal Bahadur Sunar
Typology: SMM with 2 rooms
Place: Musikot Municipality – 8, Gulmi,
Tranche: received all



Name: Ganesh Prasad Fuldel
Typology: RCC with 2.5 stories under construction house
Place: Musikot Municipality – 7, Gulmi,
Tranche: 2nd tranche received

Questions Collected		
Question	Who Asked the Question?	Response Provided (By Whom)
Houses constructed before mobilizing engineers	Local Representatives and beneficiareis	A decision to provide grant to those beneficiaries were made by NRA
Re-survey and reverification issues	Local Representatives and beneficiaries	Engineers completed collecting grievances and forward to NRA through GMALI.
Issues of receiving 2 nd tranche and not able to receive 3 rd tranche	Local Representatives and beneficiaries	Beneficiaries need to improve and correct their houses as the technical guidance provided by DSE, and Engineer
Issues regarding retrofitting – zero progress in retrofitting houses & also no retrofitting training has been provided to engineers yet,	Engineers	The concern will be reported to NRA/CLPIU
No training mason are available	Engineers	Mason training should be provided in the community

Challenges and Way Forward	
Challenge	Way Forward
Zero progress in retrofitting of houses in one of the challenging issues in private housing reconstruction	NRA should take necessary initiation to make it easier and compliant and cost effective
Houses who received up to 2 nd tranches but bot able to receive 3 rd tranche is another big issue.	Beneficiaries need to correct and improvise their houses based on the recommendation by engineers and DSE.

Case Stories

Enabling social support system via community forest user group at Maskichap

Sandhan Besauni community forest user group (CFUG) was established on 2056 BS under the Forest Act-1993 of Nepal (provision relating to formation of CFUG). From the establishment, all member is eligible to become general members of this federation and any other user group based on forest resources at community level are qualified to become elementary member. From the beginning there are 76 HHs members in which 42 are male, 34 females, including 4 Dalit & 72 Janajati members at Maskichap, Sahidlakhan rural municipality. In the start level, all member was planting, caring & raring at CFUG. They arrange their monthly meeting, made daily action plan for better livelihood option via natural resources of forest & saving and credit. This CFUG have own balance budget approx. 5,00,000 (five hundred thousand NRs). More than fifty thousand budgets were distributed annually to poor and vulnerable household on livelihood and reconstruction options among the members.



The CFUG emerged from the idea that forest users from all parts of the community should be linked in order to strengthen the role of users in local resource management & policy making processes at locally via leadership development at community to national level. Mainly focused to develop means of livelihoods and to generate opportunities to reduce poverty through sustainable forest management and utilization of resources locally, long-lasting by the approach of consensus in decision making through livelihood strengthening, financial service and enhancement of local leadership. And, to emphasize the participation of all sections of community and ethnic groups in policy decisions and its implementation through CFUGs to uphold the values of good governance, empowerment, self-respect, self-reliance and the approaches of consensus at community for resilience building.



Aftermath of mega quake in Gorkha in 2015, at Sahidlakhan people were suffered destructively and even all CFUG members too. They tried to collect natural resources via forest and try to support each other in community via their saving fund to highly affected and most vulnerable HHs. In Sahidlakhan ward number 5, Maskichap, Mr. Nanda Thapa (ANS) and community facilitator Mr. Bimal Shrestha visited with CFUG member and made a discussion on enable social support system. After of long discussion at CFUG, they decided to support to their member for reconstruction via kindling to make it HHs level. Now each of HHs has received one QFT only on six hundred & eighty only, which is quite low rate rather than market price (approx. 1500 cheap than market prices). CFUG group made support of more than 15000 NRs for reconstruction support to Gol supported beneficiaries Mr. Janga Bahadur Thapa for house reconstruction. After support from CFUG, Mr Jagat completed his DPC, planning for scaling up construction and appreciated to Sandhan Besauni community forest user group (CFUG) and Gol- NHRP team for socio technical facilitation.

Story courtesy: Government of India supported Nepal Housing Reconstruction Project – NHRP, Gorkha
