

Monthly District Report

Lalitpur, Bhaktapur

14 June - 14 July 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Lalitpur	General Coordination meeting with POs were conducted by DLPIU GMALI Lalitpur office. The meeting was attended by Mr. Pitamber Ghimire, Joint Secretary NGOs Coordination Section, NRA and by Dr. Chandra Bdr Shrestha, Member of Executive Committee of NRA along with representatives from DLPIUs (Building, GMALI and Education) of Lalitpur. The meeting was attended by representatives of 12 POs that were engaged in reconstruction works in Lalitpur district in past as well as in present times. The key agenda of this meeting was to discuss on regularizing the POs works with NRA, to take updates of POs work and the challenges of reconstruction.	2 nd July 2019	DLPIU GMALI Lalitpur, Manbhawan	Mr. Yamnath Giri M & E Specialist DLPIU NRA GMALI Lalitpur Manbhawan yamnathgiri2014@gmail.com Contact: 9851239785	Meeting minute
	HRRP Lalitpur Cluster have coordinated focused group discussion activity for two researchers from Notredam University, USA	26 June 2019	Ward no 13 Jharuwarashi, Godawari Municipality	Ms. Ambika Amatya District Coordinator HRRP Lalitpur and Myagdi Cluster ambika.amatya@hrrpnepal.org Contact: 9841356409	Field visit section
	Tranche status of Lalitpur updated to GD sheet in Palika Profile	1 July 2019		Sachin Malego IM Officer, HRRP	
	Support for preparation of Tranche Map in one sheet and Meeting with M&E Specialist, EHRP/DLPIU GMALI Lalitpur	18 June 2019		Sachin Malego IM Officer, HRRP	
	Support to National HRRP for design and publication of Experiences booklet	Ongoing		Sachin Malego, IM Officer, HRRP	
Bhaktapur	The general ward-level coordination meeting was conducted at Ward office, Ward no. 3, Jhaukhel, Changunarayan Municipality. Ward Chief in presence of representatives from DLPIU Building Bhaktapur (M & E Consultant, District Support Engineer, Palika Reconstruction Engineers) and HRRP attended the meeting.	19 June 2019	Ward no 3, Changunarayan Municipality	Er. Roshan Keshari M & E Consultant, DLPIU Building Bhaktapur roshankesari20@gmail.com 9841640357	Ward -level coordination meeting minute
	Joint M & E Visit was conducted at Ward no. 3 (Jhaukhel) & Ward 8 (Sudal) Changunarayan Municipality by HRRP Lalitpur District Coordination Team along with representatives from DLPIU Building Bhaktapur and technical staff of Changunarayan Municipality.	19 June 2019	Ward no. 3 & 8 Changunarayan Municipality	Er. Roshan Keshari M & E Consultant, DLPIU Building Bhaktapur roshankesari20@gmail.com 9841640357	Joint M & E visit section

Summary of events during this period

The general ward-level coordination meeting was conducted at Ward office, Ward no. 2, 3 and 4 of Suryabinayak Municipality. Ward Chief in presence of representatives from DLPIU Building Bhaktapur (M & E Consultant, District Support Engineer, Palika Reconstruction Engineers) and HRRP team member attended the meeting.	20 June 2019	Ward 2, 3, 4 Suryabinayak Municipality	Er. Roshan Keshari M & E Consultant, DLPIU Building Bhaktapur roshankesari20@gmail.com 9841640357	Ward -level coordination meeting minute
Joint M & E Visit was conducted at Ward no. 2, 3, & 4, Suryabinayak Municipality by HRRP Lalitpur District Coordination Team along with representatives of DLPIU Building Bhaktapur.	20 June 2019	Ward 2, 3, 4 Suryabinayak Municipality	Er. Roshan Keshari M & E Consultant, DLPIU Building Bhaktapur roshankesari20@gmail.com 9841640357	Joint M & E visit section
The general ward-level coordination meeting was conducted at Ward office, Ward no. 8, Suryabinayak Municipality, Bhaktapur district. Ward Chief, DLPIU Building Bhaktapur (M & E Consultant, District Support Engineer, Palika Reconstruction Engineers) and HRRP team member attended the meeting.	21 June 2019	Ward no 8, Suryabinayak Municipality	Er. Roshan Keshari M & E Consultant, DLPIU Building Bhaktapur roshankesari20@gmail.com 9841640357 Sachin Malego IM Officer, HRRP	Ward -level coordination meeting minute
Joint M & E Visit was conducted at Ward no. 7 & 8, Suryabinayak Municipality by HRRP Lalitpur District Coordination Team along with representatives of DLPIU Building Bhaktapur	21 June 2019	Ward no.7 & 8 Suryabinayak Municipality	Er. Roshan Keshari M & E Consultant, DLPIU Building Bhaktapur roshankesari20@gmail.com 9841640357 Sachin Malego IM Officer, HRRP	Joint M & E visit section

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Joint M & E visit to observe reconstruction efforts of beneficiaries in Bhaktapur and Lalitpur districts	11 July – 8 August 2019/ Various wards of Municipalities of Lalitpur and Bhaktapur district	DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team	Ms. Ambika Amatya District Coordinator HRRP Lalitpur and Myagdi Cluster ambika.amatya@hrrpnepal.org Contact: 9841356409
General Palika level and Ward level meeting and consultation with elected ward officials over the reconstruction progress and status of the visited wards of Bhaktapur and Lalitpur district	11 July – 8 August 2019/ Various wards of Municipalities of Lalitpur and Bhaktapur district	DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team	Ms. Ambika Amatya District Coordinator HRRP Lalitpur and Myagdi Cluster ambika.amatya@hrrpnepal.org Contact: 9841356409

News & Updates

As per decision by Government of Nepal, National Reconstruction Authority dated 14th June 2019 (31st Jestha 2076) has issued a notice regarding –


- Signing of grant partnership agreement (PA) by earthquake affected beneficiaries: The notice further reads that if the beneficiaries fail to sign PA with NRA for taking 1st tranche within an estimated time period then they will be removed from list of earthquake affected. The timeline given for signing PA is 6th July 2019 (21st Ashad 2076).
- The beneficiaries who signs grant partnership agreement (PA) till date should take 1st tranche. The deadline given for taking 1st tranche is end of Nepali Fiscal Year ie. 16th July 2019 (31st Ashad 2076)

Tranche Status (Lalitpur)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	3361	3370	3099	3089	2558	1894	252	110	107	0
Godawari Nagarpalika	10950	9598	7980	7908	2620	2152	323	94	90	0
Konjyosom Gaunpalika	2580	2154	2065	2060	1774	1348	372	251	246	0
Lalitpur Mahanagarpalika	6594	7373	6331	6312	1278	830	275	119	115	0
Mahalaxmi Nagarpalika	4409	3669	3104	3074	882	758	83	33	31	0
Mahankal Gaunpalika	2451	2271	2236	2235	1797	1117	61	55	54	0

Graph of Tranche Status:

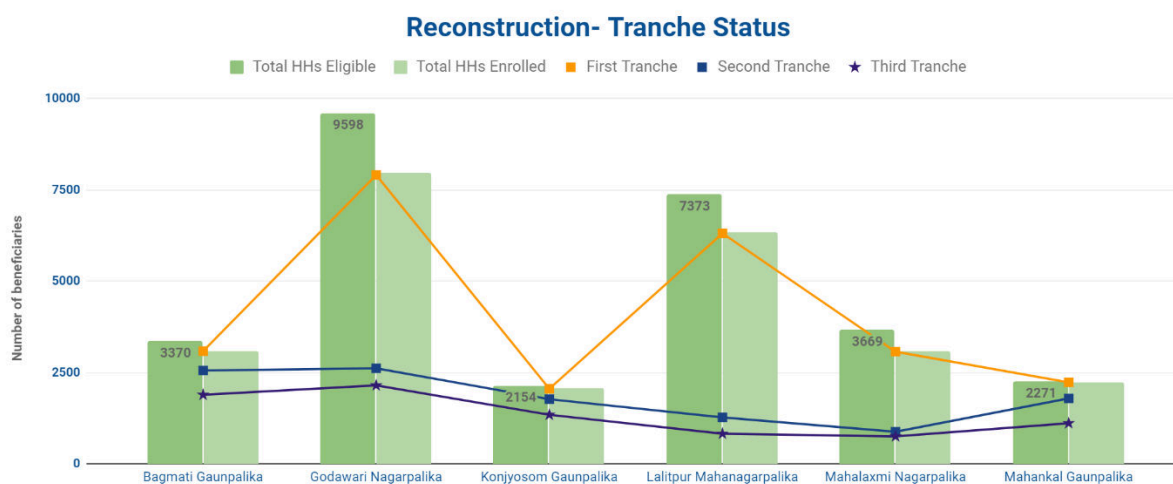

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

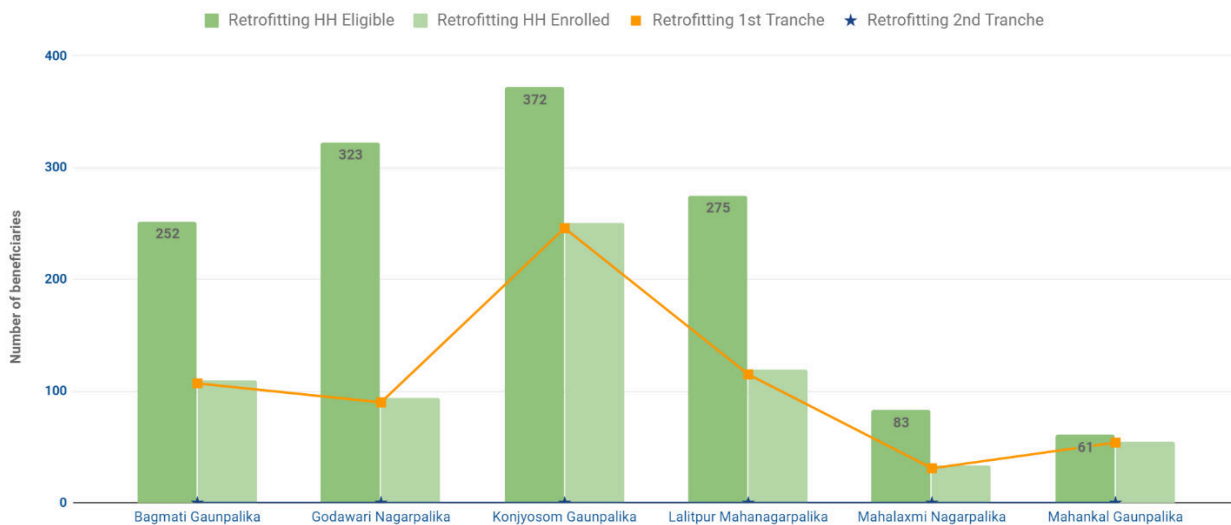


Tranche Status (Bhaktapur)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bhaktapur Nagarpalika	8175	7656	5612	5612	1703	1515	161	42	42	0
Changunarayan Nagarpalika	11059	11000	9749	9749	3332	3145	212	89	89	0
Madhyapur Thimi Nagarpalika	3015	2333	2060	2060	687	649	95	56	56	0
Suryabinayak Nagarpalika	7948	7425	6979	6979	2678	2498	234	103	103	0


Graph of Tranche Status:

Reconstruction- Tranche Status

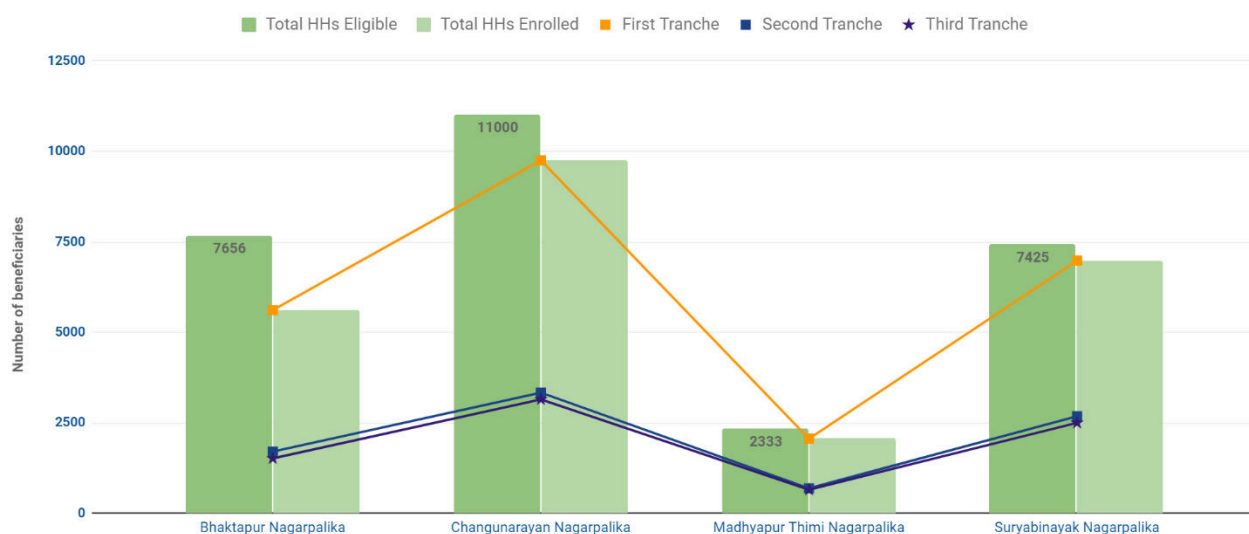

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

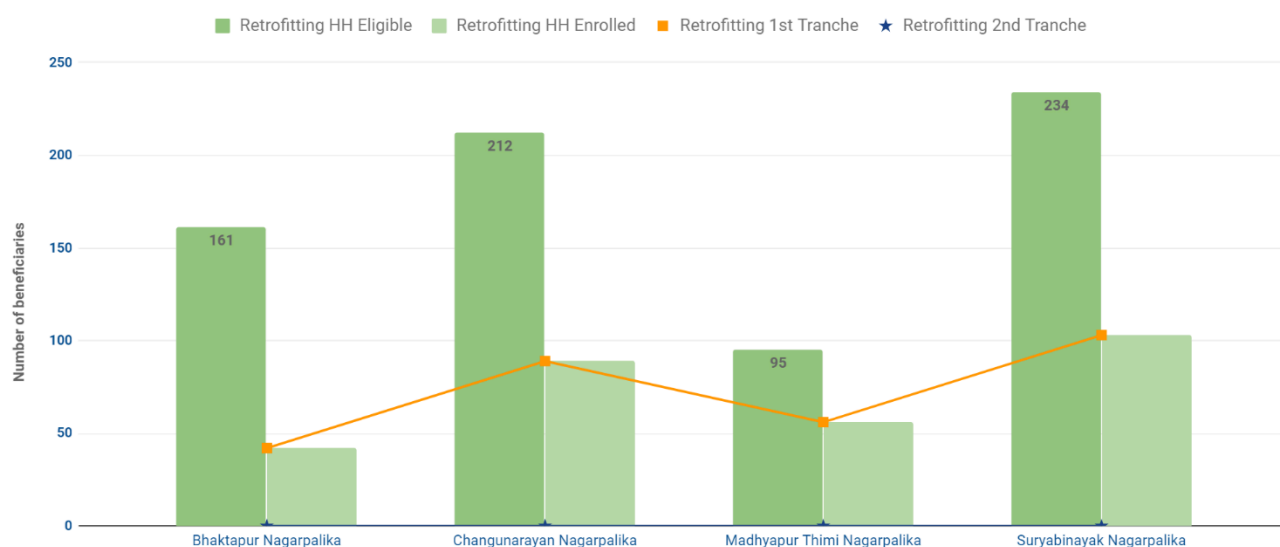

Field Visit Reports (Lalitpur)

Visit 1

Date	Location	Participants
26 June 2019	Ward no. 13, Jharuwarashi, Godawari Municipality, Lalitpur district	• Researchers (Brian Hickley and Belen) • Ambika Amatya, District Coordinator, HRRP Lalitpur Cluster • Ramraja Lamichanne, Independent Translator
Objective(s)	• To conduct focused group discussion with earthquake affected beneficiaries about tracking recovery efforts that they have taken to secure their shelter. • To involve earthquake affected beneficiaries in formulating timeline related to their recovery phase from post earthquake period till date.	
Why was the visit carried out in this location?		

- To assess the social dynamics of earthquake affected beneficiaries in post earthquake recovery.
- To track about knowledge of safe shelter among beneficiaries.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

<https://drive.google.com/open?id=1yZnEnWvscIrs03lrrb6YVSf7OfhJ5hpR>

Summary

HRRP Lalitpur District Coordination Team coordinated with two international university research students to organize a short field visit to Ward no 13, Jharuwarashi, Godawari Municipality. The researchers conducted two activities- focused group discussion and post-earthquake recovery timeline by involving participants who belongs to earthquake affected households.

Focused group discussion was attended by 10 participants while 6 participants attended formulating post-earthquake recovery timeline. The objectives of conducting focused group discussion was - to clearly define priorities of beneficiaries' shelters in order to track perceived risk of future disasters and to understand about perceived social norms that encircles their lives during recovery phase. Focused group discussion revealed that beneficiaries were supported by Lumanti, POs that has supported them with construction materials of worth Rs 300000. Lumanti also provided them technical assistance in rebuilding their house. Despite this, as revealed by beneficiaries, plenty of finishing works is still left such as final plastering, colouring, glass fitting works on windows and even toilet construction. Beneficiaries cited the reason of lack of sufficient amount to conduct remaining works of their shelter. Majority of beneficiaries had been earning livelihood by selling livestock and other agricultural farm work while male members of the house are indulged in jobs such as of driving and salaried staff in commercial sectors in Kathmandu.

The recovery timeline of post-earthquake revealed that beneficiaries has faced hard times living in temporary shelters where the insecurity was faced in various issues such as theft, torture, blowing away of temporary roof materials by windstorm and by rainfall and dangers of flooding and mudslide. However, with the reconstruction of permanent shelter, despite of building typology, has instilled a sense of peace and security among beneficiaries. Majority of beneficiaries have taken loans upto Rs 200000 from local women groups and from cooperatives to rebuild their house despite of material support from POs.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Uncompleted shelter works such as window glass fitting and toilet construction possess insecurity of women and children.	Toilet construction and window glass fitting works must be carried out as early as possible by house owners to secure safety towards family members and the property.	Concerned beneficiaries will do their best to conduct finishing works of their shelters	Beneficiaries	As soon as possible

Photos



Image: Focused group discussion activity in progress. During the discussion, the participants was told to prioritize the most preferred area of the house in order to learn about perceived future disaster risk and the knowledge about mitigation. Majority of beneficiaries highlighted the need of security to livestock which is as important as their lives because of their dependency for income.

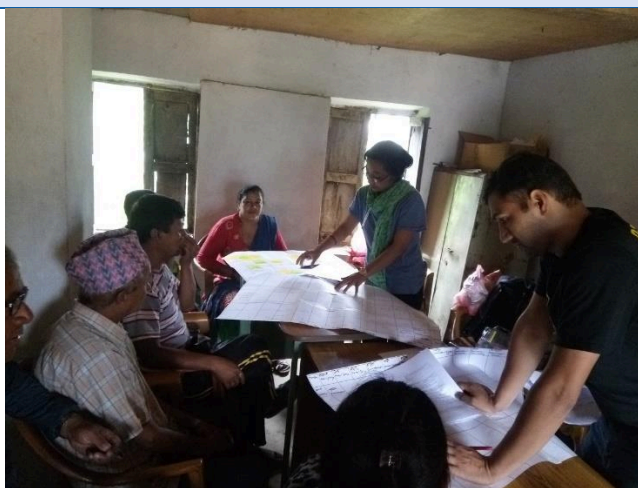


Image: Recovery timeline activity in progress. During this exercise, participants were informed to prepare recovery timeline since the period of earthquake 2015 till date. Majority of beneficiaries included residing in temporary shelter for nearly 1 year or more and headed towards reconstruction of house. The beneficiaries also prioritized the main needs during recovery period and also the drivers of recovery (things that helped them to recover their lives into normalcy)

Field Visit Reports (Bhaktapur)

Visit 2

Date	Location	Participants
------	----------	--------------

14 July 2019

19 June 2019	Ward no. 3 (Jhaukhel) and Ward no. 8 (Sudal), Changunarayan Municipality, Bhaktapur district	- Roshan Kesari, M & E Consultant, CLPIU Building - Prabesh Adhikari, DSE, DLPIU Building Bhaktapur - Deepak Saud, HRRP DMT Technical Coordinator - Technical personnel (Salina Shrestha, Ranjana Suwal, Pramila Shrestha, Kundan Jung Thapa)
--------------	--	--

Objective(s)	- To conduct Ward level coordination meeting with Ward Chief and discuss on reconstruction efforts taking place in Ward no 3, Jhaukhel - To observe the reconstruction status of the houses and provide relevant suggestions further.
---------------------	--

Why was the visit carried out in this location?

Changunarayan Municipality is in P1 priority as according to HRRP's municipal targeting in shelter reconstruction. There, this Joint Monitoring Visit was organised to influence way forward in ward level reconstruction progress through ward level coordination meeting and to provide suggestions to beneficiaries whose housing grant application cases were in pending stage in DLPIU Building Bhaktapur.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

<https://drive.google.com/open?id=18lbZ9oBEtzmUU4UaJp4Rjn21dQVNT72B>

<https://drive.google.com/open?id=1EkLxJjeto6UKq7JspkPYI7G3Zdidd9lq>

Summary

HRRP Lalitpur and Bhaktapur Coordination Team along with M & E Consultant (DLPIU Building Bhaktapur), District Support Engineer and engineers of DLPIU Building Bhaktapur and of Changunarayan Municipality conducted field visit Ward no 3 & 8 of Changunarayan Municipality. The field visit team observed nearly 6 houses in total. The visit was specifically targeted to cover the pending 2nd tranche file of some houses. The inputs from Er. Roshan Kesari, M & E Consultant has paved way forward for engineers to proceed further tranche approval of beneficiaries. Some of the engineers also did final inspection of the houses in the meantime.

Meeting with Ward Chief, Ward no 3, Changunarayan Municipality

The Joint M & E visit team also conducted ward -level coordination meeting with Mr. Shyam Sundar Dhimal, Ward Chief of Ward no 3, Jhaukhel. Meeting was focused on updating with reconstructions tatus and issues perpetuated in Ward no 3. The non –compliance cases in the exceeded size of the room, missing bands and building not as per the design. The reconstruction rate has progressed well in Ward no 3, Jhaukhel after government has made possible ways to solve reconstruction related issues but due to the difficulty in getting building permit from the municipality handful of beneficiaries have not been able to access 2nd tranche. Ward Chief insisted for supervision of housing reconstruction works as well as the utmost need of technical support to beneficiaries.

Field Visit:

- No. of HHs visited: 6
- No. of meetings with engineers: None
- No. of meetings with local officials: 1

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Technical support provided to beneficiaries were not significant as noncompliance cases continued to rising	Technical personnel deployed in concerned municipalities should assist beneficiaries in rebuilding a earthquake resistant safer houses so that hassles in grant access would be reduced.	To mobilise technical personnel in providing technical support to beneficiaries especially during reconstruction of houses.	Engineers, DLPIU Building, M & E Consultant	By Ashad end 2076 and beyond

Photos



Image: Ward level coordination meeting in progress at Ward no. 3, Jhaukhel, Changunarayan Municipality. The meeting was attended by Ward Chief and Joint M & E visit team members including of M & E Consultant (DLPIU Building Bhaktapur), District Support Engineer and engineers of DLPIU Building Bhaktapur and reconstruction engineers deployed at Changunarayan Municipality

Beneficiary name: Shyam Bahadur Yandyo, Ward no 3, Changunarayan Municipality. Two storey BMM house with attic has 2 rooms. The owner has received 1st and 2nd Tranche. Attic height was more than desired value but proper bands and connections was provided so the house was certified for 3rd tranche from the inspection visit.

Field Visit Reports (Bhaktapur)

Visit 3

Date	Location	Participants
20 June 2019	Ward no 2, 3, 4 of Suryabinayak Municipality	- Roshan Kesari, M & E Consultant, CLPIU Building - Prabesh Adhikari, DSE, DLPIU Building Bhaktapur - Monika Bajimaya, HRRP DMT IM Coordinator - Technical personnel (Bibha Joshi, Saru Chansi Shrestha, Jeena Suwal, Sweta Acharya, Rajani Pradhan Shrestha, Manju Khadka)
Objective(s)	- To observe the reconstruction status of the houses and provide way forward for beneficiaries. - To conduct Ward level coordination meeting with elected local heads. - To take building typology on KoBo Collect App.	

Why was the visit carried out in this location?

Suryabinayak Municipality is in P1 priority as according to HRRP's municipal targeting in shelter reconstruction. Large pockets of this Palika have been unreachable in terms of monitoring of the houses in reconstruction phase. Therefore, this Joint Monitoring Visit was organized to influence way forward in ward level reconstruction progress through ward level coordination meeting.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

<https://drive.google.com/open?id=1EVzso8vplxchk2jOc1oN72EyVxqXhN7S>

<https://drive.google.com/open?id=1EkLxJeto6UKq7JspkPYI7G3Zdd9lq>

<https://drive.google.com/open?id=1yZnEnWvsclrs03lrrb6YVSf7OfhJ5hpR>

Summary

HRRP Lalitpur and Bhaktapur Coordination Team along with M & E Consultant (DLPIU Building Bhaktapur), District Support Engineer and engineers of DLPIU Building Bhaktapur and of Suryabinayak Municipality conducted field visit Ward no 2, 3 and 4 of Suryabinayak Municipality. The field visit team observed nearly 3 houses in total. The visit was specifically targeted to cover the pending 2nd tranche file of some houses.

Summary of Coordination Meeting with Ward Chiefs of Ward no 2, 3 and 4 Suryabinayak Municipality

The Joint M & E visit team also conducted ward -level coordination meeting with Mr. Kamal Nath Acharya, Ward Chief of Ward 2, Mr. Shiva Sharan Khatri, Ward Chief of Ward 3 and Mr. Uttam Thapa, Ward Chief of Ward 4. The common reconstruction issues identified in the consulted Wards 2, 3 & 4 were - slow progress in tranche disbursement, land ownership issues due to multiple beneficiaries and tenant and land owners (mohi/talsing), family disputes that is causing delays in transfer of ownership. Compared to previous years, there has been slow reconstruction in current year, which could be due to beneficiaries have lost interest in reconstructing their houses and think that the government grant is not enough to build an earthquake resistant house. Further, 2nd tranche of houses that were build immediately after earthquake and before deployment of NRA engineers had been in pending stage.

Field Visit:

- No. of HHs visited: 3
- No. of meetings with engineers: None
- No. of meetings with local officials: 3

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Beneficiaries are losing interest in rebuilding of their earthquake affected houses using government grant	Beneficiaries were informed to consult with engineers in taking inputs about low cost and yet reliable and earthquake resistant houses from design catalogues.	To inform ward office about design catalogues	DLPIU Building, Engineers, Beneficiaries	As early as possible.

Photos



Beneficiary name: Ramkrishna Thapa, Ward no. 2, Suryabinayak Municipality. 1.5 storey RCC house has 6 rooms. Owner has received 1st tranche and applied for 2nd and 3rd tranche together.



Beneficiary name: Ward no 3, Suryabinayak Municipality. Owner has received 1st tranche only and applied 2nd and 3rd tranche together. The house has missed bands from the inspection visit.

Field Visit Reports (Bhaktapur)

Visit 4

Date	Location	Participants
21 June 2019	Ward no. 7 & 8, Suryabinayak Municipality	- Roshan Kesari, M & E Consultant, CLPIU Building - Prabesh Adhikari, DSE, DLPIU Building Bhaktapur - Sachin Malego, HRRP IM Officer - Technical personnel (Saru Chansi Shrestha, Jeena Suwal, Sweta Acharya, Rajani Pradhan Shrestha, Manju Khadka)
Objective(s)	- To observe the reconstruction status of the houses and provide way forward for beneficiaries. - To conduct Ward level coordination meeting with elected local heads	

Why was the visit carried out in this location?

The visit was carried out to in Ward no. 8 and 7 to observe some of the pending 2nd tranche file of houses. The inputs from Er. Roshan Kesari, M & E Consultant has paved way forward for engineers to proceed further tranche approval of beneficiaries.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

<https://drive.google.com/open?id=15Zk2be0hk0rkJuOjdhoJ3i9YmZFgeHw>

Summary

Field Visit:

- No. of HHs visited: 4
- No. of meetings with engineers: None
- No. of meetings with local officials: 1

HRRP Lalitpur and Bhaktapur Coordination Team along with M & E Consultant (DLPIU Building Bhaktapur), District Support Engineer and engineers of DLPIU Building Bhaktapur and of Suryabinayak Municipality conducted field visit Ward no 7 & 8 of Suryabinayak Municipality. The field visit team observed nearly 4 houses in total. Majority of beneficiaries have received upto 2nd tranche and some houses were inspected for 3rd tranche.

Coordination Meeting with Mr. Kiran Thapa Magar, Ward Chief, Ward no .8 Suryabinayak Municipality

Joint M and E visit team interacted with Ward Chief of Ward no. 8 about reconstruction progresses, issues and challenges taking place in Ward areas. Discussions were focused around informing beneficiaries about government deadlines to receive reconstruction grants, to inform beneficiaries to return 1st tranche if they are unwilling to reconstruct house and to sign partnership agreement with government if they are in beneficiaries list. The team informed Ward Chief to prepare list of beneficiaries that have already reconstructed houses before deployment of engineers so that necessary corrective measures can be suggested for them from Building office.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Beneficiaries have yet not taken any measures to correct the houses that were reconstructed before deployment of engineers	Ward Chief was informed to prepare list of houses that were immediately rebuilt after earthquake.	To collect the list of houses and their typologies that were made without consulting engineers so that corrective measures can be suggested to beneficiaries.	Ward office, beneficiaries and engineers	As soon as possible

Photos



Beneficiary name: Sanu Kaji Magar, Ward no 7, Suryabinayak Municipality, BMC house with 2 stories and have taken 1st tranche till now. The owner has applied for 2nd tranche.



Beneficiary name: Arjun Basnet, Ward no 8, Suryabinayak Municipality. BMC house with 1 story has received 2nd tranche till now.

Housing Typology Report



Beneficiary name: Mathura Baniya, Ward no 8, Changunarayan Municipality. Single storey wall system with shutter at front is a BMC house with flexibe roof has received 1st tranche till now. There is lack of roof bands and owner was suggested for correction by jacketing with wire mesh above lintel level



Beneficiary name: Babu Krishna Khatri, Ward no 8, Changunarayan Municipality. BMC wall system house with rigid roof with 1.5 storey has received 1st tranche. Owner has applied for 2nd and 3rd tranche together and the inspection visit has found the house in safe condition to forward further tranches.



Beneficiary Name: Sun Bahadur Jimba, Bhattedanda, Bagmati Rural Municipality One storey structure with stone as infill material. The beneficiary has requested for the 3rd tranche. Dated: 180914

Beneficiary Name: Ajaya Syangtan, Kaleshwor, Mahankal Rural Municipality. One storey plus attic structure with RC band and CGI roof. The beneficiary has requested for 3rd tranche. Dated: 180915

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Though we are in beneficiary's list, land papers issues have restricted us in reconstructing the houses that belongs to big head of the family. How can land issues be solved? How can we take 1 st tranche?	Beneficiary	The issues should be taken into discussion with ward office in presence of ward chief who is responsible for chairing the ward-level grievances management committee. Ward president will take responsibility of taking the issues to further levels of addressing. Beneficiaries should immediately forward this issues from ward level to municipality level as soon as possible in light of the short deadline of Ashad end to claim 1 st tranche. (M & E Consultant, DLPIU Building)
What are the criteria for forwarding files of houses having multiple beneficiaries living in single house?	Ward Chief	Regarding multiple beneficiaries, if they have two entrance doors and two staircases to reach two different houses in same plot of land, and have Building permit and joint land certificates, then tranche application of such houses can be forwarded. (M & E Consultant, DLPIU Building)

Challenges and Way Forward

Challenge	Way Forward
POs are putting efforts to support reconstruction and recovery works however they are conducting activities without legalizing themselves with NRA and district agencies directly.	POs that had been conducting activities related to reconstructed should come into regular system of legalization by submitting project proposal to NRA. This kind of registration of activities details with NRA helps to reduce duplication of tranche payments to beneficiaries and helps boost in transparency of funds channelized into the communities.
After receiving the complete tranche additional storey to the house without proper reinforcement, bands has been observed which makes the structure more vulnerable.	Government should come up with a modality to solve such issues. Beneficiaries should be made aware of the consequence of such construction practice
