

Monthly District Report

Nuwakot, Rasuwa

14 June - 14 July 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Nuwakot	District Facilitation and Coordination Meeting	12-Jul-19	Nuwakot, Bidur Municipality, DCC Hall	Satya Narayan Chaudhary	Meeting minutes Photos
	District Coordination Meeting with POs	26-Jun-19	Nuwakot, Bidur Municipality, DLPIU-GMaLI Hall	Badri Pyakurel District Coordinator badri.pyakurel@hrrp.nepal.oeg	Meeting Minutes Photos
	Interaction on STFC Program implementation in Nwakot by GOI/UNIPS Presentation from DLPIU and Orientation by CLPIU.	7 Jun-19	Kathmandu	Badri Pyakurel District Coordinator badri.pyakurel@hrrp.nepal.oeg	
	Email and followup calls to ALI Palika of Nuwakot Rasuwa to upload the Palika Profile. Most of the palikas have uploaded the Profiles.	19-25 Jun- 19	Office, Bidur	Badri Pyakurel District Coordinator badri.pyakurel@hrrp.nepal.oeg	Palikas Website
	Visit to Gorkha GMALI. CLPIU, GMALI and NRA team has visited Barpak and one meeting has organized in DCC Gorkha. Mayor of Gorkha Municipality, DCC Chair, GMALI and DLPIU Building have presented the meeting.	9-10 July, 19	Gorkha District, DCC Gorkha	Badri Pyakurel District Coordinator badri.pyakurel@hrrp.nepal.oeg	Photos

Summary of events during this period

Rasuwa	Joint Monitoring Field Visit with CLPIU/DLPIU building	20/21-Jun-19	Rasuwa, Uttargaya Rural municipality, Ward 1,2	Badri Pyakurel District Coordinator badri.pyakurel@hrrp.nepal.oeg	
	Follow up calls and mails to upload palika profile .	23-25 Jun, 19		Badri Pyakurel District Coordinator badri.pyakurel@hrrp.nepal.oeg	Emails

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Rasuwa District Facilitation Meeting	TBD	GMALI Rasuwa	

News & Updates

District Facilitation and Coordination Meeting in Nuwakot

A district facilitation and coordination meeting of reconstruction committee was organized by DLPIU-GMaLI in DCC hall, Bidur Nuwakot on 12 July 2019. The meeting was chaired by DCC chief Santa Man Tamang in the presence of 33 participants including all the district chief i.e., CDO, DCO, DLPIU-GMaLI, Building, Education, survey, Land and revenue, Financial Controller General Office, bank and representatives from partner organizations.

The forum had discussed over the agendas regarding relocation, displaced and landless beneficiaries' issues.

Key Points of the meeting;

- progress updated 95% second tranche 55% third tranche
- 238 relocation hh has completed in 5 integrated settlement
- Mott Macdonald has plan to extend other 4 Palikas: Belkotgadhi Municipality, Suryagadhi RM, Kispang RM and Meghang RM
- It is decided to ask the geo hazard survey report from NRA As soon as possible. The committee has requested to coordinate to partner organization with local body for coming year plan.


Tranche Status (Nuwakot)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Belkotgadhi Nagarpalika	10719	11037	10463	10463	9371	4620	256	7	7	0
Bidur Nagarpalika	15204	13103	12034	12034	11126	8034	240	90	90	0
Dupcheshwar Gaunpalika	5827	5884	5702	5702	5432	4699	35	1	1	0
Kakani Gaunpalika	6905	6954	6481	6481	5858	4170	175	49	49	0
Kispang Gaunpalika	4637	4788	4390	4390	4142	3797	51	1	1	0
Likhu Gaunpalika	4973	5110	4761	4761	4234	3031	155	15	15	0
Meghang Gaunpalika	4739	4520	4280	4280	4126	3661	152	1	1	0
Panchakanya Gaunpalika	4243	4566	4324	4324	3820	2877	96	6	6	0
Shivapuri Gaunpalika	6292	6531	6241	6241	5440	4220	65	0	0	0
Suryagadhi Gaunpalika	4560	5024	4898	4898	4451	3345	17	1	1	0
Tadi Gaunpalika	4476	4592	4480	4480	4219	3430	23	3	3	0
Tarkeshwar Gaunpalika	4573	4713	4340	4073	#REF!	3467	254	3	3	0

Graph of Tranche Status:

Reconstruction- Tranche Status

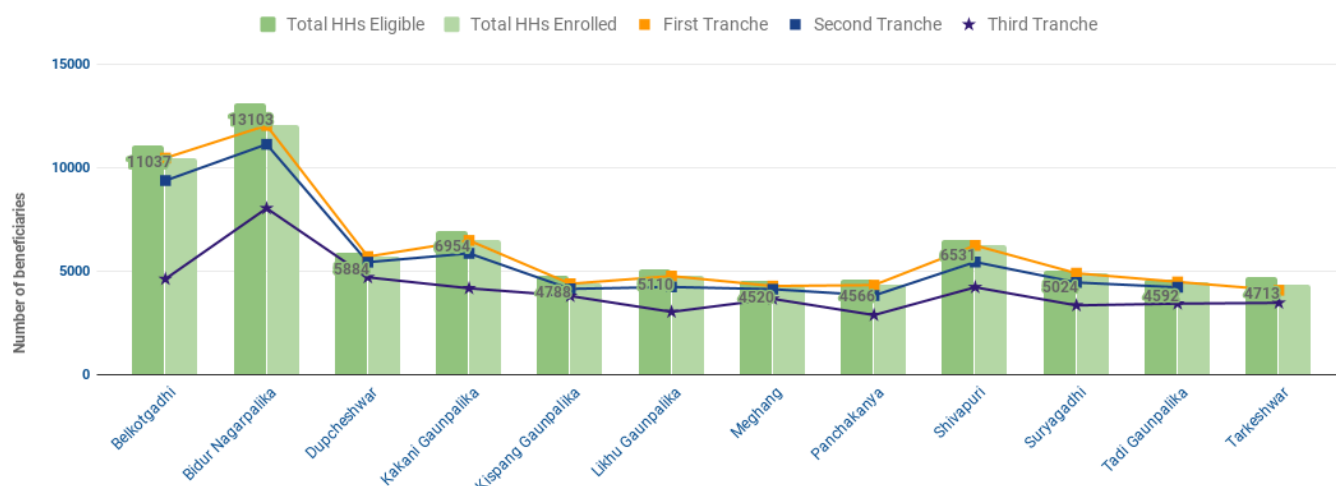

Graph for Retrofitting Status:

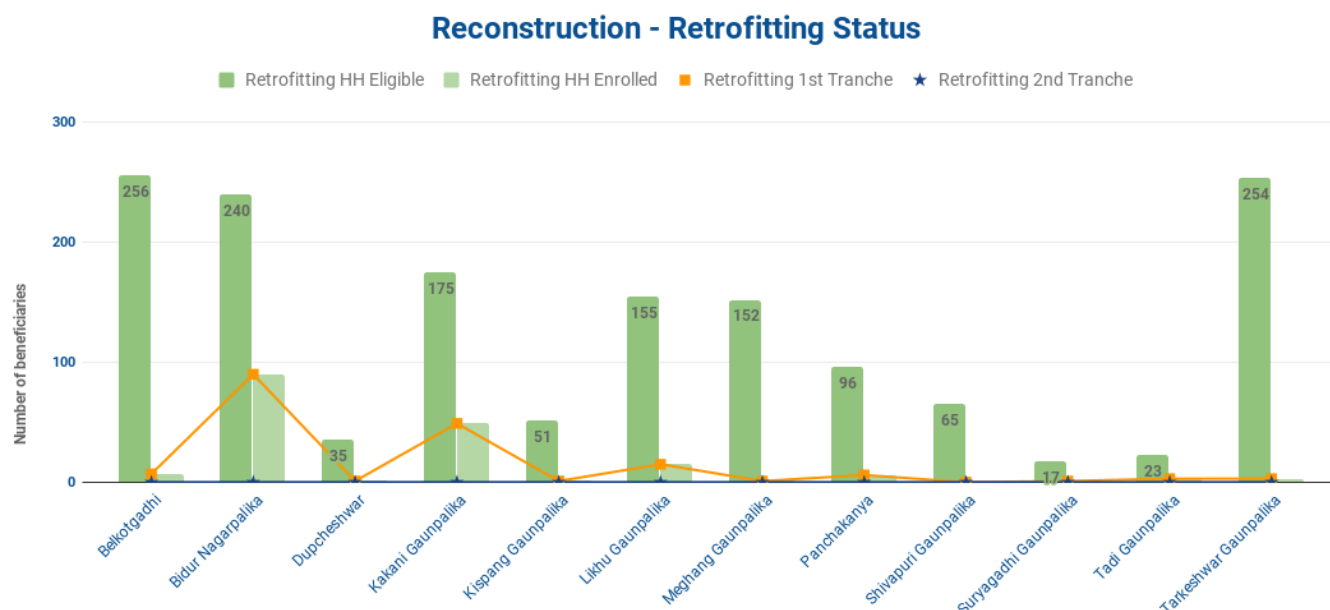


Tranche Status (Rasuwa)


Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Gosaikunda Gaunpalika	2224	1979	1872	1854	1754	1447	84	68	67	0
Kalika Gaunpalika	2530	2591	2495	2495	2425	2325	35	13	13	0
Naukunda Gaunpalika	3298	3349	3308	3308	3206	3059	18	13	13	0
Parbati Kunda Gaunpalika	1981	1964	1822	1822	1684	1438	59	34	34	0
Uttargaya Gaunpalika	2611	2631	2305	2305	2056	1909	26	11	11	0

Graph of Tranche Status:

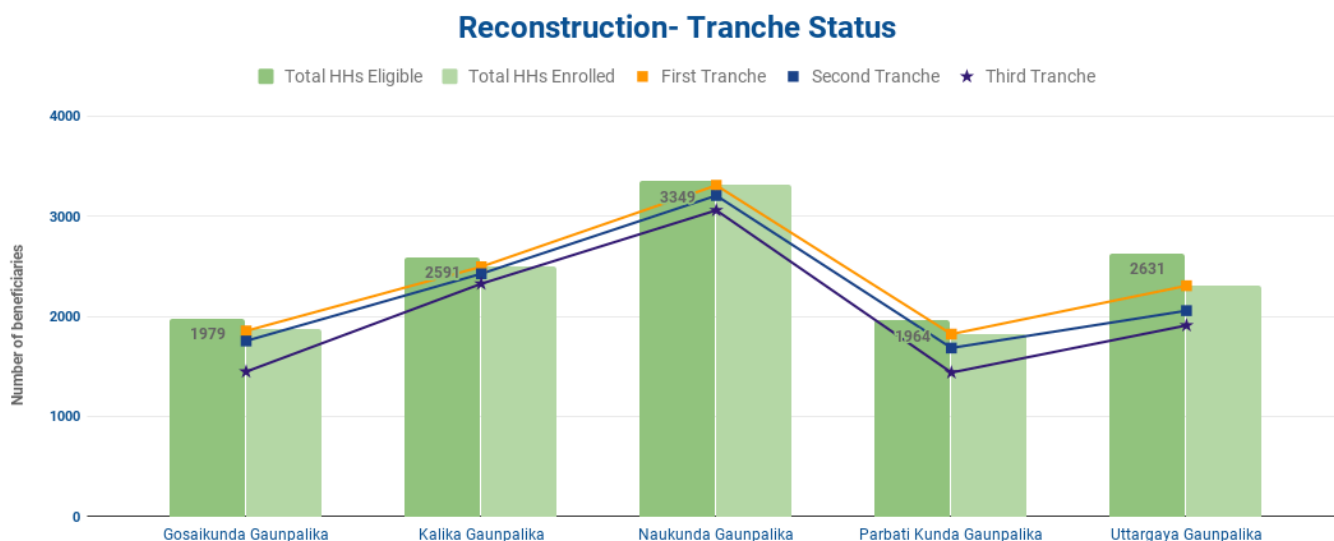

Graph for Retrofitting Status:

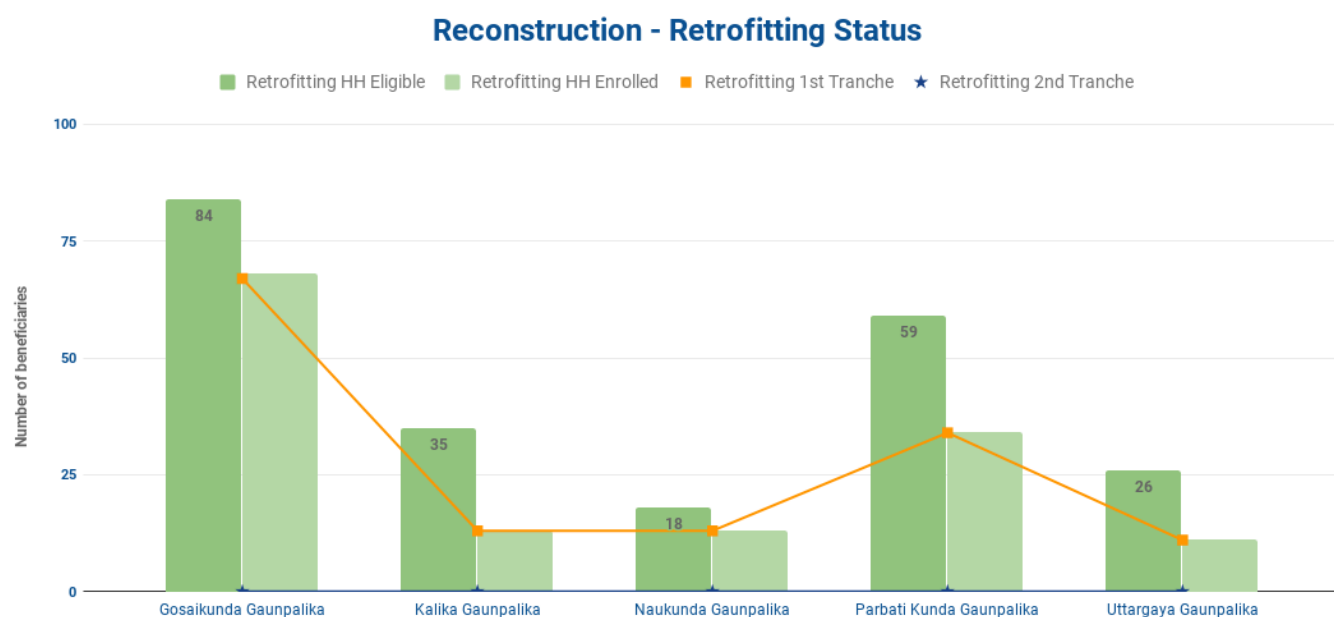

Field Visit Reports (Rasuwa)

Visit 1

Date	Location	Participants
20/21-Jun-19	Ward no. 1, Uttargaya Rural Municipality, Rasuwa	- Prabhu Ram Pokharel, M/E consultant-CLPIU - Badri Pyakurel, District Coordinator, HRRP-Nuwakot - Manisha Rai, Hub Team- Information Management Officer, HRRP-Nuwakkot
Objective(s)	- To understand the factors of low reconstruction progress - To interact with the beneficiaries to understand their status - To discuss with ward representatives and field engineers on reconstruction issues and updates	

Why was the visit carried out in this location?

HRRP Rasuwa/Nuwakot team conducted a joint monitoring field visit with M/E specialist from CLPIU-Building to ward no 1 and 2 of Uttargaya Rural Municipality in Rasuwa district. The visit was organized to find the blocking factors in reconstruction progress as data shown as 53% in first tranche, and low progress in 2nd and 3rd tranche by 30% and 22% respectively in ward no. 1 of Uttargaya RM.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

- No. of HHs visited: 6
- No. of meetings with engineers: 2
- No. of meetings with local officials: 1


HRRP Rasuwa/Nuwakot district team along with M & E Consultant from DLPIU NRA Building conducted joint field monitoring at Ward no 1 and 2 of Uttargaya Rural Municipality, Rasuwa district. All among the observed houses were compliant. The main reconstruction issue in the area is vulnerable beneficiaries from unsafe land as reported by geological study. By the reason, 738 beneficiaries out of 1020 are listed as vulnerable beneficiaries from ward no.1 who are to be relocated in safer land. However, 407 beneficiaries have purchased land in safer place among the 738 beneficiaries for relocation. In addition, most of them have purchased land in out of the place of ward no. 1. By the relocation case, reconstruction progress is show as low in this ward.

Interaction with ward chairperson and DLPIU technical staffs in ward no. 2

A brief update and sharing discussion of reconstruction status made with ward chairperson Mr. Khuwa Bahadur Gurung along with ward secretary, ward member, and NRA field engineers at ward office. Also, field engineers were suggested to keep CS entry on priority and inspection for third tranche simultaneously.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Beneficiaries' complain of delaying in tranche release	Coordination and follow up with respective and responsible bodies		HRRP, Field Engineers, DLPIU, Bank	

Photos

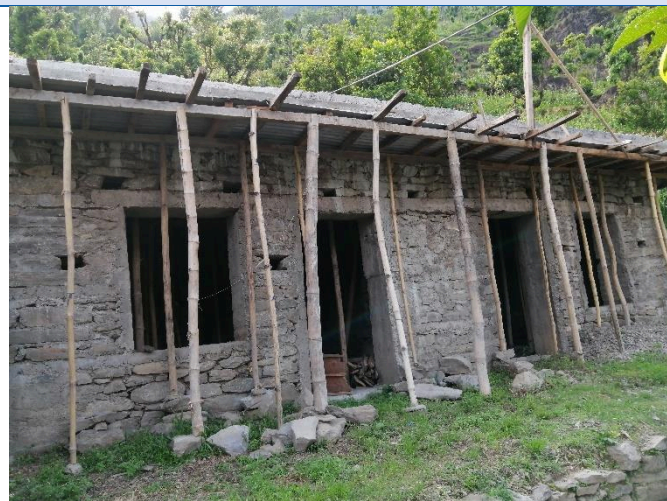

Beneficiary name: Prem Kumari Tamanag, Bhage Tole, Dadagau ward no.2, Uttargaa Rural Municipality, Rasuwa. 1 storey 2 roomed Stone Mortar Cement (SMC) with rigid roof. Beneficiary has received all the tranches.



One roomed house of Ratna Bahadur Tamang reconstructed used dry stone with flexible roof in Salletar, ward no. 1 in Uttargaya RM, Rasuwa.

Photos



A ward level coordination meeting held in the ward office of ward no.2, Uttargaya RM in the presence of ward chief, ward secretary, ward member and field engineers.




Beneficiary name: Bam Bahadur Adhikari, Dadagau, Ward no 2, Uttargaya RM. A Loadbearing BMC structure of 4 rooms and one storey with attic. Beneficiary received all the 3 installments of GoN housing grant already.

Housing Typology Report



Beneficiary name: Ram Sharan Adhikari, Ward no 2, Dadagau, Uttargaya RM. 1 storey, 2 roomed Hollow block structure with rigid roof. The beneficiary has already received all tranches.

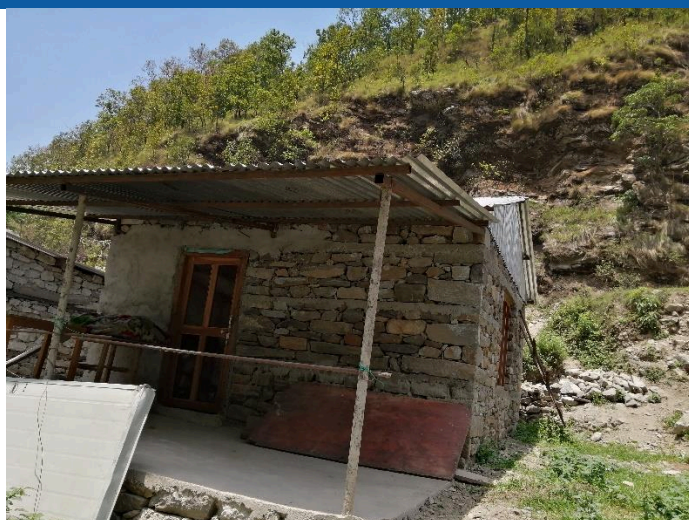

Beneficiary name: Ratna Bahadur Tamang, Ward no. 1, Salletar, Uttargaya RM. 1 roomed dry-stone house.
