

Monthly District Report

Lalitpur, Bhaktapur

23 August – 27 September 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Lalitpur	CRS Nepal along with HRRP has organized field visit of Mr. Marc DSilva, Asia Regional Director, CRS International in Ward no 22, Lalitpur Metropolitan City. The purpose of field visit was to take stock of urban reconstruction activities, its issues, challenges and way forward in areas of Bungmati. The field visit in Bungmati was attended by key program personnels of CRS Nepal and HRRP along with POs (UNHabitat, CIUD, Lumanti, Sabah Nepal and BARDEC) that are currently involved in conducting urban reconstruction, heritage recovery and tourism promotion activities in Bungmati area.	17 Sept. 2019	Ward no 22 (Bungamati), Lalitpur Metropolitan City, Lalitpur district	Mr. Minar Thapa Magar Deputy National Coordinator HRRP Contact: 9841076869 minar@hrrpnepal.org	field visit section
	HRRP Lalitpur district team joined NRA DLPIU GMALI Lalitpur in Joint M & E visit at Ward no 1, Bukhel, Mahankal Rural Municipality, Lalitpur district. Ward coordination meeting was organised with Ward Chair of Ward no 1, Bukhel where several issues of delays in shelter reconstruction was discussed. The team also observed reconstruction status of 4 houses in total.	25 Sept. 2019	Ward no 1, Bukhel, Mahankal Rural Municipality, Lalitpur district	Mr. Yamnath Giri M & E Specialist DLPIU GMALI Lalitpur Manbhawan, Lalitpur Contact: 9851239785, yamnathgiri2014@gmail.com	field visit section, ward-level meeting minute
	Tranche status of Lalitpur updated to GD sheet in Palika Profile	25 Sept. 2019		Sachin Malego IM Officer, HRRP	
	Preparation of Ward wise GIS maps of Ward no 21 and 22, Lalitpur Metropolitan City	16 Sept. 2019			
	Contact list update, 5 W update, upload of shelter photos	23 Sept. 2019		Sachin Malego IM Officer, HRRP Ms. Ambika Amatya District Coordinator	
	Tranche Maps Prepared of Lalitpur	24 Sept. 2019		Sachin Malego IM Officer, HRRP	
	Palika Profile Updated Lalitpur	24 Sept. 2019		Sachin Malego IM Officer, HRRP Ms. Ambika Amatya District Coordinator	
Bhaktapur	The general ward-level coordination meeting was conducted at Ward office, Ward no. 7, Gundu, Suryabinayak Municipality. Ward Chief in presence of	10 Sept 2019	Ward no 7, Gundu, Suryabinayak Municipality		Ward -level coordination meeting minute

Summary of events during this period

representatives from DLPIUs GMALI and Building Bhaktapur (M & E Consultant, M & E Specialist, Palika Reconstruction Engineers) and HRRP attended the meeting. The key agenda of the coordination meeting was to discuss on delays in reconstruction in Ward no 7 and suggest way forward.					
Joint M & E Visit was conducted at Ward no. 9 (Nangkhel) of Suryabinayak Municipality by HRRP Lalitpur District Coordination Team along with representatives from DLPIUs GMALI and Building Bhaktapur (M & E Consultant, M & E Specialist, Palika Reconstruction Engineers)	10 Sept. 2019	Ward no. 9, Nangkhel, Suryabinayak Municipality	Er. Roshan Keshari M & E Consultant, DLPIU Building Bhaktapur roshankesari20@gmail.com 9841640357	Joint M & E visit section	
The general ward-level coordination meeting was conducted at Ward office, Ward no. 9, Nangkhel, Suryabinayak Municipality. Ward Chief in presence of representatives from DLPIUs GMALI and Building Bhaktapur (M & E Consultant, M & E Specialist, Palika Reconstruction Engineers) and HRRP attended the meeting. The key agenda of the coordination meeting was to discuss on delays in reconstruction in Ward no 9 and suggest way forward.	10 Sept 2019	Ward no 9, Nangkhel, Suryabinayak Municipality	Er. Roshan Keshari M & E Consultant, DLPIU Building Bhaktapur roshankesari20@gmail.com 9841640357	Ward -level coordination meeting minute	
The general palika level coordination meeting was conducted at Palika office of Bhaktapur, Madhyapur Thimi and Suryabinayak Municipality. The coordination meeting at Madhyapur and Suryabinayak Municipality was attended by Chief Administrative Officer along with Palika Reconstruction engineers in presence of representatives from DLPIU GMALI and Building Bhaktapur (M & E Consultant, M & E Specialist) and HRRP team member attended the meeting.	11 Sept 2019	Respective Palika office Bhaktapur, Madhyapur Thimi and Suryabinayak Municipality		Palika -level coordination meeting minute	
Joint M & E Visit was conducted at Ward no. 8, Sipadol, Suryabinayak Municipality by HRRP Lalitpur District Coordination Team along with representatives of DLPIU Building Bhaktapur (District Support Engineer, Palika Reconstruction Engineers).	12 Sept 2019	Ward 8, Sipadol, Suryabinayak Municipality		Joint M & E visit section	
DLPIU GMALI Bhaktapur organized an interaction program on preparing action plan to track the reasons of delays in accessing 2 nd tranche and 3 rd tranche by beneficiaries of Bhaktapur district further. The program was attended by NRA CEO, elected local heads, heads and deputy heads of CLPIUs (Building and GMALI), DLPIU Building, focal engineers and media personnel.1	12 Sept. 2019	Home Sweet Home Events, Bhaktapur	Mr. Dhruva Gaida Chief, DLPIU GMALI Bhaktapur Contact: 9851221570 dgaida022@gmail.com		
HRRP Bhaktapur Coordination Team along with DLPIU Building Bhaktapur organised an interaction & orientation program for retrofitting beneficiaries at Ward no 4 of Changunarayan Municipality and also observed houses of few beneficiaries who	16 Sept 2019	Ward no 4, Changunarayan Municipality	Er. Shiva Kumar Bhandari District Support Engineer DLPIU Building Bhaktapur diyabhandari80@gmail.com 9857045118	Joint M & E visit section	

Summary of events during this period

intends to conduct retrofitting of their houses. The team also organised Joint M & E Visit was conducted at Ward no. 1, Sirutar, Suryabinayak Municipality		Ward no. 1, Sirutar, Suryabinayak Municipality		
Contact list update, 5 W update, upload of shelter photos	23 Sept. 2019		Sachin Malego IM Officer, HRRP	
Tranche Maps Prepared of Bhaktapur	24 Sept. 2019		Ms. Ambika Amatya District Coordinator	
Palika Profile Updated Bhaktapur	24 Sept. 2019		Sachin Malego IM Officer, HRRP	
			Ms. Ambika Amatya District Coordinator	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Joint M & E visit to observe reconstruction efforts of beneficiaries in Bhaktapur and Lalitpur districts	October 2019/ Various wards of Municipalities of Lalitpur and Bhaktapur district	DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team	Ms. Ambika Amatya District Coordinator HRRP Lalitpur and Myagdi Cluster
General Palika level and Ward level meeting and consultation with elected ward officials over the reconstruction progress and status of the visited wards of Bhaktapur and Lalitpur district	October 2019/ Various wards of Municipalities of Lalitpur and Bhaktapur district	DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team	

News & Updates


- Under Secretary Mr. Shiva Ram Gelal has been appointed as Chief of DLPIU GMALI Lalitpur effective from 18 September 2019 (1st Ashoj 2076)
- Palikas of Bhaktapur district are engrossed in preparing actionplan related to tracking reasons of delays in accessing 2nd tranche and 3rd tranche by beneficiaries who are enrolled in partnership agreement with NRA and those who have taken 1st tranche.

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bagmati Gaunpalika	3361	3370	3138	3127	2642	2126	252	197	180	0
Godawari Nagarpalika	10950	9604	8062	7999	2868	2365	323	136	133	0
Konjyosom Gaunpalika	2580	2156	2086	2082	1947	1448	372	328	319	0
Lalitpur Mahanagarpalika	6594	7408	6357	6338	1374	887	275	125	120	0
Mahalaxmi Nagarpalika	4409	3669	3132	3105	1056	903	83	53	50	0
Mahankal Gaunpalika	2451	2271	2239	2238	1837	1260	61	58	57	0

Tranche Status (Lalitpur)

Graph of Tranche Status:

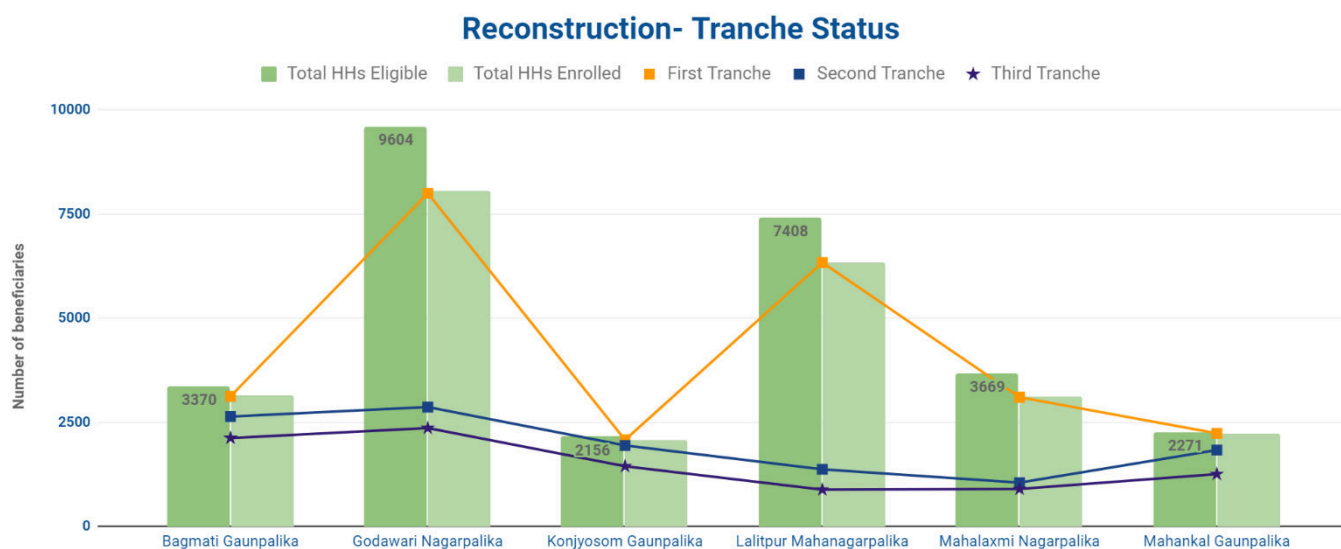

Graph for Retrofitting Status:

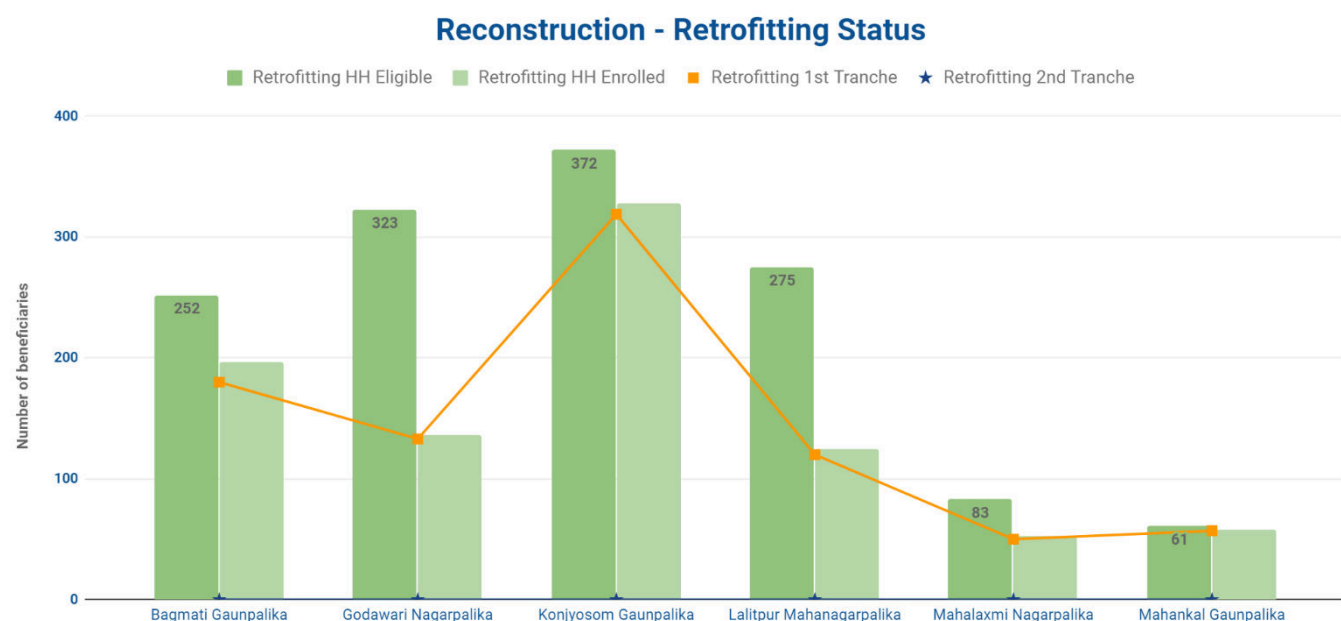


Tranche Status (Bhaktapur)

Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Bhaktapur Nagarpalika	8175	7656	5637	5637	1816	1621	161	43	43	0
Changunarayan Nagarpalika	11059	11000	9826	9826	3744	3585	212	109	109	0
Madhyapur Thimi Nagarpalika	3015	2333	2080	2080	725	704	95	61	61	0
Suryabinayak Nagarpalika	7948	7425	6998	6998	2933	2748	234	105	105	0

Graph of Tranche Status:

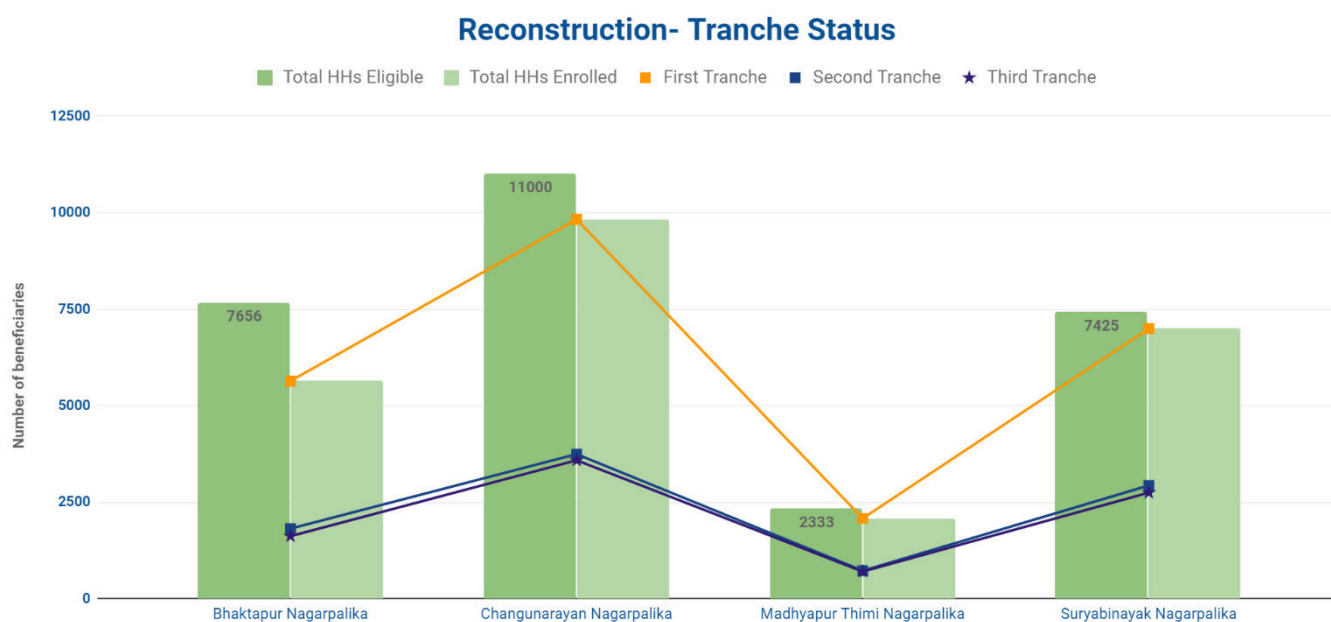

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

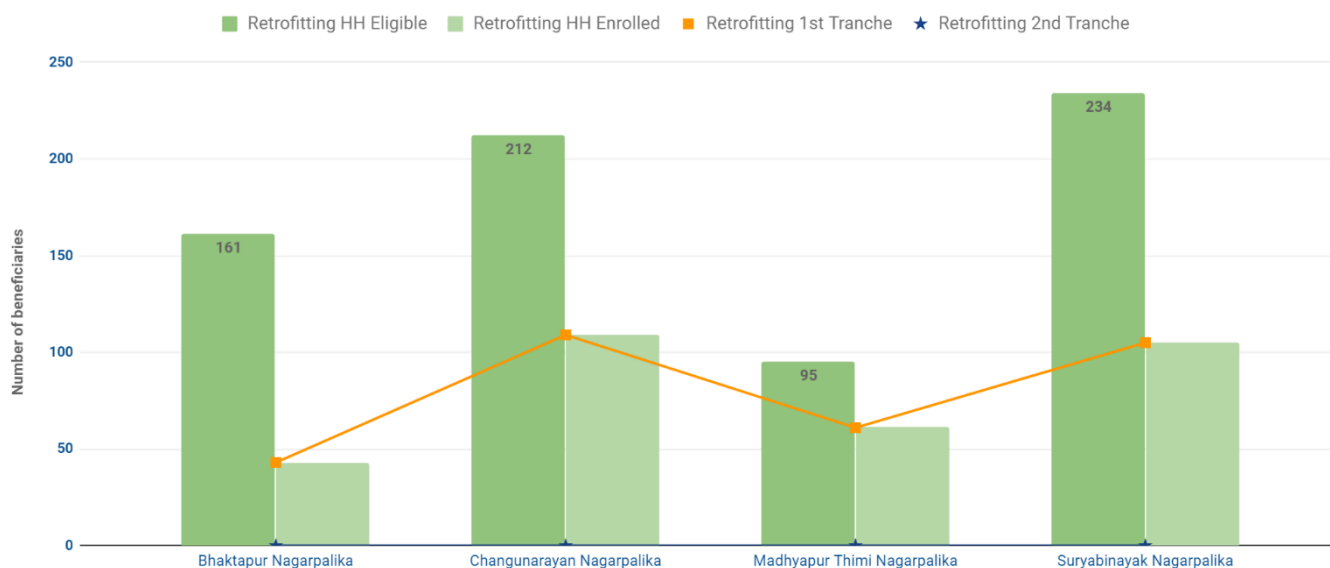

Field Visit Reports (Lalitpur)

Visit 1

Visit 1		
Date	Location	Participants
17 September 2019	Ward no. 22, Bungmati, Lalitpur Metropolitan City Municipality, Lalitpur district	• Marc DSilva, Asia Regional Director, CRS International • Milan Mukhia, Assistance Country Director, CRS Nepal • Joanna Olsen, Emily Lobo, Adeel Javaid (CRS Nepal) • Minar Thapa Magar, Deputy National Coordinator, HRRP • Sufi Mohammad Faiz, DMT Coordinator, HRRP • Ambika Amatya, District Coordinator, HRRP Lalitpur Cluster • Anil Tuladhar, Administration and Finance Coordinator, CIUD • Ichha Shova Maharjan, DLPIU Engineer, LMC • Newton Maharjan and Lumanti Joshi (Lumanti) • Prabin Bajracharya, Senior Programme Officer, UNHabitat • Ambir Raj Shakya, Ward Chair, Ward no 22, Bungmati, LMC • Ward Secretary, Ward no 22, LMC • Prem Bhakta Maharjan, Advisor, BARDEC • Sagar Tuladhar, Jamuna Tamang, Junu Rijal (Ward no 22, Ward Members) • Rita Maharjan, Social Mobilizer, BARDEC
Objective(s)	• To observe reconstruction status and progresses of beneficiaries in Ward no 22, Bungmati, LMC • To take updates of urban reconstruction and recovery initiatives taken forward by POs in Ward no.22 in Bungmati • To take feedbacks by beneficiaries and from ward stakeholders about recovery initiatives taking place in Ward no 22, Bungmati.	
Why was the visit carried out in this location?		
• To organize the urban recovery and reconstruction initiatives taking place in Ward no 22 Bungmati to complement the visit of CRS Asia Regional Director.		
Summary		
ASIA Regional Director, Marc D'Silva visited Nepal in 3 rd week of September. A short visit to Ward no 22, Bungmati, Lalitpur Metropolitan City was organised by HRRP and Lalitpur District Coordination Team whereby focusing on getting to explore CRS Nepal team, programming and operational context from urban recovery and urban reconstruction to development moving forward.		
There are four POs involved in reconstruction efforts taking place in Bungamati area; Center for Integrated Urban Development (CIUD) in infrastructure development. Lumanti in social mobilization. Sabah Nepal in carrying forward income generation initiatives and BARDEC looking		

after regeneration and reconstruction of culturally important heritage monuments of Bungmati area. Currently NRA in direct coordinating with BARDEC is reconstructing Rato Machhindranath temple, in which fund assistance were provided by Government of Srilanka.

The key challenges of shelter reconstruction highlighted in Ward no. 22 is related with maintaining the cultural authenticity of heritage areas, addition of extra storeys by beneficiaries other than mentioned in building drawing, disputes over land ownership among multiple beneficiaries and small parcel land holding and poor economic capacity of beneficiaries. Lack of proper awareness among beneficiaries about building bylaws and minimum requirements have questioned the resilience capacity of the reconstructed houses. Short presentation was conducted by Senior Programme Officer of UNHabitat on Urban Recovery and Private Housing Reconstruction Works on-going in core areas of Bungmati.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Beneficiaries are rebuilding their houses in core area by adding storeys upto 4 or more than 4 storeys however the municipal bylaws don't allow to rebuild houses more than 3.5 stories.	There is need of strong motivation to forward among beneficiaries in order to maintain cultural authenticity of Bungmati area as well as increasing the resilience capacity of rebuild houses.	Concerned stakeholders (Ward and POs) should do their best to conduct awareness among beneficiaries to adhere to municipal bylaws.	Beneficiaries, Ward Office, LMC	As soon as possible

Photos



Image: Marc DSilva, Asia Regional Director, CRS International is observing the private housing reconstruction as well as the urban recovery of heritage settlements in Bungmati, Ward no 22, Lalitpur Metropolitan City.



Image: Sharing by POs to the team from Asia Regional Director of CRS, programme personnel from CRS Nepal, HRRP and that is implementing private housing initiative as well as regeneration of heritage settlements and tourism promotion activities in Bungmati, Ward no 22, Lalitpur Metropolitan City

Field Visit Reports (Bhaktapur)

Visit 2

Visit 2		
Date	Location	Participants
10 September 2019	Ward no. 9, Nangkhel, Suryabinayak Municipality, Bhaktapur district	• Ambika Amatya, District Coordinator, HRRP Lalitpur Cluster • Roshan Kesari, M & E Consultant, CLPIU Building Bhaktapur • Vibek Gautam, M & E Specialist, DLPIU GMALI Bhaktapur • Ajay Gelal, Engineer, DLPIU GMALI Bhaktapur • Engineers, Suryabinayak Municipality (Dhana Kumari Tamang, Jeena Suwal, Kiran Kawa, Sujata Gainju)
Objective(s)	• To conduct Ward level coordination meeting with Ward Chief and discuss on reconstruction efforts taking place in Ward no 7 (Gundu) & Ward no 9 (Nangkhel), Suryabinayak Municipality • To observe the reconstruction status of the houses and provide relevant suggestions further in Ward no 9, Nangkhel, Suryabinayak Municipality	
Why was the visit carried out in this location?		

Suryabinayak Municipality is in P1 priority as according to HRRP's municipal targeting in shelter reconstruction. Therefore, this Joint Monitoring Visit was organised to influence way forward in ward level reconstruction progress through ward level coordination meeting and to influence the roles from Ward office for expediting the reconstruction progress.

Summary

HRRP Bhaktapur Coordination Team along with team members from DLPIU GMALI and Building Bhaktapur (M & E Consultant, M & E Specialist and Palika Engineers) conducted field visit Ward no 9, Nangkhel, Suryabinayak Municipality. The field visit team observed nearly 2 houses in total that have accessed all three tranches from government of Nepal.

Meeting with Ward Chief, Ward no 7, Gundu, Suryabinayak Municipality

The Joint M & E visit team also conducted ward -level coordination meeting with Mr. Rabindra Sapkota, Ward Chief of Ward no 7, Gundu. Meeting was focused on updating with reconstruction status and issues perpetuated in Ward no 7 that propelled delayed reconstruction. There are total of 1350 beneficiaries, among which 1208 have taken 1st tranche, 492 have taken 2nd tranche and 490 have accessed 3rd tranche. The Ward Chief agreed to issue public notice for earthquake affected beneficiaries that have taken 1st tranche but neither has taken 2nd tranche nor initiated reconstruction of their houses. Ward Chief insisted for interacting with beneficiaries one to one to track the reasons of not initiating reconstruction of their houses and to convince them to return 1st tranche if reconstruction did not proceed.

Meeting with Ward Chief, Ward no 9, Nangkhel, Suryabinayak Municipality

The Joint M & E visit team also conducted ward -level coordination meeting with Mr. Upendra Raj KC, Ward Chief of Ward no 9, Nangkhel. Meeting was focused on updating with reconstruction status and issues perpetuated in Ward no 9. Ward Chief highlighted reasons of delays in reconstruction in Ward no 9 because of presence of houses in other place, poor economic condition, Mohi Talsing case and disputes between siblings. There are total of 1214 beneficiaries, among which 1129 have taken 1st tranche, 439 have taken 2nd tranche and 394 have accessed 3rd tranche. By issuing public notice for earthquake affected beneficiaries that have taken 1st tranche but neither has taken 2nd tranche nor initiated reconstruction of their houses, the Ward Chief insisted to discuss with individual beneficiaries who are interested in retrofitting work of their house and also with beneficiaries who are delaying rebuilding of houses.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Beneficiaries are reluctant towards rebuilding of their quake damaged houses despite passing 4.5 years of Nepal earthquake 2015	Ward office should proactively issue public notice for earthquake affected beneficiaries that have taken 1 st tranche but neither has taken 2 nd tranche nor initiated reconstruction of their houses in order to interact with them on individual basis as far as possible. Even after this serious discussion, if beneficiaries donot want to rebuild their houses, then Ward Office must put effort to convince them to return 1 st tranche.	To issue public notice earthquake affected beneficiaries for tracking the delays in reconstruction of houses.	Ward Office, engineers, DLPIU(GMALI & Building), M & E Consultant	By Kartik end 2076 and beyond

Photos



Image: Ward level coordination meeting in progress at Ward no. 9, Nangkhel, Suryabinayak Municipality. The meeting was attended by Ward Chief and Joint M & E visit team members including of M & E Consultant, M & E Specialist and engineers of concerned palika/ward



Beneficiary name: Rajan Pariyar, Ward no 9, Nangkhel, Suryabinayak Municipality. One storey wall system BMC house with rigid roof has rebuild soon after earthquake & before deployment of engineers. The beneficiary applied correction methods by keeping all kinds of bands such as lintel, sil and corner stitch. After correction methods, beneficiary accessed all three tranches from government of Nepal.

Field Visit Reports (Bhaktapur)

Visit 3

Date	Location	Participants
12 September 2019	Ward no 8, Sipadol, Suryabinayak Municipality, Bhaktapur district	- Shiva Kumar Bhandari, Prabesh Adhikari (District Support Engineers, DLPIU Building Bhaktapur) - Manisha Suwal, Engineer, Suryabinayak Municipality - Ambika Amatya, District Coordinator, HRRP
Objective(s)	To observe the reconstruction status of the houses and provide way forward for beneficiaries.	

Why was the visit carried out in this location?

Suryabinayak Municipality is in P1 priority as according to HRRP's municipal targeting in shelter reconstruction. Large pockets of this Palika have been unreachable in terms of monitoring of the houses in reconstruction phase. Therefore, this Joint Monitoring Visit was organized to influence way forward in ward level reconstruction progress through ward level coordination meeting.

Summary

HRRP Lalitpur and Bhaktapur Coordination Team along with District Support Engineer and engineers Suryabinayak Municipality conducted field visit Ward no 8, Suryabinayak Municipality. The field visit team observed nearly 4 houses in total. The visit was specifically targeted to cover the pending 2nd tranche file of some houses as well as observed one house that is in retrofitting list. Among the observed houses, one house belonged to multiple beneficiaries in which separate entrance and separate staircase was kept with joint building drawing.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Beneficiaries are also intending to retrofit their houses but they lack proper technical assistance as well as motivation to conduct.	Beneficiaries were informed to consult with municipal engineers and also with DLPIU Building office in discussing the proper designs for retrofitting.	To inform ward office about retrofitting of houses	DLPIU Building, Engineers, Beneficiaries	As early as possible.

Photos



Beneficiary name: Gauri Thapa, Ward no. 8, Sipadol, Suryabinayak Municipality has 2 storey load bearing house which was damaged from 2015 earthquake. Gauri Thapa is the full reconstruction beneficiary, but the owner intended to apply retrofitting measures therefore has applied application to shift into retrofitting list. Beneficiary was suggested to contact reconstruction engineers once approves for retrofitting list.



Beneficiary name: Surya Bahadur Khaitu and Indra Bahadur Khaitu, Ward no 8, Sipadol, Suryabinayak Municipality. The house belongs to multiple beneficiaries. 2.5 storey RCC pillar system structure is in rebuilding phase and owners have placed two staircase and 5 rooms in each house. Owner has already received 1st tranche only and is eligible for 2nd tranche too.

Field Visit Reports (Bhaktapur)

Visit 4

Date	Location	Participants
16 September 2019	Ward no. 1, Sirutar, Suryabinayak Municipality	- Shiva Kumar Bhandari, Prabesh Adhikari (District Support Engineers, DLPIU Building Bhaktapur) - Manisha Suwal, Engineer, Suryabinayak Municipality - Ambika Amatya, District Coordinator HRRP - Monika Bajimaya Shrestha, DMT IM Coordinator, HRRP - Technical personnel of Suryabinayak Municipality
Objective(s)	To observe the detail status of the houses of beneficiaries who intends to conduct retrofitting measures in their houses	

- To provide way forward and suggestions to beneficiaries in rebuilding or retrofitting of their houses.

Why was the visit carried out in this location?

The visit was carried out in Ward no. 1, Sirutar, Suryabinayak Municipality to observe details of houses in order to provide suggestions to them regarding conducting retrofitting process in their houses.

Summary

HRRP Lalitpur and Bhaktapur Coordination Team along with Support Engineer and engineers of DLPIU Building Bhaktapur and of Suryabinayak Municipality conducted field visit Ward no 1 of Suryabinayak Municipality. The field visit team observed nearly 5 houses in total. Majority of beneficiaries have received upto 1st tranche and intends to conduct retrofitting measures in their houses.

Orientation on retrofitting measures to beneficiaries in retrofitting list

Joint M and E visit team interacted with beneficiaries in retrofitting list belonging to Ward no 2, 3, 4 and 5 of Changuanarayan Municipality, Bhaktapur district. Ward Chief of Ward no. 4 expressed the participants about reconstruction progresses, issues and challenges taking place in Ward no 4. The team of District Support Engineers, DLPIU Building Office, Bhaktapur informed the participants about types of retrofitting designs and its advantages along with tentative cost of retrofitting process in different housing typologies.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Large number of beneficiaries have yet not taken any measures to either rebuild or retrofit their houses despite of taking 1 st tranche and passing 4.5 years of reconstruction process	Ward Chief was informed to prepare list of houses that were immediately rebuilt after earthquake and also issue public notice for beneficiaries who intends to conduct retrofitting of their houses.	To collect the list of houses and their typologies that were made without consulting engineers so that corrective measures can be suggested to beneficiaries. Similarly, intending beneficiaries were informed to contact GMALI office for shifting from full beneficiary to retrofitting.	Ward office, beneficiaries and engineers	As soon as possible

Photos



Beneficiary name: Kul Bahadur Bista, Ward no 1, Sirutar, Suryabinayak Municipality, BMM house with 2 small rooms, 1 storey plus attic have taken 1st tranche till now. The wall in other side of house is slanted from earthquake 2015. The house cannot be rebuild due to right of way issue, therefore the owner was suggested to submit applications in ward/palika office stating to retrofit the house.



Beneficiary name: Bidur Neupane, Ward no 1, Sirutar, Suryabinayak Municipality. 5 storey RCC pillar system house was damaged due to collapse of newly built wall during earthquake 2015. The beneficiary is in retrofitting list & has received 1st tranche. DSE suggested retrofitting measures for this house and informed beneficiary to conduct retrofitting if he can offer. The house has 9'x12" inch walls.

Field Visit Reports (Lalitpur)

Visit 4

Date	Location	Participants
25 September 2019	Ward no. 1 Bukhel, Mahankal Rural Municipality, Lalitpur district Ward no 5, Konjyosom RM, Lalitpur district	- Shivaram Gelal, Project Chief, GMALI Lalitpur - Jeewan Ghimire, Section Officer, GMALI Lalitpur - Yamnath Giri, M & E Specialist, EHRP/GMALI Lalitpur - GMALI Lalitpur representatives (Prakash Pokhrel, Sarada Ghimire) - Ambika Amatya, District Coordinator, HRRP Lalitpur and Bhaktapur District Team

Objective(s)

- To observe the reconstruction status of the houses.
- To interact with beneficiaries and provide relevant suggestions further.
- To conduct ward- coordination meeting with elected local heads.

Summary

HRRP Lalitpur and Bhaktapur Coordination Team along with representatives of GMALI Lalitpur conducted field visit Ward no 1 of Mahankal Rural Municipality, Lalitpur. The field visit team observed nearly 6 houses in total. One of the observed house were not in liveable condition while another already completed house have received 2nd tranche, which was in hybrid housing typology with SMC on ground floor with attic constructed by using BMC with flexible roof.

Meeting with Ward Chief, Ward no 1, Bukhel, Mahankal Rural Municipality

Total Beneficiaries	464
PA enrolled	458
1st tranche	458
2nd tranche	356
3rd tranche	249
Retrofitting	1
Retrofitting- enrolled beneficiary	0
Retrofitting 1 st tranche	0

The ward has 464 beneficiaries under full reconstruction however many of them who havenot proceeded reconstruction have applied application to shift into retrofitting list. retrofitting. Majority of beneficiaries that have taken 2nd tranche have not received 3rd tranche because of the cases of hybrid houses and non completion of houses with roof. Some of the completed houses were found un-liveable and in stranded condition to be utilized as domestic animal shed. Many houses were left stranded with completion of DPC level. Ward Chair claimed that such houses with DPC level only have received 2nd tranche however they havenot proceeded for raising the wall and roof works. It was revealed from Ward Chair that, the technical staffs visits Ward areas upon request from Ward Chief however there has not been any at the spot technical assistance provided by engineers yet. Ward office have been very active and helping beneficiaries to build earthquake resistant structures and encouraging beneficiaries to start reconstruction within the government deadline.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Technical personnel visit the ward areas whenever there is call from Ward Chair.	Technical personnel need to be placed at least twice a week in ward areas for effective technical assistance to the beneficiaries.	Ward Chair will discuss with engineers for their deployment in ward areas twice a week	Ward Chair, Engineer, DLPIU Building,	As soon as possible

Photos



Beneficiary name: Tul Prasad Timilsina, Ward no 1, Bukhel, Mahankal Rural Municipality has 4 roomed house reconstructed with hybrid typology, wall system SMC on ground floor and BMC in attic with flexible roof. The owner has received upto 2nd tranche only. The owner revealed



Beneficiary name: Jhirke Moktan, Ward no 5, Konjyosom Rural Municipality, Lalitpur is reconstructing RCC house with 4 rooms. The owner has received 1st tranche till and has applied for 2nd and 3rd tranche.

that they have-not seen engineer inspecting their house. The owner was informed to contact the Palika office for tracking reasons behind delays in issuing 3rd tranche. The owner was informed about correction measures need to be applied to become complaint for access 3rd tranche.

The beneficiary revealed that engineer deployed in Ward no 5 have not inspected the house but has informed him to send the images of reconstructed house for inspection through viber

Housing Typology Report (Max 4 Photos, Select best photos from each district)



Beneficiary name: Kale Bhandari, Ward no 2, Changunarayan Municipality. RC frame structure, non-Compliance (9"x12" column) was considered unsafe during analysis, constructed immediately after earthquake



Beneficiary name: Pavitra Poudel, Ward no 4, Changunarayan Municipality. Non-Compliance (missing beam, bands, constructed immediately after earthquake)



Beneficiary Name: Bhumi Nanda Timilsina, Kaleshwor, Mahankal Rural Municipality. One storey plus attic SMM structure with RC bands. The beneficiary has received 3rd tranche.

Beneficiary Name: Bishnu Prasad Dulal, Kaleshwor, Ward no 4, Mahankal Rural Municipality. 1 storey plus attic SMM structure with RC bands has requested 3rd tranche from government of Nepal

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Though we are in beneficiary's list & accessed 1 st tranche too. Our current land is not suitable to resettle with rebuilding the house. We also don't have land in another place in whole of Nepal. How can land issues be solved?	Beneficiary	In light of zero existence of any land inside any district of Nepal and upon the unsuitability of current land for rebuilding of house, the beneficiary is eligible to access land right from any assigned forest land with the approval from certified district government counterparts. (M & E Specialist, DLPIU GMALI)
The case related to beneficiaries residing on public land & Guthi land has also caused delays in reconstruction. Such issues have not been properly addressed yet by palika. When such issues will be solved.	Ward Member	NRA has solved many kinds of land related cases therefore, proper documentation Concrete conclusion has not been achieved despite of frequent interactions on legal usage of public land for reconstruction by beneficiaries. District NRA office should take up the issues seriously with concerned agencies. (M & E Specialist, DLPIU GMALI)

Challenges and Way Forward

Challenge	Way Forward
Beneficiaries are adding storeys by avoiding following the standard building bylaws which has added value in increasing risk of the houses	Concerned ward office and municipality office should properly disseminate information of following building bylaws by the beneficiaries. The key messages of resilient structures should be the highlight of such information sharing.
After receiving the complete tranche additional storey to the house without proper reinforcement, bands has been observed which makes the structure more vulnerable.	Government should come up with a modality to solve such issues. Beneficiaries should be made aware of the consequence of such construction practice
