

Reconstruction Progress Update

Dr. Bhishma K. Bhusal

National Reconstruction Authority

Presentation for HRRP on 2074.01.08

Outline

- **Shelter Support**
- **Housing Reconstruction**
- **Beneficiaries, Agreement and First Tranche Status (2074-01-06)**
- **Kathmandu valley: Beneficiaries, Agreement and First Tranche**
- **Grievance Handling**
- **Training**
- **Resettlement**
- **School Reconstruction**
- **Government Buildings**
- **Historically important building**
- **Heritage sites**
- **Budget allocation and expenditure**



Shelter Support

14 hard-hit district

- Identified beneficiaries 626695+ = in 14 districts
- PA made with 90%
- First tranche for 97% of PA signed till 19th April

17 districts


- Survey completed in 17 less affected districts
- 61307 beneficiaries identified




Housing Reconstruction

- Houses under construction 49509
- Already completed without support 18580
- Request for second tranche 33,872. Certified for second tranche 14,312
- 1640 have applied for third tranche and 567 are verified

Beneficiaries, Agreement and First Tranche Status (2074-01-06)

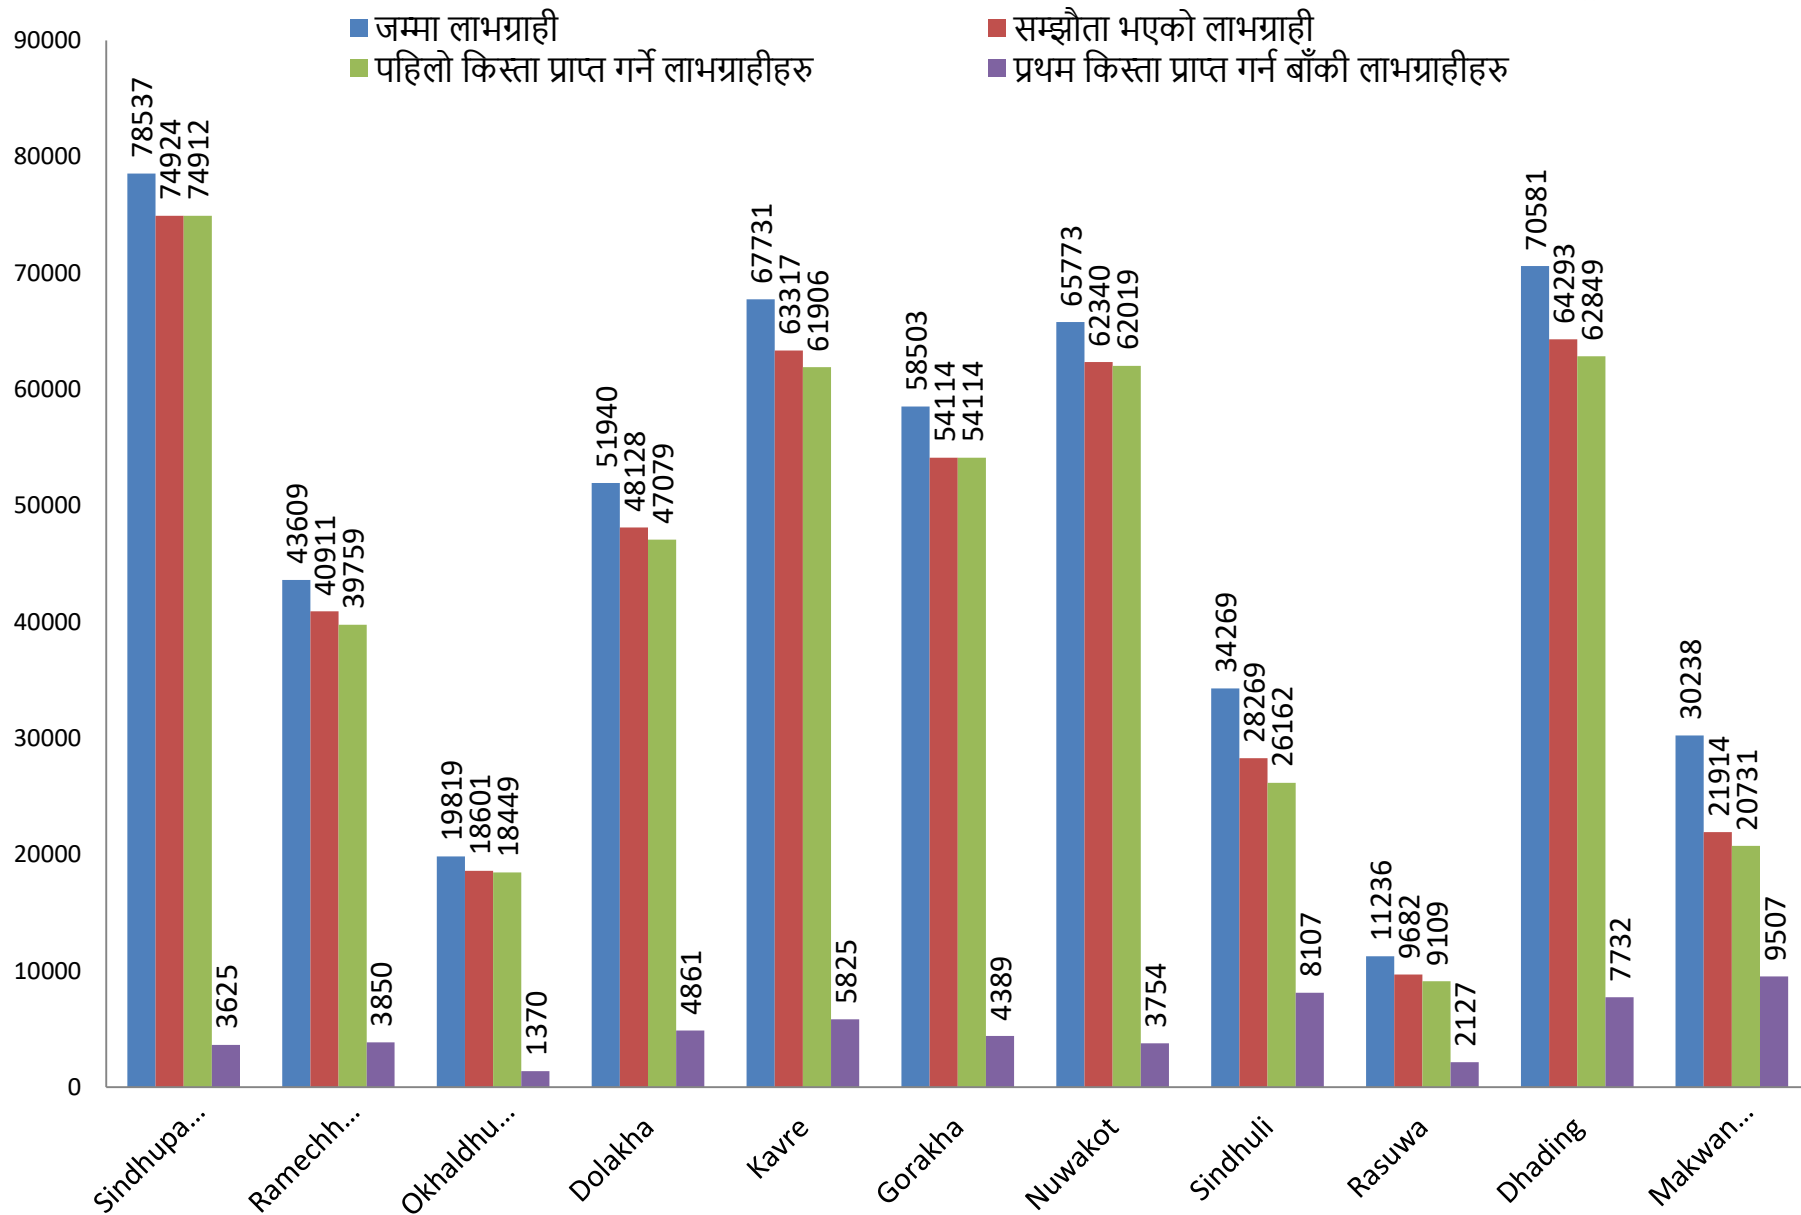


Kathmandu valley: Beneficiaries, Agreement and First Tranche

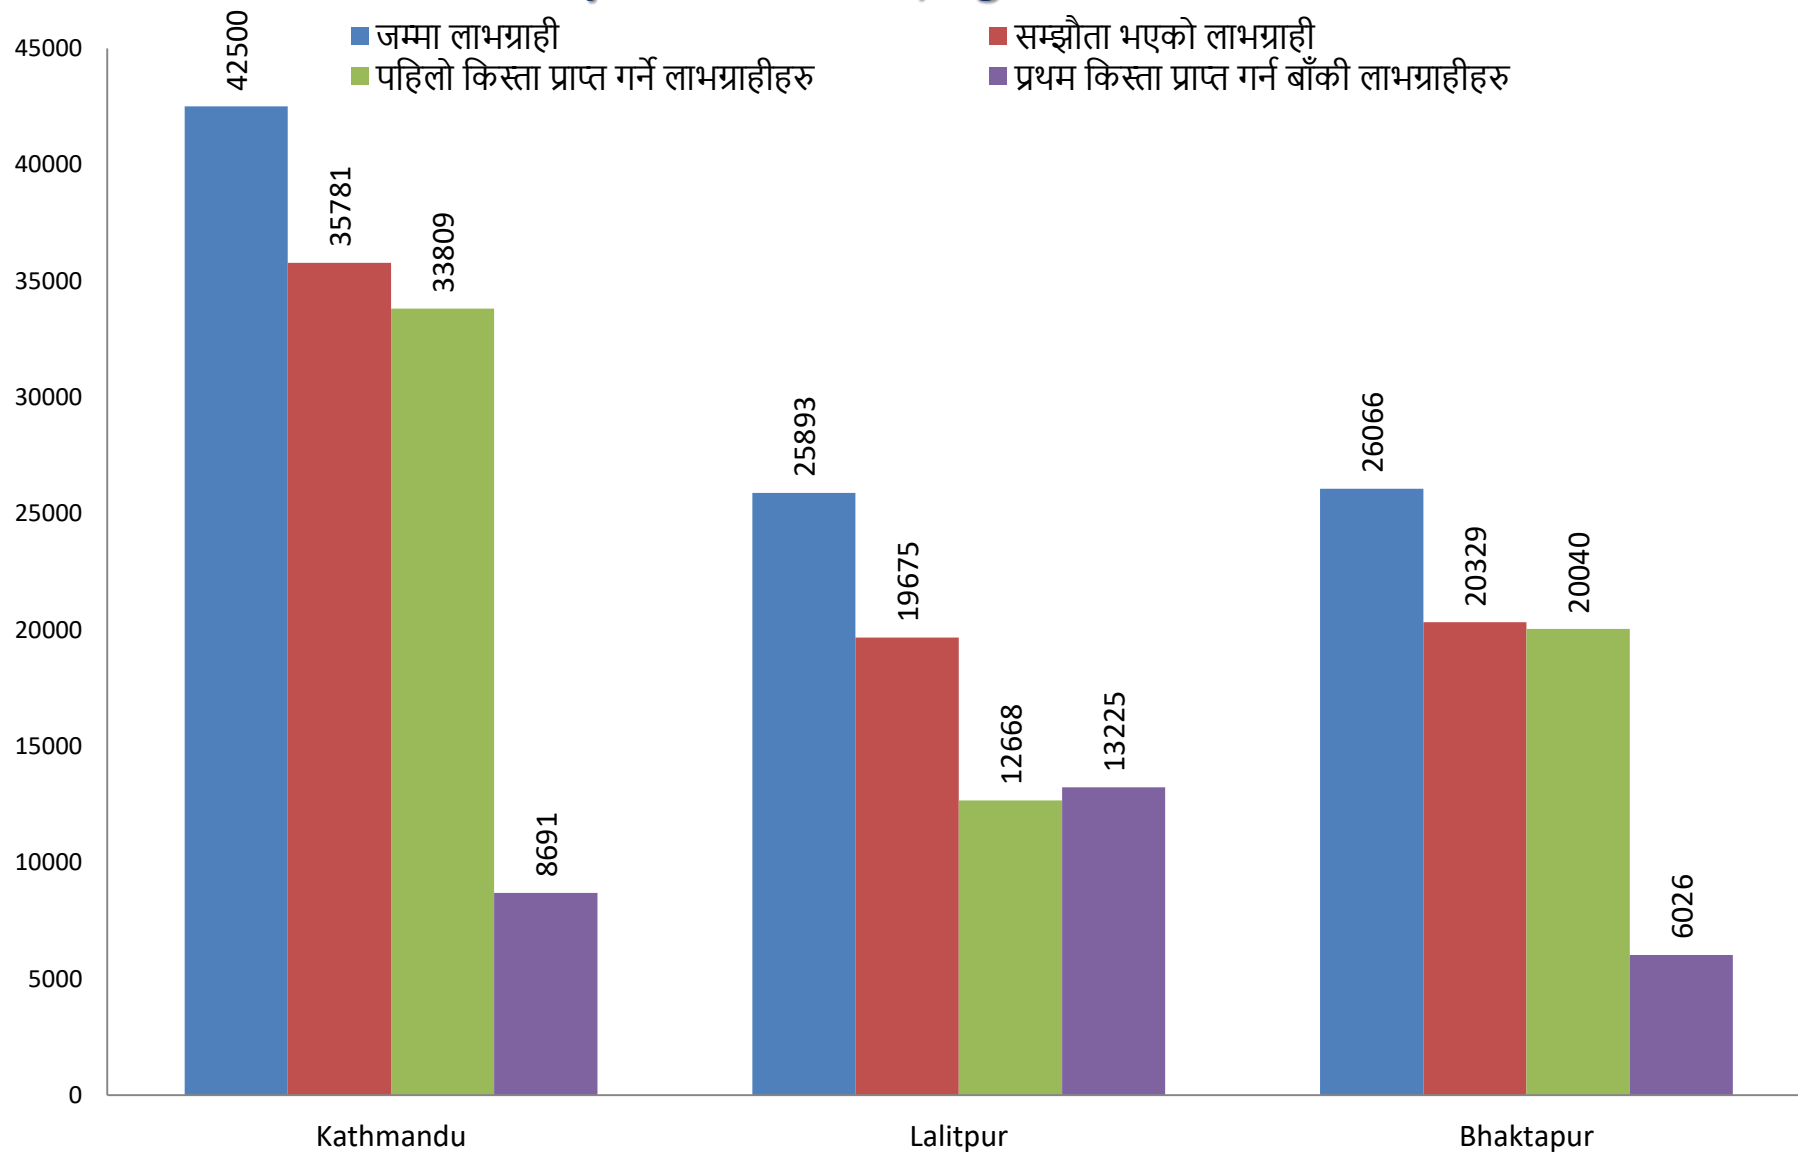


Grant distribution- tranches (2074-01-06)

■ पहिलो किस्ता प्राप्त गर्ने लाभग्राहीहरु

■ दोस्रो किस्ता प्राप्त गर्ने लाभग्राहीहरु

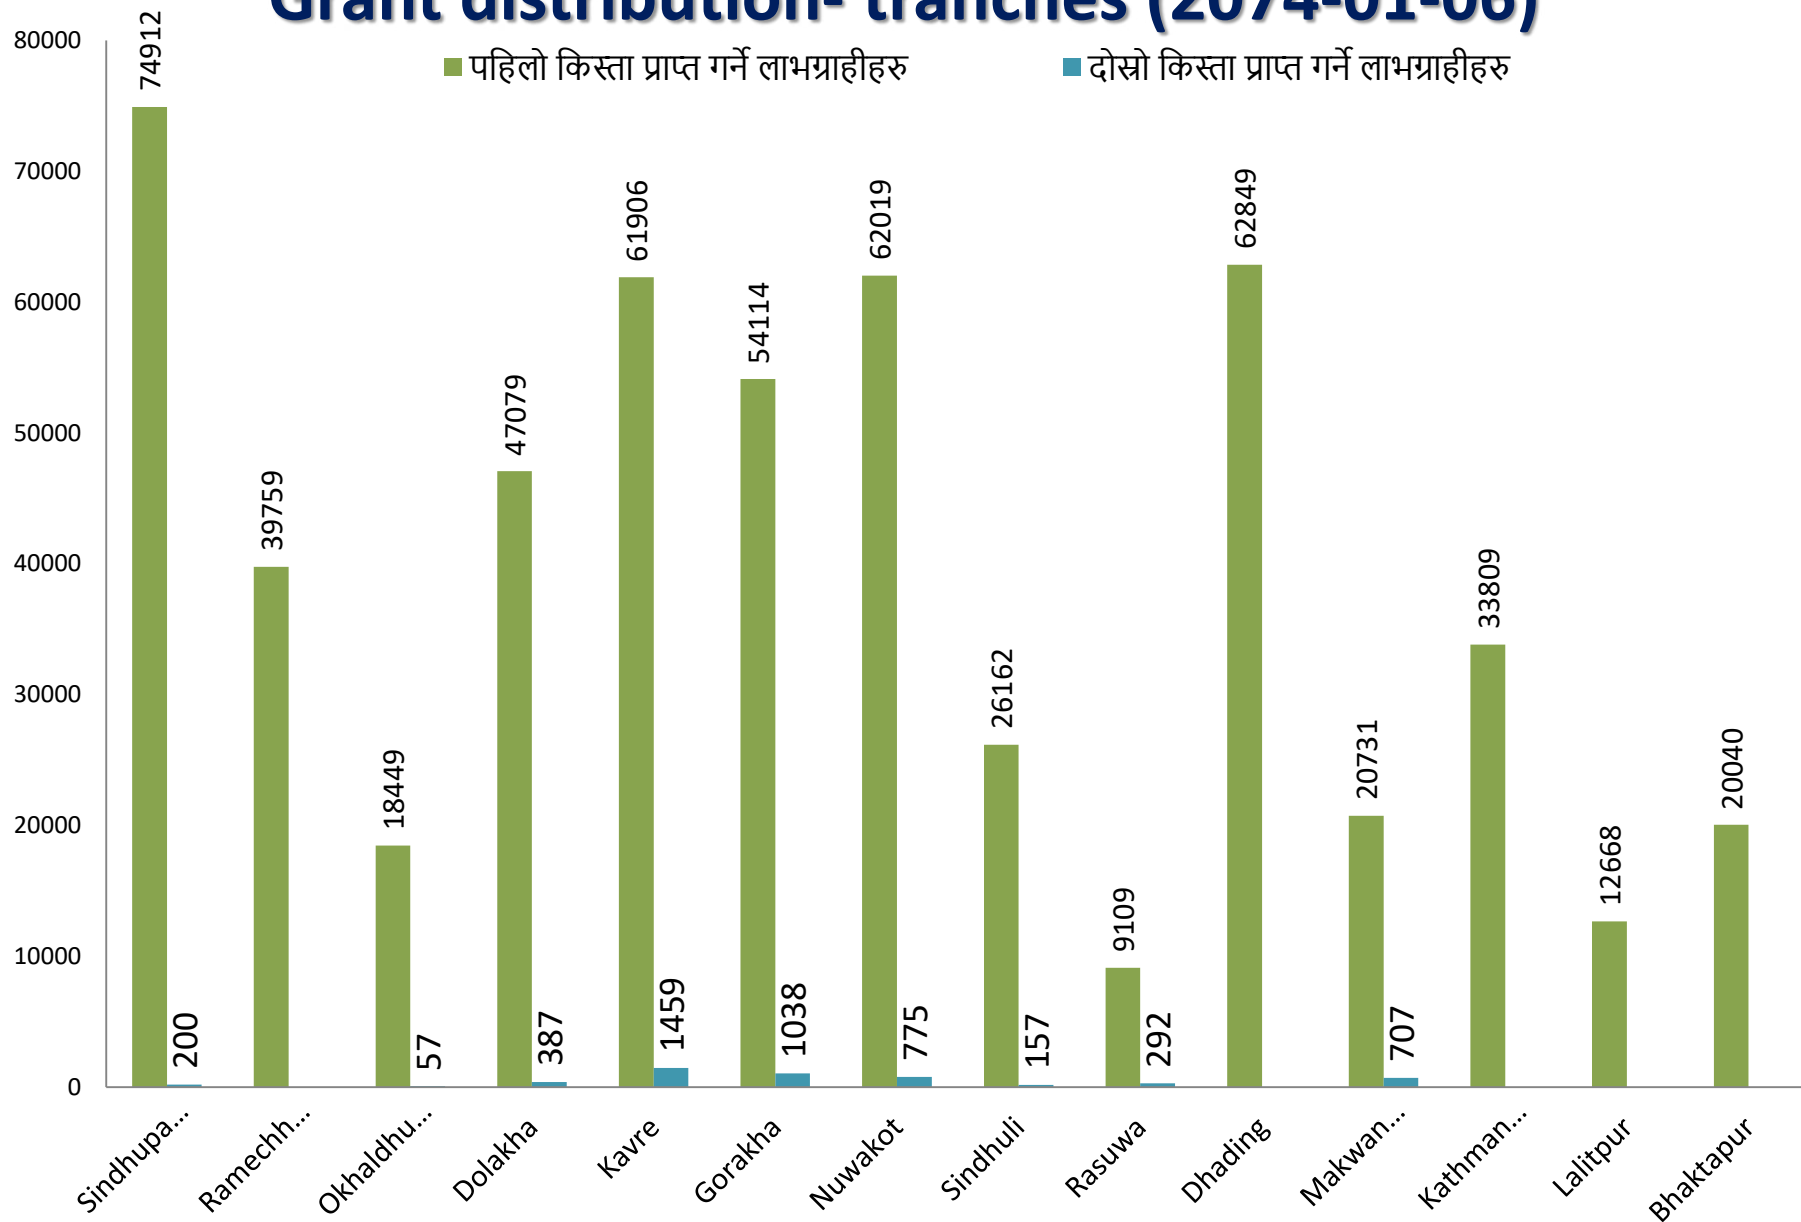

■ अनुदान सम्झौता भएका मध्ये प्रथम किस्ता भुक्तानी गरिएको प्रतिशत

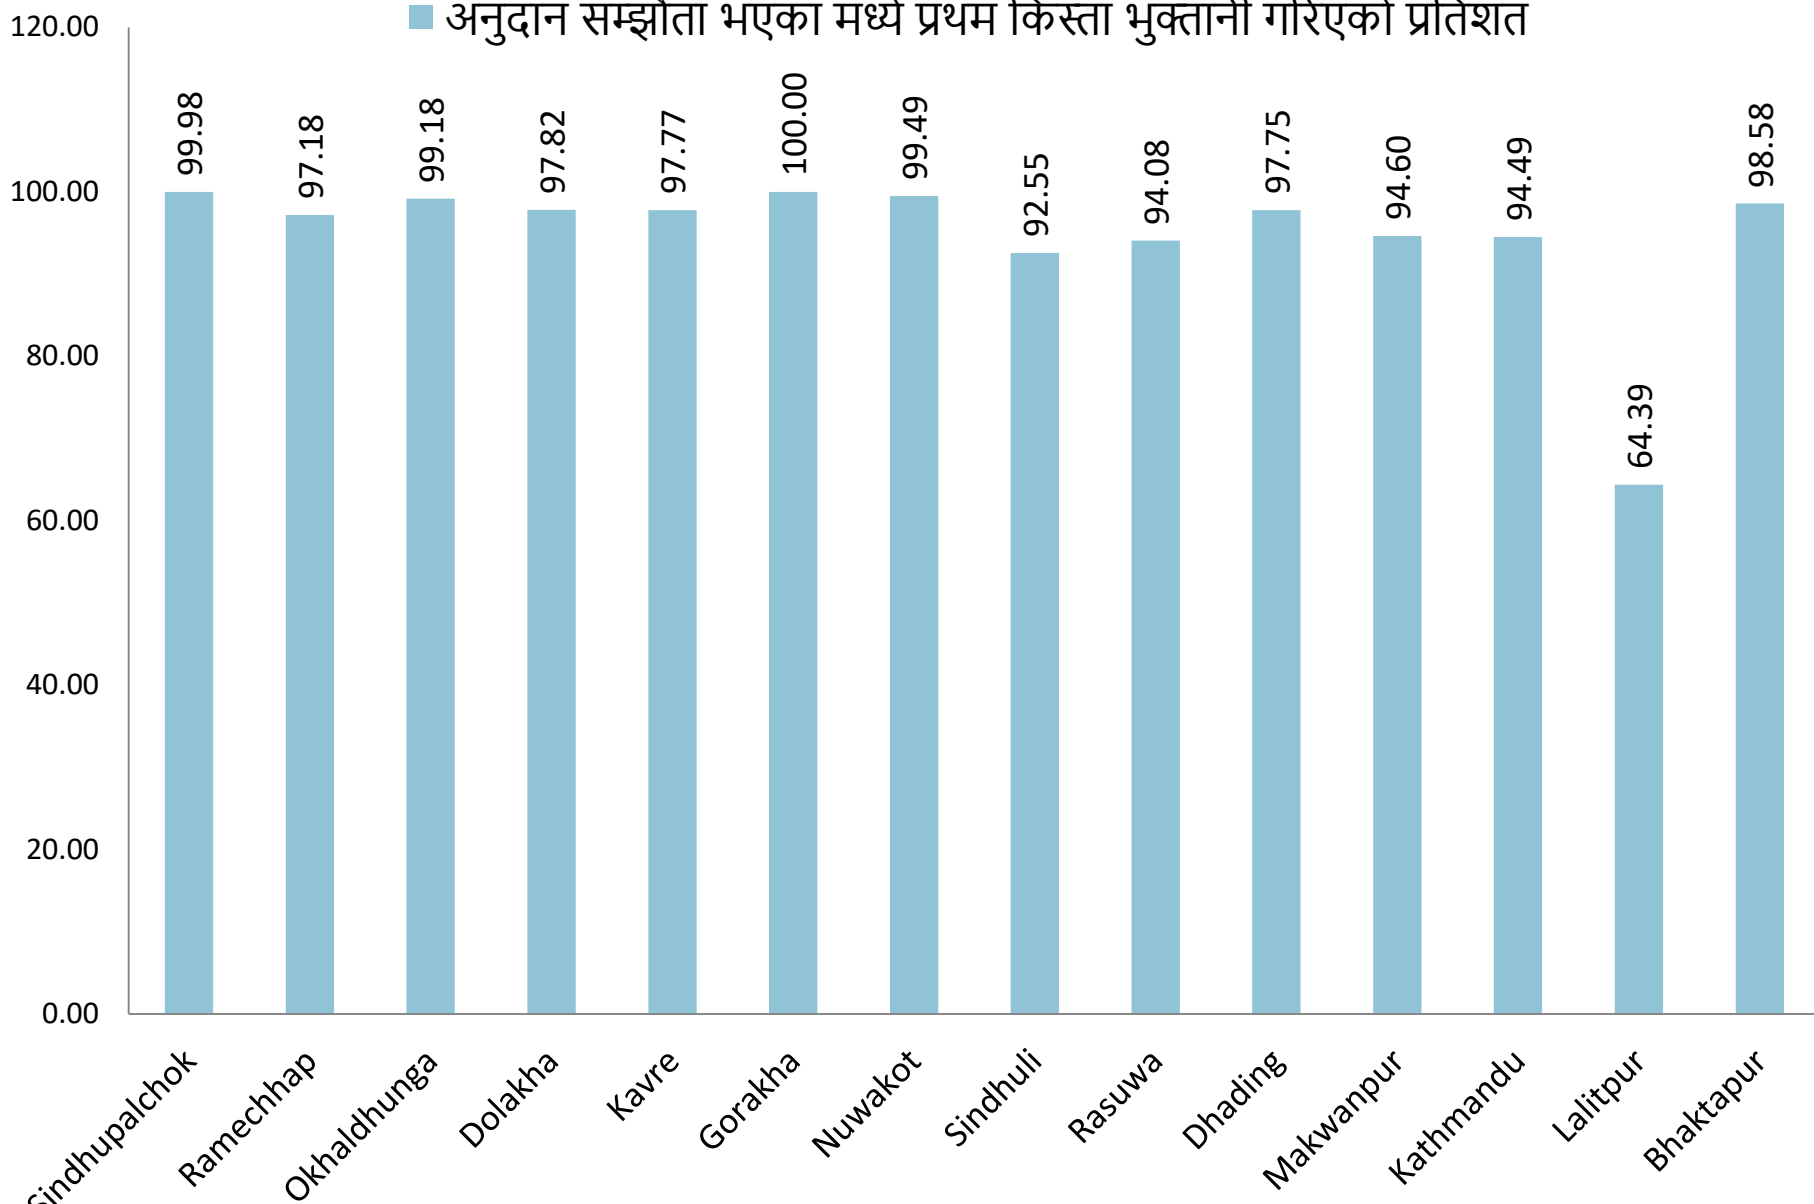

Grievance Handling

- Total grievance filed: 207,453
- Grievance received at NRA's MIS- 159,314
- Reviewed from MIS, 140,000
- Total addressed grievances from Executive Committee 117,300 (83.8% of MIS entry)
- Beneficiaries added: Eligible to get three tranches , Eligible for retrofit support 19,866



Training

- Mason training for 17,306
- TOT and Inspection Manual Training for 2,500 technical staff
- 200 Army men were trained and mobilized in three districts (Ramechhap, Okhaldhunga, Sindhuli) to build 27 schools and train others
- 1056 University students mobilized in 5 districts for 3 weeks
- Orientations for livelihood and grievance redressal in 5 districts



Resettlement

- Geo-hazard survey of 117 out of 475 vulnerable settlement completed. Total number of study in this F/Y- 358 (report yet to receive)
- Feasibility study of proposed resettlement areas for $56+55=111$ settlements ongoing
- Additional 20 settlements requested by local level also studied.
- Modality for the resettlement is being prepared.



School Reconstruction

- School Reconstruction Procedure and 100 type design approved
- 83 schools from JICA support, 66 from ADB support, 1250 from I/NGO being reconstructed.
- School reconstruction completed: 325 schools from POs and 816 from GoN support
- One third of damaged schools being reconstructed



Government Buildings

- Contract award for 45 buildings
- Tendered for 22
- Drawing designs for 98 buildings
- Repair of 51 buildings: contract being awarded
- Temporary office for Rt Hon President prepared
- Out of 288 prefab-structure offices, 76 completed



Historically important buildings

- Detailed Damage Assessment completed for 8 Rana-era buildings (Western-lounge of Singh Durbar, Gallery Baithak, Keiser Mahal, Babarmahal, Shreemahal, Juddha Fire Brigade Office, Contral Law Library, Central Childen Welfare Office Naxal)
- Retrofit of Main facade (western part) of Singh Durbar Main Building is decide under process



Heritage sites

- Reconstruction of 28 sites at Patan Durbar Square, 12 at Basantpur Durbar Squire, 19 at Bhaktpur Durbar Squire, 4 at Swayambhu area, 21 at Pashupatinath, 5 at Changuanarayan undergoing.
- Detail design of Dharahara completed and telecom is going to reconstruct.
- Baudhdhanath stupa has been reconstructed by users group
- Procurement modality has been sent for cabinet approval
- MOU with 5 DPs for heritage reconstruction

Source-wise expenditure

Source	Sum of Total	Sum of Recurrent	Sum of Capital
ADB - General	1142893044	9122800	1133770244
China - General	397600000	397600000	0
EU - General	1149734838	577397428.1	572337409.7
GoN	13426392169	11841132723	1585259445
IDA - General	3731930996	3691057899	40873097.38
IMF	3416550000	3416550000	0
India - General	4713950000	4713950000	0
Japan - JICA	1568096089	1043600000	524496088.9
Reconstruction Pool Fund	974750000	974750000	0
Grand Total	30521897135	26665160850	3856736285

Ministry-wise budget utilization in current F/Y (till 20th April)

Ministry	Progress %		
	Total	RECURRENT	CAPIAL
अदालत	0	0	0
प्रधानमन्त्री तथा मन्त्रिपरिषद्को कार्यालय	16.11	10.90	0.00
उद्योग मन्त्रालय	29.76	41.27	1.78
कृषि विकास मन्त्रालय	7.61	7.73	6.86
खानेपानी तथा सरसफाई मन्त्रालय	42.18	0.00	42.18
गृह मन्त्रालय	6.64	0.00	6.64
सस्कृति, पर्यटन तथा नागरिक उड्डयन मन्त्रालय	295.04	41.92	0.00
पशुपन्छी विकास मन्त्रालय	1.45	1.47	0.00
बन तथा भू-संरक्षण मन्त्रालय	16.20	4.37	16.68
भौतिक पूर्वाधार तथा यातायात मन्त्रालय	15.92	0.00	15.92
रक्षा मन्त्रालय	87.45	0.00	87.45
सहरी विकास मन्त्रालय	23.24	30.19	19.71
शिक्षा मन्त्रालय	19.29	10.52	19.72
सिंचाइ मन्त्रालय	55.30	0.00	55.30
संघीय मामिला तथा स्थानीय विकास मन्त्रालय	57.88	61.21	10.58
स्वास्थ्य मन्त्रालय	0.00	0.00	0.00
Total	45.67	57.88	18.58

Thank You
