

HRRP BULLETIN

23 July 2018



Ward No. 4, Chum Nubri Rural Municipality, Gorkha: a one room, single storey, stone and mud mortar masonry house. The owner has received all three tranches of Government housing reconstruction grant as this is a very remote area so multiple inspection visits are difficult to carry out. However, there are some technical issues evident such as the stone gables and wide opening that look to be potentially non-compliant. This photo was shared by the HRRP District Coordination Team (DCT) in Gorkha through their [district report covering 6-19 July](#). All HRRP DCT district reports are available on the website here: <http://hrrpnepal.org/resources-materials/district-reports->.

Highlights


- HRRP advocates for the tranche disbursement deadlines to be extended for at least the next two building seasons in rural areas, and the next four in urban areas, to allow a realistic period for households to complete their reconstruction.
- [Updated overview of status of reconstruction in 18 districts](#)
- **Change of date:** technical session on 'Experience Sharing on Key Issues and Challenges in Urban Housing Reconstruction' now on [Friday, 27 July](#)
- Summary of [preparation Session for World Bank Stakeholder Consultation on Lessons Learned and Way Forward for the Housing Reconstruction Programme, 19 July](#)
- Summary of '[Supporting Vulnerable Households to Reconstruct: Learning from Field Experience](#)' session, 13 July
- Transition from HRRP 4W to NRA 5W: POs are requested to submit activity updates at district level by the 23rd of each month, using the data collection template which can be downloaded [here](#)
- Shelter Cluster Coordination Meeting, 26 July – contact Sanjeev Hada, sanjeev.hada@ifrc.org, for more information.
- [The Development of Alternative Building Materials and Technologies for Nepal, Book 1 \(December 1993\) and Book 2 \(August 1994\)](#)

UPDATES & REQUESTS

National

NRA, CLPIU GMAI and Building, Grant Disbursement Data, as of 23 July:

	24 June	8 July	23 July
Total No. Eligible HHs	781,733	807,486	807,486
HHs Enrolled	720,482	721,281	722,087
HHs Received 1 st Tranche	711,988	712,943	713,999
HHs Applied for 2 nd Tranche	463,780	475,619	490,167
HHs Received 2 nd Tranche	421,341	441,307	465,903
HHs Applied for 3 rd Tranche	210,931	243,440	261,924
HHs Received 3 rd Tranche	169,526	195,657	225,830

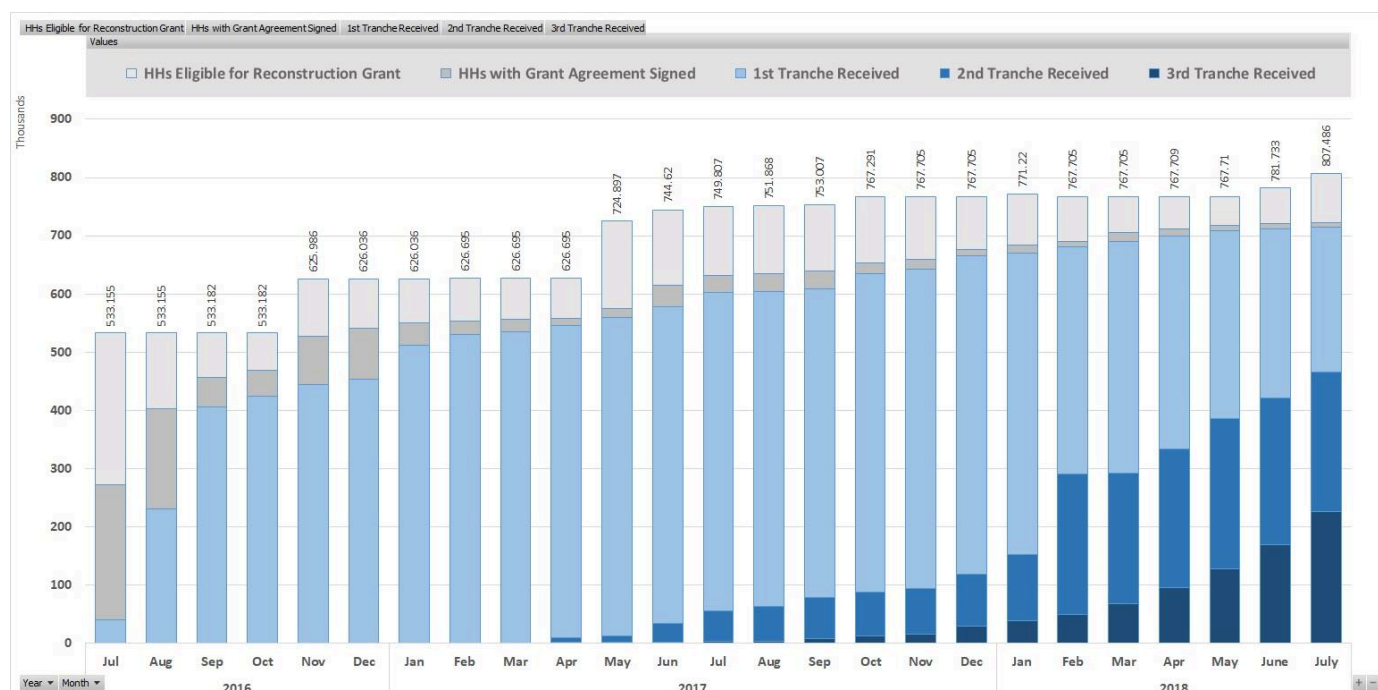

Housing reconstruction progress based on MoFALD CLPIU enrolment data from July 2016 to 23 July 2018.

Second Tranche Disbursement Deadline, 16 July: it has been almost one year since the NRA first announced the tranche disbursement deadlines ([see HRRP Bulletin from 24 July 2017](#)) and there has been mounting evidence that the the deadline is causing trauma and stress for people trying to manage their housing reconstruction. The deadlines are part of the reason for the large-scale borrowing at high interest rates that look set to cause a potential debt crisis. They are also the reason for people building small houses just to collect the grant. These houses do not meet people's living requirements and cannot represent a successful housing reconstruction. It is very positive that the numbers of households progressing with their construction is consistently increasing, but as of 8 July there are 581,656 households that need support to get to completion. This is not possible within the current deadlines. Experience from other post-disaster reconstruction efforts shows that approximately 5 years is required at least, and urban requires more time. **HRRP advocates for the deadlines to be extended for at least the next two building seasons in rural areas, and the next four in urban areas, to allow a realistic period for households to complete their reconstruction.**

Preparation Session for World Bank Stakeholder Consultation on Lessons Learned and Way Forward for the Housing Reconstruction Programme, 19 July:

the World Bank is holding a stakeholder consultation on 'Lessons Learning and Way Forward for the Housing Reconstruction Programme' on 24 July. The objective of the consultation is to "understand the concerns and issues of the relevant stakeholders and their views on how to improve and expedite the reconstruction activities. These consultations will assist in preparing for the upcoming Mid Term Review (MTR) of Nepal Earthquake Housing Reconstruction Project (EHRP). The MTR provides stakeholders with the opportunity to review progress, draw learning and, if required, make necessary adjustments in implementation arrangements". In preparation for this, HRRP held a meeting with partners on 19 July to agree the points that HRRP should raise at the stakeholder consultation. The following are the points that were developed and agreed during that session:

- Remove the tranche disbursement deadlines, or at least extend for the next two building seasons in rural areas and the next four in urban areas
- Scale up coverage of socio-technical assistance, under a collective approach with common standards
- Provide targeted support for vulnerable households and consider seasonal support or support for temporary shelter improvement
- Address supply chain constraints and material quality issues, and develop material vendors and producers as agents of technical assistance
- Mass communications campaign required to address confusion, misinformation, and rumours
- Develop solutions to address the potential debt crisis we are facing
- Urban housing reconstruction needs investment and targeted policies and approaches
- Increase support to the 18 moderately affected districts
- Increase support for NRA, Building DLPIU engineers, sub-engineers, and assistant sub-engineers, and District Support Engineers
- Develop common approach for continuous capacity building support to municipal and ward officials on reconstruction
- Develop and disseminate design guidelines for alternative / emerging construction technologies and materials
- Invest in coordination at all levels
- Consider long term institutionalisation of recovery experience now, not just at the end of the reconstruction


Please share any feedback on these points with Siobhan Kennedy, HRRP Recovery Advisor, siobhan@hrrpnepal.org.

Supporting Vulnerable Households to Reconstruct: Learning from Field Experience, 13 July: during the last meeting of the [HRRP's Vulnerable Support Working Group \(VSWG\) on 2 July](#), it was agreed that there is a need to bring together the experiences of partners that have field experience supporting vulnerable households to guide scale up of this support. This session was organised based on this, with the objective of providing an opportunity to learn what worked well, what didn't work well, and what should be considered moving forward. Six Partner Organisations (POs) presented their experience during the event; Save the Children, JICA, NSET, CARE Nepal, Feminist Dalit Organisation (FEDO), and UNDP; many thanks to all the presenters. HRRP is now compiling the experiences shared and will circulate a summary soon. For more information, please contact Rupa Panday, HRRP MEAL Coordinator, meal@hrrpnepal.org, and Minar Thapa Magar, HRRP National Coordination Officer, minar@hrrpnepal.org.

Transition from HRRP 4W to NRA 5W: the HRRP 4W has been phased out from July 2018 to streamline data collection fully to the NRA 5W. HRRP has been supporting the NRA to establish and roll out the 5W data collection system focused on multiple sectors of recovery. To rollout the transition, an orientation session took place at [national level on 20 July](#) and sessions at district level have been taking place last week and will be completed early this week. HRRP is using a revised template for data collection which can be downloaded [here](#). The 5W will be collected by HRRP district teams to make 5W reporting timely. To support with the process, POs are requested to

submit activity updates by the 23rd of each month. Please contact your relevant [HRRP District Coordination Team](#) or Uttam Paudel, im.manager@hrrpnepal.org, if you have any questions or need support.

Monsoon Impact: heavy rainfall since the beginning of July has caused loss of life and damage to property and infrastructure in many areas of Nepal. The infographic below from the UN RCO, provides a summary of the situation as of 12 July.

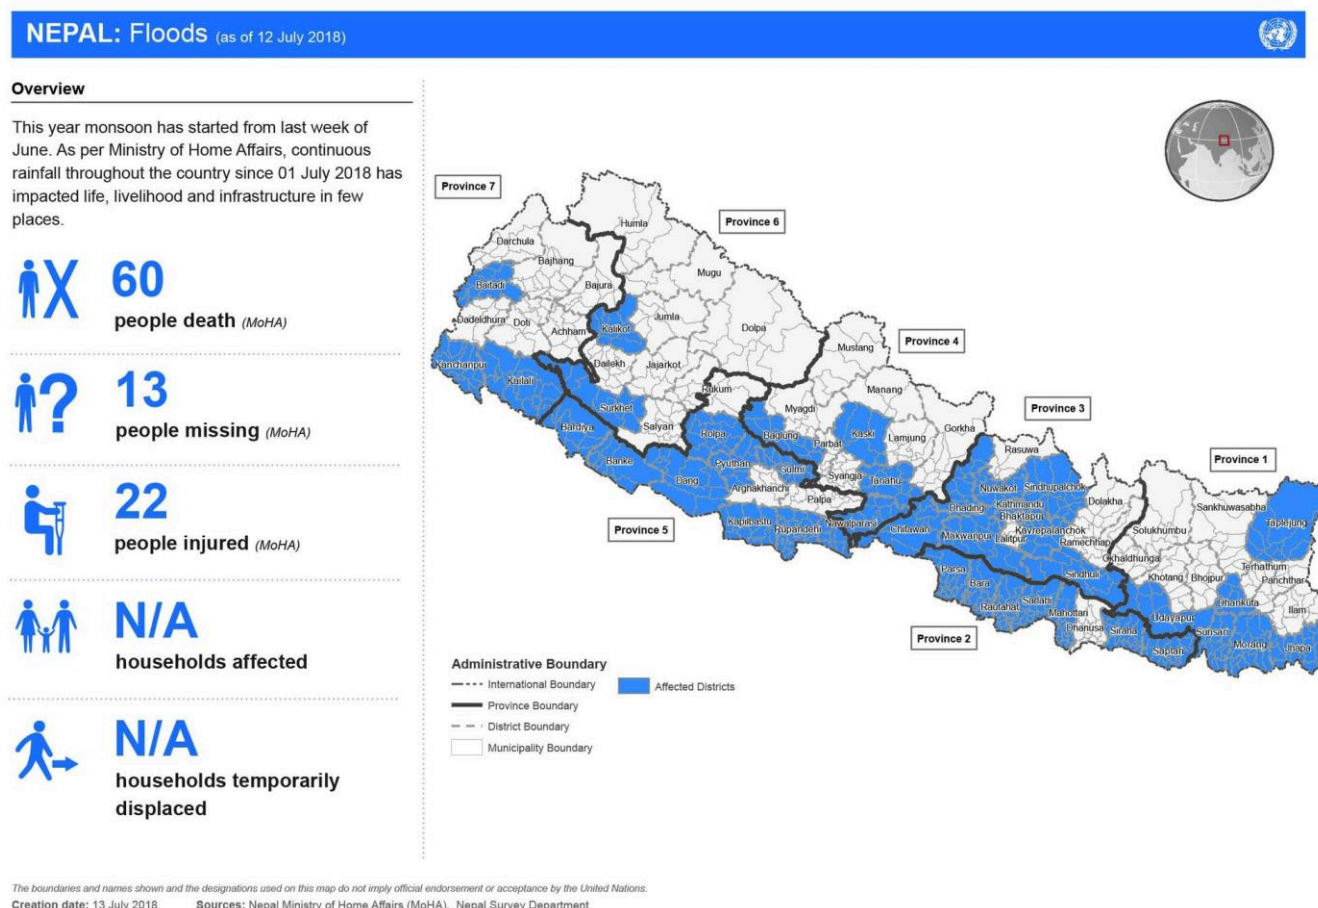

Districts & Municipalities

HRRP District and Municipal Coordination Meetings, 9 – 23 July: during this period district coordination meetings took place in Kavrepalanchok (9 July), Makwanpur (16 July), Sindhupalchok (19 July), and Gorkha (20 July). Municipal level meetings took place in Bhimeshor Municipality (12 July), Dolakha. Some of the highlights from these meetings include:

- In **Kavrepalanchok**, discussion points were: the results of the resurvey and reverification have been received and will be sent to all municipalities for final verification and further process. 19 applications that would like to switch to reconstruction beneficiaries from retrofitting have been approved by NRA. Only 584 retrofit beneficiaries have been enrolled and none have requested for final tranche. The error list of inspection files at GMAI need to be delivered to either the respective engineers or at DLPIU for further action. Frequent transfer of engineers is a major concern and plans are being thought for their longer stay at their workplace. Many wrong trends of Earthquake houses are seen in the district such as, one room houses, small size houses and still living in the old houses. To discourage unsafe addition or alteration of houses after receiving the third tranche, distribution of completion certificate to be started from Balthali.

- In **Makwanpur**, the main concerns raised were the low rate of third tranche i.e. 28% of the beneficiaries have received third tranche, lack of technical man power for retrofitting, 8,000 beneficiaries who have taken first tranche have not started reconstruction, what would happen to the 8,000 beneficiaries who have not signed the partnership agreement yet, and when will the grievances issues will be resolved. The meeting emphasized on proper planning to incorporate and expedite reconstruction of around 8,000 beneficiaries who've already received 1st tranche.
- In **Sindhupalchok**, discussion points were: Grievances of Helmbu 4 and 5 (Mahankal) has not been handled till date and the earthquake victims have been pressurising the concerned authorities regarding the resurvey. The displaced households from Simpalkavre were relocated at Bhedichaur, Nawalpur but land in the area that they have been relocated to is now sinking as they did not consult the technicians prior to preparing the land. They straightened the land by themselves but now the walls of some of the constructed houses are developing cracks on them. RCC structure houses are especially non-complaint in the district. Most of the non-compliant houses are joint DPC houses whereby the two beneficiaries are making single DPC but constructing two houses in the same DPC and claiming tranches separately. Similarly, single-bay houses and the stepping houses are on rise. The names of all the displaced households have not been listed by NRA.
- In **Gorkha**, the main discussion point of the meeting was update on the partners plan for vulnerable support. 697 vulnerable HHs have been supported by various partner organisations and 300 additional HHs support is planned by the partners. Discussion was also on partners further plans and programs in other sectors as livelihood, governance, WASH, and health. Similarly, Partners presented their updates while CARE shared their experience of vulnerable support through refresher training. In the meeting, GMALI office chief also put his remarks and requested all partners to coordinate for reconstruction work in the days ahead.
- In **ward no. 4, Bhimeshor Municipality**, the meeting mainly focused the integrated settlement of 183 HHs in Jilu. All the necessary process has been completed with the collection of fund from different Government agencies, also 2 million NPRs has been provided by Bhimeshor Municipality for the management of the temporary shelter. The master plan was prepared through a series of technical surveys and interactions with local people. The master plan has been finalised and approved from MoUD-DLPIU and NRA for the development of the infrastructure. Recently, tender has also been issued to the construction company and the work is expected to be completed within 8 months. Apart from this, the reconstruction process is moving at a good pace in this ward. Few issues as hike in the cost of construction materials, insufficient construction materials, degrading road condition due to monsoon, high transportation cost, and insufficient trained masons were discussed in the meeting.

HRRP District Coordination Team Dhading, Weekly District Report, 6 – 19 July 2018



Ward No. 7, Galchi Municipality, Dhading: a two room, load bearing structure, stone masonry in cement mortar. The owner has received first tranche of Government housing reconstruction grant and has been approved for the second tranche.

HRRP District Coordination Team Dolakha, Weekly District Report, 6 – 19 July 2018



Ward No. 4, Bhimeshor Municipality, Dolakha: a single storey, dry stone masonry. The owner has received all three tranches of Government housing reconstruction grant.

HRRP District Coordination Team Kavre, Weekly District Report, 6 – 19 July 2018



Ward No.13, Banepa Municipality, Kavrepalanchok: a single storey, two-roomed brick in cement masonry. A separate kitchen is constructed. The owner has received all three tranches of Government housing reconstruction grant. The total cost of construction was 750,000 NPR.

HRRP District Coordination Team Makwanpur, Weekly District Report, 6 – 19 July 2018



Ward No.4, Bhimfedi Rural Municipality, Makwanpur: a single storey, two-roomed stone in mud mortar with RCC bands and flexible roof. The owner has received all three tranches of Government housing reconstruction grant. The total cost of construction was 5,00,000 NPRs.

HRRP District Coordination Team Nuwakot, Weekly District Report, 6 – 19 July 2018



Ward No. 5, Shivauri Rural Municipality, Nuwakot: brick in cement mortar. The owner has received second tranche of Government housing reconstruction grant and has been approved for the third tranche is on process.

Requests for Partner Support

Invitation and Change of Date, Technical Session on ‘Experience Sharing on Key Issues and Challenges in Urban Housing Reconstruction’ now on Friday, 27 July: please join us for this session on Friday from 10:30AM at the DUDBC Hall. There will be presentations from M&E, CLPIU Building, NSET, Lalitpur Metropolitan City, and Lumanti. It is hoped that the session will result in a useful summary document that can contribute to the scale up reconstruction of urban houses.

Shelter Cluster Coordination Meeting, 26 July: the meeting is taking place at 11AM in the DUDBC Hall. The agenda will cover feedback from partners on their monsoon preparedness plans, sharing draft version of revised shelter Cluster contingency plan 2018, sharing findings from simulation exercise held in Banke district on July 16, and private sector engagement. For further information please contact Sanjeev Hada, Head of National Society Development Unit, IFRC, sanjeev.hada@ifrc.org.

Hollow Concrete Block Technical Working Group: during the meeting of the NRA technical committee on Thursday 7 June, the committee members endorsed the [HRRP report on production and use of Hollow Concrete Blocks \(HCBs\)](#), including the next steps. The first meeting of the technical working group to support with the development of guidelines for HCB producers, inspection checklists and minimum requirements for HCB construction, and options for corrections for non-compliant HCB construction is to take place tomorrow at the NRA. Those interested to participate are requested to contact Kuber Bogati, National Technical Coordination Officer, techofficer1.national@hrrpnepal.org.

Call for Presentations for next ‘20x20 Partner Sharing Session’, August: many thanks to the partners that presented at the first of these sessions on 14 June. Partners interested to present are requested to write to Ruplal Aidi, HRRP National Coordination Officer, nco2@hrrpnepal.org, to indicate their interest to present and what the proposed topic of the presentation is. N.B. this session will use the ‘Pecha Kucha’, 20 X 20 style of presentation. Each presentation will have 20 slides with 20 seconds allowed per slide, totaling 6 minutes and 40 seconds. The presentation is automated and therefore no additional time is possible.


DOCUMENTS & PRODUCTS

Government of Nepal

[NRA Newsletter, June 2018](#)

HRRP

[Map of Urban Wards in Earthquake Affected Districts:](#) these wards have been identified through consultations with municipal and district officials, NRA, Building DLPIU technical staff, and HRRP District Coordination Teams.

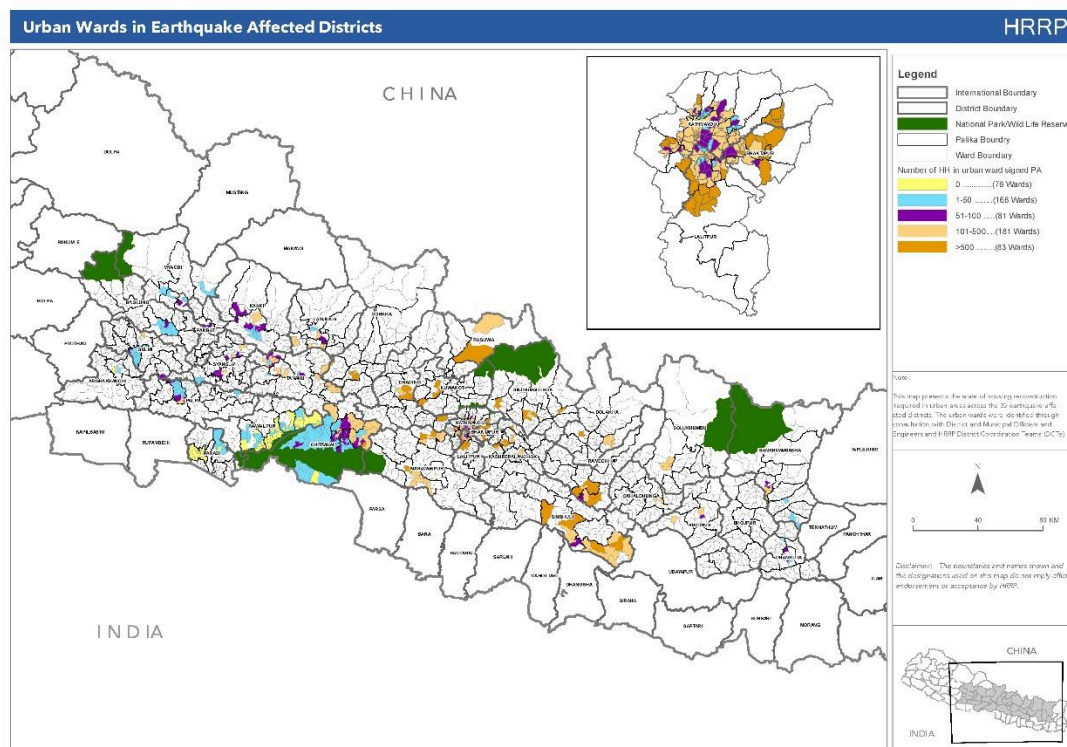

[Updated HRRP Tool to prioritize additional support for Vulnerable HH:](#) the tool now includes a column for rural / urban so that the analysis can be done on the basis of rural or urban wards.

[18 Districts, Updated Overview of Reconstruction Status in Moderately Affected Districts](#)

[Map of Coverage of Approved Partner Organisation Support for Vulnerable HHs Identified by the NRA – as of 9 July:](#) this map has been prepared based on currently available data. Please contact Uttam Paudel, HRRP IM Manager, im.manager@hrrpnepal.org, if you have any updates to share regarding this map.

[Housing Reconstruction Progress Maps:](#) based on MoUD CLPIU inspection data as of 22 June.

[Partnership Agreement between HHs and GoN](#)

[Construction Started](#)

[1st tranche received](#)

[Compliance rate 2nd tranche](#)

[Compliance rate 3rd tranche](#)

[Construction Completed](#)

Partners

Milijuli Nepali, BBC Media Action, Episode 994: this week's Milijuli Nepali episode is recorded in different places. The first story is from Nuwakot where a group of women are working together to cook a huge meal for the builders. The neighbours of the home owner help cook the meal. The episode also has a drama, which tells the story about a man, who suffers from severe lack of sleep from being uncomfortable in his temporary shelter. Then there's a story about a man from Kavre who was among the first to rebuild his house after the earthquake. His house has become an example of a safe and good home for the others in the neighbourhood. The last conversation in the episode is a conversation with a couple who invest time in taking care of their goats, because they are part of their family and livelihood.

Baliyo Ghar TV, Episode 113: this week's episode is focused on the inspiring stories of 3 Baliyo Ghar trained masons from Dolakha who have contributed their best to rebuild seismic resilient communities. The masons featured are Mrs. Bimala Basnet (Old Dolakha Bazar), Mr. Tirtha Bahadur KC (Bhimeshwor-Makaibari), and Mr. Karna Bahadur Thami (Kalinchwok-Babare).



The graphic is a promotional poster for the TV show 'Baliyo Ghar'. At the top, it says 'बालियो घर' (Baliyo Ghar) and 'BALIYO GHAR'. Below that, in Nepali, it says 'आवास पुनर्निर्माणमा दौलखाका प्रेरणादायी तीन पात्र' (Inspiring three people from Dolakha in housing reconstruction) and 'भाग - ११३' (Part - 113). The poster features three portraits of the featured masons: Mrs. Bimala Basnet, Mr. Tirtha Bahadur KC, and Mr. Karna Bahadur Thami. Below each portrait are their respective broadcast times and logos of the supporting organizations: USAID, NSET, and Media Partner.

Supported By:	Presented By:	Media Partner:
		

The Development of Alternative Building Materials and Technologies for Nepal, Book 1 (December 1993) and Book 2 (August 1994): this inventory of prototype construction in Nepal was part of the building code development. It is a really interesting and useful document, that includes detailed sketches and information on common building types in Nepal at this time.

[Media Digest](#) | [FAQ](#) | [Briefing Pack](#) | [Meeting & Events](#) | [4W](#) | [Housing Progress](#) | [Housing Typologies](#)
