


[FAQs](#) | [Briefing Pack](#) | [Meeting & Events](#) | [5W](#) | [Housing Progress](#) | [Housing Typologies](#)



Edition Number: 98

 Housing Recovery and
Reconstruction Platform
BULLETIN
21 January 2019

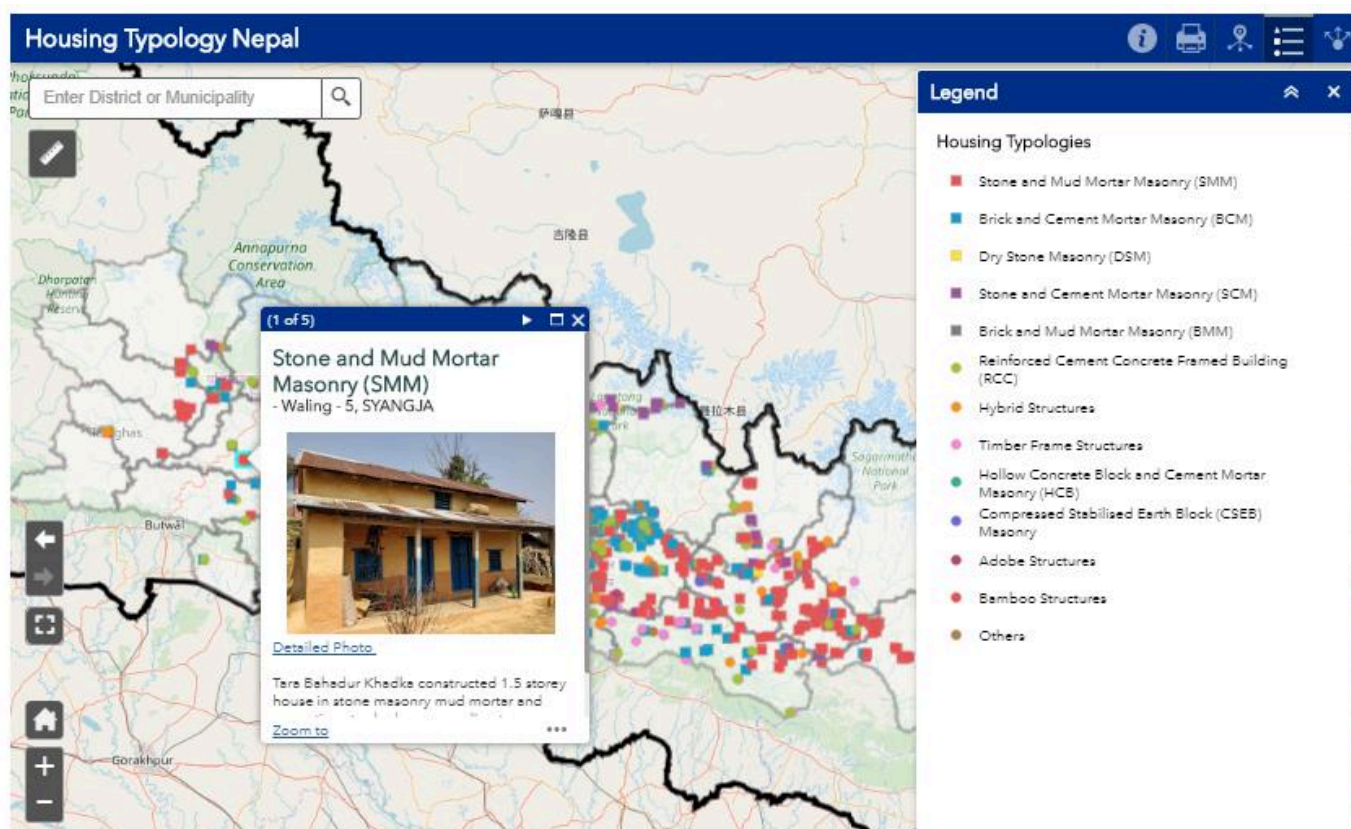

The HRRP website has a new interactive dashboard on housing typology. The dashboard is available on the home page of the website. Please share any photos for inclusion in the dashboard with the relevant HRRP District Coordination Team or with Monika Bajimaya, dmt.im@hrrpnepal.org.

Notice Regarding HRRP3 Extension

As you probably know, HRRP3 was due to run until the end of February 2019. In the middle of 2018, the HRRP's Strategic Advisory Group (SAG) requested that HRRP3 be extended until the end of July 2019 in order to better align with the construction season. The plan was to maintain the current HRRP organisational management structure and priorities for this five-month extension. However, the anticipated level of funding has not been forthcoming, and it now looks likely that HRRP3 will be extended until the end of July but will not be able to provide the same type of activities and coverage will be reduced at district and municipal level.

HRRP3's contribution to the recovery and reconstruction process has been appreciated by the NRA, CLPIUs, donors, and POs and we have taken on board your suggestions to continue to expand the platform's focus at local level. Whilst the funding issues are a challenge, they also represent an opportunity for new contributions and collaboration to ensure continuation of coordination services. Any organisations interested to support (either by providing funding, seconding / embedding staff, or in other ways) should contact the HRRP National Coordinator, Loren Lockwood, loren.lockwood@hrrpnepal.org for more information.

Featured Technical Staff Person



*NRA/HRRP Focal Person for Coordination
Arughat Rural Municipality Gorkha*

This week's featured technical staff person is Sunil Pokharel who was the NRA/HRRP focal person for coordination of reconstruction in Arughat Rural Municipality, Gorkha from September 2017 until the end of 2018.

Sunil was the first municipal focal point for reconstruction, supported by SDSC and CRS, and working as per the [TOR for municipal focal person](#) jointly developed by all reconstruction actors in the district.

Sunil shares the challenges he experienced during his work in Arughat RM and reflects on the focal point role.


Highlights

- New and improved HRRP website launched last week - <http://hrrpnepal.org/>
- INVITATION, Vulnerable Support Working Group (VSWG) meeting, 2-3:30 PM, 22 January, HRRP Office Jwagal. Please contact Minar Thapa Magar (minar@hrrpnepal.org) or Rupa Pandey (meal@hrrpnepal.org) if you have any questions or need any additional information about the meeting.
- [The State of Humanitarian Shelter and Settlements 2018, Beyond the Better Shed: Prioritising People, Global Shelter Cluster](#)
- In Ward 3, Likhu RM, Nuwakot, the majority of houses in the ward are one room
- In Bhotekoshi RM, Sindhupalchok, there are some households in remote villages who are intending to start reconstruction only after receiving all three tranches at once.
- In Manahari RM, Makwanpur, 80% of households have not signed the PA due to landless issues

National Updates


NRA, CLPIU GMALI and Building, Grant Disbursement Data, as of 21 January:

Reconstruction Grant	24 December	7 January	21 January
Total No. Eligible HHs	823,385	823,385	811,154
HHs Enrolled	740,907	744,228	749,783
HHs Received 1 st Tranche	734,392	738,430	744,050
HHs Applied for 2 nd Tranche	594,354	542,667	549,549
HHs Received 2 nd Tranche	523,889	526,794	531,210
Non-compliant at 2 nd Tranche	4,823	4,599	4,673
HHs Applied for 3 rd Tranche	415,664	381,097	386,136
HHs Received 3 rd Tranche	336,263	342,839	354,396
Non-compliant at 3 rd Tranche	2,355	2,506	2,431
Houses Completed	367,334	347,748	350,762
HHs with Completion Certificate	4,750	4,421	4,560
Retrofit Grant	24 December	7 January	21 January
Total No. Eligible HHs	61,591	61,591	61,591
HHs Enrolled	13,591	15,025	15,462
HHs Received 1 st Tranche	11,974	13,689	14,148
HHs Received 2 nd Tranche	4	4	20

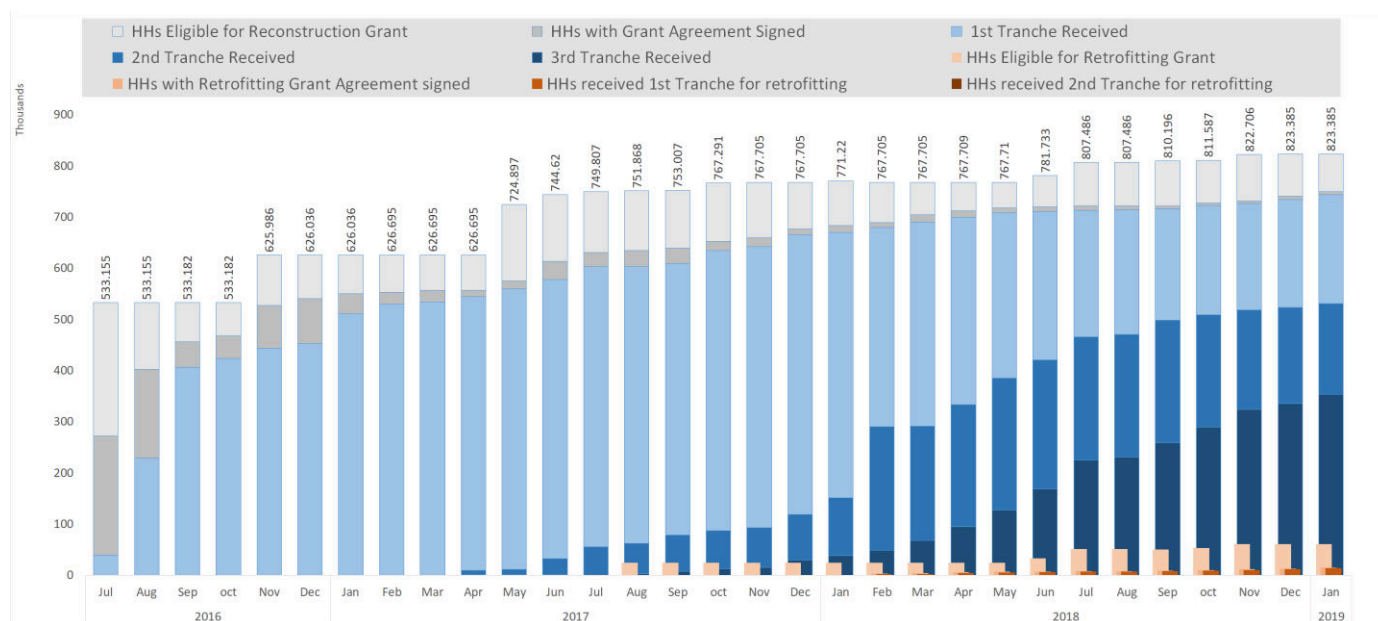

Progress with the disbursement of the GoN housing reconstruction and retrofit grants based on NRA, GMALI CLPIU, and Building CLPIU data from July 2016 to 21 January 2019.

Tracking Return of First Tranche: numbers are based on data collected by HRRP District Coordination Teams (DCTs) through the GMALI DLPIU offices. As of 21 January, the total number of households that have returned the first tranche is 107, an increase of 36 since 7 January.

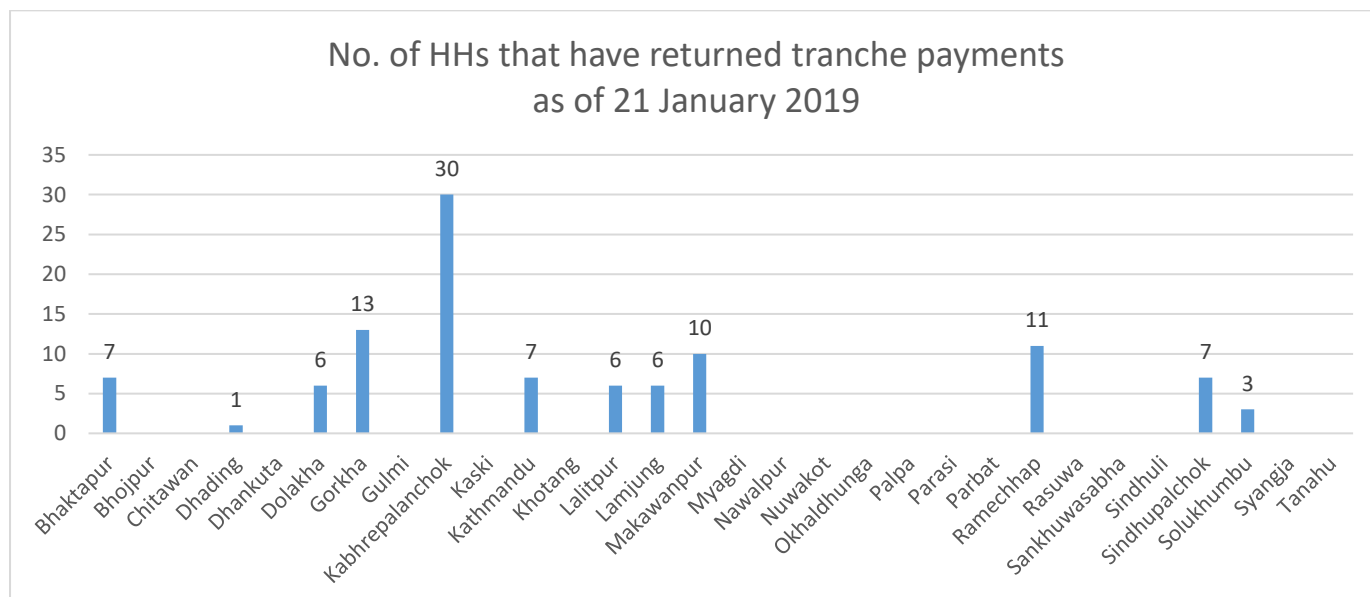

New and Improved HRRP Website: the website now has a couple of new features which we hope will make it easier for users. The interactive dashboards are now available on the home page and there is a new dashboard for housing typology. In the reconstruction stories section [Partner Organisations \(POs\) can submit stories](#) from the field, or their experiences, directly onto the website (when stories are submitted they will be reviewed by HRRP before publishing). The website also has a separate page for [each of the 32 earthquake affected districts](#). Each district page includes an interactive dashboard, maps, infographics, district reports, and information on meetings and events. Please share any feedback on the website with Karishma Chand Thakur, Communications and Content Officer, comms1@hrrpnepal.org.

Market Development of Clean Cookstoves in Nepal, Project Sharing Session by Practical Action, 18 January: Practical Action, with funding support from DFID via GIZ/EnDev, has been implementing a Result Based Financing (RBF) project since 2014 to promote a sustainable clean cookstoves market in Nepal. The Practical Action team presented that this is the right time to promote clean cookstoves in earthquake affected districts and discussed options for collaboration with partners. The project provides a certain percentage result based incentives for cookstoves market chain actors, local financing institutions, and users and HRRP partners could contribute to creating awareness, making people aware about the project, supporting to organize marketing campaigns, etc. You can watch Bhume Lama, the owner of Lama Metal Steel, share his experience as part of the programme [here](#). For further information please contact to the Project Manager of the project at min.malla@practicalaction.org.np.

21st Earthquake Safety Day, 16 January: the theme for this year's ESD was "Committed Governments at all levels to ensure Citizen's Right to Safety from Disasters". In the earthquake affected districts the day was marked with various programmes and activities. Rallies and formal programmes were carried out with Government officials, different international and national organisations, and other participants to observe ESD and generate awareness of earthquake safety and preparedness. In Nuwakot a simulation exercise on Search and Rescue was carried out to raise awareness and disseminate knowledge and practices. Across all districts the district authorities remarked on planning and implementation of resilient programmes in all phases of disaster management cycle by all concerned stakeholders, implementation of National Building Codes, and building a culture of safety across the country. As part of the national programme to mark ESD, Prime Minister, Mr. KP Sharma Oli visited the reconstruction sites of archeological monuments in Patan Durbar Square. The Prime Minister highlighted the need to "Build a Safe Nation" by building safe housing, schools, and settlements. He also emphasised the importance of restoring and regenerating the ancient originality, cultural authenticity, and historical identity of the archeological monuments as part of the reconstruction efforts. A panel discussion was also held with an emphasis on the roles and responsibilities of all concerned stakeholders in building safer communities.



Search and Rescue simulation in Nuwakot as part of events to mark Earthquake Safety Day last week.

District & Municipal Updates

District Level Reconstruction Orientation and Review Workshops, NRA CLPIUs (Building and GMALI): these workshops have been completed in 21 districts so far and will be carried out in the remaining districts in the coming weeks. The major outcomes of the workshops are NRA signing an MoU ([Nepali](#), [Unofficial English Translation](#)) with each of the municipalities and the municipalities preparing [draft municipal reconstruction action plans](#). Municipal profiles developed as part of the process, which will be updated monthly, are available [here](#).

Videos from the events are available on YouTube. Some recently uploaded videos include interviews with:

- [Sandesh KC, Focal Person, DLPIU Building, Baglung](#)
- [Mr. Jok Lal Budha, Mayor, Tamaankhola Rural Municipality, Baglung](#)
- [Bishwas Pandey, Engineer, MadhyaNepal Municipality, Lamjung](#)
- [Janak Raj Mishra, Chairperson, Sundarbazar Municipality, Lamjung](#)
- [Rachana Paudel, Focal person, DLPIU Kathmandu](#)

For further information please contact Minar Thapa Magar, HRRP National Coordination Officer, minar@hrrpnepal.org.

HRRP District and Municipal Coordination Meetings, 4 – 17 Jan 2019: during this period district coordination meetings took place in Kavrepalanchok (9 January), Makwanpur (10 January), and Kathmandu (14 January). Municipal level meetings took place in Kalika Rural Municipality, Rasuwa (4 January), Dudouli Municipality, Sindhuli (4 January), Namobuddha Municipality, Kavrepalanchok (9 January), Siddhicharan Municipality, Okhaldhunga (9 January), Chisankhugadhi Rural Municipality, Okhaldhunga (10 January), Likhu Rural Municipality, Nuwakot (9 & 10 January), Bhotekoshi Rural Municipality, Sindhupalchok (9 & 10 January), Ramechhap Municipality, Ramechhap (10 January), Jiri Municipality, Dolakha (11 January), and Manahari Rural Municipality, Makwanpur (14 January). Some of the highlights from these meetings include:

- In **Kavrepalanchok**, 87% of eligible households have received the first tranche, 57% have received the second tranche, and 30% have received the third tranche. In municipalities there is a higher % of households that have received the second tranche and many households have almost completed their reconstruction. In Rural Municipalities there is a higher % of households that have received the first tranche but not the second tranche and have not progressed beyond the foundation. This indicates that households in municipalities are rebuilding without waiting for inspection and tranche payments. Habitat for Humanity shared that they have completed 35 out of 37 houses for the most vulnerable, have provided 67 households with vulnerable top-ups, and 4 out of 31 households who were not interested in reconstruction and were cancelled from second tranche support have again re appealed for reconstruction and tranche support. Durable Solutions shared that they have collected details of 206 landless beneficiaries and submitted to GMALI Kavre for further processing.
- In **Makwanpur**, there has been slow progress on reconstruction based on the updates from GMALI. A delay in addressing the problems and challenges related to grievances, landlessness, soft loan and other bank related issues were noted and respective authorities will follow up to take necessary actions such as for policy review and reform for resolution of landlessness issues and organising a meeting with banks to ease the service delivery. The meeting also decided to collect information of households - from all Wards/Municipalities - who have not signed the partnership agreement, who have not started reconstruction despite receiving the first tranche, and who have left their reconstruction incomplete.
- In **Kathmandu**, Partner Organisations (POs) have either completed or almost completed their projects. Lumanti has completed a social audit and wrapping up of its activities in Ward 9, Machhegaun, Chandragiri Municipality where the organisation supported construction of 95 houses. Lumanti was urged to conduct a project exit strategy meeting with the purpose of handing over the remaining reconstruction work in the area to the Municipality / Ward office. NRCS has completed its planned activities in Tarkeshor, Shankarapur Municipality, and Ward 17 of Kathmandu Metropolitan City and the project will end in February 2019. The retrofitting of Jansewa Primary School at Kirtipur Municipality by Home Net Nepal with support from Action Aid is also nearly complete and it will be handed over to the school authority by April 2019. NSET's Baliyo Ghar programme has planned to retrofit 31 houses in Kageshor Manahara Municipality.



Jansewa School in Panga, Kirtipur Municipality, Kathmandu. Home Net Nepal, with funding from Action Aid Nepal, is retrofitting the school. The retrofitting work is almost complete, and the school building will be handed over to the school authorities by April 2019. Home Net Nepal also supported the school to set up a Temporary Learning Centre so that the school could continue while the retrofitting work is going on.

- In **Ward 5, Kalika RM, Rasuwa**, the meeting mainly discussed the technical issues and challenges concerning various housing typologies. The major issues in BMC/SMM/SMC were two storey structure with 9" wall, attic made up of CGI and more than 5 feet height, bands missing, and two households sharing a single roof. For RCC houses the main issues were use of 9" x 12" columns, one bay and two storey, flat slab structure i.e. reinforced slab built monolithically with supporting columns and is reinforced in two or more direction with no provision of beam. The major problem in the ward is the modification of houses by households after they have received the third tranche (see the technical case study in [last week's bulletin](#) for an example of this).
- In **Dudhouli Municipality, Sindhuli**, the chairperson from each of the wards and the technical staff all participated. The main challenge in the municipality is that households living on Elani land (Government land where the people have been living for generation) have not been able to start reconstruction even though they have signed the PA. It was also reported that the resurvey was carried out in some places but did not cover all wards. Delays in grievance results, insufficient technical staff in the field, and a lack of clarity on retrofitting guidelines and models have also delayed reconstruction.
- In **Namobuddha Municipality, Kavrepalanchok**, reconstruction is comparatively slower as most of the households are not interested to rebuild because they have other houses elsewhere. It was reported that enrollment of households identified through the resurvey and verification process is on hold as the wards are yet to receive the list of non-eligible households from the municipality. Further, there has been delay in tranche release and some files missing are missing from the DLPIU. There was also discussion on support to vulnerable households. Other points discussed included need for control of forestry to avoid deforestation and to expand planting programmes, improving and maintaining drinking water resources and search different drinking and irrigation water resources, identifying and mapping disaster risk areas like landslide area due to new road network and plots for house construction, and waste management issues and challenges.
- In **Ward 2, Siddhicharan Municipality, Okhaldhunga**, some houses have applied correction measures just to show that they have been corrected like timber bands that are not properly placed as horizontal bands. These households were provided with technical advice on how to carry out the corrections as per the as per the guidelines and informed that they will only be approved to receive subsequent tranches once this is complete. Some households raised complaints regarding delays in the grievance process and some households are not willing to apply correction measures.
- In **Ward 5, Chisankhugadhi RM, Okhaldhunga**, 99% of households have received the third tranche and they are in the process of getting the completion certificates. The ward chief expressed his gratitude to the field technical staff for their hard work and dedication to the reconstruction. He also said that in future houses will be built following the guidelines on earthquake resistant compliant construction which they have learned from the reconstruction. The availability of trained masons, awareness of earthquake resistant housing construction guidelines among households, proper use of local materials (timber, stone, mud and aggregate), and good technical assistance from technical persons have contributed to successful reconstruction in the area.
- In **Ward 1, Likhu RM, Nuwakot**, mainly in the hilly areas stone in mud mortar houses have been constructed and some brick and cement mortar masonry. Some reconstruction challenges exist in areas where houses have been built near the roads. It was found that ward level authorities have been controlling construction of one room houses in the area.
- In **Ward 3, Likhu RM, Nuwakot**, it was reported that due to transportation access in most parts of the ward it has been a challenge for technical personnel to travel and conduct inspections. There are 44 households eligible for the retrofitting grant, but 12 of these want to switch to the reconstruction grant and their files have been forwarded to GMALI. It was found that the majority of houses in the ward are one room.
- In **Bhotekoshi RM, Sindhupalchok**, the ward chairpersons are facing pressure from households because of delays in grievance results. The ward chairpersons requested the NRA to make this a priority. Reconstruction is relatively slow due to geographical remoteness as the challenges for technical staff to access houses for inspections. The tranche disbursement process has been slower because the funds provided to the district treasury from central level is not sufficient. This has impacted in increase of

interest for households who have built houses by borrowing from friends and relatives or taking loans. On top of that households are facing pressure due to the NRA's tranche disbursement deadline. The Chief Administration Officer of Bhotekhoshi RM said the RM has been only verifying the attendance of field engineers and noted the lack of coordination between the RM, the wards, and the DLPIU engineers. Mostly, the issues or progress of the reconstruction does not reach the RM as the ward levels coordinate directly with the DLPIU offices. Field engineers were requested to submit progress reports along with their attendance every month. It was also reported that some households in remote villages are intending to start reconstruction only after receiving all three tranches at once. The technical staff have tried to encourage them to start their reconstruction, but the households are persisting with waiting to receive all three tranches at once. There is also no PO present in the area. The District Support Engineer (DSE) reported an increase in timber houses in Fulpinkatti and advised to apply studs batten for making them compliant.

- In **Ward 2, Bhotekhoshi RM, Sindhupalchok**, the reconstruction progress is good in the ward. The ward secretary thanked the field engineers for their continuous presence and support in reconstruction. The secretary also noted that grievances issues had been resolved. Almost 30 households in the ward have received the first tranche but do not have plan to reconstruct their houses since they have houses in other places. There are 150-200 HHs displaced due to landslides triggered by the earthquake. The displaced HHs in hazard prone Tatopani do not want to move to other places in the hope that the Nepal China border would reopen, and they can do business which is common in the area. It was reported that hollow concrete block houses are increasing due to the low cost and easy access to the blocks.
- In **Ward 3 Ramechhap Municipality, Ramechhap**, it was reported that reconstruction is progressing well and there is regular presence and support of technical persons to the households. At times, unavailability of local skilled masons and labour has caused delays in the reconstruction, but people have been constructing with support from masons from other districts. Community mobilisation in Sanghutar was reported to be positive in regard to reconstruction. Technical persons recommended for mason training to the community in Sanghutar. Technical persons also requested orientation and ToT to themselves time to time. Most of the households in the area have moved to their new houses. About 20-25 houses have been identified as non-compliant and the files have been forwarded to DLPIU office. A total of 55 households have been identified as eligible for the retrofit grant but none have signed the PA yet.
- In **Ward 8 Ramechhap Municipality, Ramechhap**, about 65% of houses have been constructed and technical persons are doing the final inspection for the distribution of the completion certificate. The most common non-compliant issues in the municipality are two storey houses built with stone and mud mortar masonry and houses without bands. Some of these have been solved through application of corrections. A total of 120 households eligible for the retrofit grant are reluctant to sign the PA as they feel 100,000 NPRs is not enough to retrofit their houses. The Executive Officer of the municipality noted regular presence of technical persons in the field and encouraged for close coordination and reporting between municipality and technical persons.
- In **Wards 5 & 6, Jiri Municipality, Dolakha, 11 Jan**, the meeting focused mainly on delays in the grievance process, resurvey process, issues with timber houses, households who have been left out of the grants, MIS problems, and joint family issues in reconstruction. It was reported that technical staff are not approving timber structures now even though they were approved before. Regarding the MIS, due to absence of technical staffs, the system has not been updated regularly. Hybrid structure correction manual was shared with technical staffs and were asked to contact DSE for further information and clarification. Municipality representative shared that the households identified through the resurvey and verification will be enrolled in the system soon.
- In **Manahari RM, Makwanpur**, 80% of households have not signed the PA due to landless issues. Among the 20% who have signed and started reconstruction, only a few have received the third tranche. Many of them had constructed before the deployment of technical persons and the houses are non-compliant. The meeting mainly decided to keep proper record of the reconstruction status, conduct final inspection of houses for certificate distribution, complete the CS entry, and conduct proper/regular supervision of houses under construction and of houses that need correction.

HRRP District Coordination Team Gorkha, Weekly District Report, 4 – 17 Jan 2019



Ward No. 6, Gandaki Rural Municipality, Gorkha: brick and cement mortar masonry house. The home owner has received all three tranches of the GoN housing reconstruction grant.

HRRP District Coordination Team Kavrepalanchok, Weekly District Report, 4 – 17 Jan 2019



Ward No. 5, Temal Rural Municipality, Kavrepalanchok: two storey, stone and mud mortar masonry house. The home owner has received all three tranches of the GoN housing reconstruction grant.

HRRP District Coordination Team Makwanpur, Weekly District Report, 4 – 17 Jan 2019



Ward No. 6, Manahari Rural Municipality, Makwanpur: a three room, load bearing brick masonry structure with light roof. The house looks like it is L-shaped, but there is a wall in the middle. All seismic resistant elements have been provided with the truss connected to the wall. The home owner has received the second tranche of GoN housing reconstruction grant.

HRRP District Coordination Team Nuwakot, Weekly District Report, 4 – 17 Jan 2019



Ward No. 3, Likhu Rural Municipality, Nuwakot: two room, brick and cement mortar masonry house. The home owner has received all three tranches of GoN housing reconstruction grant.

HRRP District Coordination Team Ramechhap, Weekly District Report, 4 – 17 Jan 2019



Ward No. 3, Ramechhap Municipality, Ramechhap: a brick and cement mortar, load bearing structure with ground floor constructed with RCC bands. The first floor is constructed using timber and CGI. The house has excessive openings and there is no proper connection between ground and first floors. The home owner has received the first tranche of GoN housing reconstruction grant.

HRRP District Coordination Team Sindhuli, Weekly District Report, 4 – 17 Jan 2019



Ward No. 11, Dudhouli Municipality, Sindhuli: brick and cement mortar, load bearing structure. The house was constructed before the deployment of DLPIU Engineers. The home owner has received second tranche of the GoN housing reconstruction grant. The house has 5" wall and discontinuous bands without proper spacing.

Case Studies

Shyam Prasad Adhikari, an employee of Nepal Electricity Authority is a permanent resident of Ward No. 6, Daraunepokhari RM, Kavrepalanchok. His house was partially damaged by the 2015 earthquake and after a few months, he along with his 3-member family moved to Kathmandu. He now lives in a rented house in Kathmandu. He returned the first tranche due to lack of time and because of fear of being blacklisted. However, he has intention to reconstruct the house if the NRA tranche disbursement deadline is extended.

Santa Devi Lamicchane from Nayapati, Ward No. 12, Dhulikhel Municipality lives in a repaired house with her husband. Her one and a half storey, load bearing, brick and cement mortar masonry house was damaged by the 2015 earthquake. The family spent 200,000 NPRs for the repair and maintenance of the house which was carried out by a contractor that they hired to do the work. Santa returned the first tranche of 50,000 NRs to the Government due to fear of being blacklisted and that this would mean the family would be restricted in accessing other Government services. The technical staff suggested to Santa that she will need to build another house since the house they are living cannot be repaired. The family already has spent money on repair and are not willing to construct another house.

Prem Lama of Salle Bhumlu-04 wants to return the first tranche of 50,000 NPRS as he is not able to start reconstruction on time and meet the NRA tranche disbursement deadline. His brother (whose name is listed as eligible for the grant) has been working as a labourer outside of Nepal for 4 years. Prem says that he does not have sufficient funds to start reconstruction and that there isn't enough skilled manpower available in his village. Prem came to the GMALI office to get information on how to return the first tranche as he did not have any information on the procedure for this. He shared that if the NRA tranche disbursement deadline will be extended, the family will reconstruct the house.

Featured Technical Staff Person, Sunil Pokharel: Sunil was the NRA/HRRP focal person for coordination of reconstruction in Arughat Rural Municipality (RM), Gorkha from September 2017 until the end of 2018. Sunil was the first municipal focal point for reconstruction, supported by SDSC and CRS, and working as per the [TOR for municipal focal person](#) jointly developed by all reconstruction actors in the district. In this role, Sunil conducted orientation programmes with different reconstruction stakeholders, conducted regular socio technical assistance with households (including type of house, cost, materials etc.), coordinated and facilitated some 7 day and 50 day mason training courses, conducted regular coordination meetings between ward engineers, DLPIU engineers, ward chairpersons, and RM representatives, provided information to households on when their tranche payments were expected to be in their bank account, conducted monthly coordination meetings at ward level and RM level, ran a helpdesk at the RM to provide information to households coming to the RM office, planning reconstruction activities and targets, ensuring information on new decisions, policies, procedures, etc. were disseminated in the municipality, and supporting establishment of the [municipality's revolving fund to support vulnerable households](#).

Sunil faced some challenges in this role, including how he was perceived as someone contracted by an NGO deployed in a government office, the lack of uniformity in technical assistance, lack of access to information on retrofitting options, non-compliance issues (many people had constructed very quickly after the earthquake and their houses did not meet the minimum standards), no technical person at the RM office, elected representatives had just started in their role and had limited knowledge of the reconstruction policies and processes, transportation was difficult, and confusion amongst households as they found it hard to access information on the reconstruction.

Sunil's experience in Arughat RM contributed to expansion of the focal point role into other municipalities in Gorkha following an exposure visit carried out in Arughat. One municipality funded the role directly and in three other municipalities the role was funded by POs (Oxfam and CRS). During the district level reconstruction orientation and review workshops carried out by the NRA CLPIUs (Building and GMALI) in all 32 earthquake affected districts in November, December, and January, each municipality has appointed a focal to coordinate and communicate reconstruction efforts. The major responsibility for each of these focal points, normally one of the

NRA/DLPIU engineers, is to support the municipal authority in regularly updating their reconstruction action plan, progress, and municipal profile. Contact details for these focal points are available [here](#).



Sunil conducting a community orientation on earthquake resistant construction techniques.

Salang, Ward No. 4, Siddhalekh Rural Municipality, Dhading: this house was approved for the second tranche of the housing reconstruction grant due to a technical error in the MIS. This is the home owner's pre-earthquake house that was damaged in April 2015. The home owner has no plans to demolish the house, but it is unclear how it could be retrofitted / corrected so it would be compliant with the technical requirements.



Requests for Partner Support

INVITATION, Vulnerable Support Working Group (VSWG) meeting, 2-3:30 PM, 22 January, HRRP Office Jwagal:
please do join us for this meeting where the agenda will be as follows:

- 'Refresh'-Objective of the WG 30 min
- Experience sharing 30 min
 - 10 min: summary of previous experiences shared by the members in 2018
 - 15 min: new learning (PIN/PA, Swiss contact, UNOPS, etc.)
 - 5 min: Discussion
- Identification of vulnerable households - a way forward: 30 min
- National sharing session, Round Table to be planned for Feb 19
- AOB

Please contact Minar Thapa Magar (minar@hrrpnepal.org) or Rupa Pandey (meal@hrrpnepal.org) if you have any questions or need any additional information about the meeting.

GoN Products

Contact Details:

- [NRA District Support Engineers](#)
- [District Survey Offices](#)
- [Municipal Focal Points](#)

HRRP Products

5W Products are prepared based on the [latest round of 5W data, as of 25 December 2018](#). **Housing reconstruction progress maps** are prepared based on Building CLPIU data as of 5 January 2019.



Technical Assistance for Housing Reconstruction - Coverage of Activities

[7 TA Activities-32 districts](#)
[7 TA Activities - Eastern Cluster](#)
[7 TA Activities - Central Cluster](#)
[7 TA Activities - Western Cluster](#)
[Short Training Coverage](#)
[Vocational Training Coverage](#)
[Community & HHs Orientation](#)
[Demonstration Construction](#)
[Door to Door Technical Assistance](#)
[Helpdesks/Tech. Resource Centres](#)



Sector Wise Maps of EQ affected districts

[Agriculture, Livestock Dev, Irrigation](#)
[Disaster Risk Management](#)
[Education](#)
[Employment and Livelihood](#)
[Gender Equality and Social Inclusion](#)
[Health](#)
[Nutrition](#)
[Social Protection](#)
[Water, Sanitation, and Hygiene](#)
[Number of POs in each ward](#)
[Number of sectors in each ward](#)



Housing Reconstruction Progress Maps

[PA agreement between HHs and GoN](#)
[Construction Started](#)
[1st tranche received](#)
[Compliance rate 2nd tranche](#)
[Compliance rate 3rd tranche](#)
[Construction completed](#)

Partner Products

[The State of Humanitarian Shelter and Settlements 2018, Beyond the Better Shed: Prioritising People, Global Shelter Cluster](#): this is the first report on The State of Humanitarian Shelter and Settlements and it aims to paint a broad picture of the sector, discuss major issues and links to other disciplines, and identify difficulties and gaps. It covers a wide array of topics, emphasising the complexity, relevance, and foundational nature of shelter and settlements, providing the basis for future reports, which will focus on particular topics. The report aims to support more effective and accountable humanitarian responses through the sharing of knowledge and approaches that examine more deeply the complexities of humanitarian shelter and settlements. The report also provides analysis of current trends such as urban response, involvement of government, civil society and the private sector, localization, and cash-based responses. The publication is also intended to raise the profile and provide a better understanding of the humanitarian shelter and settlements sector. The report is for humanitarian policy makers, donors, governments, academics, and senior managers of humanitarian agencies and institutions and it is hoped that it will help them to better prepare for and meet the shelter and settlement needs of populations affected by humanitarian crises.

[Paani - a short film about water shortage in Kathmandu, Record Docs](#): this short film illustrates the water shortages faced by residents in the Kathmandu Valley. It was made by students at Kathmandu University School of Art and Jade University of Applied Sciences, Germany and was produced by Nishon Shakya, Alena Wedell, Bipin Bnajara, Mario Grabowski, and Jenina Stellpflug.

[Milijuli Nepali, Episode 1162](#): this episode was recorded in Bhimphedi, Makwanpur. The first story is of Gyan Kumari and Devi Kumari Rana who are eligible for the government's retrofitting grant. They have already collected the first tranche and share that it is important to follow an engineer's instructions for retrofitting. Their neighbour Chitra Singh Waiba shares that he wants to retrofit his old house because he cannot afford to build a new house. The second story is of Thuli Pakhrin, who shares that she has already built a new house. Thuli still has her old house which she has tried to repair by covering the cracks. The presenter, Bhawana Gurung, suggests that Thuli should get advice from an engineer so that she can retrofit her house. The third story is of father and son, Chandra Bahadur and Indra Bahadur Rana Magar, whose houses have small cracks. Their house is being inspected by the engineer, Rabi Kiran Tiwari to check the possibilities for retrofitting. Chandra Bahadur used to work as a mason and he built his house approximately 40 years ago. The engineer explains the importance of tie beams and how Chandra and Indra's houses can be retrofitted. The final story is of ward member, Chet Kumari who explains how ward officials can support households eligible for the retrofitting grant. Chet also discusses the benefits of retrofitting the old houses in the villages.

[Baliyo Ghar TV, Episode 127](#): this episode looks at what the preliminary concept behind Earthquake Safety Day was and what the achievements of ESD have been so far. The episode also includes discussion with Mr. Chiribabu Maharjan, Mayor, Lalitpur Metropolitan City, Dr. Gangalal Tuladhar, DRR expert, and Mr. Surya Narayan Shrestha, Executive Director, NSET on the past, present, and future efforts for disaster risk reduction.



'What Matters for Households - Recovery Trajectories Following the Gorkha Earthquake?', a Two-Year Panel Study, Mercy Corps, April 2018: to understand what mattered for recovery in the short and long-term, this study followed the same households 10 weeks, one year, and two years after the Gorkha earthquake. The analysis explores what factors mattered most for short-term coping and long-term recovery in order to improve humanitarian response and design of recovery programs in the aftermath of acute disasters.

'Fighting Inequality in Nepal, the road to prosperity', Oxfam: this report seeks to take stock of the context and drivers of inequality in Nepal and offer evidence-based recommendations that can support the government's commitment to tackling inequality.

[FAQs](#) | [Briefing Pack](#) | [Meeting & Events](#) | [5W](#) | [Housing Progress](#) | [Housing Typologies](#)



CONTACT US

HRRP Nepal Office

Jawagal, Lalitpur, Nepal

Tel: (+977) - 01 - 5544149

Email: info@hrrpnepal.org
