

Monthly District Report

Dolakha, Ramechhap, Sindhuli

27 September – 21 October 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Dolakha	Palika Level Coordination Meeting on Reconstruction	22-Oct-2019	Kalinchowk RM – 1 & 8.	prabin.gautam@hrrpnepal.org	GD link
	Palika profile link upload at Palika website	23-Oct-2019	Bhimeshwor Municipality – 3.	prabin.gautam@hrrpnepal.org	GD link
	Updated palika profile.	24-Oct, 2019	-	prabin.gautam@hrrpnepal.org	GD link
	Support GMAI for compilation of INGOs tranche released detail and submitted to nation IM.	18-Oct. 2019	-	prabin.gautam@hrrpnepal.org	
	Field visit at Kalinchowk RM and Bhimeshwor municipality in order to find Palika issues on present reconstruction process and monitoring POs activities on reconstruction at ward and Palika.	21 - 23 Oct. 2019	Kalinchowk RM and Bhimeshwor Mun.	prabin.gautam@hrrpnepal.org	Refer to field visit section - 1
Sindhuli	Palika Level Coordination meeting	2019/10/22	Tinpatan RM	Tulasi Ram Lamichhane; tulasi.lamichhane@hrrpnepal.org	Refer to field visit section
Ramechhap	Field Visit to Khadadevi RM	2019/10/21 to 2019/10/23	Ramechhap, Khadadevi RM	Pranjal Bhandari	
	Ward Level Coordination Meeting	2019/10/22	Ramechhap, Khadadevi-4	Pranjal Bhandari	Minutes of the Meeting


Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Partners Coordination Meeting	(20 Nov, 2019) Ramechhap, Manthali Municipality	HRRP, DLPIU GMALI	Pranjal Bhandari
Joint Monitoring Field Visit	Ramechhap Municipality, (11-15 Nov)	HRRP, DLPIU Building	Pranjal Bhandari


Tranche Status (Dolakha)

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Baiteshwor Gaunpalika	6392	8359	8204	7826	7341	7015	342	54	54	0
Bhimeshwor Nagarpalika	10796	12515	11617	11371	9173	8216	353	179	179	0
Bigu Gaunpalika	5758	6733	6358	6303	5899	5639	35	8	8	0
Gaurishankar Gaunpalika	5405	6876	6697	6604	5895	5714	134	51	51	0
Jiri Nagarpalika	4764	5850	5665	5177	4383	3864	171	77	77	0
Kalinchok Gaunpalika	7527	8916	8534	8513	8120	7871	32	21	21	0
Melung Gaunpalika	7006	7685	7207	6922	6203	5861	476	262	262	0
Sailung Gaunpalika	6800	8424	7308	7293	6352	5756	918	213	213	0
Tamakoshi Gaunpalika	6191	7461	6979	6981	6564	6193	115	41	41	0

Reconstruction- Tranche Status

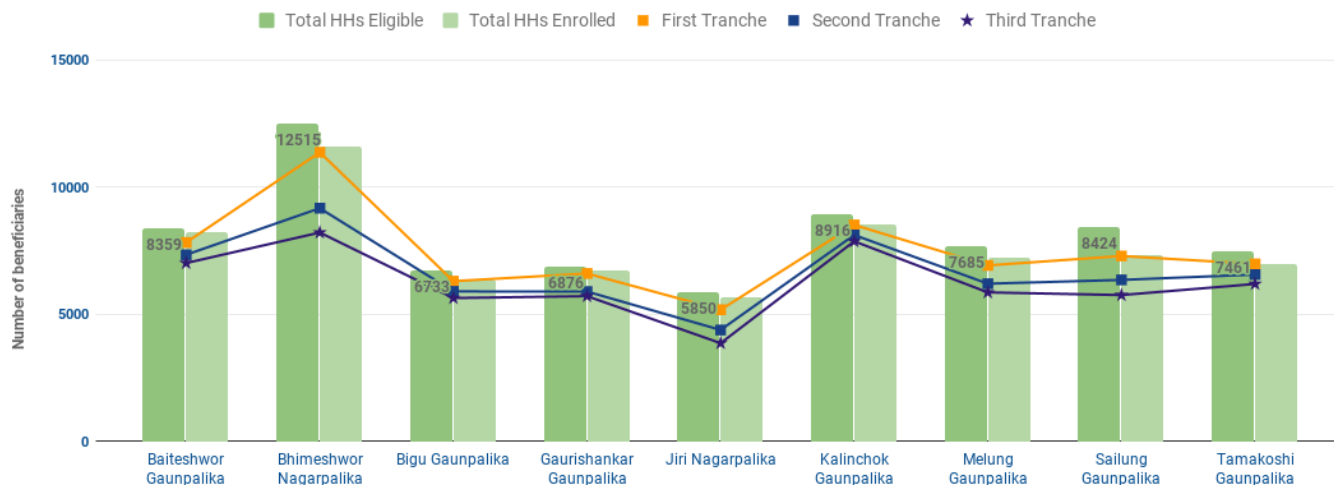

Reconstruction - Retrofitting Status

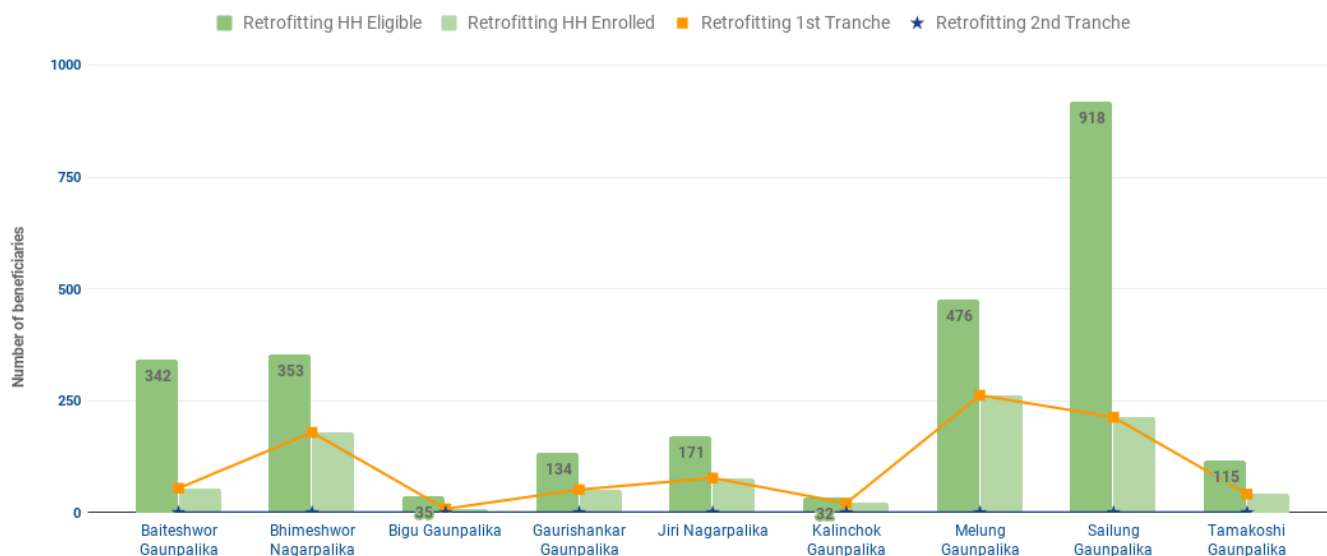


Tranche Status (Sindhuli)


Tranche update:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Dudhouli Nagarpalika	15002	5203	5203	4494	2698	1213	3910		2480	0
Ghanglekh Gaunpalika	3032	2247	2247	2135	1879	1500	533		406	0
Golanjor Gaunpalika	4835	3235	3235	3116	2818	2481	683		234	0
Hariharpurgadhi Gaunpalika	5176	2632	2632	2511	1991	629	1786		1104	0
Kamalamai Nagarpalika	15659	8578	8578	8043	5465	3748	2042		1331	0
Marin Gaunpalika	5717	3773	3773	3450	2446	1282	1371		972	0
Phikkal Gaunpalika	4072	2669	2669	2571	2230	1984	928		161	0
Sunkoshi Gaunpalika	6393	5058	5058	4821	4420	3656	343		35	0
Tinpatan Gaunpalika	8863	4719	4719	4606	4142	2778	2513		2132	0

Graph of Tranche Status:

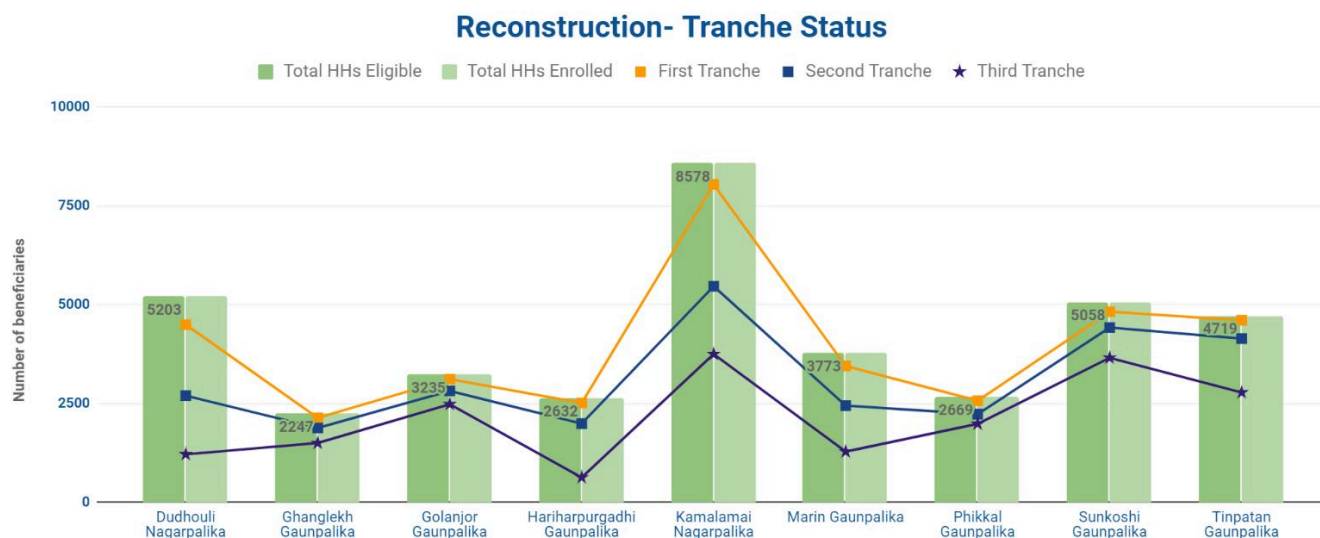

Graph for Retrofitting Status:

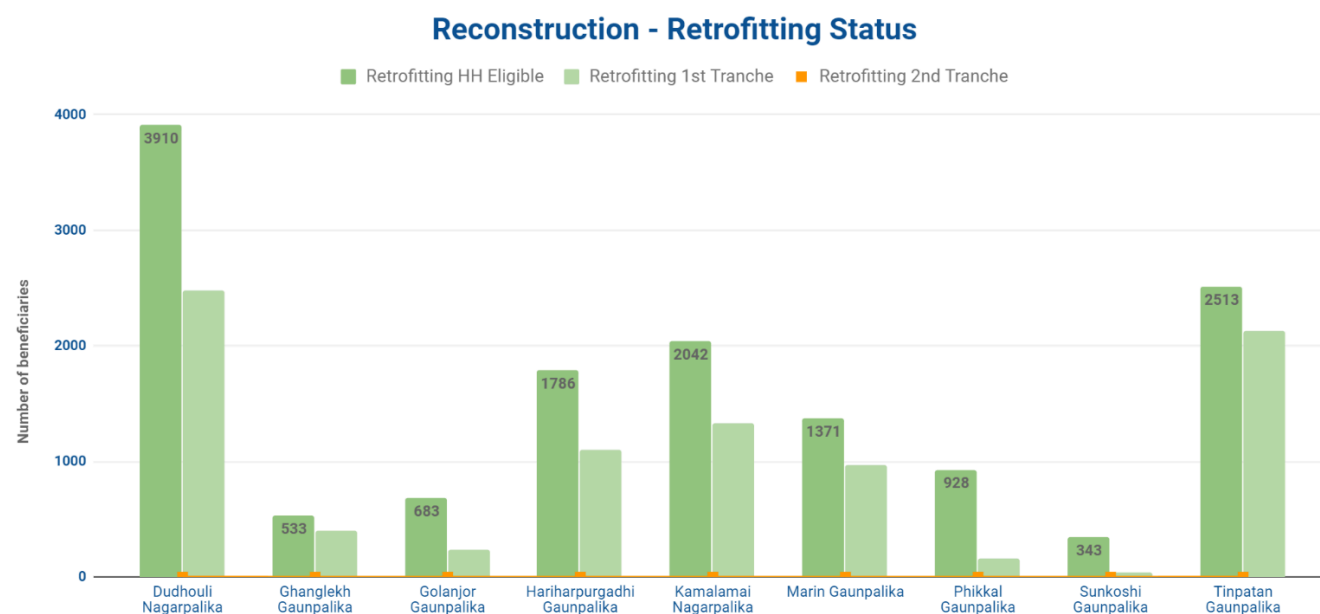


Tranche Status (Ramechhap)


Tranche Status Table:

	Total Eligible HHs	PA Agreement Signed	Tranche I	Tranche II	Tranche III	Retrofit Eligible	Retrofit Tranche I	Retrofit Tranche II
Doramba Gaunpalika	5275	4855	4849	4115	3449	1116	84	0
Gokulganga Gaunpalika	6744	6124	5489	5489	4822	367	14	0
Khadadevi Gaunpalika	5223	5128	5128	4848	4452	1317	222	0
Likhu Gaunpalika	5688	5570	5570	5226	4857	1010	26	0
Manthali Nagarpalika	11123	10800	10796	9913	8953	1321	136	0
Ramechhap Nagarpalika	6555	6424	6424	5939	4982	971	6	0
Sunapati Gaunpalika	3697	3563	3561	3206	2614	954	21	0
Umakunda Gaunpalika	4997	4643	4643	4205	3301	346	10	0

Graph of Tranche Status:

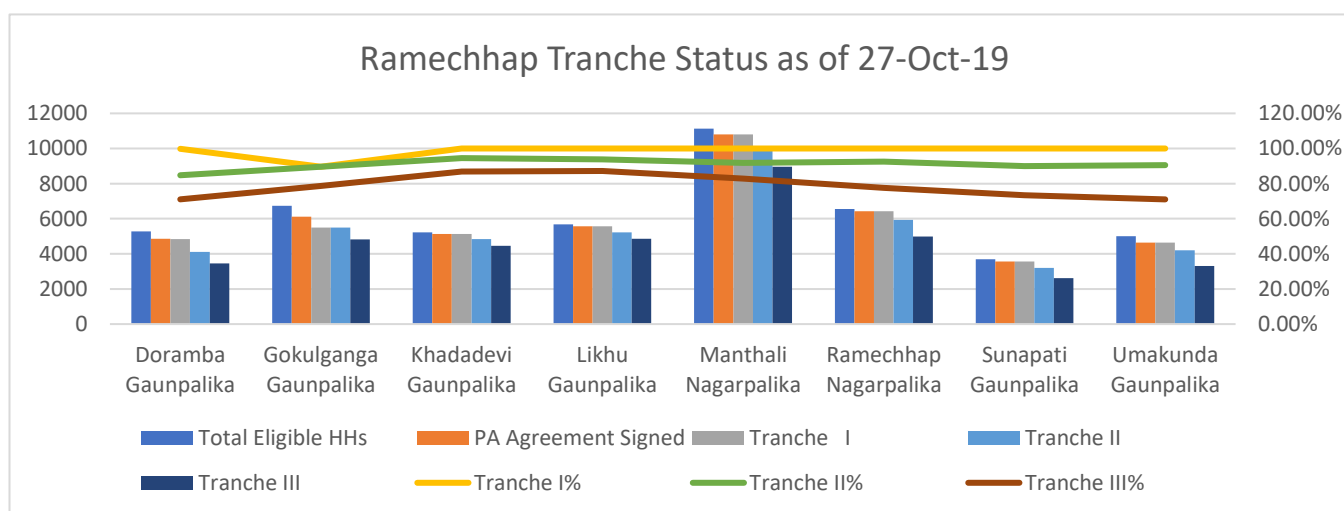

Graph for Retrofitting Status:

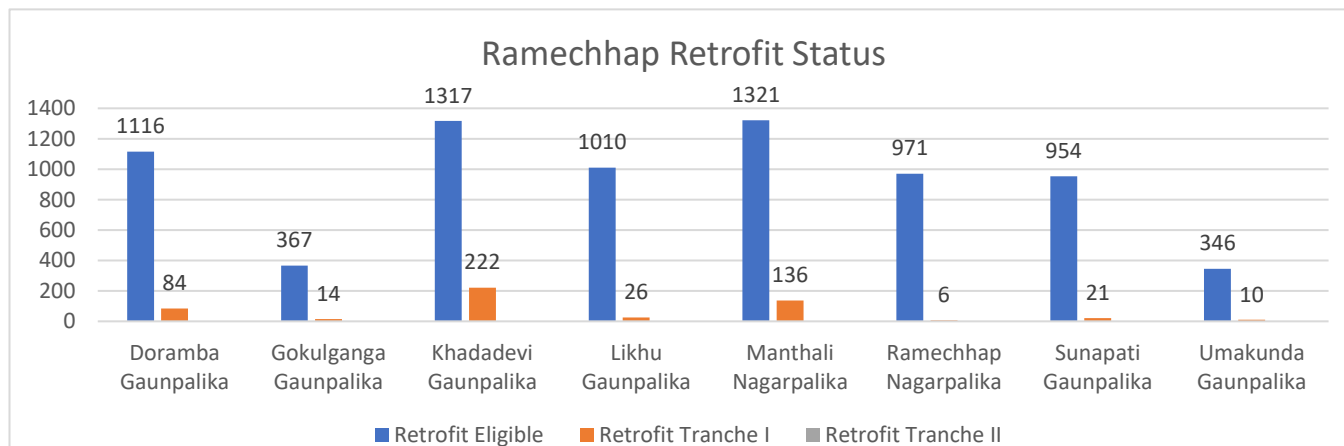

Field Visit Reports (Dolakha)

Visit 1

Date	Location	Participants
(21 – 23) October 2019	• Kalinchowk RM and Bhimeshwor Municipality.	• Aaysha Joshi (DLPIU-Palika focal person) • Prabin Gautam (HRRP) • Tika Joshi (GMAI)
Objective(s)	• Ward and Palika level coordination meeting and identification of housing completion HHs. • Conduct palika assessment/survey. • Housing Typology Survey collection • Distribution of HRRP info pack to stakeholders at ward and RM. • Find non-compliant issues, retrofit HHs and suggest as per need from NRA engineers.	

Why was the visit carried out in this location?

Palika issues on present reconstruction process and monitoring POs activities on reconstruction at ward and Palika.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

- No. of HHs visited:3
- No. of meetings with engineers: 2
- No. of meetings with local officials: 2

During the field visit of two palikas namely Bhimeshwor municipality, ward no.: 3 and Kalinchowk rural municipality, ward no.: 1 and 8, HRRP conducted coordination meeting in order to identify issues on present reconstruction progress and monitoring POs activities on reconstruction at ward and palika.

Palika /ward	Count of PA No.:	RCB	RTB	GRB	Agreement	1st Tranche	Retro 1st Tranche	Total 1st	2nd Tranche	Total 2nd	3rd Tranche	Total 3rd	Rank	
Bhimeshwor Municipality														
3	840	544	68	228	746	679	36	715	511	511	440	440	63.74	6
Kalinchowk RM														
1	825	645	3	177	784	779	2	781	741	741	721	721	93.24	8
8	1029	828	10	191	1006	987	10	997	963	963	942	942	94.68	3

Table: Bhimeshwor and Kalinchowk Palika/ward tranche detail

Following were some of the major point of discussion during coordination meeting:

Kalinchowk Gaupalika, ward 8 meeting:

1. Ward chief Mr. Khem Bahadur Khadka said that in Kalinchowk RM many of the private house have been built while many of the historical places like temple and monasteries are at critical condition.
2. Focused on quick result of resurvey and reverification from NRA so that needy beneficiary can reconstructed their house sooner.
3. Kalinchowk Gaupalika member emphasized ward no. :1 to have a potential on Urbanization with greater tourism income for Palika.
4. It seems a good progress in reconstruction due to continuous effort of DLPIU/BUILDING and aware beneficiary.

It stands at rank 3 out of all wards of Kalinchowk RM with 94.68% reconstruction progress.

Bhimeswor municipality, ward 3.

1. Reconstruction at ward -3 with growing urbanization, unplanned settlement, irregular housing i. e. gaps between houses. These issues have added more challenges for speeding up the reconstruction.
2. Retrofit beneficiaries are in large no. but they are not willing to retrofit due to high cost to do it. They do not want to cut-throw the standing building to meet the municipality norms.

It stands at rank 6 out of all wards of Bhimeswor Municipality with 63.74% reconstruction progress.

[Meeting minute of 22-Oct-2019, Kalinchowk RM, ward no. 8](#)

[Meeting minute of 23-Oct-2019, Bhimeshwar Municipality, ward no.3](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
When will the resurvey and reverification task result be publish from NRA?	.		Beneficiary, NRA, Plaika/Ward and NRA/GMaLI	
When will the beneficiary receive house completion certificate?	After completion of construction of building/house.		NRA/GMaLI and DLPIU/Build ing	
How will the retrofit beneficiary be supported technically from NRA?	RTB beneficiary can be converted to RCB only through recommendation of NRA field engineers and palika/ward officials to central NRA. Or they might need to retrofit their houses on time.	Orientation on retrofit technique should be provided.	NRA/GMaLI, DLPIU/Build ing, POs and Palika/Ward	

Photos



Photo: Need of reconstruction at a historic temple of a village of Kalinchowk RM, ward no.: 8.



Photo: Kalinchowk RM, ward no.: 1, Kuri village with a growing planned urbanization settlement area.

Field Visit Reports (Ramechhap)

Visit 1

Date	Location	Participants
21-23 Oct-2019	Khadadevi RM	Pranjal Bhandari, Kishor Bikram Shahi, Rajesh Sunuwar, Nikesh Shrestha
Objective(s)	- To observe the retrofit houses being constructed by Build Change, To interact with the beneficiaries and elected representatives on retrofit - To identify the pressing issues on the reconstruction facing the Rural Municipality	

Why was the visit carried out in this location?

- The Palika has the highest number of retrofit beneficiaries in the District
- To Distribute the HRRP Info Packs to the stakeholders
- To observe the retrofit houses being done by Buildchange.
- To interact with the beneficiaries and the ward representatives regarding retrofitting.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

Summary

Field Visit:

- No. of HHs visited: 4
- No. of meetings with engineers: 1
- No. of meetings with local officials: 1

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)

[Meeting Minutes](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Khadadevi RM-4, Pakarbas has the lowest enrollment rate of the retrofit beneficiaries in the RM.	The beneficiaries need orientation on retrofit	The DLPIU Building and the Ward office would jointly conduct an interaction program with the beneficiaries	DSEs, Ward Chief	ASAP
There are a lot of beneficiaries who are not living in the newly constructed earthquake resistant houses but are living in their old earthquake affected houses	The ward office should begin an awareness campaign	The ward officials would visit the beneficiaries door to door to encourage them to shift to their newly constructed earthquake resistant houses.	Ward Office	ASAP

Photos



Ramechhap DSE Mr. Nikesh Maharjan interacting with the Buildchange Officer and retrofit beneficiary at Khadadevi RM-7

DLPIU Building officials observing the house of vulnerable retrofit beneficiary belonging to backward Thami community at Khadadevi RM-7

Field Visit Reports (Sindhuli)

Visit 1

Date	Location	Participants
22nd Oct 2019	Meeting Hall of Tinpatan RM	- Dinesh Sanjel, DSE - Rajib Kr. Sah, DSE - Niraj Kr. Singh, DLPIU Building - Mohan Shrestha, DLPIU Building - Tulasi Ram Lamichhane, DTC HRRP
Objective(s)	- Information regarding Retrofitting - Status of Reconstruction in Palika. - Challenges the Rural Municipality is facing in reconstruction. - Updates form UNOPS/Build Change	

Why was the visit carried out in this location?

- To start the orientation on retrofitting as a initiation of activities of retrofitting task force team.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

N/A

Summary

Field Visit:

- No. of HHs visited: 4
- No. of meetings with engineers: 1
- No. of meetings with local officials: 1

The program was chaired by the Vice chairperson of Tinpatan Rural Municipality Padam Maya Tamang. DSEs, Member of district task force team were the guests in the program. The program was facilitated by Mohan Shrestha, Sub Engineer of DLPIU Building.

- DSE Dinesh Sanjel updated the reconstruction status of ward level of Tinpatan Municipality.

वडा नं.	पुनर्निर्माण तर्फ				प्रवलीकरण तर्फ		जम्मा लाभग्राही
	लाभग्राही संख्या	पहिलो किस्ता लिने	दोस्रो किस्ता लिने	तेस्रो किस्ता लिने	लाभग्राही संख्या	पहिलो किस्ता लिने	
१	२२८	२१४	२००	९८	५४६	३७०	७७४
२	५६३	५६२	४७४	२७६	२८०	२६७	८४३
३	४०७	४०२	३६६	१६८	१२६	९५	५३३
४	३५७	३५७	३०४	२१४	३४२	३३१	६९९

५	५६५	५५२	५२३	४७०	१११	५९	६७६
६	८६२	८५८	७७३	४६६	९७	८७	९५९
७	२७७	२७३	२५०	२३८	९७	६२	३७४
८	२८६	२६७	२३८	१९८	२०१	१६६	४८७
९	४२८	३९४	३४६	२७५	३३७	२७४	७६५
१०	३७०	३६६	३४३	१६८	११८	११३	४८८
११	३७६	३६१	३२५	२०७	३५९	३१७	७३५
जम्मा	४७१९	४६०६	४१४२	२७७८	२६१४	२१४१	७३३३

प्रतिशत	९८%	८८%	५९%		८२%
---------	-----	-----	-----	--	-----

- He also stated that the several reasons delay in reconstruction in the district. He stated that the number of retrofitting beneficiaries in the district is about 22% of the total retrofitting beneficiaries of the earthquake affected districts and the guidelines and training programs have been just introduced. He also stated that CLPIU is demanding the details of the retrofitting beneficiaries and requested the engineers deployed in the field to send the details in the format provided within the end of month of kartik. He also stated that a task force for retrofitting has been formed in the palika and district level whose responsibility is to boost the retrofitting in the district. The coordinator of the task force is DSE in the district and focal person of the palika in palika level. He also requested the ward chairperson to motivate the beneficiaries for retrofitting.
- Chairperson of ward no 4 stated that there are beneficiaries residing in ailani land but still have numberi land which is vulnerable. So, they are not being able to reconstruct the houses.
- Vice Chairperson of Tinpatan Rural Municipality gave the closing remarks. She committed all the support from the palika to complete the reconstruction in time. She also expressed her support to the retrofitting task force in the palika.

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
The timber houses constructed are not complying with the building code	Some corrections should be provided as suggested by DSE	DSE	DLPIU Building and house owner	ASAP
There are people residing in <i>ailani</i> land and have <i>numberi</i> land nearby the river which is vulnerable to construct house.	First the list of such beneficiaries should be provided for geological study. If the land is considered as vulnerable, then the house owner can leave the current land and get 2 lakhs to reside in new land. If the owner is willing to reside in the current land a	HRRP/DLPIU Building	GMALI, NRA, Cabinet	ASAP

	decision from cabinet must be made			
Photos				
				
DSE sharing the updates of reconstruction		Coordination meeting at Tinpatan Rural Municipality		

Housing Typology Report



Write caption here: The house of Tilak Bahadur Ramauli Magar being retrofitted in Ambote of Tinpatan RM. The house is being retrofitted under the technical assistance of UNOPS/Build Change. The organization has also been providing material and labour support to the house owner. The house is timber structure.



Write caption here: The house of Barta Maya Gautam being retrofitted in Ambote of Tinpatan RM. The house is being retrofitted under the technical assistance of UNOPS/Build Change. The organization has also been providing material and labour support to the house owner. The house is timber structure.



Name: - Jagat Bdr. Gurung
Location: - Kalinchowk Rural Municipality, ward no.: 1, Dolakha.
It is three storey Stone in cement mortar building with RCC bands.
The house owner is planning to run home stay in future.



Name: - Dip Bahadur Magarati
Location: - Kalinchowk Rural Municipality, ward no.: 8, Dandakharka village.
The beneficiary has built double storey hybrid structure building using brick in cement mortar with RCC bands. The house owner has received all tranches of government grant.



The house belongs to Mr. Chamar Singh Ghising and is situated at Khadadevi RM-7. The house is SMM loadbearing structure. The House Owner has received all three tranches, the cost of construction is Rs.600,000 appx. The houseowner has taken a loan of Rs. 200,000 from local lenders at 24% annual interest rate.



The house belongs to Bishnu Bahadur Shrestha and is situated at Khadadevi RM-5, Fulpa. The House is SMM loadbearing structure. The House Owner has received all three tranches. The total cost of construction of the house is appx. 400,000. The Owner has taken a loan of Rs. 100,000 for the construction of the house from the local cooperative at 18% annual interest rate.

Case Study



Retrofit Builder Trainer Dil Bahadur Gharti Magar

Dil Bahadur Gharti Magar hails from Rolpa Tribeni Gaunpalika and he has been working as a mason since the past 18 years and he has been working as the mason for the last 12 years. He has completed his secondary education. Throughout his life he has travelled to several places to work as mason. He is currently survived by his mother and his son.

The great earthquake came as an opportunity for him, he shares. The earthquake opened new job opportunities for him at the time when the job was hard to find, and the wages were low. After the earthquake, he began at working at Charikot where he was involved in the construction of about 10 houses. Then, he moved to Jiri where he constructed about 10 RCC houses. He was working at Manthali where he saw the vacancy for builder trainer at UNOPS and decided to apply for it. His happiness knew no bounds when he got selected as builder trainer.

Understanding retrofit was difficult at the initial phase recalls Dil Bahadur but with the effective guidance from the trainers at UNOPS/Build Change, he was able to learn about the techniques used. After the completion of the training, he was stationed at Ramechhap district. He was involved in the retrofitting of 8 retrofit model houses as builder trainer. He was also involved in retrofitting of wooden houses at Sindhuli district.

He is currently involved in the construction of 10 model houses at Khadadevi Rural Municipality. As a builder trainer, the major challenge that he faces is the lack of the competence of the masons. Most of the masons working in the reconstruction lack the work-related knowledge and experience because of which it gets difficult to gel as a team and the retrofit work gets delayed and are prone to error. Also, the expectations of the masons are very high, and they expect more wages from the organization.

In order to speed up the retrofit, he believes that a greater number of mason trainings are needed, and he is also hopeful that with the start of the retrofitting in the district, additional retrofit manpower could be developed. With the increasing number of houses enrolled into retrofit in Khadadevi RM and many beneficiaries enquiring about retrofitting, he expects retrofitting to pick up pace in the coming months.
