

District Report

Kathmandu Valley

22 – 28 December 2017

Activity Summary

Activity	Contact Person	Reference Document
District level project closure meeting of LWF Lalitpur program with implementing partner Solve Nepal and ICDO was organized on 22 December 2017 at Bagaicha Restaurant, Jawalakhel, Lalitpur. The representatives from Solve Nepal, ICDO and LWF along with the GoN representatives from NRA, DLPIU-MOUD, DLPIU-MOFALD, representatives from the local bodies, beneficiaries and HRRP Kathmandu actively participated during the completion meeting. In total 240 houses were reconstructed in Bagmati rural municipality under this program. With the successful completion of the project there were also some challenges that were faced during its implementations too. Some of them are listed below • Participation and Enthusiasm from the communities to reconstruct the house was not as expected that have given the impression of not having the ownership towards the reconstruction. • The trained masons were not enough and those available too busy which has caused some delay in reconstruction • Transport of the materials from the city to the site was expensive • There were two cases from ICDO where even after signing the contract and receiving the 1st tranche the beneficiaries were not able to complete the construction since they do not have their own land. The participating beneficiaries who were also the part of the Household management committee shared their experience about the program during the meeting and expressed their gratitude to LWF, Solve Nepal and ICDO making helping them build their houses.	Kamal Prasad Poudel kamalp@lwf.org.np	
General coordination meeting of Bhaktapur district with NRA, DLPIU, and DLPIU deployed engineers, M&E consultant, DSE and HRRP was conducted on 26 December 2017 at DLPIU Bhaktapur office. The agendas of the meeting were as follows: → NRA decision to DLPIU → Updates of each municipality from DLPIU deployed engineers. → Updates of HRRP activities	Ambika Amatya dc.ktm@hrrpnepal.org	The minute of the meeting will be forwarded later.

Activity Summary

→ Updates from the Monitoring and Evaluation consultant (MOUD, MOFALD) The major decision made during the were as follows: → Beneficiaries should be encouraged for the tranche requested before the end of Kartik. → For addressing issues on- multiple beneficiaries with flat system, a central level committee in NRA central office has been formed. Relevant directives will be released soon. → If there are two beneficiaries in same house with one drawing and same footing but with two stairways, then 2nd tranche release should be forwarded. → Requests for making house using unburned brick can be forwarded with a condition that the cement and roofing should fall into standard as guided by GoN for such houses. → Engineers were requested to participate in the orientation on repair and retrofitting manual and hybrid structure manual organized by HRRP on 27 December 2017.		
Orientation on Repair and retrofitting manual and Hybrid structure on 27 December 2017 at Bagaicha restaurant, Jawalakhel. The orientation was conducted for the technical staffs of POs, Municipality/rural municipality and DLPIU of Kathmandu, Lalitpur and Bhaktapur district. In total 51 technical staffs from GoN and POs participated in the orientation.	Sweata Sijapati techcord.ktm@hrrpnepal.org	The report of the orientation will be shared separately.
Public hearing program of IDP communities of Khokana and Bungamati was organized by Lumanti in support with OXFAM on 28 December 2017 in Ghantaghar party palace, Bhaishapati, Lalitpur. NRA chief of Lalitpur, Ward chairperson of Khokana, Lalitpur Metropolitan city were the chief guest of the program. There was participation of beneficiaries who are still living the IDP camps. In general the discussion was focused on the achievements of activities undertaken in the project "Supporting Durable Solutions for Earthquake Displaced and Affected People Living in Camps" and its way forward so that all beneficiaries can have their own residence.	Kumari Shova Tandukar kumari@lumanti.org.np	

Upcoming Events & Meetings

Event / Meeting	Date, Time, and Location	Contact Person
Mason training has been planned in Ward no 1, Sundarijal of Gokarneshwor Municipality. The training will be conducted by the ward office.	January 2, 2017 (Poush 18, 2074) at Okhrenei School, Sundarijal	Ram Manandhar Ward Chairperson, Ward no. 1 Gokarneshwor Municipality
General coordination meeting of NRA Kathmandu	To be decided	Sweata Sijapati techcord.ktm@hrrpnepal.org

Upcoming Events & Meetings

Technical coordination meeting of Bhaktapur district with NRA, DLPIU, DLPIU deployed engineers, M&E consultant, DSE and HRRP Bhaktapur	27 December 2017, DLPIU office, Bhaktapur	Sweata Sijapati techcord.ktm@hrrpnepal.org
Orientation to the ward chief, ward secretary and DLPIU technical staffs	To be decided	Yamnath Giri, M&E, EHRP yamnathgiri2014@gmail.com
Mason trainings in rural municipalities have been planned by NRA Lalitpur.	Date and location has still not been finalized	NRA Lalitpur nralalitpur@gmail.com
To include details of upcoming events and meetings in the next bulletin, please share details with dc.ktm@hrrpnepal.org by COB Wednesday of each week.		

News & Updates

Reconstruction update of Bhaktapur district: As of 27 December 2017

S.no	Municipality	Total identified Beneficiary	Additional beneficiary after Grievance	Total Beneficiary	Grant Agreement	Received 1st tranche	Received 2nd tranche	Received 3rd tranche	In process for 2nd tranche	In process for 3rd tranche
1	Bhaktapur	6888	597	7485	5213	5200	451	3	92	36
2	Changunarayan	10203	444	10647	8894	8794	525	254	62	52
3	Madhyapur Thimi	2254	46	2300	1910	1837	145	33	0	0
4	Suryabinayak	6721	491	7212	6519	6400	476	131	0	0
Total		26066	1578	27644	22536	22231	1597	421	154	88

Field Visit Reports


Date	Location	Participants
22 December 2017	Ward no. 1, Okhrene village, Sundarijal, Gokarneshwor Municipality	- Er. Narakanta Sapkota, M and E Consultant, CLPIU -MoUD - Ambika Amatya, District Coordinator, Kathmandu Valley, HRRP Nepal - Er. Kusum Deo, Er. Sumi Deo and Er. Sudha Shrestha, Gokarneshwor Municipality
Objective(s)	- To inspect the houses that are in reconstruction phase. - To provide technical feedbacks to the beneficiaries for earthquake resistant construction	

Summary	A visit to Okhreni village, Sundarijal, Gokarneshwor Municipality, Ward No. 1 was conducted on 22 December 2017 along with Monitoring and Evaluation Consultant, DLPIU-MoUD, Kathmandu and with DLPIU deployed engineers of the municipality. In total three engineers have been deployed to the municipality by DLPIU, Kathmandu. Gokarneshwor Municipality has been providing technical assistance and grant support in these areas.		
	The Chairperson of Ward no. 1 office revealed that in Okhreni village many people were confused that getting building permit requires paying money. However through regular presence of technicians from Gokarneshwor municipality office as well as community orientation highlighting the fact that no charge shall be paid for the building permit in Gokarneshwor municipality for the earthquake process of reconstruction in the area has been in rapid progress. In this case, ward office is only taking nominal charge for measurement of land only.		
	The reconstruction process of 11 houses were monitored and inspected by the team; the technical inputs were provided by M & E Consultant along with engineers from Gokarneshwor Municipality. Beneficiaries that have met with standard norms in reconstructing their houses were advised to proceed for 2nd tranche. Whereas, beneficiaries were suggested to build the house as per the building drawing approved by the municipality and follow the GoN standard for the earthquake resistant construction to receive the GoN grant.		
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Though majority of households have received 1 st tranche, reconstruction process is slow.	Community orientation and awareness program must be conducted in the area to encourage beneficiaries for reconstruction. Engineers and social mobilizers should also notify the timeframe set by the NRA for those who have already received the 1 st tranche.	Ward No. 1 Office, Sundarijal, Gokarneshwor Municipality	
Many beneficiaries still don't have the land ownership papers.	Ward office should visit beneficiaries in order to bring clarity in accessing the land ownership papers as per GoN guidelines for earthquake affected people.	Ward No. 1 Office, Sundarijal, Gokarneshwor Municipality	
Some beneficiaries have not followed the technical standard which has increased the non-compliance cases in the area	DLPIU engineers should put more effort in on-site monitoring and awareness programs.	DLPIU Engineers, Gokarneshwor Municipality	

Photos



RC structure, Plinth level completed and proceeding for RCC casting, ward no. 1, Okhrenei, Sundarijal, Gokarneshwor Municipality. Beneficiary has received 1st tranche.

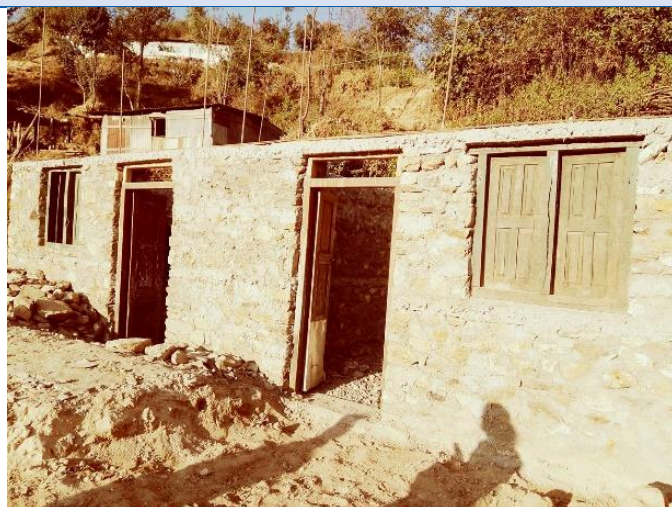


Load bearing structure with Stone in cement, ward no. 1, Okhrenei village, Sundarijal, Gokarneshwor Municipality, Inspection conducted for 2nd tranche.

Housing Typology Report



Ward no 1, Gokarneshwor Municipality, Kathmandu district, RC structure in stone cement mortar. Beneficiary has received 1st tranche.

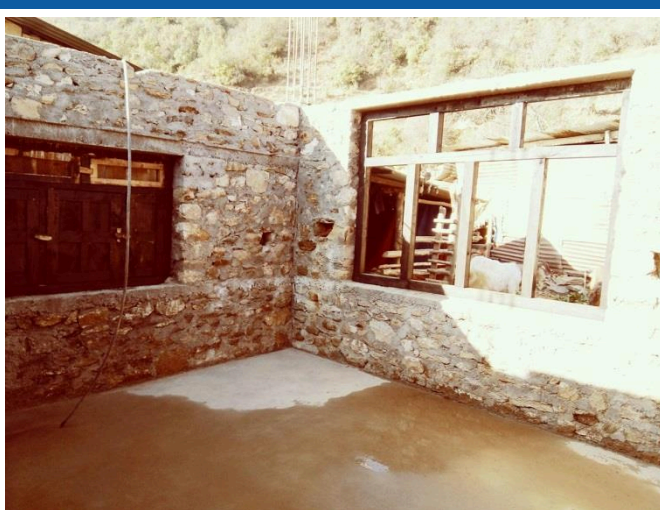

Ward no 1, Gokarneshwor Municipality, Kathmandu district, Load bearing structure in stone cement mortar. Beneficiary has received 1st tranche.



Ward no 1, Gokarneshwor Municipality, Kathmandu district, Hybrid structure with stone in cement mortar and CGI sheet. Beneficiary has received 1st tranche but will not be eligible for the 2nd tranche.



Ward no 1, Gokarneshwor Municipality, Kathmandu district, RC structure with brick infill. Beneficiary has received 1st tranche. The process for 2nd tranche has not been conducted due to multiple beneficiaries.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
The house has flexible roof as per the building design. Can I change to RC roofing?	Beneficiary	Through amendment in building drawing from the concerned municipality office, RC roofing can be done. (M&E consultant, Kathmandu)
I have received 1 st tranche and managed to make house but it is considered temporary house from engineers as it surrounded by CGI sheet. How can I receive 2 nd tranche and make the house permanent?	Beneficiary	The CGI sheets attached 2 feet above from plinth level should be removed and should be made as per the GoN standard (example-stone with cement mortar) to proceed with tranche process. (M&E consultant, Kathmandu)
My house is load bearing structure with stone in cement mortar. As per the building design the house has 1 door and 2 windows, but I want to add 1 more door. Is it possible?	Beneficiary	The construction is aligned with the design, but to add the extra door; building design should be amended at the earliest. Later construction should meet the conditions and structure should be earthquake resilient. Beneficiary should be aware that whatever is in the design should be replicated in the field. (M&E consultant, Kathmandu)

Challenges and Way Forward

Challenge	Way Forward
Even though there are trained mason, the reconstructed houses are not technically sound.	Site monitoring and inspection of the reconstructed building should be made by the technical person and knowledge evaluation of the mason after the training must be conducted on regular basis.
Though beneficiaries have received 1 st tranche, reconstruction process has delayed.	As reconstitution process is based on owner driven approach, Community orientation and door to door technical assistance must be conducted to encourage beneficiary to build earthquake resistance houses within

Challenges and Way Forward

Challenge	Way Forward
	the time frame set by NRA.
Building permit has been provided for the reconstruction of the masonry structure up to 3.5 storey which will not be eligible for the grant as per GoN grant criteria.	The process for the tranche releases must be conducted only after the structural analysis of such buildings.
NRA has approved for the reconstruction of the houses in guthi land but the revenue of the land has not been paid for years which sums up to more than the grant that will receive from the GoN. This has discouraged the beneficiary to start the reconstruction.	A central level meeting with the municipalities, NRA official needs to conducted to address such issues.
