

District Report

Kathmandu Valley

23 Nov – 6 Dec 2018

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
HRRP Kathmandu valley team with a monitoring team from DLPIU Building Kathmandu conducted monitoring field visit at Ward no. 8, Bhimdhunga, Nagarjun Municipality, Kathmandu district	22 Nov. 2018	3	2	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org Contact: 9861796464	
HRRP Kathmandu valley team with a monitoring team from DLPIU Building Bhaktapur conducted monitoring field visit at Ward no. 3 & 6 Jhaukhel & Nagarkot areas of Changuarayan Municipality, Bhaktapur district	27 Nov. 2018	2	4	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
General Coordination Meeting of DLPIU NRA GMaLI and DLPIU Building was organized on 3rd December 2018 at GMaLI Bhaktapur Office. The purpose of meeting was: i) To share the reconstruction updates from the municipalities. ii) To discuss on the issues of reconstruction of each municipality, iii) To strengthen the linkages between municipalities and DLPIU deployed engineers. Key highlights of the coordination meeting are as follows- • Engineers were requested to inform immediately to DLPIU Building and GMaLI Bhaktapur office about relevant environment, social, health, administration and technical factors of reconstruction that is affecting reconstruction. • Engineers deployed at municipalities should properly inform beneficiaries about types of correction measures to apply for correcting their houses. • Engineers were requested to explore about rotational shifting of their	3 Dec. 2018	16	23	Mr. Durba Gaida GMaLI Chief, Bhaktapur Contact: 9851221570	

Summary of events during this period

working wards to enrich the details about reconstruction efforts taking place in each ward. - In current times, municipalities are receiving less number of applications from reconstruction. - Third inspection revealed that majority of beneficiaries still don't have building permit of their houses.					
Upload of training database and relevant other information has been updated in 5W.	23 Nov. - 6 Dec. 2018			Ms. Manisha Rai IM Officer HRRP Kathmandu Valley im.ktm@hrrpnepal.org Contact: 9842062006	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Joint M & E visit to observe reconstruction efforts of beneficiaries in districts of Kathmandu Valley	Date- 1 st week of Dec. – 3 rd week of Dec. 2018	HRRP Kathmandu valley team	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org
District level Reconstruction Review Meeting of DLPIU GMaLI Lalitpur	9 -10 December 2018, 9 AM onwards Venue- Godawari Village Resort, Taukhel	NRA/CLPIU GMaLI	Mr. Bir Bahadur Rawal Chief, DLPIU GMaLI Lalitpur Contact: 9851201088 nralalitpur@gmail.com
District level Reconstruction Review Meeting of DLPIU GMaLI Bhaktapur	11-12 December 2018, 9 AM onwards Venue- Sweet Home Events, Bhaktapur	NRA/CLPIU GMaLI	Mr. Dhruva Gaida Chief, DLPIU GMaLI Bhaktapur Contact: 9851221570 dgaida022@gmail.com
District level Reconstruction Review Meeting of DLPIU GMaLI Kathmandu	18-19 December 2018, 9 AM onwards Venue- TBD	NRA/CLPIU GMaLI	Er. Samar Bahadur Khanal Chief, DLPIU GMaLI Kathmandu Contact: 9851209362 samar.khanal@gmail.com
Field visit monitoring of working sites of NSET	13 December 2018, 10.30 AM onwards, Ward no 1, 2, 3 of Kageshwori Manahara Municipality	DLPIU NRA GMaLI Kathmandu	Mr. Achyut Shrestha Section officer DLPIU NRA GMaLI Kathmandu Contact: 9860784954 achyutshrestha121@gmail.com

News & Updates

- Ms. Mahalaxmi Joshi has been given the responsibility of Chief, DLPIU Building Bhaktapur along with of DLPIU Building Kavre too. Contact no- 9751090249
- Mr. Chandra Kaji Guring has been given the responsibility of Chief, DLPIU Building Kathmandu along with of DLPIU Building Lalitpur too. Contact no-9841576783
- Mr. Bir Bahadur Rawal has been appointed as Chief, DLPIU NRA GMaLI Lalitpur. Contact no-9851201088

Tranche Status

Tranche status of Kathmandu district

Rural /Municipality	Budanilkantha	Chandragiri	Dakshinkali	Gokarneshwor	Kageshwori-Manahara	Kathmandu MC	Kritipur	Nagarjun	Shankharapur	Tarakeshwor	Tokha
Total HHs Surveyed	2693	5785	4091	2977	3667	7514	2941	4362	6064	6193	1752
Total HHs Eligible	2693	5785	4091	2977	3667	7514	2941	4362	6064	6193	1752
Total HHs Enrolled	2054	4707	3760	2491	3239	5953	2475	4103	5509	5124	1549
First Tranche	2054	4661	3731	2484	3228	5928	2459	4099	5470	5093	1530
Second Tranche	906	1055	1178	1202	1573	1308	860	1254	2024	1596	595
Third Tranche	623	911	669	922	779	995	684	971	1248	1289	403
Total HH Constructed											
Grievance Registered											
Grievance Addressed											
RF HH Eligible											
RF HH Enrolled	0	46	29	7	4	25	16	4	39	31	19
RF 1 st Tranche	0	46	29	7	4	25	16	4	39	31	19
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	0	0
NC Registered											
NC Addressed											


Tranche status of Lalitpur district

Rural /Municipality	Mahankal RM	Konjyosom RM	Bagmati RM	Godawari UM	Mahalaxmi UM	Lalitpur MC
Total HHs Surveyed	2267	2154	3370	9588	3657	7346
Total HHs Eligible	2267	2154	3370	9588	3657	7346
Total HHs Enrolled	2218	2042	3018	7873	2967	6293
First Tranche	2218	2034	3006	7790	2928	6267
Second Tranche	1589	1628	2219	2084	721	1093
Third Tranche	837	1104	1465	1521	570	633
Total HH Constructed						
Grievance Registered	331	611	776	2011	890	2759
Grievance Addressed	296	514	713	1777	822	2296
RF HH Eligible	61	372	252	325	90	281
RF HH Enrolled	42	231	8	61	2	119
RF 1 st Tranche	42	220	7	60	2	115
RF 2 nd Tranche						
Non-Compliance Registered						
Non-Compliance Addressed						


Tranche status of Bhaktapur district

Rural /Municipality	Bhaktapur	Changunarayan	Madhyapur Thimi	Suryabinayak
Total HHs Surveyed	7622	10937	2333	7416
Total HHs Eligible	7622	10937	2333	7416
Total HHs Enrolled	5568	9610	2040	6927
First Tranche	5552	9595	2030	6910
Second Tranche	1434	2533	568	2004
Third Tranche	1194	2332	528	1841
Total HH Constructed	1617	2737	664	2379
Grievance Registered	1592	2096	2407	1926
Grievance Addressed	1542	1696	1431	1661
RF HH Eligible	148	212	101	233
RF HH Enrolled	36	78	56	86
RF 1 st Tranche	29	75	44	59
RF 2 nd Tranche	0	0	0	0
Non-Compliance Registered				
Non-Compliance Addressed				


Graph of Tranche Status: Kathmandu District as of 6 December 2018

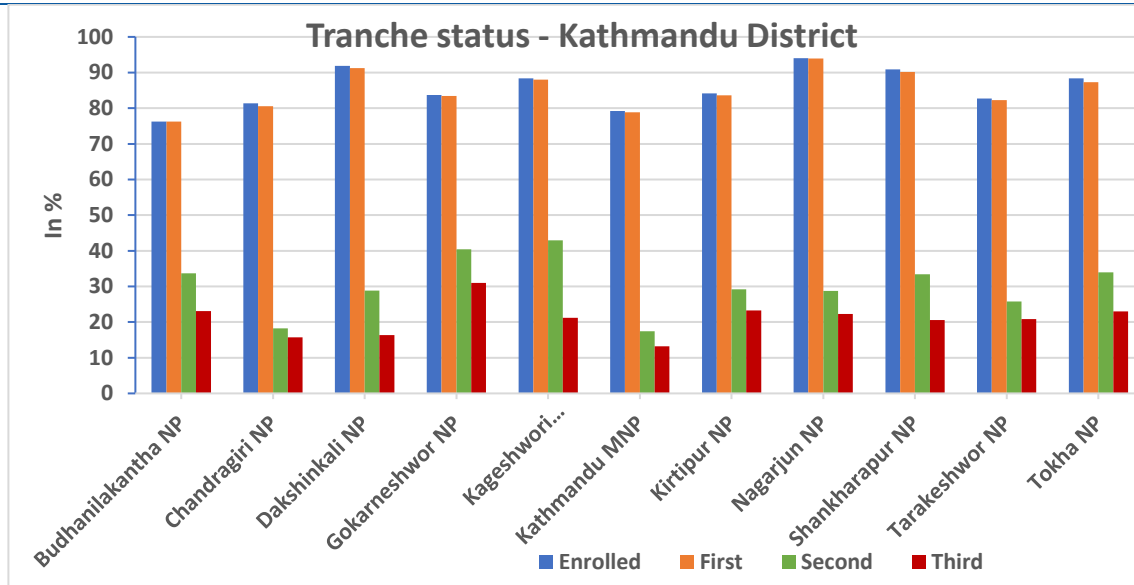


Graph of Tranche status: Bhaktapur District as 6 December 2018

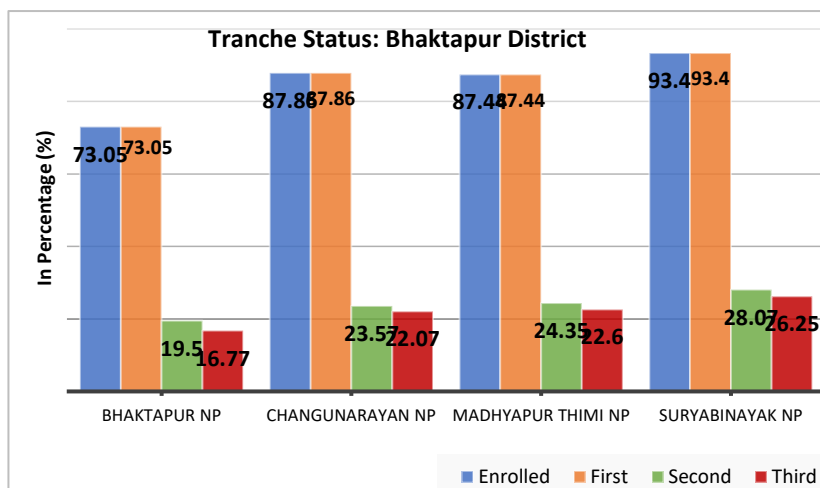

Graph of Tranche Status: Lalitpur District as of 6 December 2018

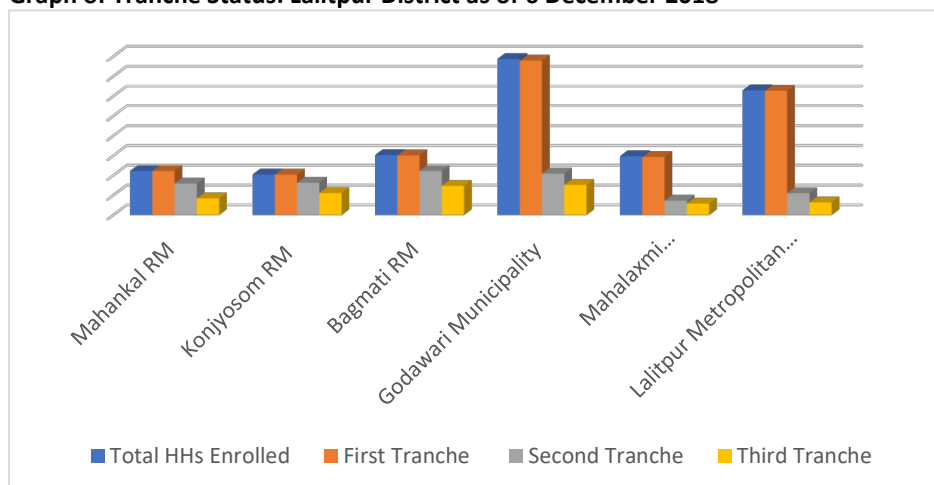


Graph for Retrofitting Status: Bhaktapur district

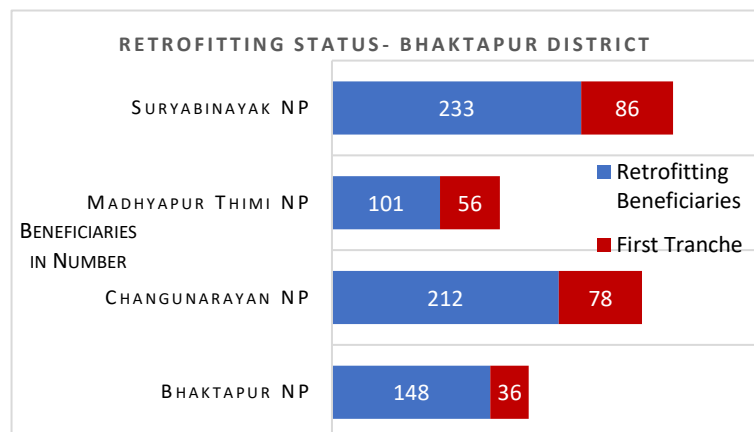


Graph for retrofitting status: Kathmandu district

Graph for Grievance Status: Bhaktapur District

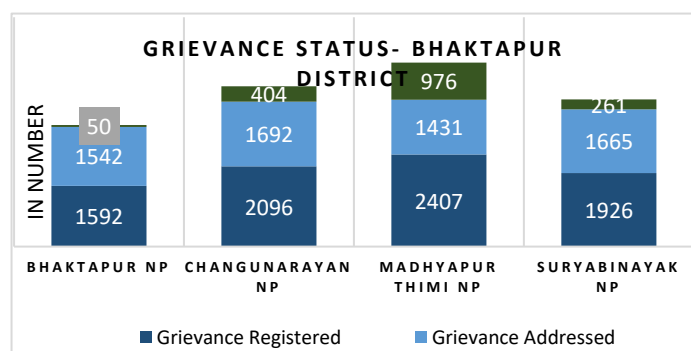

Graph for Grievances Status: Lalitpur district

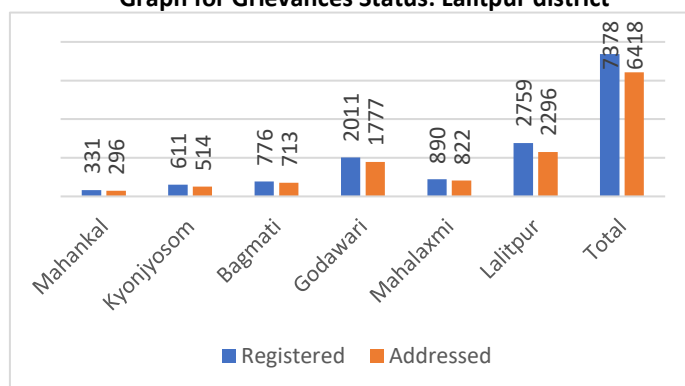

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
22 November 2018	Ward no 8, Nagarjun Municipality, Kathmandu district	- Narakanta Sapkota, M & E Consultant/ DLPIU NRA-Building - Sweata Sijapati, District Technical Coordinator, HRRP Kathmandu Valley Team - Shristi Gautam, Engineers, DLPIU Building, Nagarjun Municipality - Yogendra Kunwar, Engineers, DLPIU Building, Nagarjun Municipality - Pramod Acharya, Engineers, DLPIU Building, Nagarjun Municipality
Objective(s)	- To interact with local representatives along with engineers of municipality regarding the reconstruction issues and ways forward. - To observe the reconstruction status of the beneficiaries. - To provide inputs to the beneficiaries in regarding the technical assistance, government deadlines of housing reconstruction and grant access process.	

Summary	HRRP Kathmandu valley team along M & E Consultant from DLPIU NRA Building conducted joint field monitoring at Ward no 8, Nagarjun Municipality, Kathmandu district. <u>Interaction with the Mayor of Nagarjun Municipality:</u> The monitoring visit began with the brief meeting with the Mayor Mr. Mohan Bahadur Basnet, Nagarjun Municipality. He highlighted that the reconstruction process was slower in the Municipality due to various issues such as insufficient technical staffs, lack of public awareness but after those issues were solved reconstruction has taken a rapid speed. In Nagarjun Municipality lots of houses (about 40%) were constructed immediately before any government guidelines on the reconstruction and technical specification. Thus, most of such houses are non-compliance and applying the correction measures are difficult and financially not feasible for the beneficiaries. So, Mr. Basnet requested If NRA could address such cases then the reconstruction issues of the municipality would be solved to greater extend. He insured that the municipality will support the technical staffs to coordinate with the ward representative as well as beneficiaries to increase the reconstruction rate and solve the issues which has been delaying the progress.
-----------------------	--

Challenges / Issues Identified	Action Required	Responsible	Timeframe
Most of the house build before the government guidelines and technical specification are non-compliance. Almost 40 % of the constructed houses have missing roof bands.	Engineer deployed in the municipal must suggested the correction measure for such non-compliance construction to be eligible for the grant.	DLPIU Engineers, Municipality office	As soon as possible
The land of beneficiaries along the road extension plan are unbale to construct their house due to small land parcel after complying with the municipality bylaws and development plan.	NRA should coordinate with Municipality to address such issue and find the possible way forward.	Municipality, NRA, District- GMaLI	As soon as possible

Photos



Beneficiary Name: Mangal Tamang, ward no 8, Pakhure, Nagarjun Municipality. Two storey RC structure. The beneficiary has received all tranche and has been living in the newly constructed house.



Beneficiary Name: Bhagwati Tamang, ward no 8, Pakhure, Nagarjun Municipality. The beneficiary has received 2nd tranche but due to financial condition has not been able to

		continue the reconstruction. Ms. Tamang is Interested in getting the soft loan if possible.
Visit 2		
Date	Location	Participants from HRRP and stakeholders
27 November 2018	Ward no 3 & 6, Jhaukhel and Phedi (Nagarkot area), Changunarayan Municipality, Bhaktapur district	- Ambika Amatya, District Coordinator, HRRP Kathmandu Valley - Narakanta Sapkota (M & E Consultant, DLPIU Building, Kathmandu) - Prabesh Adhikari, DSE, DLPIU Building Bhaktapur - Engineers, DLPIU Building, Bhaktapur (Bibha Sainju, Radha Sandh) - Archana Shrestha, DLPIU Engineer, Changunarayan Municipality
Objective(s)	- To interact with local representatives along with engineers of municipality regarding the reconstruction issues and ways forward. - To observe the reconstruction status of the beneficiaries in landslide prone areas. - To provide suggestions to beneficiaries in line with reconstruction of their houses.	
Summary	HRRP Kathmandu valley team along M & E Consultant from DLPIU NRA Building conducted joint field monitoring at various places of Ward no. 3 and Ward no. 6, Jhaukhel & Phedi areas respectively of Changunarayan Municipality, Bhaktapur district. The focus of the visit was to observe the houses that were reconstructed in landslide prone areas. All the houses have applied for 2nd and 3rd tranche together. Beneficiaries were recommended to construct shear wall and proper outlet system for water leaked from the landslide prone walls. The joint monitoring team observed 8 houses in the reconstruction phase in aforementioned areas. <u>Details of some houses-</u> - The 1 storey house of Meghnath Ghimire, Ward no. 3, Jhaukhel is RCC BMC. It has 14" wall outside and 9" wall inside. The owner has approved building drawing and applied for 2nd and 3rd together. During the time of applying tranche, the house was found to have cracks on interiors parts. - Located at Ward no. 6, Phedi Telkot, the house belongs to Nawaraj Lamichhane is 2.5 storey with rigid and flexible roof. The owner has approved building drawing and applied for 2nd and 3rd together. - Located at Bastola Gaun, Ward no. 6, Nagarkot, the house belongs to Rajkumar Bastola is 2 storey and RCC frame structure. The house lies in extremely landslide prone area and is left with .5 storey to reconstruct. The DPC level of house is done in different parts of plot due to very slope area. The owner has approved building drawing and applied for 2nd and 3rd together. - The house of Niran Nepali, Ward no. 6, Pipalbot, Nagarkot area is reconstructed with hollow concrete blocks, single storey and wall system with flexible roof. The beneficiary revealed that tie beam and bands has been properly kept. The owner has approved building drawing and applied for 2nd and 3rd together.	

	- The house of Kanchi Maya Tamang located at Ward no. 6, Bakhri Gaun, Nagarkot is RCC pillar system with rigid roof, 1 storey and single bay. The owner has approved building drawing and applied for 2nd and 3rd together. The house is located very close to road and in landslide prone area. - The house of Putali Tamang located at Ward no. 6, BakhriGaun, Nagarkot is single storey and made from interlocking bricks with flexible roof. DPC works has been properly done. The owner has approved building drawing and applied for 2nd and 3rd together.
--	---

Challenges / Issues Identified	Action Required	Responsible	Timeframe
Beneficiaries have reconstructed houses in landslide prone areas without taking sufficient precautions.	Beneficiaries need to take care of proper precautions such as construction of retention wall and water drainage system (water inlet and outlet) along with the wall of the houses. Further, placement of sand sacks should be done on premises part in order to check the soil erosion.	Beneficiaries, Ward Office, Municipality office DLPIU Engineers	As soon as possible

Photos



Beneficiary name: Rajkumar Bastola, Bastola Gaun, Ward no. 6, Nagarkot, 2 storey and RCC frame structure. The house lies in extremely landslide prone area and is left with .5 storey to reconstruct. The DPC level of house is done in different parts of plot due to very slope area. The owner has approved building drawing and applied for 2nd and 3rd together.



Beneficiary Name: Meghnath Ghimire, Ward no. 3, Jhaukhel, RCC BMC with single storey. House has 14-inch wall outside and 9-inch wall inside. The owner has approved building drawing and applied for 2nd and 3rd together. During the time of applying tranche, the house was found to have cracks on interiors parts.



Beneficiary name: Kanchi Maya Tamang, located at Ward no. 6, Bakhri Gaun, Nagarkot is RCC pillar system with rigid roof, 1 storey and single bay. The owner has approved building drawing and applied for 2nd and 3rd together. The house is located very close to road and in landslide prone area.



Beneficiary name: Niran Nepali, Ward no. 6, Pipalbot, Nagarkot area is reconstructed with hollow concrete blocks, single storey and wall system with flexible roof. The beneficiary revealed that tie beam and bands has been properly kept. The owner has approved building drawing and applied for 2nd and 3rd together.

Field Visit Report



Beneficiary Name: Ms. Pramila Budathoki, Ward no 14, Lalitpur Metropolitan city, Lalitpur district. Two storey RC structure. The beneficiary has requested for the 2nd and 3rd tranche. Dated: 180830



Beneficiary Name: Mr. Balram Sunwar, Bhardeu, Ward no. 5, Konjyosom Rural Municipality, Lalitpur district. One storey structure with CGI roof. The beneficiary has requested for the 2nd and 3rd tranche. Dated: 180603

Visit 3

Date	Location	Participants from HRRP and stakeholders
5 December 2018	Ward no 10, Suryabinayak Municipality, Bhaktapur district	- Narakanta Sapkota, M & E Consultant/ DLPIU NRA-Building - Sweata Sijapati, District Technical Coordinator, HRRP Kathmandu Valley Team - Prabesh Adhikari, DSE, DLPIU Building Bhaktapur - Suraj Shrestha, Engineers, DLPIU Building, Bhaktapur District - Asmita Shrestha, DLPIU Building, Bhaktapur District - Pramita Nepaune, Engineers, DLPIU Building, Suryabinayak Municipality - Jeena Suwal, Engineers, DLPIU Building, Suryabinayak Municipality

Objective(s)	- To interact with local representatives along with engineers of municipality regarding the reconstruction issues and ways forward. - To observe the reconstruction status of the beneficiaries. - To provide inputs to the beneficiaries in regarding the technical assistance, government deadlines of housing reconstruction and grant access process.
---------------------	---

Summary	HRRP Kathmandu valley team along M & E Consultant from DLPIU NRA Building conducted joint field monitoring at Ward no 10, Suryabinayak Municipality, Bhaktapur district. The field visit was mainly focused on the observation of the Non-compliance cases in the ward. The visit was accompanied by the DSE who gave suggestion to the beneficiaries for being eligible for the tranche. In total 11 houses were visited among which only few were able to be suggested for the correction measures. During the visit small community orientation was conducted in Khadka Gaun, where
----------------	--

Field Visit Report



Beneficiary Name: Ms. Pramila Budathoki, Ward no 14, Lalitpur Metropolitan city, Lalitpur district. Two storey RC structure. The beneficiary has requested for the 2nd and 3rd tranche. Dated: 180830



Beneficiary Name: Mr. Balram Sunwar, Bhardeu, Ward no. 5, Konjyosom Rural Municipality, Lalitpur district. One storey structure with CGI roof. The beneficiary has requested for the 2nd and 3rd tranche. Dated: 180603

beneficiaries has still many not began reconstruction due to less knowledge on the government grant process and the technical specification needed to be followed. Due to the issues of Ghuti land and low economic status the reconstruction was delayed. The beneficiaries were told about the government deadlines and the type design published by NRA/MOUD. Also, they were suggested to be in regular contact with the engineers from the DLPIU building throughout the building process beginning from the building drawing.

Interaction with the Engineers of Suryabinayak Municipality:

The monitoring visit began with the brief meeting with the technical staffs of Suryabinayak Municipality. M&E consultant basically focused on delay of the CS entry in the Municipality. The technical staffs were strictly asked to complete the CS entry of the inspected houses. As the deadline for the second tranche is approaching, technical staffs were told to conduct the inspection of the houses even though the inspection request has not been submitted.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
Most of the house build before the government guidelines and technical specification are non-compliance. Almost 40 % of the constructed houses have missing roof bands.	Engineer deployed in the municipal must suggested the correction measure for such non-compliance construction to be eligible for the grant.	DLPIU Engineers, Municipality office	As soon as possible
Most of the houses designed by the Municipal engineer are mixed typology- i.e BMC structure with RCC pillar at only back section. Such houses are non-compliance and	DLPIU Building engineers/ DLPIU Kathmandu should coordinate with the municipal engineers and demoralize such houses design.	NRA building, DLPIU engineers, Municipal Engineers	As soon as possible

Field Visit Report



Beneficiary Name: Ms. Pramila Budathoki, Ward no 14, Lalitpur Metropolitan city, Lalitpur district. Two storey RC structure. The beneficiary has requested for the 2nd and 3rd tranche. Dated: 180830

engineers have not been able to forward such cases.



Beneficiary Name: Mr. Balram Sunwar, Bhardeu, Ward no. 5, Konjyosom Rural Municipality, Lalitpur district. One storey structure with CGI roof. The beneficiary has requested for the 2nd and 3rd tranche. Dated: 180603

Photos



Beneficiary Name: Tek Bahadur Ale Magar, ward no 10, Puwar Gaun Suryabinayak Municipality. Two storey BMC structure at front and 4 12"X12" pillar at rear side. The beneficiary requested for the 2nd and 3rd tranche but as the structure is non-compliance the file has been on hold. To resolve the issue, the municipal engineer who designed the structure has been requested to meet



Beneficiary Name: Ajay Khadka, ward no 10, Khadka Gaun, Suryabinayak Municipality. 1 storey BMC structure with 14" wall and a rolling shutter. The beneficiary has requested for the 2nd and 3rd tranche. Due to the rolling shutter, the house was considered as non-compliance but after the monitoring visit the structure was found to be safe and eligible for the remaining tranche

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
There was an article in newspaper claiming that all the beneficiary irrespective of the housing typology will be getting full tranche. Is that true?	Beneficiary	To be eligible for the full government tranche the house should constructed within the government guideline and technical specification. (M&E consultant)
It's been more than 3- 4 months that I have requested for the 2nd tranche but have not received it. Why is it so?	Beneficiary	The files have already been forwarded to GMaLI. The status of the tranche will be checked at GMaLI and will be informed accordingly (DLPIU engineer, Nagarjun Municipality)
What are the further measures to be taken to safeguard the houses from unwanted landslide or soil erosion?	Beneficiary	Shear wall along or retention wall should be constructed by consulting with trained masons or engineers that helps in preventing soil erosion. After few years (3-4 years), the retention wall will be strengthened more that safeguards the property from soil erosion. (M&E consultant)

Challenges and Way Forward

Challenge	Way Forward
The houses that were reconstructed in landslide prone areas were found to have taken inadequate precaution to safeguard the property from seasonal soil erosion.	Beneficiaries need to be sensitized about effects of soil erosion and the precautions to be taken while constructing houses in such areas. Concerned DLPIU offices should take proactive steps in such kind of sensitization programs.
