

District Report

Dolakha

23 November - 6 December 2018

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
NRA CEO Mr. Sushil Gyewali interacted with reconstruction stakeholders in Dolakha: NRA CEO Mr. Sushil Gyewali interacted with the reconstruction stakeholders in Dolakha. In the programme, left genuine beneficiaries, multi-ownership. Significantly, CEO Mr. Gyewali committed the problems Dolakha faced to complete reconstruction in time. The programme was attended by Palika officials, GMaLI, DLPIU (Education/Building, CDO, Development Partners, journalists. HRRP Dolakha DCT team coordinated POs interaction with CEO. Further, Mr. Gyewali visited Singati, Bigu Gaunpalika where the first agreement with earthquake beneficiary (Mr. Jagat B Khatri, 78) started after the earthquake by him.	3 December	M: 36	F: 11	Rita Lamsal, Information Officer, GMaLI Dolakha Cell: 9846075504 Email: ritalamsal@gmail.com	

News & Updates


<http://rajdhanidaily.com/136406/>

First beneficiary told, " *Pahilo Labhgrahi bhanchhan, Gharle khoseko khusi gharaile pharkayo* (Taken back happiness by house returned by house) Dec 4, 2018; Rajdhani National Daily By Dhruva Lamsal


Tranche Status

Rural /Municipality	Baiteshwor	Bhimeshwor	Bigu	Gaurishankar	Jiri	Kalinchowk	Melung	Sailung	Tamakoshi
Total HHs Surveyed	8550	13693	6799	6656	5991	9062	8067	8524	7537
Total HHs Eligible	8308	12394	6699	6762	5805	8866	7474	8110	7428
Total HHs Enrolled	7563	11810	6186	5576	4948	8060	6337	6762	6245
First Tranche	7649	10285	5879	5587	4754	8184	6325	6437	6429
Second Tranche	6435	7411	5007	5028	3447	7088	5349	5034	5671
Third Tranche	5742	5305	4355	4733	2618	6549	4313	3714	4879
Total HH Constructed	5763	5329	4384	4751	2632	6572	4327	3727	4891
Grievance Registered	248	546	132	123	222	378	1191	226	84
Grievance Addressed	1795	2235	719	760	961	1238	1100	1257	828
RF HH Eligible	339	348	34	74	153	32	402	746	110
RF HH Enrolled		50	2						
RF 1 st Tranche		50	2						
RF 2 nd Tranche		0	0						
Non-Compliance Registered	1799 (9 Palikas in total)								
Non-Compliance Addressed	1234 (9 Palikas in total)								


Graph of Tranche Status:

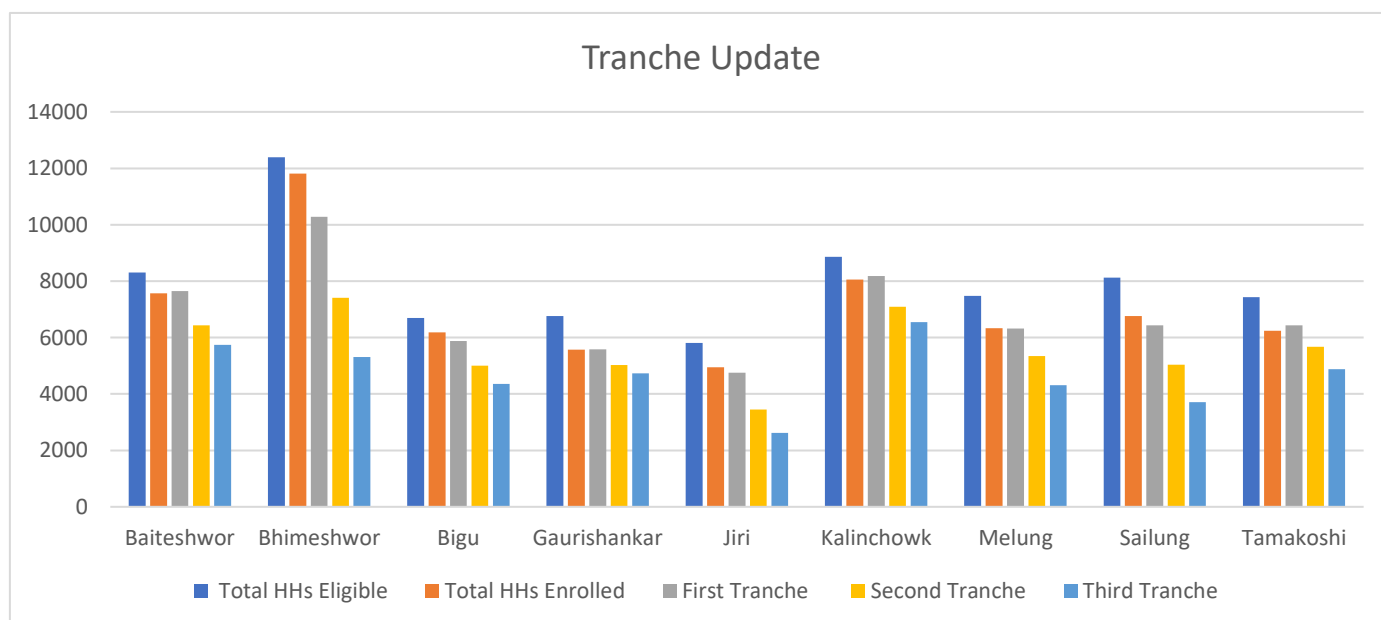

Graph for Retrofitting Status:

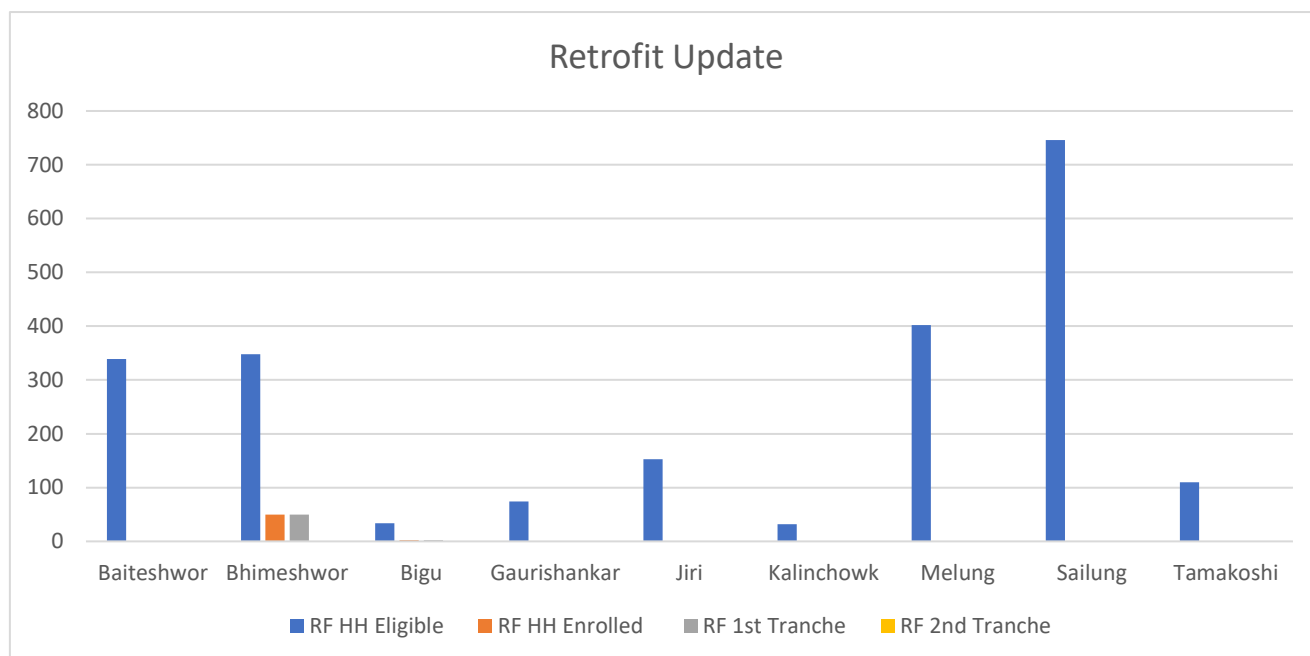


Graph for Grievance Status:

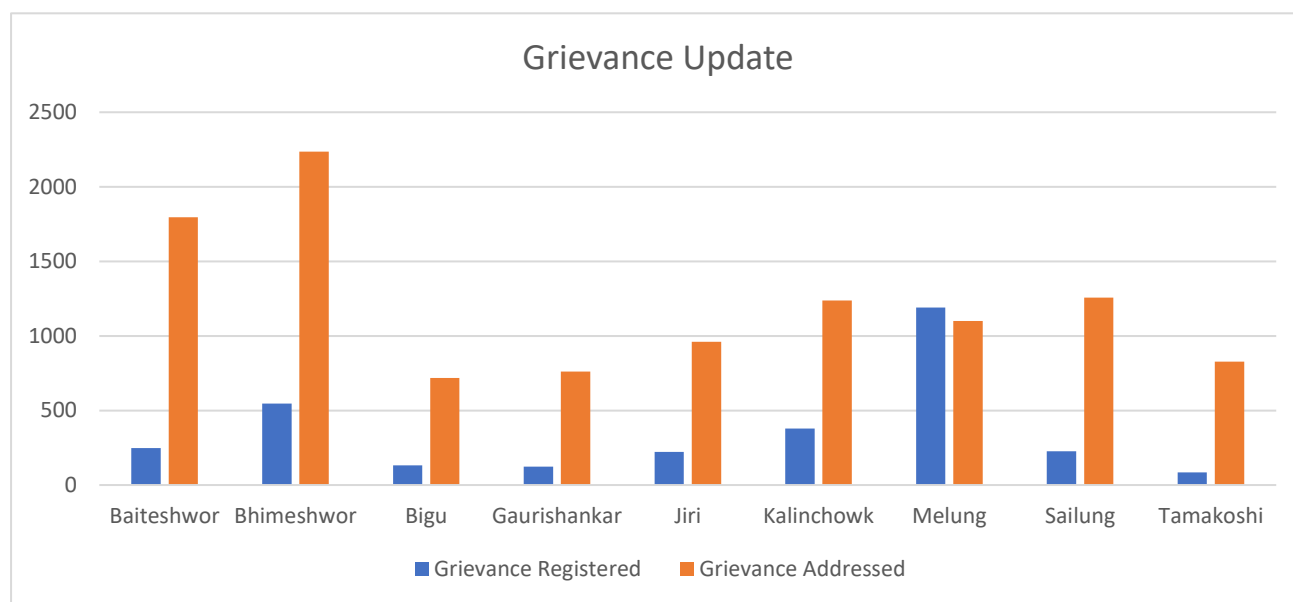

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
28 th -29 th Nov 2018	Sailung Gaunpalika-3, Baghkhori and Sailung-08, Jhor	- Binod Kumar Kalauni - Kamal B Mahat - Bhogendra Kr Sah (DLPIU/Focal Person) - Hisila Maharjan, Mohan Pokhrel, DSE - Rukmita Gautam, Sub-Engineer, DLPIU(Building) - Krishna Chandra Yadav, DLPIU(Building) - Niroj Maharjan, Unicef
Objective(s)	- To conduct Palika Level Meeting - To Collect Housing Typologies - To discuss with technicians - To collect case stories	
Summary	Ward level meeting was concluded on 28th Nov 2018 at Sailung-3, Baghkhori. In the meeting, reconstruction related issues were discussed. The meeting also joined by Engineers Mr. Laxman Khatri and Mr. Dundu BK from NSET who have been working there. Mr. Bikash Khatri, Engineer informed that nearly 400 houses yet to be constructed; further, he informed that second tranche 800 and third tranche 518 houses in that ward. In rainy season, construction materials transportation was difficult but now the problem is sorted out. Their main personal concern is allowance to boost the morale. As for shortage of money, some houses may be delayed in reconstruction according to them. Further, they informed us that Rural Enterprise Development Center(REDC) from the support of UNDP has been constructing 66 vulnerable groups houses. Similarly, in Sailung Gaunpalika, Ward-8, we met with reconstruction stakeholders. The ward secretary Ms. Durga Neupane told that the beneficiaries have been facing problem from bank on minor mistake. According to her, initially, the Citizen bank who has branch in Bhaishain distributed tranches from there in their doorstep but later the bank stopped to distribute tranches from there and they have been going Charikot, district headquarter which is costly, time consuming and even most difficult to senior citizen, persons with disability. Further, they have been facing problem by retrofitting beneficiaries. Mrs. Nil Kumari Basnet and Lila Kumari Basnet who attended the meeting told that retrofitting is not possible in their houses (interestingly, the largest numbers of retrofitting beneficiaries (746 houses) enlisted in Sailung Gaunpalika among 9 Palikas in Dolakha district). In that ward, more than 200 households enlisted as retrofitting beneficiaries. From last 4 months, they have been facing absenteeism of technicians in the ward which has been hurdling to speed up the reconstruction process. Another problem they have been facing is soaring prices of construction materials viz. sand Rs 13,000, Cement Rs. 1200(OPC), Aggregate Rs. 2,000. In that ward, more than 196 genuine victims left to be enlisted as earthquake beneficiaries. Further, one squatter person is there in the ward who can't construct house himself. Moreover, they have been facing water problem there. The skilled manpower paid Rs, 1200 per day and unskilled Rs 500-700 per day including meal and snacks.	



Photos



Ward Level Meeting at Ward Office Sailung-3, Baghkhori Pic: Krishna Yadav



Ward Level Meeting at Ward Office Sailung-8, Bhaisain Pic: Krishna Yadav

Housing Typology Report



SMM Building has been constructed using RCC bands in Sailung Gaunpalika-08, Jhor. Mr. Narayan Shrestha is the house owner and he has received third tranche.
Pic: Binod Kalauni



RCC Building under construction in Sailung Gaunpalika-08, Jhor. Mr. Heera Lal Shrestha house owner and he has received first tranche. During the inspection we found insufficient encourage between reinforcements and widely spaced stirrups. DSE suggested necessary corrections and informed about the critical things where especial attention required.
Pic: Binod Kalauni



SMM building with Rcc bands have been constructed in Jhor, Sailung RM -08. Mrs Krishan Kumari Shrestha has received all three tranches of housing reconstruction grant.
Pic: Binod Kumar Kalauni



SMM building under construction in Jhor, 08- ward of Sailung RM. Trained manpower has been employed by the house owner. Mr. Tara Bdr Shrestha is the house owner and he has received second tranche.
Pic: Binod Kumar Kalauni



SMM building with Rcc bands has been constructed in Mangaun, 08-ward of Sailung RM. Mr Ripu Bdr Karki is the house owner and he has received third tranche of housing reconstruction.

Pic: Binod Kumar Kalauni



SMM Building with Rcc bands has been constructed in Bhaisain, 08-ward of Sailung RM. Mr. Sher Bdr Basnet is the house owner and he has received third tranche of the housing grant. Pic: Kamal Bahadur Mahat

Case Study

Birkha Bahadur Shrestha expected to be enlisted in beneficiary

[Video here](#)

Birkha Bahadur Shrestha from Sailung -8, Jhor is living in temporary makeshift since April 2015 earthquake with his wife and two children. His mother also has been living separately in the temporary makeshift where 2 rooms there in the makeshift.

He told us that the April 25th earthquake and the powerful aftershock of May 12th destroyed his house.

He has been trying to enlist as earthquake beneficiaries but unable to be enlisted yet.

He has been always filled(survey) as left beneficiaries but till date he has not enlisted as earthquake beneficiaries.

He told us, He has been filling the grievance forms every time, but he has not enlisted yet as earthquake beneficiary. 'what are the reason, why I am not enlisted as earthquake beneficiaries, either from top level official missed or the surveyor missed. May they write wrong information.'

He further added, 'All villagers in Jhor's names have been enlisted as earthquake beneficiaries but his name has not been enlisted yet as earthquake beneficiaries.'

Currently, his mother name has been enlisted in retrofitting beneficiary though her house destroyed and not livable (see video of house).

DLPIU(Building) focal person Mr. Bhogendra Sah suggested him in few days survey team will visit his village, that time he should approach the team to be enlisted as earthquake beneficiaries. Further, he directed the ward level technician to support convert retrofitting beneficiary to regular beneficiary.
