

HRRP

Technical Coordination Meeting, *Dhading*

Date: 31st October, 2017

Time: 2:00 PM

Location: DUDBC Division Office, Dhading.

Organized by:

DUDBC Division Office, Dhading

Housing Recovery and Reconstruction Platform- (HRRP)

Agenda :-

- 1) Welcome & Introduction.*
- 2) Sharing of Information about Retrofitting Manual & Hybrid Structure Manual.*
- 3) Updates from DUDBC/DLPIU on the Reconstruction.*
- 4) Updates from NRA/DLPIU about ongoing Resurvey & Re verification in the districts.*
- 5) Sharing of the field visit learning and challenges during the field visit (HRRP).*
- 6) National and district updates, maps presentations on gaps and coverage in reconstruction.*
- 7) Short briefing from PO's about their challenges Lesson learned, Probable solutions & new plan.*
- 8) Briefing about Major/Repetitive technical problems by District Support Engineers.*
- 9) AOB*

Reconstruction Update - Nepal :-

CLPIU Update 29 October, 2017


• Total no of Beneficiaries	=	7,67,291
• No of eligible HHs	=	7,26,324
• Grant Agreement	=	6,52,786
• First Tranche	=	6,34,850
• Second Tranche	=	88,012
• Third Tranche	=	12,844
• Eligible for Retrofitting Grant	=	24,991

- Total House Completed = 62,188
 - Running House = 1,47,292
 - Grand Total = 2,09,480
 - Remaining to built = 5,50,000
-
- Loan + Grant (3lakh + 3 Lakh) = 6 Lakhs
 - Total Amount = 3 Kharab, 30 Aarab
 - Ie F/Y Budget = More than 25 %

Reconstruction Update - Nepal :-

S. N.	Districts	No. of Eligible HHs	No. of beneficiaries added after grievances redressal	Total no. of beneficiaries	No. of HHs with grant agreem	No. of HHs received 1st tranche			No. of HHs received 2nd tranche			No. of HHs received 3rd tranche			No. of grievan ces register ed	No. of grievances cleared	No. of beneficiaries eligible for retrofitting grant
						GoN	I/NGO	Total	GoN	I/NGO	Total	GoN	I/NGO	Total			
1	2	3	4	5	6	7			8			9			10	11	12
Cluster 1- Highly affected 14 Districts																	
1	Sindhupalchok	78537	5126	83663	75304	70737	4455	75192	11680	1574	13254	1155	810	1965	14447	10838	376
2	Okhaldhunga	19819	346	20165	18794	18485	505	18990	4754	215	4969	1816	67	1883	8019	7810	1643
3	Nuwakot	65773	3516	69289	62825			63187			11020			1028	11503	11416	936
4	Ramechhap	43609	1431	45040	42015	40716	1282	41998	7442	610	8052	332	430	762	14005	13972	2149
5	Dolakha	51940	10893	62833	52594	49933	1679	51612	11067	1159	12226	1718	844	2562	24379	24379	637
6	Gorkha	58503	2813	61316	54521	54627		54627	8737	546	9283	1822	326	2148	1164		2019
7	Dhading	70581	2759	73340	66682	66651		66651	7414		7414	35		35	17044	16577	1494
8	Kavrepalanchok	67731	4689	72420	64012	61598	2414	64012	6444	502	6946	15	213	228	23939	23486	2415
9	Rasuwa	11236	397	11633	10700	8875	1023	9898	1218	581	1799	430	470	900	1418	1288	117
10	Sindhuli	34269	719	34988	30288	29425	863	30288	3908	453	4361		182	182	28627	28627	2408
11	Makwanpur	30238	1579	31817	23226	21006	1359	22365	3963	844	4807		705	705	23961	23919	4150
12	Kathmandu	42500	3300	45800	36559	36455	107	36562	1675	0	1675			0	11296	11296	575
13	Lalitpur	25892	1821	27713	22071	20348	756	21104	614	532	1146		427	427	7004	5882	667
14	Bhaktapur	26066	1578	27644	22175	21638		21638	985		985	19		19	6340	6330	280
Sub-total		626694	40967	667661	581766			578124			87937			12844	193146	185820	19866
Cluster 2 - Less affected 17 Districts																	
1	Sankhuwasabha	1953		1953	1583	1201		1201			0						326
2	Bhojpur	6202		6202	4500	3082		3082			0				8000		453
3	Dhankuta	2866		2866	2252	2252		2252			0						70
4	Khotang	8443		8443	7200	7200		7200			0						253
5	Solukhumbu	10794		10794	8095	6021		6021			0						456
6	Chitwan	7335		7335	4000	1426		1426									593
7	Nawalparasi	872		872	814	708		708			0				139		8
8	Tanahu	14287		14287	10145	9595		9595			0						466
9	Lamjung	13959		13959	12202	8502	200	8702		75	75				3042		539
10	Baglung	2375		2375	1107	1109		1109			0						82
11	Syangja	8549		8549	5342	4340		4340			0						567
12	Palpa	4652		4652	3500	1946		1946			0						384
13	Parbat	5269		5269	4138	4070		4070			0						417
14	Gulmi	4144		4144	2877	2068		2068			0						195
15	Kaski	6026		6026	1770	1770		1770			0						242
16	Arghakhachi	1036		1036	850	591		591			0						67
17	Myagdi	868		868	645	645		645			0						7
Sub-total		99630		99630	71020	56526	200	56726	0	75	75	0	0	0	11181	0	5125
Total		726324	40967	767291	652786	56526	200	634850	0	75	88012	0	0	12844	204327	185820	24991

निजी आवास पुनर्निर्माण अपडेट

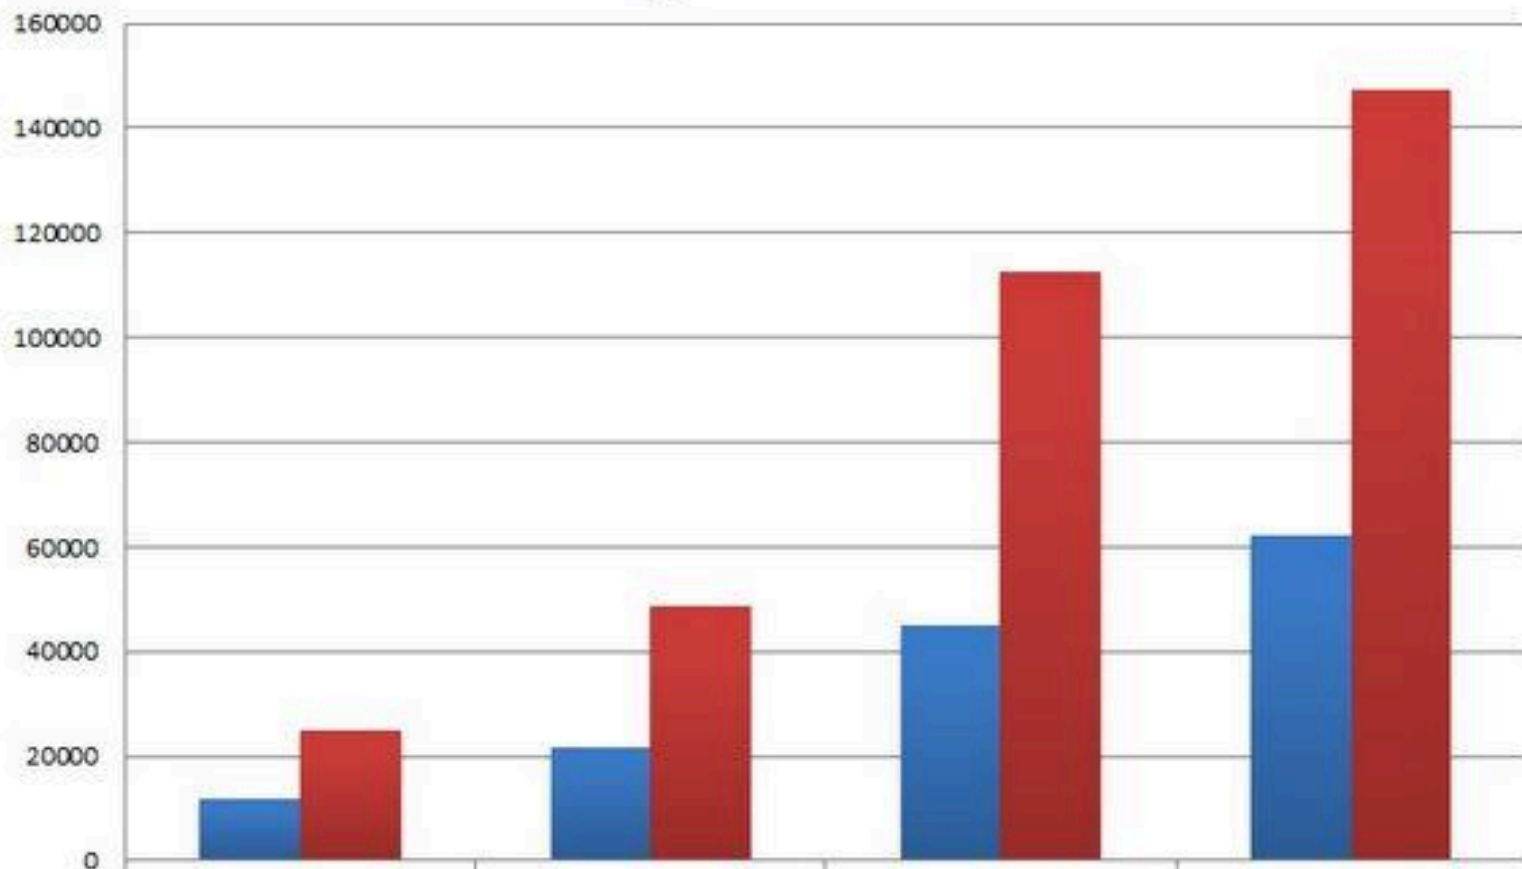

■ निर्माण सम्पन्न घर
■ बन्दै गरेका घरहरु

DUDBC Update - Dhading :-

• Total no of Beneficiaries	=	73,340
• Grant Agreement	=	66,682
• Added after Grievances	=	2,759
• First Tranche	=	66,651
• Second Tranche	=	8,595
• Third Tranche	=	1,284
• House Completed	=	12,500

Non Complaisance Cases :- (UNDP DSE)

• Total Check	=	507
• No of Failure house	=	45

EHRP Update - Dhading :-

• Total no of Beneficiaries	=	73,340
• Grant Agreement	=	66,682
• First Tranche	=	66,642
• Second Tranche	=	7,412
• Third Tranche	=	34

Sharing of Information about Retrofitting Manual & Hybrid Structure Manual.



Updates from DUDBC/DLPIU on the Reconstruction :-



Updates from NRA/DLPIU about ongoing resurvey & re-verification.



Sharing of the field visit learning and challenges (HRRP).

- *Huge lack of Awareness at local level*
- *Door to door technical Assistance is insufficient*
- *NRA lengthy approval process (community buildings, mason trainings, Shelter).*
- *Water scarcity hindering the construction of buildings at villages eg. Pida, Mulpani, Kiranchok.*
- *There is no Electricity in Kiranchok so it's not possible even to take water by lift i.e. Pumping System*
- *Unavailability of government engineers for technical support to beneficiaries at municipalities and rural municipalities.*

- *High number of non-compliance houses at rural-municipality and even at municipalities.*
- *Different perception and view of newly elected ward leaders has created obstacles in work as they have high expectation from Partner Organizations (POs).*
- *Challenge in transportation of construction materials at most of the areas of Dhading.*

Rate of Reconstruction :-



18.72 %

• District Profile Dhading :-

RECONSTRUCTION ACTORS

Organisation	Implementing Partner(s)
ADRA	RIMS
AMDA-M	
ASF	POURAKHI
CA	FOCUS
CARE-N	SAHAS
DCA	AN
EFF	
GIZ	
GON	
GON - DUDBC	
GON - PAF	CIRDS, NRCS, COSOC, ICDC, HDSC, PSBS
HEL VETAS	RIMC, MSED, JAYAN
ICDC	
NRCS	
NSET	
OXFAM-GB	PRAYAS-N, ACTION-N, FOCUS
UMN	PRAYAS-N, HIMS, NRDS

17 organizations

This table indicates the reconstruction actors and their respective implementing partner(s)

SUMMARY AND HIGHLIGHTS³



SHORT TRAINING

5,843

VOCATIONAL TRAINING
(Targets Achieved)

566

6,434

Reached

Remaining



18 Demonstration Constructions in 17 VDCs

Helpdesk/Technical support center covering 19 VDCs



0 VDC with Household WASH Assistance



66,682 beneficiaries enrolled, 88%

66,651 beneficiaries received the 1st Tranche, 88%⁴


6,305 beneficiaries received the 2nd Tranche⁴

35 beneficiaries received the 3rd Tranche⁴

- a. Community/household orientation with more than 1 session.
- b. Continuous Door to door technical assistance (Mobile Technical Support)
- c. Short training for Masons (Target achieved)
- d. Vocation/on the job training for masons (Target achieved)
- e. Helpdesk/Technical Support Center
- f. Demonstration construction
- g. Reconstruction Coordination Committee

Disclaimer:

The highlighted VDCs indicate that at least one of the aforementioned activities is being conducted/planned by partner organizations, irrespective of the methodology or household level coverage of the activity. For activity c and d, it is highlighted when there are more than 70% of masons trained according to the targets defined by NRA and field surveys.

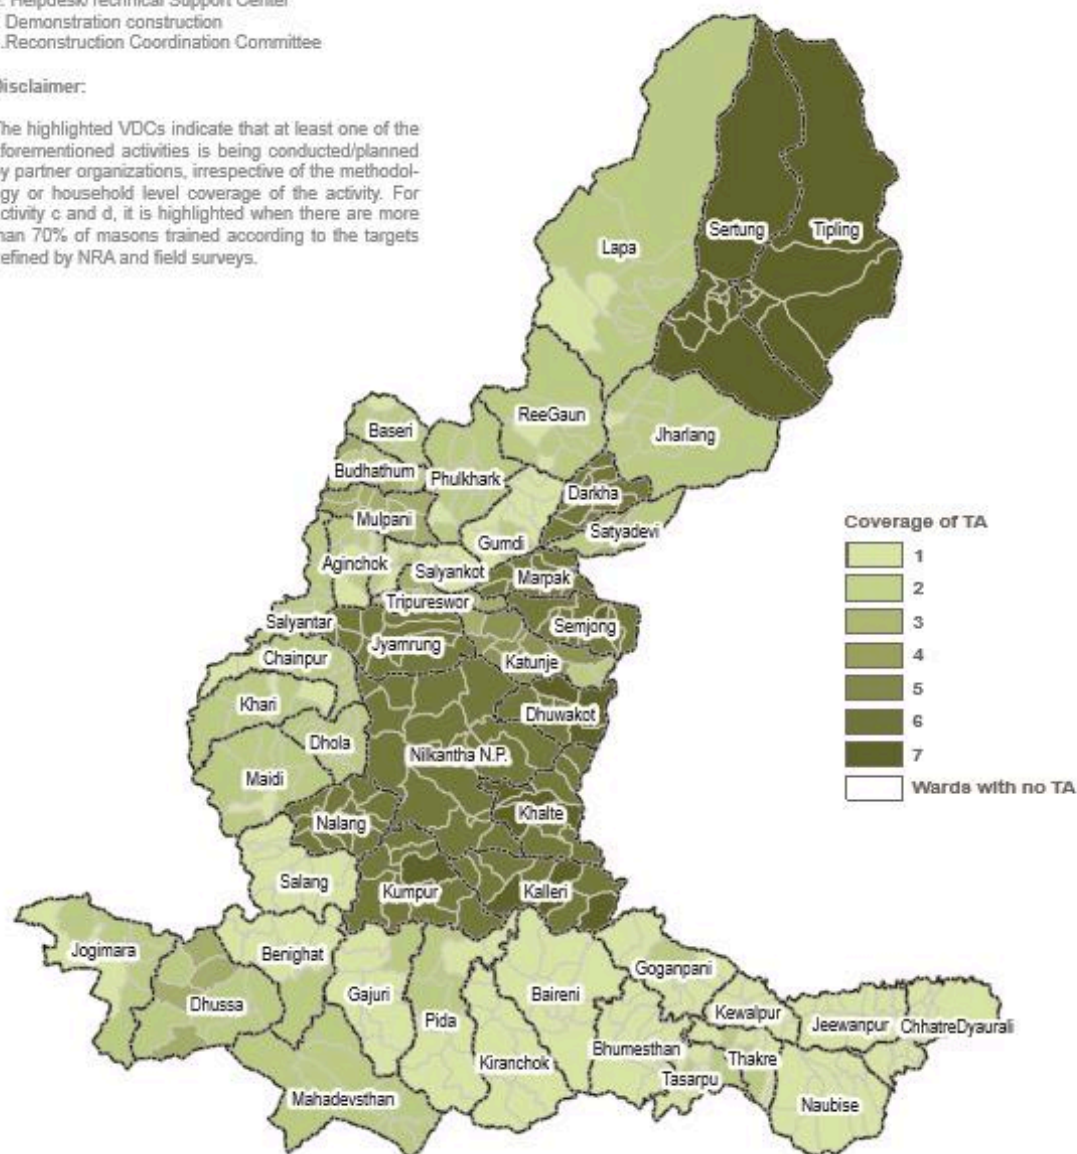

Short briefing from PO's about their challenges, lesson learned, probable solutions & their new plan.

Briefing about major/repetitive technical problems seen in reconstruction by District Support Engineers.

Communications Skills & FAQs



Thank You ☺
