

[Media Digest](#) | [FAQ](#) | [Briefing Pack](#) | [Meeting & Events](#) | [4W](#) | [Housing Progress](#) | [Housing Typologies](#)

HRRP BULLETIN

28 May 2018



Training on correction measures for non-compliant houses. Photo Credit: Hiroshai Imai.

Highlights

- [Invitation, second round table discussion on support for vulnerable households, 31 May, 3-4:30 PM, Bougainvilla Events, Tripureshwor, Kathmandu](#)
- HRRP [report](#) and [database](#) on Hollow Concrete Block production and use in earthquake affected districts
- Based on Building CLPIU data, 430,885 households have applied for the second tranche of the GoN housing reconstruction grant and based on GMALI CLPIU data, 385,449 of these households have received the second tranche.
- In Siranchowk RM, Gorkha, engineers are not able to inspect the retrofitting beneficiaries' houses since they have not received a checklist for retrofitting inspection.
- HRRP [Housing Reconstruction Progress maps](#) based on MoUD CLPIU inspection data as of 22 May
- HRRP [maps of Coverage of Technical Assistance](#) based on HRRP 4W data as of 25 April.


UPDATES & REQUESTS

National

NRA, GMALI CLPIU, and Building CLPIU Grant Disbursement Data, as of 27 May (Unofficial English Translation):

	29 April	11 May	27 May
Total No. Eligible HHs	767,709	767,710	767,710
HHs Enrolled	712,173	713,580	718,325
HHs Received 1 st Tranche	699,684	702,373	709,031
HHs Applied for 2 nd Tranche	309,287	340,398	430,885*
HHs Received 2 nd Tranche	334,071	351,506	385,449
HHs Applied for 3 rd Tranche	92,744	106,502	163,837*
HHs Received 3 rd Tranche	95,646	107,968	127,734

All numbers are based on Grants Management and Local Infrastructure (GMALI) CLPIU data except for numbers of households that have applied for 2nd and 3rd tranche which are based on Building CLPIU data.

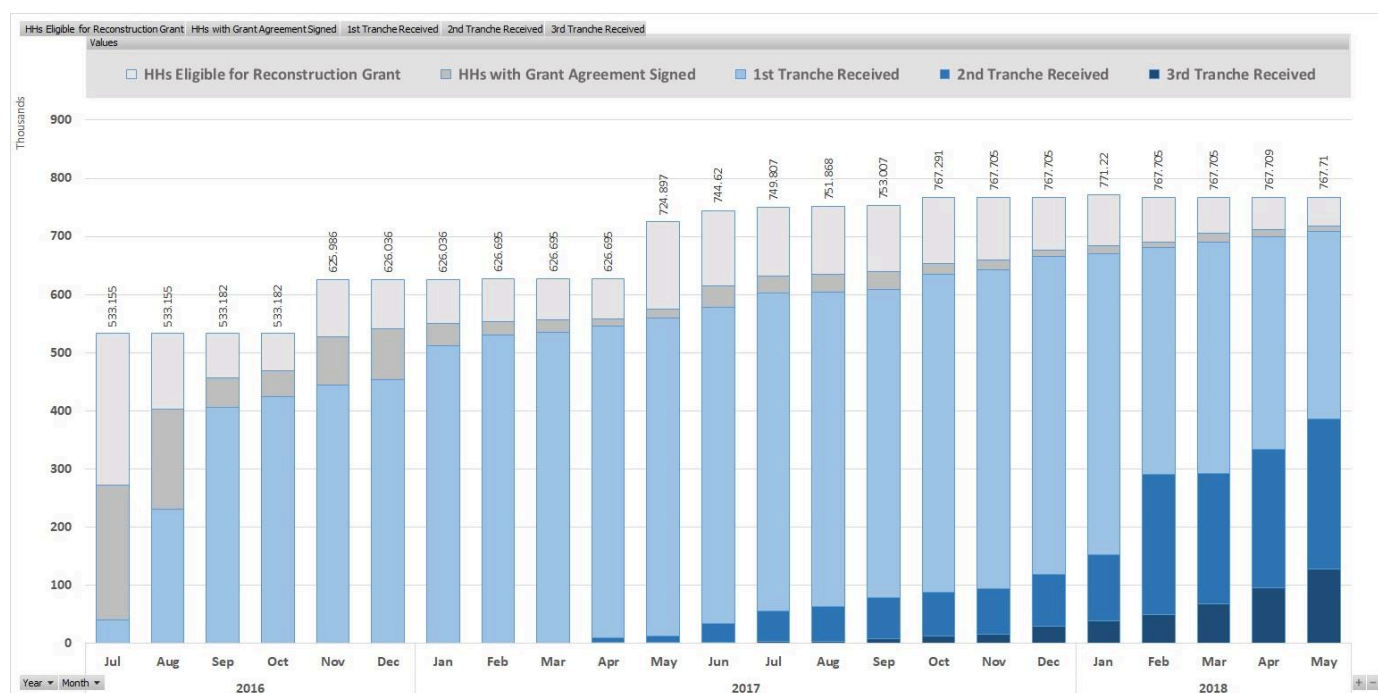

Housing reconstruction progress based on MoFALD CLPIU enrolment data from July 2016 to 27 May 2018.

Districts & Municipalities

HRRP District and Municipal Coordination Meetings, 15 – 28 May: during this period district coordination meetings took place in Sindhuli (17 May), Dolakha (21 May), and Gorkha (23 May). Municipal level meetings took place in Kailash Rural Municipality, Makwanpur (17 May), Thaha Municipality, Makwanpur (18 May), Siranchowk Rural Municipality, Gorkha (18 May), and Sahid Lakhani Rural Municipality (25 May). Some of the highlights from these meetings include:

- In **Sindhuli**, the discussion focused on technical issues observed during joint monitoring and field visits conducted by HRRP and Building CLPIU. These included the impact of absence and transfer of DLPIU engineers and the need for training for DLPIU engineers on the new timber frame structure manual given the high number of timber houses in the district.

- In **Dolakha**, a briefing was provided on the restructure of the NRA. Partner Organisations provided updates on their livelihood programmes and were requested to coordinate with NRA. The quality of mason training in the district was also discussed and all involved were asked to make every effort to maintain the quality of training provided. It was also agreed that mason training should be provided to masons working on housing construction in Dolakha even if they have come from other districts.
- In **Gorkha**, a briefing was provided on the restructure of the NRA. Technical issues related to retrofitting, mapping of active partners, rural and urban municipality wise reconstruction status, and some issues and challenges found during field visits were also discussed. Further, all the partners working in reconstruction, livelihood, WASH agreed to submit their monthly progress report to HRRP for NRA status update purpose by the 3rd of the month.
- In **Kailash RM (previous Gogane VDC), Makwanpur**, there is no GoN housing reconstruction grant since reconstruction of houses of all enrolled beneficiaries are supported financially by NRCS with technical assistance by Build Change, Nepal. Around 50% of houses have been completed and 85% of households have received the second tranche. In the meeting it was decided that local government, NRCS, and Build Change will support the remaining households to complete up to DPC level and get the second tranche by end of Asar 2075, i.e. to meet the Government tranche deadline. This will help to expedite reconstruction as well as motivate the households for reconstructing their houses. Further, the concerned stakeholders will also carry out the survey to find out the fake beneficiaries.
- In **Thaha Municipality, Ward No. 7 and 8, Makwanpur**, RADO Nepal has completed the reconstruction of 300 HHs with financial support from Tearfund and these houses have already been handed over to the beneficiaries. The reconstruction support of GoN is going on well but only a few households have received the third tranche. Delay in inspection and submission of files and lack of supervision were the major concerns. Decisions taken during meeting were: Inspection files to be submitted to DLPIU by the technicians within 7 days for the houses constructed to DPC level for second tranche and roof band level with toilet constructed for the third tranche to speed up reconstruction. Regular supervision and inspection will be carried out by local representatives and engineers. Engineers will be provided a working space in the ward office.
- In **Siranchowk RM, Gorkha**, the main concerns raised by the local representatives were: delays in the grievance process and engineers are not able to inspect the retrofitting beneficiaries' houses since they have not received a checklist for retrofitting inspection.
- In **Sahid Lakhan RM, Gorkha**, discussion focused on coordination, facilitation, and roles of local representatives. Some of the concerns raised were: beneficiaries not receiving grants on time from the banks even if they have already been approved to receive the grant, technical staff in the field do not know the status of inspection files rejected by the DCC, and uncertainty in processing of the files. The Chairperson of Sahid Lakhan RM also shared his initiation to support community people to understand that they do not have to construct a single room house.

HRRP District Coordination Team Gorkha, Weekly District Report, 11 – 24 May 2018



Ward No. 14, Gorkha Municipality, Gorkha: an RCC masonry house at plinth level with columns already poured. The owner has received the second tranche of the GoN housing reconstruction grant.

HRRP District Coordination Team Kathmandu, Weekly District Report, 11 – 24 May 2018




Ward No. 9, Madhyapur Thimi Municipality, Bhaktapur: a single storey, brick and mud mortar house. This is two houses attached belonging to two brothers. Salvaged materials such as old bricks, woods have been used for the construction of these houses. They have received the second tranche of the GoN housing reconstruction grant.

HRRP District Coordination Team Makwanpur, Weekly District Report, 11 – 24 May 2018



Kailash Rural Municipality, Makwanpur: one room, brick and cement mortar house with RCC bands and flexible roof. The home owner has received all three tranches of the housing reconstruction grants provided by NRCS with technical assistance from Build Change, Nepal. The total cost of construction was 250,000 NPRs.

HRRP District Coordination Team Nuwakot, Weekly District Report, 11 – 24 May 2018

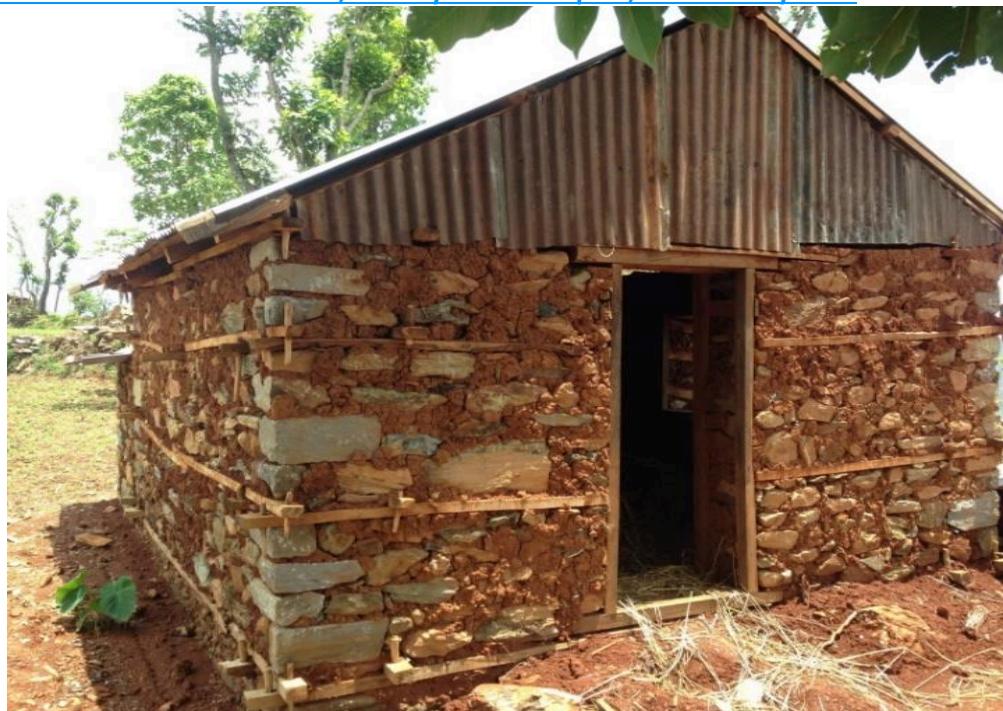

Ward No. 8, Bidur Municipality, Nuwakot: a stone and mud mortar house with timber bands. The house belongs to a vulnerable family. The home owner has received the second tranche of the GoN housing reconstruction grant and will be recommended for third tranche after shuttering.

HRRP District Coordination Team Ramechhap, Weekly District Report, 11 – 24 May 2018



Doramba Rural Municipality, Ramechhap: a three roomed, stone and mud mortar house, with RC bands. The home owner has received the second tranche of the GoN housing reconstruction grant and has been approved for the third tranche.

Requests for Partner Support

[Invitation, second round table discussion on support for vulnerable households, 31 May, 3-4:30 PM, Bougainvillea Events, Tripureshwor, Kathmandu:](#) those interested to participate are requested to RSVP to admin@hrrpnepal.org by 3 PM, 30 May.

[Urban Resilience Asia Pacific 2018 Conference, 7-8 November, Sydney, Australia:](#) the event is organised in collaboration with Arup, Australian Red Cross and the South Asia Institute at Harvard University. The website - <https://www.urap2018.com/> - gives details on registering, hosting a session and submitting abstracts.

DOCUMENTS & PRODUCTS

Government of Nepal

[NRA Newsletter, April 2018](#)

HRRP

[Report on Hollow Concrete Block Production and Use in Earthquake Affected Districts:](#) this report presents the findings of findings of two rounds of HRRP data collection on the production and use of Hollow Concrete Blocks (HCBs) across earthquake affected districts. Across the two rounds of data collection interviews were conducted with 76 block producers across 11 districts, with compressive strength testing carried out on 110 blocks, and interviews with 37 households that have built with HCBs, across 5 districts (HCBs are being used for reconstruction in more than 5 districts but HRRP District Coordination Teams were unable to conduct interviews with households in other districts). 86 of the 110 blocks tested (or 78%) failed to meet the compressive strength requirements specified in the Nepal Standards NS 119/2042. The next steps suggested in the report include, continuing

28 May 2018

Page 6 of 7

documentation of production and use of HCBs, developing a manual for HCB construction under the NRA Standardisation Committee for Reconstruction of Earthquake Resistant Houses, and developing and implementing support packages for HCB producers to improve quality of blocks.

Housing Reconstruction Progress Maps: based on MoUD CLPIU inspection data as of 22 May.

[Partnership Agreement between HHs and GoN](#)

[Construction Started](#)

[1st tranche received](#)

[Compliance rate 2nd tranche](#)

[Compliance rate 3rd tranche](#)

[Construction Completed](#)

Maps of Coverage of Technical Assistance: based on HRRP 4W data as of 25 April.

Coverage of 7 TA Activities – [32 Districts](#) and [Western](#), [Central](#), and [Eastern](#) Clusters

[Door to Door Technical Assistance](#)

[Demonstration Construction](#)

[Community and Household Orientation](#)

[Helpdesks / Technical Resource Centres](#)

[Vocational Training for Masons](#)

[Short Training for Masons](#)

Partners

Milijuli Nepali, BBC Media Action, Episode 958: in this episode, the presenter travels to Kaule, Kispang Rural Municipality-3 in Nuwakot district where most of the residents are masons. The presenter interacts with ward chairman Amrit Bahadur Tamang, mason Renu Tamang, and Renu's husband, Bishnu Tamang. Renu Tamang shares how she became a mason after working as a labourer for a long time and how she has contributed to the construction of houses in the village. Bishnu Tamang appreciates his wife for the work that she has been doing. Amrit Bahadur Tamang explains how the municipality is supporting the reconstruction process. The presenter also talks with other residents in the village.

Baliyo Ghar TV Programme, Episode No. 105: this programme is an interview with Mr. Mani Ram Gelal, Deputy Director General (DDG) of DUDBC, focused on the effective implementation of the National Building Code.

