

District Report

Gorkha

12 April – 9 May 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
HRRP team, M & E consultant, and DSE conducted field visit at Barpak Sulikot and Dharche Rural Municipality from 15 th to 19 April 2019. The details action plans and objective of the meeting has been stated in the field visit section.	15 th to 19 April 2019			techcord.gorkha@hrrpnepal.org ; im.gorkha@hrrpnepal.org	
HRRP/GMALI jointly organized preparatory meeting with POs for the program of Earthquake Memorial Day in presence of CDO, Gorkha, Mayor of Gorkha Municipality, and key POs in the district. The agenda of the meeting to jointly organize the earthquake Memorial Day effectively to disseminate message of safer construction and resilient community.	17 th April 2019	14	1	Techcord.gorkha@hrrpnepal.org , dc.gorkha@hrrpnepal.org , im.gorkha@hrrpnepal.org	
GMALI Gorkha organized 4 th Earthquake Memorial Day in Gorkha on 25 th April 2019 at DCC Hall. HRRP Gorkha has facilitated the program and planning. All the active POs, government stakeholders, political leaders, local representatives, media, civil societies, representatives of bank were actively participated in the program.	25 th April 2019			dc.gorkha@hrrpnepal.org im.gorkha@hrrpnepal.org	
HRRP participated Demo house handover program organized by SDSC in partnership with CRS Nepal at Shahid Lakhan Rural Municipality, Bungkot.	23 rd April 2019			dc.gorkha@hrrpnepal.org , im.gorkha@hrrpnepal.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
HRRP Exit plan meeting with POs and government stakeholders	16 th May 2019	HRRP	dc.gorkha@hrrpnepal.org , im.gorkha@hrrpnepal.org

News & Updates

- Earthquake day memorial in the district

बर्ष २१ अर्क २०४ २०७६ विहिबार बैशाख १२ Thursday April. 25 2019 नेपाल सावत १९३९ पुष्ट संख्या ४ मूल्य रु. ५

गोरखा भूकम्पको चारबर्ष पूरा

गोरखाको नीजि आवासको पुनर्निर्माण औसतमा ८२ प्रतिशत

लाप्राक एकीकृत बस्ती निर्माण अन्तिम चरणमा, मिलनबस्तीको प्रगति ३० प्रतिशत

शिव / अनुपमा
बैशाख १२, गोरखा
गोरखा भूकम्प गएको आज चार बर्ष पूरा भई पाँचौ बर्षमा प्रवेश गरेको छ। भूकम्पबाट गोरखामा चारसय ७२ जनाको निधन भएको थियो। आठसय ४८ जना गम्भीर घाइते भएका थिए। ५९ जना अपांग भएका थिए भने छ जना अहिलेसम्म पनि हराइरहेका छन्। भूकम्पबाट ७१ हजार पाँच वटा नीजि घर क्षतिग्रस्त भएका थिए। त्यस्तै पाँचसय १३ विद्यालय, ६६ वटा स्वास्थ्य चौकी क्षतिग्रस्त भएका थिए। भूकम्पको चारबर्ष पूरा हुँदा केन्द्रबिन्दु गोरखाको पुनर्निर्माणको काम ८२ प्रतिशत सकिएको छ। ७२ प्रतिशत लाभग्राहीले तेस्रो किस्ताको अनुदान रकम लिइसकेको जिल्ला आयोजना कार्यान्वयन इकाइ (अनुदान व्यवस्थापन तथा स्थानीय पूर्वाधार) का प्रमुख रामशरण आचार्यले जानकारी दिए। भूकम्पमा गोरखाका ७१ हजार पाँच घर क्षतिग्रस्त भएका थिए।

‘अहिलेसम्म ४९ हजार एकसय १६ जनाले घर बनाइसकेर तेस्रो किस्ता लगेका छन्’ आचार्यले भने, ‘४७ हजार नौसय ४४ जनाले दोस्रो किस्ता लगेका छन् भने ६४ हजार सातसय ६९ जनाले पहिलो किस्ता लगेका छन्।’ भूकम्प प्रभावित जिल्लाहरू मध्य गोरखाको पुनर्निर्माण अगाडि रहेको उनले दाबी गरे।

नीजि आवासबाहेक अन्य क्षतिग्रस्त संरचना पनि कुनै बाँकी पुष्ट ३ मा

पुनर्निर्माणमा एनजीओको योगदान उल्लेखनीय

दरौडी : गोरखाको पुनर्निर्माणमा गैरसरकारी संस्थाको योगदान पनि अविस्मरणीय रहेको जिल्ला आयोजना कार्यान्वयन इकाइका प्रमुख रामशरण आचार्यले बताए। ‘गैरसरकारी संस्थाले पुर्ण काम गरेका छन्। २३५ वटा विद्यालय भवन, ५३ वटा स्वास्थ्य चौकी भवन, २९ वटा गाउँघर क्लिनिक, १९४ वटा सिँचाई कुलो गैरसरकारी संस्थाले निर्माण गरिएका छन्’ उनले भने, ‘३४६ वटा खानेपानी आयोजनाहरू पुनर्निर्माण गैरसरकारी संस्थाहरूले गरेका छन्। ११ वटा लघु जलविद्युत आयोजना, २९४ वटा गोरेटो, घोडेढो बाटो पुनर्निर्माण गरेका छन्। नीजि आवास पुनर्निर्माणमा पनि गैरसरकारी संस्थाले सघाएका छन्।’ १३२ वटा साना उद्योगहरू, तरकारी, बिउ, बिजन केन्द्र, दुधजन्य सामग्री उत्पादन केन्द्रहरू ६१ वटा स्थापनाको काम पनि एनजीओहरूले गरेको भन्दै उनले प्रसंसा गरे।

पुनर्निर्माणमा निजीको सर कारलाई प्रसस्त उपयोग गरेको भन्दै आचार्यले भन्नुभयो। ‘४७ वटा सामुदायिक भवन, २३७ वटा नमूना घर बनाएर समुदाय बाँकी पुष्ट ४ मा

लाप्राकको गुप्तीपाखामा एनआरएनएद्वारा निर्माणधिन एकीकृत बस्ती। तस्विर : शिव / दरौडी


दरौडी : भूकम्प र संगमौलीको पहिरोले बिस्थापित भएका लाप्राकका बासिन्दालाई पुनर्स्थापित गर्न गैरआवासीय नेपालीहरूको संगठन (एनआरएनए) ले गुप्तीपाखामा निर्माण गरेको एकीकृत नमूना बस्ती निर्माणको काम अन्तिम चरणमा पुगेको छ। एउटै साइज र एउटै रङका पाँचसय ७३ घरधुरी निर्माण सम्पन्न हुने चरणमा पुगेको एनआरएनएका प्रमुख कार्यकारी अधिकृत हेमन्त दबाडीले जानकारी दिए।

‘भूकम्प गएको दिन बैशाख १२ गतेकै अवसर पारेर हस्तान्तरण गर्ने योजना थियो, तर निर्माण सम्पन्न हुन सकेन’ उनले भने, ‘काठ लगायतका सामग्री स्थानीय बासीले उपलब्ध गराउने सम्भव थियो। तर समयमै निर्माण सामग्री बाँकी पुष्ट ३ मा


Tranche Status

Rural /Municipality	Aarughat	Ajirkot	Bhimsen	Chum Nubri	Dharche	Gandaki	Gorkha	Palungtar	Sahid Lakhani	Siranchok	Sulikot
Total HHs Surveyed	6919	4169	6616	2132	3905	5790	13413	11362	7494	6951	7160
Total HHs Eligible	6924	4125	6835	2275	4169	5616	10156	9794	7061	6833	7200
Total HHs Enrolled	6924	4125	6835	2275	4169	5616	10156	9794	7061	6833	7200
First Tranche	6615	3951	6612	1853	3217	4816	9191	8425	6083	5752	6826
Second Tranche	6090	3721	6092	1546	2584	3975	7912	6741	5239	5248	6511
Third Tranche	4978	3226	4805	1216	2007	2716	7050	5114	4384	4338	5916
Total HH Constructed	4978	3226	4805	1216	2007	2716	7050	5114	4384	4338	5916
Grievance Registered	16622 (Total in district)										
Grievance Addressed	967	452	941	279	1121	1390	2496	3770	2282	2023	901
RF HH Eligible	177	63	168	49	280	441	1104	1099	836	913	180
RF HH Enrolled	177	63	168	49	280	441	1104	1099	836	913	180
RF 1st Tranche	31	3	35	1	83	29	551	340	28	20	2
RF 2nd Tranche							6	1	4	1	
Non-Compliance Registered	2413 (Total in district)										
Non-Compliance Addressed	58-Failed for tranche 2298- Recommended for 2 nd Tranche 2139- Recommended for 3 rd Tranche										


Graph of Tranche Status:

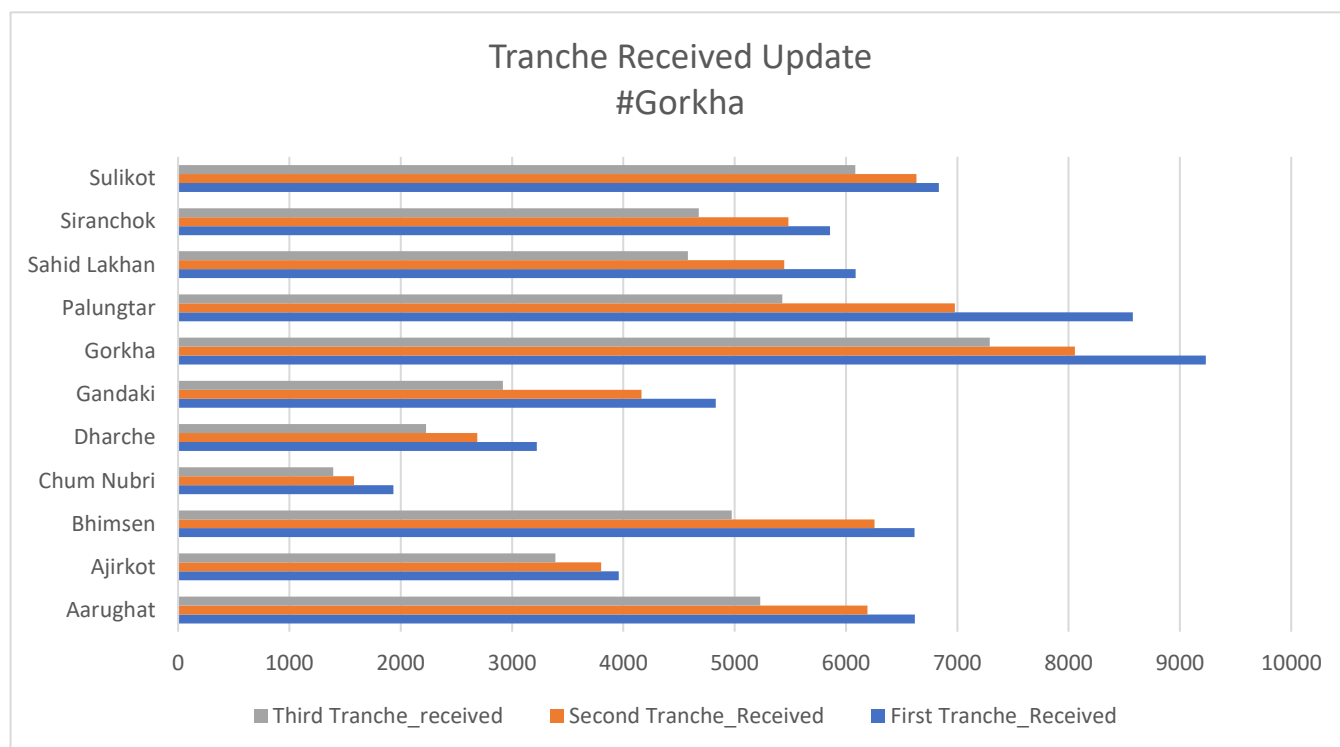

Graph for Retrofitting Status:

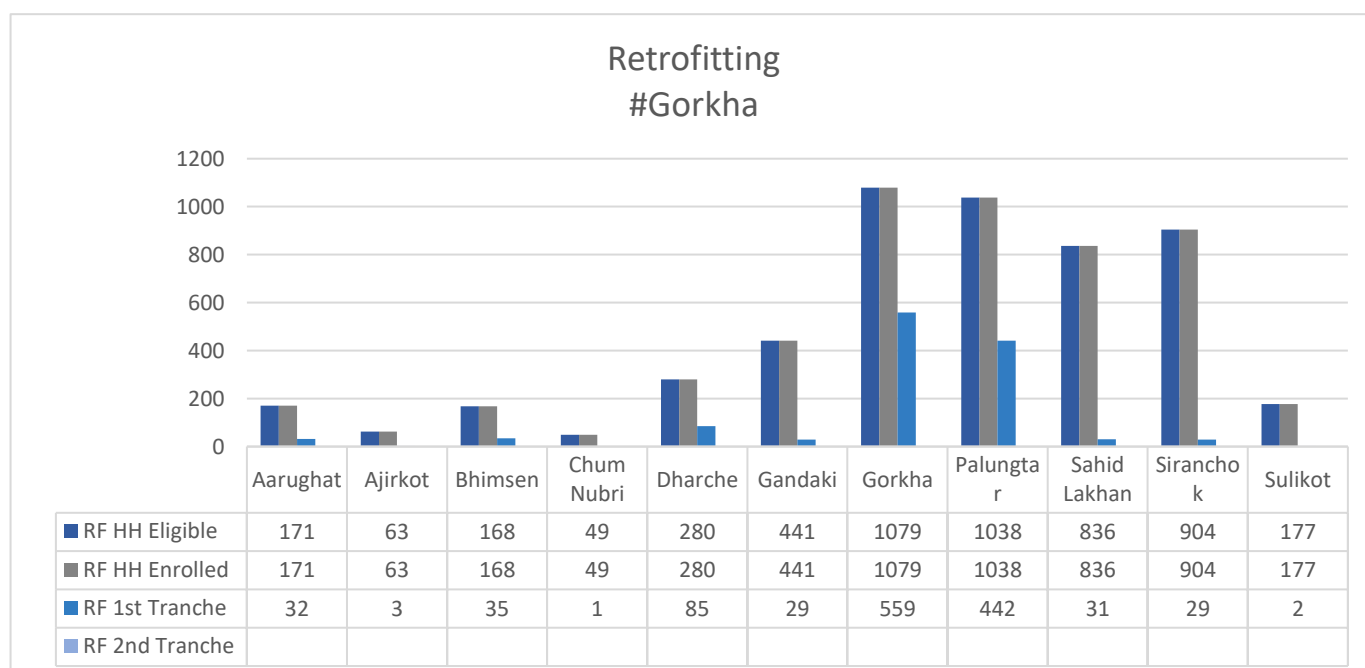

Graph for Grievance Status:

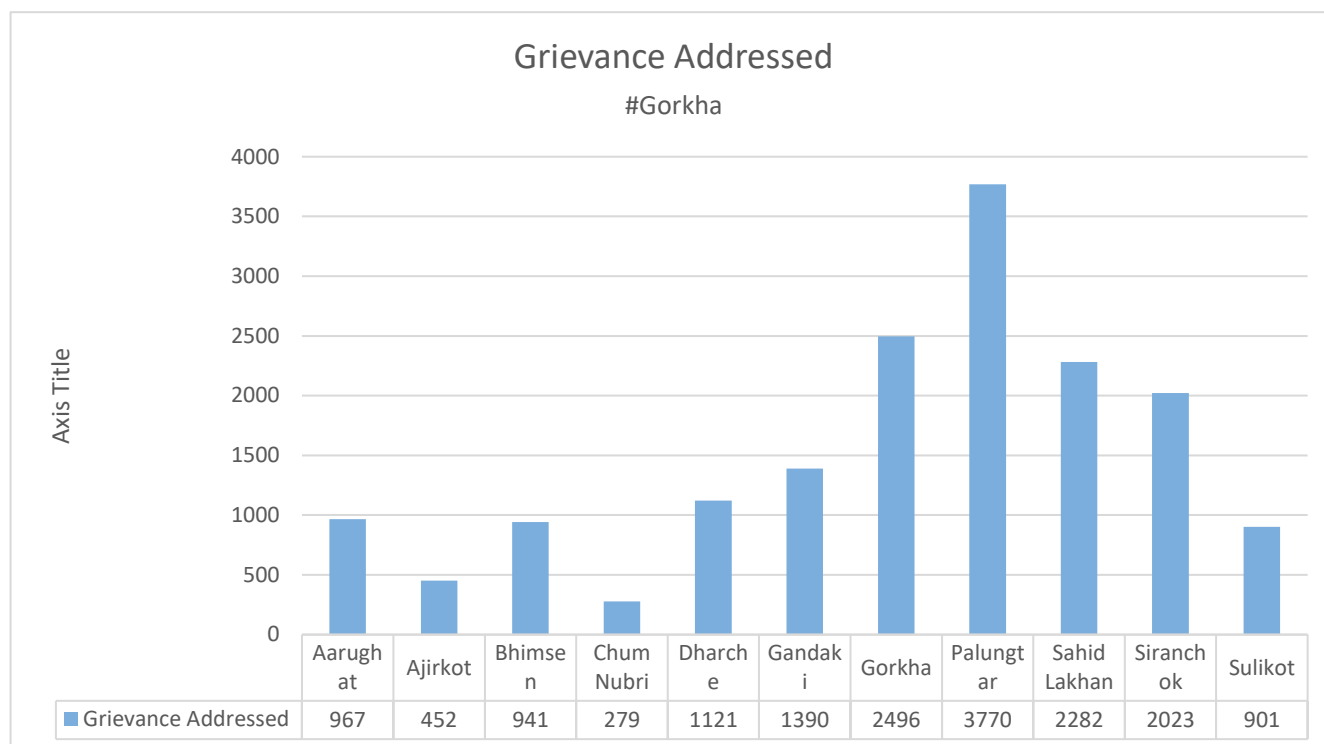

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
15 - 19/04/2019	Barpak Sulikot Rural Municipality – Barpak, Dharche Rural Municipality – Laprak, Gumda & Lapu	- Mr. Chandra Gurung – DC, HRRP - Mr. Birodh Kattel (DIMO, HRRP) - Mr. Khagendra Awasthi – M & E consultant - Mr. Rajesh Adhikari - DSE, DLPIU-Buidling

Objective(s)

- Joint Monitoring field visit of HRRP and CLPIU Building
- Palika and ward level coordination meeting
- Reconstruction action plan updates
- Housing typology collection survey assessment

Summary

HRRP Gorkha team and CLPIU Building consultant and DSE from DLPIU conducted joint monitoring field visit to barpak Sulikot and Dharche Rual Municipality beginning from 15 to 19 April 2019. The purpose of the field visit were: Joint Monitoring field visit of HRRP and CLPIU Building, Palika and ward level coordination meeting, Reconstruction action plan updates and housing typology collection.

The monitoring team conducted ward level coordination meeting [click here for minutes](#) at Lapu - 7, Dharche Rural municipality and discussed the retrofitting issues, houses in other places and reverification survey. The ward chairperson also updated the ward level reconstruction progress updates, issues, and challenges. HRRP team also collected housing typology from Barkpak, Gumda and Lapu. In Gumda, the joing monitoring team observed one-room houses with vertical and horizontal extension and analyze the compliance standard and resiliency. The team had brief meeting with Gol supported NHRP field staffs regarding their socio-technical support provided by field engineers and ANS.

Visit 2

Date	Location	Participants from HRRP and stakeholders
23 rd April 2019	Shahid Lakhan Rural Municipality – 5, Bungkot	- Mr. Atit Shrestha – HRRP - Mr. Ram Saran Acharya – GMALI Chief - Mr. Ram Hari Devkota – CRS - Mr. Rabin Adhikari – SDSC - Ms. Kamala Lamichane – SDSC – ED - Mr. Rajan Pant - Mayor, Gorkha Municipality

Objective (s)

- To handover over the demo house to ward office constructed by SDSC in support from CRS Nepal

Summary

HRRP/GMALI participated in the demo house handover program organized by SDSC on 23rd April 2019 at Bungkot in partnership with CRS. The program was attended by GMALI chief, mayor of Gorkha Municipality, HRRP, CRS and journalist. The objective of the handover of demo house is to formally transfer the ownership of the building to ward office. In the program, mayor of Gorkha Municipality appreciated the work that has been done by development partners in the reconstruction. Likewise, GMALI chief also responded queries raised by the beneficiaries regarding private housing construction and also updated overall progress of reconstruction in the district. He urged that 80% of housing reconstruction have completed in the district but there are still a significant

number of community infrastructure which are desperately waited for reconstruction. So, he further requested POs to support in community infrastructure in the days.

Challenges / Issues Identified	Action Required	Responsible	Time Frame
Changing retrofitting beneficiaries to full beneficiaries	Need to address and resolve from NRA	NRA, GMALI	As soon as possible
Access to soft loan from bank	Facilitate from GMALI for the documentation to the banks	GMALI, beneficiaries	As soon as possible

Photos



Palika level coordination meeting at Dharche Rural Municipality in presence of chairperson Mr. Surya Man Gurung, HRRP team, DSE and M & E Consultant



Preparatory meeting with POs, local bodies, HRRP, GMALI to memorize 4th Earthquake Memorial Day at DCC Hall, Gorkha.

Housing Typology Report



Caption: Pahal Man Gurung's stone masonry mud mortar house with RCC band in Ajirkot rural municipality ward no. 1, Ghyachok. The house owner has received all three tranches.



Caption: Til Maya Gurung's hollow concrete block house in Gorkha urban municipality ward no. 10. The house did not have any horizontal and vertical bands. Correction measures have been applied as per the correction exception manuals

Photo Courtesy: NHRP Gorkha Team



Caption: Ananda Prasad Devkota's brick masonry cement mortar house with RCC band in Ajirkot rural municipality, ward no. 5, Mucchowk. The house owner was supported (financial and technical) by INF and he has received all the tranches.

Photo Courtesy: INF Gorkha team

using GI wire mesh. Technical support was provided by GOI funded NHRP.

Photo Courtesy: NHRP Gorkha Team



Caption: Gopal Damai's brick masonry cement mortar house with RCC band in Ajirkot rural municipality, ward no. 5, Mucchowk. The house owner was supported (financial and technical) by INF and he has received all the tranches.

Photo Courtesy: INF Gorkha team

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
When will start the re-survey and reverification work?	Ward Chairpersons	Engineers were in pen down movement demanding their allowances and government has agreed to fulfil their demand, and the selected engineers will come to respective ward and will start as soon as possible.
What will happen to those beneficiaries who have built houses immediately after the earthquake and their houses are not meeting the minimus standard?	Ward Chairperson & beneficiaries	CLPIU has circulated letter through DLPIU to collect the information regarding the beneficiaries and exact number of houses from the palika and ward level. Once data collected, government will provide grant to them from government own grant.

Challenges and Way Forward

Challenge	Way Forward
Distribution of construction completion certificate	Final inspection to be carried out by DLPIU engineers and issuing construction completion certificate to beneficiary through ward offices

Case Story

Vulnerable support brings happiness

Mr. Chet Bahadur Roka, differently able is a permanent resident of Gorkha Municipality – 9, Dal Vanjyang. He lives with his wife and two children. His house was destroyed by the 2015 earthquake and lived in temporary shelter for 3 years. He received the housing grant of 50 thousand initially and just laid the foundation but could not build his house due to acute financial crisis. HRRP and GMALI visited the site and tried to know the real situation why he was unable to build his house. And then, HRRP raised this issue in HRRP monthly coordination meeting on the agenda of vulnerable support and its gaps. Initially, no any POs showed interests to support him due to differently working coverage of POs program. But, HRRP frequently discussed with POs and eventually Asal Chimeki Nepal extended its supportive hands to construct his house as vulnerable top up support.



Mr. Roka standing of his newly constructed house

Photo by: Chandra Gurung - HRRP

After field verification with HRRP and GMALI, Asal Chimeki Nepal agreed to provide material support up to 60 thousand Nepali rupees thereby, making agreement with him in presence of Ward Chairperson. When ACN provided technical and materials support – bricks, sand, cements, he could complete his house up to plinth band level and received 2nd tranche of government housing grant. Now, Mr. Roka has completed his house and shifted to his new house. He thanked to ACN, HRRP and GMALI to provide such huge support to construct his house.

Story by HRRP Gorkha
