

## District Report

### Ramechhap

15 February - 14 March 2019

#### Summary of events during this period

| Name of activity/event                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Event date                     | Participants summary |        | Contact Person                                   | Reference Document              |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------|----------------------|--------|--------------------------------------------------|---------------------------------|
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         |                                | Male                 | Female |                                                  |                                 |
| HRRP Ramechhap has successfully completed the Joint Field monitoring visit to Likhu Tamakoshi Rural municipality Ward-2, Duragaoun starting from 27 Feb -2 March 2019. During the field visit ward level meeting was conducted at Duragaun ward-2 office. In the meeting ward chairperson and DLPIU technical person were participated and discussion about reconstruction status and issue/challenge. Similarly, team has observed the typology of private housing construction in the area as well as interaction and discussion with the reconstruction beneficiaries                | 27 Feb-2 March 2019            | 9                    |        | Mr. Prakash Bishwakarma                          | <a href="#">Report link</a>     |
| Ramechhap HRRP team has successfully completed the General coordination meeting on 27 <sup>th</sup> February 2019 at District coordination meeting hall. The meeting was chaired by Gmali chief Mr. Krishna Lal piya. A total of 25 participants are participated in the meeting from government and partner organization. All the partner's organization present their progress and update of their project. MIS specialist from Gmali and DLPIU building MIS officer present the reconstruction status of the district. The program was closed with the remarks from the Gmali chief. | 27 <sup>th</sup> February 2019 | 23                   | 2      | Mr. Prakash Bishwakarma                          | <a href="#">Report link</a>     |
| Fortnightly Housing typology of Ramechhap has been updated.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             | 9 <sup>th</sup> March 2019     |                      |        | Tulasi Ram lamichhane                            |                                 |
| Coordination and facilitation for action plan update in the respective palika website. A total of 4 palika and Municipality had been updated their action plan in their respective website.                                                                                                                                                                                                                                                                                                                                                                                             |                                |                      |        | Prakash BK /Javeed Mohamad/Tul si ram lamichhane |                                 |
| Housing Typologies has been updated in Flickr                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           |                                |                      |        | Tulasi ram lamichhane                            | Shortly update on google drive. |
| Ramechhap team has successfully completed An Orientation on Hollow Concrete Block                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | 12 <sup>th</sup> March 2019    | 24                   | 1      | Tulshi ram Lamichanne                            |                                 |

## Summary of events during this period

|                                                                                                                                                     |                           |  |  |                |                            |
|-----------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------|--|--|----------------|----------------------------|
| Manual on 12 <sup>th</sup> MRCH 2019. A total of 25 participants were participated in the Orientation program from DLPIU and partners organization. |                           |  |  |                |                            |
| 5 W update of Ramechhap round 8                                                                                                                     | 25 <sup>th</sup> Feb 2019 |  |  | Mohamad Javeed | <a href="#">Click here</a> |

## Field Visit /Joint Field Monitoring Visit Reports

### Visit 1

| Date                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | Location                                                                                                                                                                                                                                                                                                                             | Participants from HRRP and stakeholders                                                                                                                                                                                                                                                                 |                         |                         |                            |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------|-------------------------|----------------------------|
| 27 FEB -2March 2019                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        | Likhu Tamakoshi Rural Municipality ward-2, Duragaun                                                                                                                                                                                                                                                                                  | <ul style="list-style-type: none"><li>✓ Janak Raj Joshi, CLPIU, M&amp;E consultant</li><li>✓ Nikesh Maharjan District Support Engineer, DLPIU Ramechhap</li><li>✓ Prakash Bishwakarma, District General Coordinator-HRRP</li><li>✓ Tulasi Ram Lamichhane, District Technical Coordinator-HRRP</li></ul> |                         |                         |                            |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                            |                                                                                                                                                                                                                                                                                                                                      |                                                                                                                                                                                                                                                                                                         |                         |                         |                            |
| Objective(s)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               | <ul style="list-style-type: none"><li>• To observe the reconstruction status of respective ward.</li><li>• To provide inputs to the beneficiaries in regards of housing reconstruction and non-compliances issues.</li><li>• Meeting with the local representatives to discussion on reconstruction challenges and issues.</li></ul> |                                                                                                                                                                                                                                                                                                         |                         |                         |                            |
| Summary                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    | Description of field visit (maximum 300 words)                                                                                                                                                                                                                                                                                       |                                                                                                                                                                                                                                                                                                         |                         |                         |                            |
| <p>Previously Duragaun is a village development committee in Ramechhap in the Janakpur Zone of north-Easter Nepal. Recently Duragaoun is located at Likhu Tmakoshi Municipality ward-2 in new local governance structure. A total 681 beneficiaries are identified as an earthquake beneficiary. Among them a total of 677 beneficiaries have been done agreement with the government for reconstruction grant. The reconstruction status of the ward-2 Duragaoun listed below:</p>                                                                                                                                                                                                                                                                                                                                                                                                        |                                                                                                                                                                                                                                                                                                                                      |                                                                                                                                                                                                                                                                                                         |                         |                         |                            |
| Total Beneficiaries                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        | Total Agreement                                                                                                                                                                                                                                                                                                                      | 1 <sup>st</sup> Tranche                                                                                                                                                                                                                                                                                 | 2 <sup>nd</sup> Tranche | 3 <sup>rd</sup> Tranche | Retrofitting beneficiaries |
| 616+65 (Grievance)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         | 677                                                                                                                                                                                                                                                                                                                                  | 677                                                                                                                                                                                                                                                                                                     | 559                     | 483                     | 134                        |
| <b>Key point of the visit at Ward-2, Likhu Tamakoshi RM</b>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                                                                                                                                                                                                                                                                                                                                      |                                                                                                                                                                                                                                                                                                         |                         |                         |                            |
| <ul style="list-style-type: none"><li>• A total of 681 is identified as a reconstruction beneficiary at Likhu Tamakoshi ward-2 Duragaun. Among them a total of 677 have been done agreement to the government for government reconstruction grant. A total of 559 beneficiaries had got 2<sup>nd</sup> tranche and 483 beneficiaries had got 3<sup>rd</sup> tranche of government.</li><li>• A total of 4 beneficiaries had not done agreement yet with the government. One of the beneficiaries is vulnerable beneficiaries therefore he was not able to do agreement and remaining are not yet contact with technical person and ward office.</li><li>• 134 beneficiaries have been identified in the retrofitting beneficiaries and till date no any beneficiaries have done agreement to the government for grant. They are willing to be a full reconstruction beneficiary.</li></ul> |                                                                                                                                                                                                                                                                                                                                      |                                                                                                                                                                                                                                                                                                         |                         |                         |                            |

- A total of 23 households integrated community has been construction at Duragaun. Among them 4 household have done DPC and other are being construction.
- A total of 132 household have been identified as a non-compliance issue. Among them 85 household have been apply correction manual and recommended for tranche. Remaining 12 households are still not doing correction and waiting for the government decision and remaining are difficult to do correction.
- Most of the non-compliances issue in the area are house constructed before technical person in the area and some have the issue of access attic height.
- Social mobilization of technical person was found very satisfactory at community level. Technical person is frequent in community and supporting beneficiaries in construction of house as well as inspection of house. Therefore socio-technical support from the government technical person was doing very well says Chairperson of ward-2 Duragaun.
- A total of three technical person is mobilized at ward-2 duragaun. Among them two are engineer and one is assistant engineer.
- Overall 95% of work has been completed at Duragaun reported by Sub-engineer of Duragaun.
- A total of 15-20 non-compliance issue applying houses were observation and interaction by District support engineer and joint monitoring team at Duragaun of Likhutamaokhaosi RM.

**Some photo of Activities during the period**



Ward level meeting at Ward-2, Duragaun , Likhutamakoshi RM



Joint monitoring team observation and interaction with the workers working in integrated community at Duragaoun.


**Graph of Tranche Status:**

| Rural/Municipality      | Doramba | Gokulganga | KhadaDevi | Likhu | Manthali | Ramechhap | Sunapati | Umakunda |
|-------------------------|---------|------------|-----------|-------|----------|-----------|----------|----------|
| Total HHs Surveyed & GR | 5252    | 6343       | 5212      | 5686  | 11077    | 6554      | 3671     | 4984     |
| Total HHs Eligible      | 5252    | 6343       | 5212      | 5686  | 11077    | 6554      | 3671     | 4984     |
| Total HHs Enrolled      | 4674    | 5936       | 5106      | 5498  | 10640    | 6394      | 3473     | 4561     |
| First Tranche           | 4667    | 5911       | 5102      | 5497  | 10629    | 6385      | 3470     | 4560     |
| Second Tranche          | 3816    | 5083       | 4627      | 4888  | 9425     | 5590      | 3105     | 4008     |
| Third Tranche           | 2474    | 3923       | 3731      | 3966  | 7477     | 4674      | 2022     | 2510     |


|                           |      |      |      |      |      |      |      |      |
|---------------------------|------|------|------|------|------|------|------|------|
| Total HH Constructed      | 2038 | 3660 | 3460 | 3590 | 7045 | 4250 | 2175 | 2190 |
| Grievance Registered      | 2448 | 1031 | 2007 | 1562 | 2815 | 1841 | 1392 | 843  |
| Grievance Addressed       | 2448 | 1031 | 2007 | 1562 | 2815 | 1841 | 1392 | 843  |
| RF HH Eligible            | 1076 | 347  | 1317 | 1010 | 1271 | 960  | 821  | 343  |
| RF HH Enrolled            | 47   | 1    | 222  | 16   | 39   | 6    | 20   | 5    |
| RF 1st Tranche            | 47   | 1    | 222  | 16   | 39   | 6    | 20   | 5    |
| RF 2nd Tranche            |      |      |      |      |      |      |      |      |
| Non-Compliance Registered | 31   | 57   | 7    | 69   | 78   | 26   | 7    | 2    |
| Non-Compliance Addressed  | 31   | 57   | 7    | 69   | 78   | 26   | 7    | 2    |

Source: DLPIU-Building, GMALI

Graph of Tranche Status:

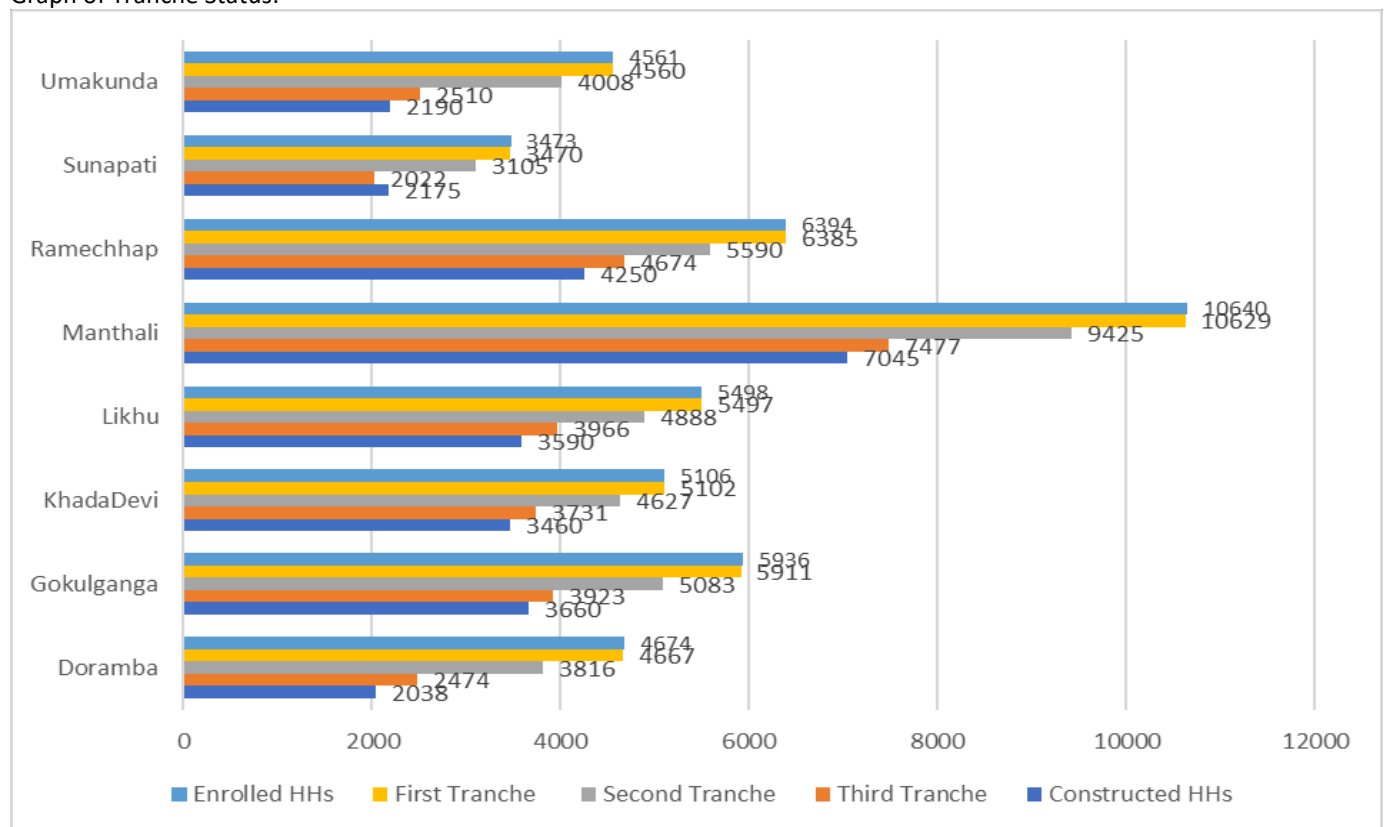

Graph for Non - Compliance Status:

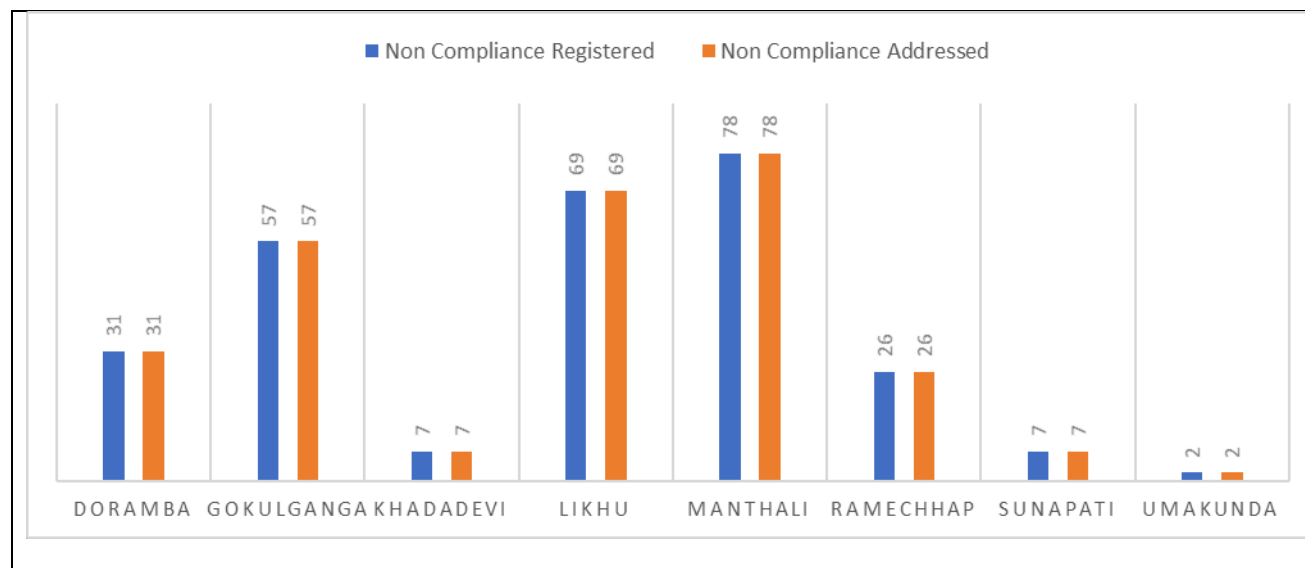



## Housing Typology Report



The house of Pawan Gurung built in Duragaun, Likhu Tamakoshi Gaupalika ward no. 1. He is one of the retrofitting beneficiaries, but he has reconstructed a new house without making any changes to the house which needs to be retrofitted. The new constructed house is a hybrid structure. The ground floor is made of stone in mud mortar with timber bands provided and there is proper connection between two floors. However, the cross bracing has not been sufficiently provided. He has done agreement on retrofitting beneficiary and wanted to shift to the reconstruction beneficiary.



The house of Chandra Maya Bhujel being constructed under the 50 days training provided by EFSR II implemented by HELVETAS in Duragaun, Likhu Tamakoshi Gaupalika ward no 1. During the visit, the training was conducted upto 21 days and the field practical was conducted since last 4 days. The house owner is a single woman. The trainees were divided in a group of 10 masons who were involved in the construction of particular house. The house is being constructed using stone in mud mortar with RC bands provided. The house will be constructed up to 1 floor without attic. The house is a part of unified settlement being developed in the gaupalika.



The house of Sita Damai being constructed under the 50 days training provided by EFSR II implemented by HELVETAS in Duragaun, Likhu Tamakoshi Gaupalika ward no 1. During the visit, the training was conducted upto 21 days and the field practical was conducted since last 4 days. The house owner is a single woman. The trainees were divided in a group of 10 masons who were involved in the construction of particular house. The house is being constructed using stone in mud mortar with RC bands provided. The house will be constructed up to 1 floor without attic. The house is a part of unified settlement being developed in the gaupalika.



The house of Shanta Bahadur Sunuwar being constructed under the 50 days training provided by EFSR II implemented by HELVETAS in Duragaun, Likhu Tamakoshi Gaupalika ward no 1. During the visit, the training was conducted upto 21 days and the field practical was conducted since last 4 days. The house owner is a physically disabled. The trainees were divided in a group of 10 masons who were involved in the construction of particular house. The house is being constructed using stone in mud mortar with RC bands provided. The house will be constructed up to 1 floor without attic. The house is a part of unified settlement being developed in the gaupalika.





The house of Akklae Sarki constructed in Duragaun , Likhu Tamakoshi Gaupalika ward no. 1. The house was constructed using stone in mud mortar with timber bands. The house was initially built with an attic which is not allowed by the building guidelines. Later after the correction provided by District Support Engineers, the vertical timber bars have been provided between the lintel band and the roof band. The house owner has received the third tranche of reconstruction grant.



The house of Ana Bahadur Sarki constructed in Duragaun , Likhu Tamakoshi Gaupalika ward no. 1. The house was constructed using stone in mud mortar with timber bands. The house is built with an attic which is not allowed by the building guidelines. The house is missing the plinth band as well. The house owner has only received the first tranche of reconstruction grant.



The house of Phatta Bahadur Sarki constructed in Duragaun, Likhu Tamakoshi Gaupalika ward no. 1. The house was constructed using stone in mud mortar with timber bands. The house was initially built with an attic which is not allowed by the building guidelines. Later after the correction provided by District Support Engineers, the vertical timber bars have been provided between the lintel band and the roof band. The house owner has received the third tranche of reconstruction grant. The PA number of the house owner is 21-16-7-0-29. The house owner is a mason who has been applying correction to the noncompliance houses who has been provided correction by DSE.



The house of Shanta Bahadur Gajmer constructed in Duragaun, Likhu Tamakoshi Gaupalika ward no. 1. The house was constructed using stone in mud mortar with timber bands. The house was initially built with an attic which is not allowed by the building guidelines. Later after the correction provided by District Support Engineers, the vertical timber bars have been provided between the lintel band and the roof band. The house owner has received the third tranche of reconstruction grant.

## Questions Collected

| Question                                                                                             | Who Asked the Question? | Response Provided (By Whom)                                                                                  |
|------------------------------------------------------------------------------------------------------|-------------------------|--------------------------------------------------------------------------------------------------------------|
| What is the process for to transfer from Retrofitting beneficiaries to Reconstruction beneficiaries? | Ward Chair person       | The beneficiaries must perform the retrofitting of the damage house in case the building collapse during the |

## Questions Collected

|                                               |                   |                                                                                                                                                                                                  |
|-----------------------------------------------|-------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|                                               |                   | retrofitting process the beneficiaries can be transfer to reconstruction beneficiaries after the recommendation of respective technical person and ward office. (Janka raj Joshi M&E consultant) |
| What is the process of appellate application? | Ward chair person | Beneficiaries should fill appellate from provided by Gmali if they are not satisfied with the result of grievance address. With strong evidence to prove the damage cause by earthquake.         |

## Challenges and Way Forward

| Challenge                                                                                              | Way Forward                                                                                                         |
|--------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------|
| The transportation of materials is very difficult due to the adverse road condition after the rainfall | The necessary materials have to be collected before the dry season and use of local materials should be prioritized |
