

District Report

Dhading

15 March – 11 April 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
HRRP Dhading Team successfully organized Orientation on Hollow Concrete Block (HCB) Manual at RK Hotel, Dhading with 51 participants from NRA DLPIU and Partner Organizations.	18 March 2019			dc.dhading@hrrpnepal.org techcord.dhading@hrrpnepal.org	Link to GD Orientation Minute
The HRRP conducted District coordination meeting on 18th March 2019 at RK Hotel, Dhading.	18 March 2019			dc.dhading@hrrpnepal.org techcord.dhading@hrrpnepal.org	Link to GD Meeting Minute
HRRP Dhading Team together with GMaLI, Building DLPIU & DCC conducted informal meeting regarding Re-Survey & Re-Verification	20 March 2019			dc.dhading@hrrpnepal.org techcord.dhading@hrrpnepal.org	NA
HRRP Dhading Team together with Building DLPIU Team, NSET, M & E CLPIU, DSE conducted informal meeting regarding issues occurred in Marpak, Netrawati Rural Municipality	22 March 2019			dc.dhading@hrrpnepal.org techcord.dhading@hrrpnepal.org	NA
A joint monitoring visit of DLPIU/Building, GMaLI/NRA, DAO, DCC, Khagendra Awasthi (M & E/CLPIU), Sachin Sapkota (HRRP-DTC), Rajesh Shrestha (DSE/NRA) to Jwalamukhi Rural Municipality was conducted. The visit was focused on monitoring different houses constructed during reconstruction technically assisted and supported by "Hamro Ghar" Pariyojana in Jwalamukhi Rural Municipality.	25 th March 2019			techcord.dhading@hrrpnepal.org	Field Visit Section 1 Below
Dhading HRRP organized and participated in the Ward level meeting at ward 01, Jwalamukhi RM. The meeting was chaired by ward chief Mr. Ramprasad Silwal . Some key points and highlights in the meeting have been detailed in field visit section.	25 th March 2019			techcord.dhading@hrrpnepal.org	Field Visit Section 1 Below
Dhading HRRP organized and participated in the Ward level meeting at ward 03, Jwalamukhi RM. The meeting was chaired by ward chief Mr. Rudraman Shrestha .	25 th March 2019			techcord.dhading@hrrpnepal.org	Field Visit Section 1 Below

Summary of events during this period

A joint monitoring visit of DLPIU/Building, GMaLI Chief Rajendra K.C, Sachin Sapkota (HRRP-DTC), Rajesh Shrestha (DSE/NRA), Hariram Pathak (NSET/Baliyo Ghar) to Jyamire 09, Nilkhantha Municipality was conducted. The visit was focused on monitoring "On the Job Retrofitting Training" Program organized by NSET/BALIYO GHAR.	27 th March 2019			techord.dhading@hrrpnepal.org	Field Visit Section 2 Below
One day orientation program on resurvey and reverification to palika chief, representative and all the partner organisations working on reconstruction sector was conducted in DCC hall, Dhading organized by DLPIU Building	28 th March 2019			techord.dhading@hrrpnepal.org	Refer News & Update Section Below
Two-day orientation program on resurvey and reverification to technical group (Engineer, Sub-Engineer) working on reconstruction sector was conducted in DLPIU Building hall, Dhading organized by DLPIU Building	01 - 02 April 2019			techord.dhading@hrrpnepal.org	Refer News & Update Section Below
Joint field visit with CLPIU- M & E, DLPIU/building, GMaLI and HRRP team at Netrawati Rural Municipality and Nilkhantha municipality was conducted. The visit was focused on typology collection, non-compliance issues, identification of fake beneficiaries and palika/ward meeting.	01 - 04 April 2019			techord.dhading@hrrpnepal.org	Field Visit Section 3 Below
Dhading HRRP organized and participated in the Rural Municipality level meeting at Netrawati rural municipality. The meeting was chaired by rural municipality chairperson, Mr. Durga Narayan Shakya , GMaLI Finance Specialist, CLPIU M & E Khagendra Awasthi and Beneficiaries. Some key points and highlights in the meeting have been detailed in field visit section.	2 April 2019			techord.dhading@hrrpnepal.org	Field Visit Section 3 Below
HRRP District Technical coordinator updated MEAL report of Dhading and forwarded it to central HRRP	5 April 2019			techord.dhading@hrrpnepal.org	NA
Updated reconstruction action plan of Gajuri rural municipality has been uploaded to the rural municipality website.	5 April 2019			techord.dhading@hrrpnepal.org	NA



Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
District Coordination Meeting	22nd April 2019 on 2:00 PM. at DCC hall	HRRP	dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org
Public Hearing Program	12 th April 2019	TI Nepal	Sanubabu Timalisina


Tranche Status

Rural /Municipality	Beni Ghat Rorang RM	Dhuni Besi M	Galthi RM	Gangajamuna RM	Gajuri RM	Jwalamukhi RM	Khaniyabas RM	Netrawati RM	Nilkhanta M	Ruby Valley RM	Siddhalekh RM	Thakur RM	Tripurasundari Rm	Total
Total HHs Surveyed	5501	7499	6724	6732	5625	6014	3632	4016	13471	3270	5975	6722	6474	81655
Total HHs Eligible	4910	7158	5997	6447	5105	5390	3469	3866	12183	2850	5359	6384	5697	74815
Total HHs Enrolled	4435	6633	5676	6345	4696	4952	3413	3713	11671	2751	5055	6084	5571	70995
First Tranche	4435	6633	5676	6345	4696	4952	3413	3713	11671	2751	5055	6084	5571	70995
Second Tranche	3815	5097	5275	5944	4234	4020	3081	3465	10316	2429	4529	5189	5066	62460
Third Tranche	2910	3318	3277	4784	3088	3140	2293	2937	8079	1876	3553	3229	3590	46074
Total HH Constructed	2507	3177	2545	4252	2731	2848	1874	2782	7826	1615	3395	3419	3499	49470
Grievance Registered	1690	1067	1273	720	1427	2424	658	641	2394	650	1521	1310	1002	16777
Grievance Addressed	599	356	728	285	530	700	164	153	1374	420	640	341	785	7075
RF HH Eligible	618	98	314	42	432	675	12	43	559	187	463	255	215	3913
RF HH Enrolled	618	98	314	42	432	675	12	43	559	187	463	255	215	3913
RF 1 st Tranche	0	9	36	2	45	35	0	1	53	43	0	10	10	244
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	0	0	0	0	0
NC Registered	22	252	130	31	268	87	7	27	281	0	291	275	144	1815
NC Addressed	20	174	91	27	207	73	7	22	210	0	219	160	126	1336


Tranche Status

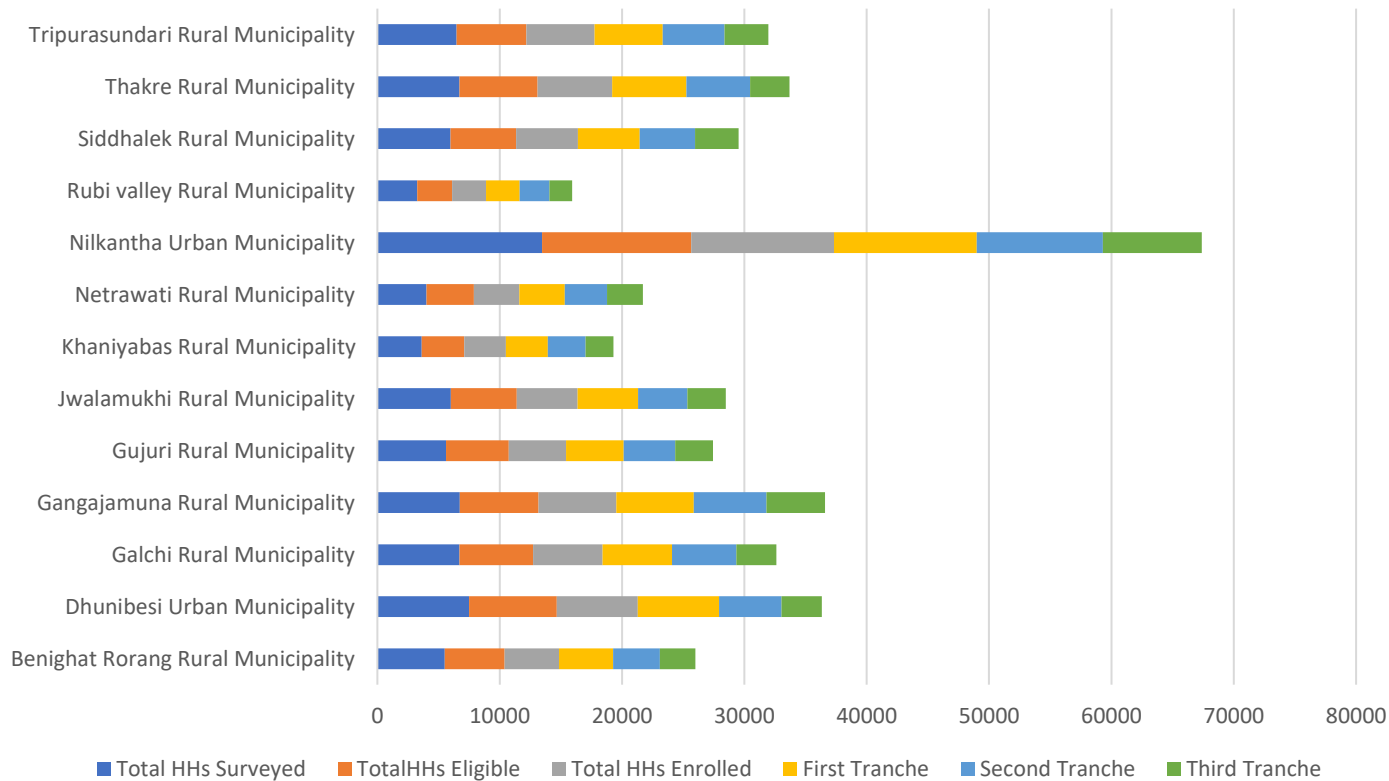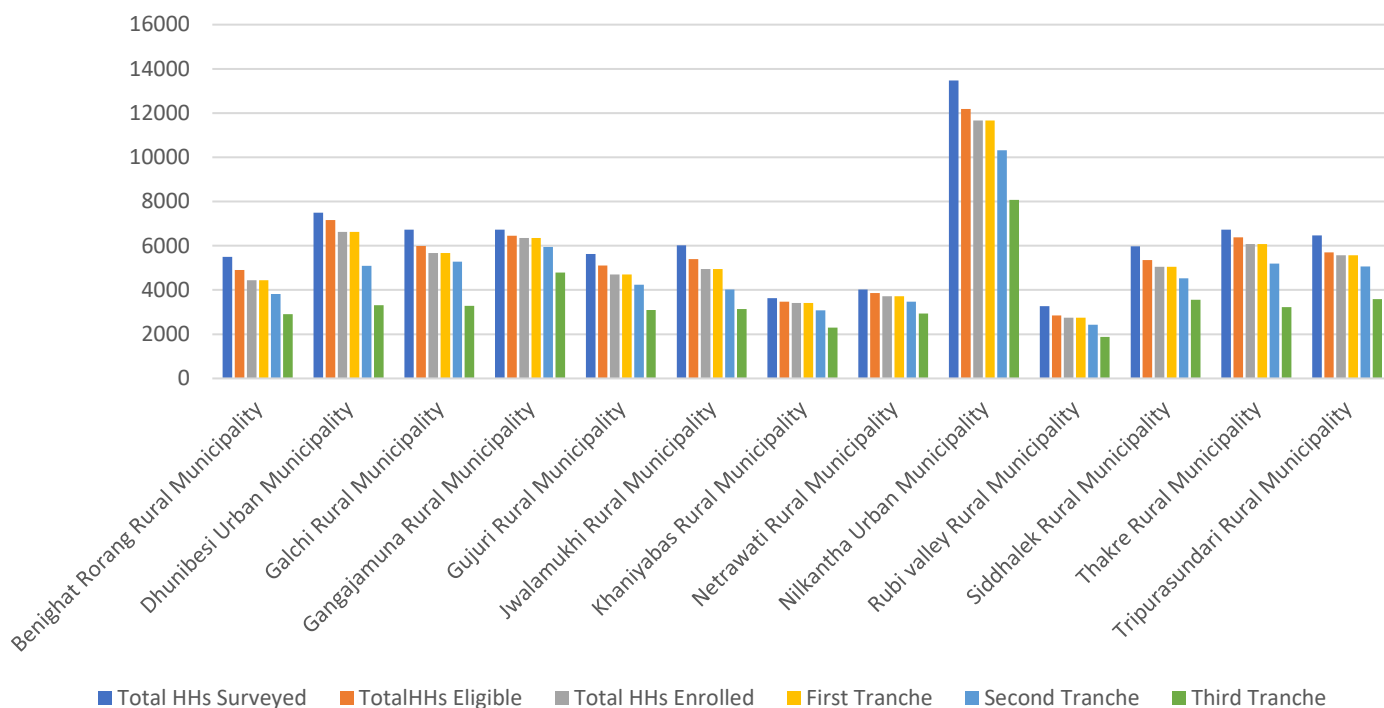


Total HH Constructed

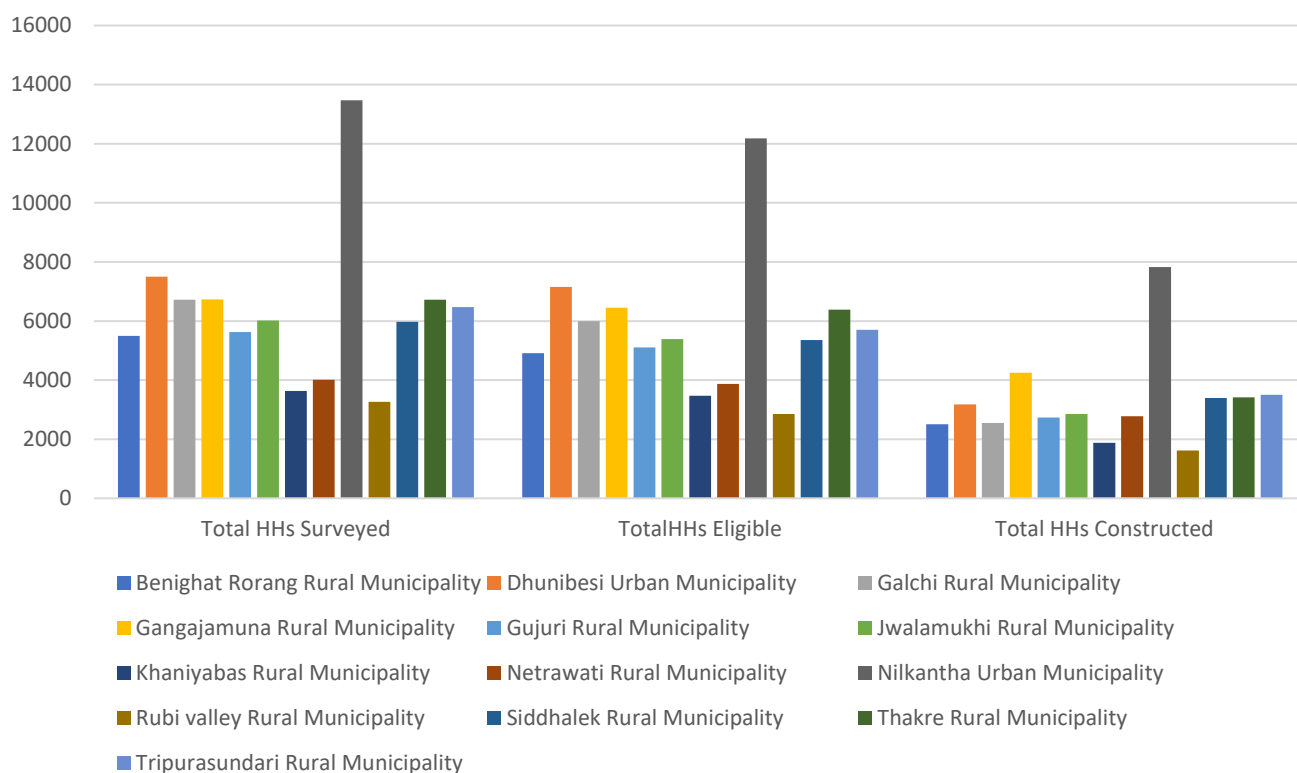




Palika wise Retrofitting Status :-

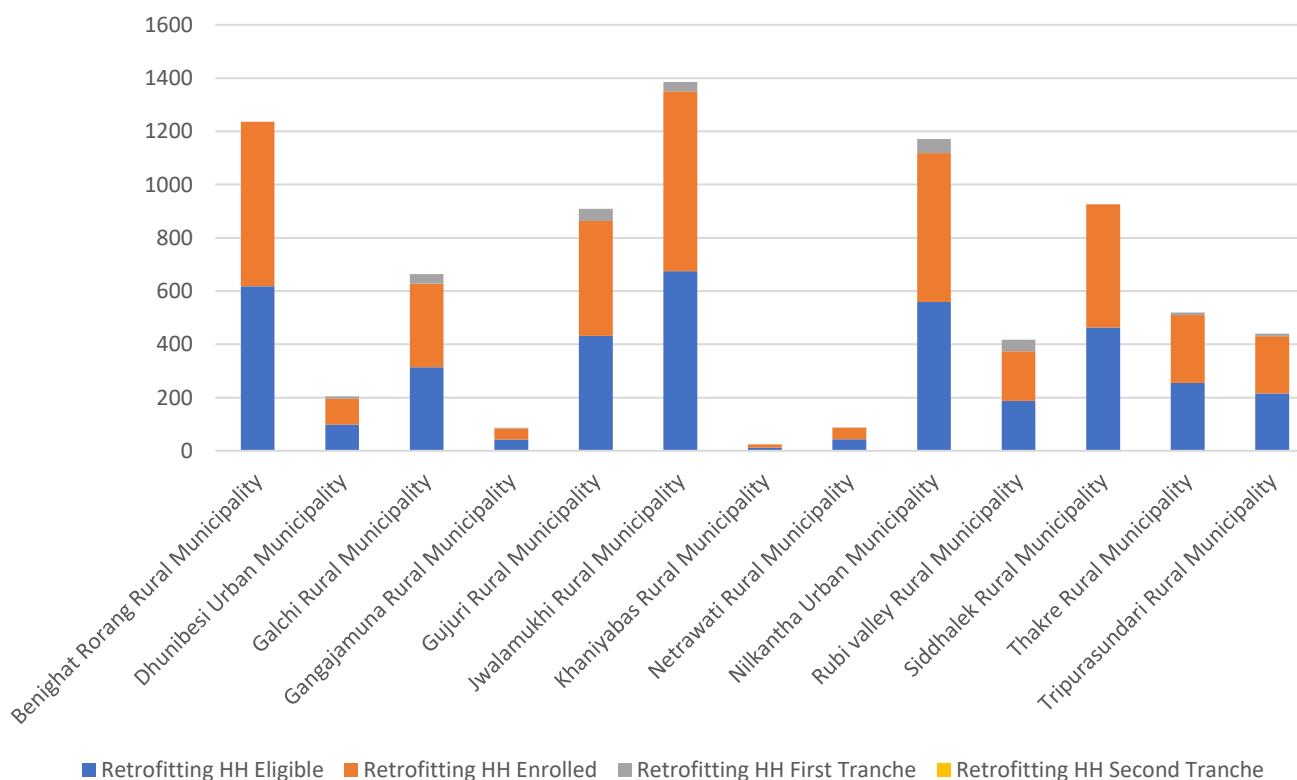

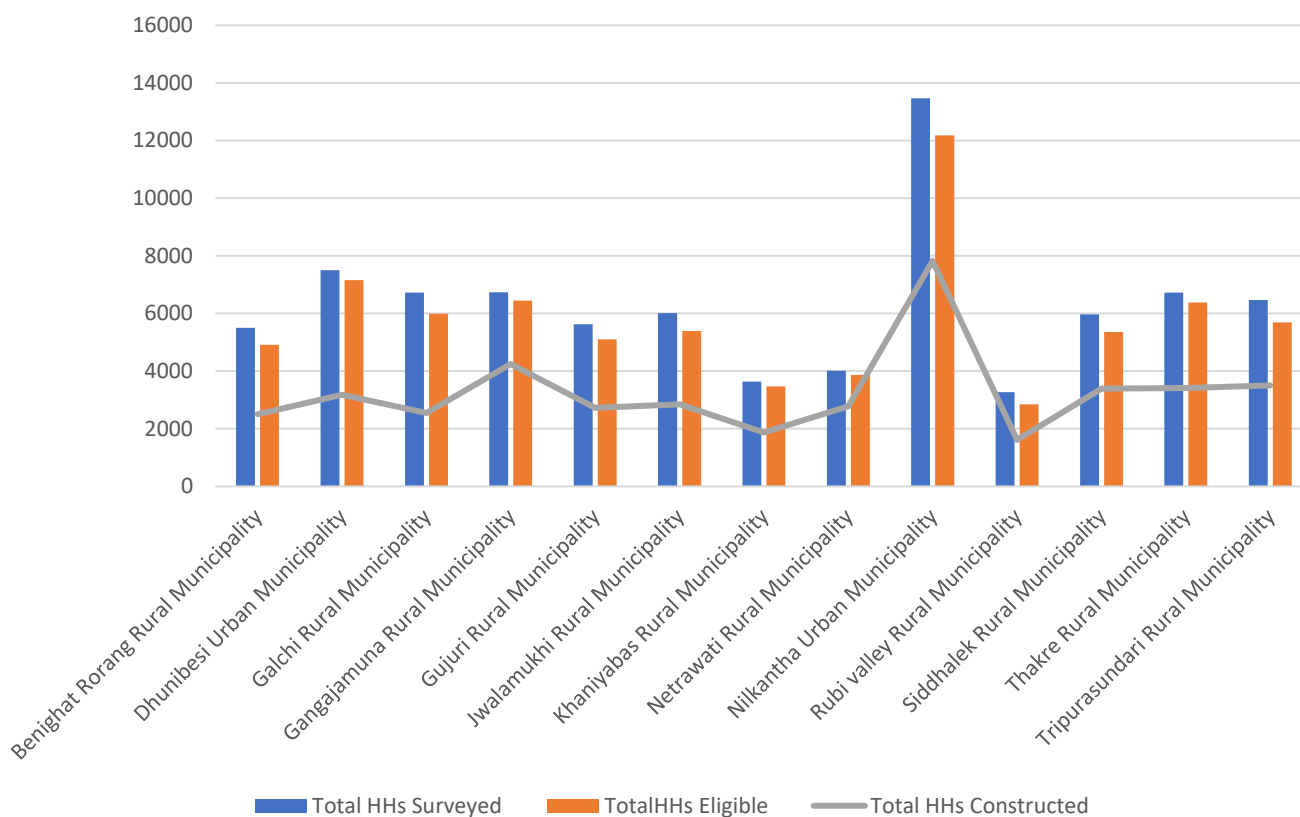

Grievance Status

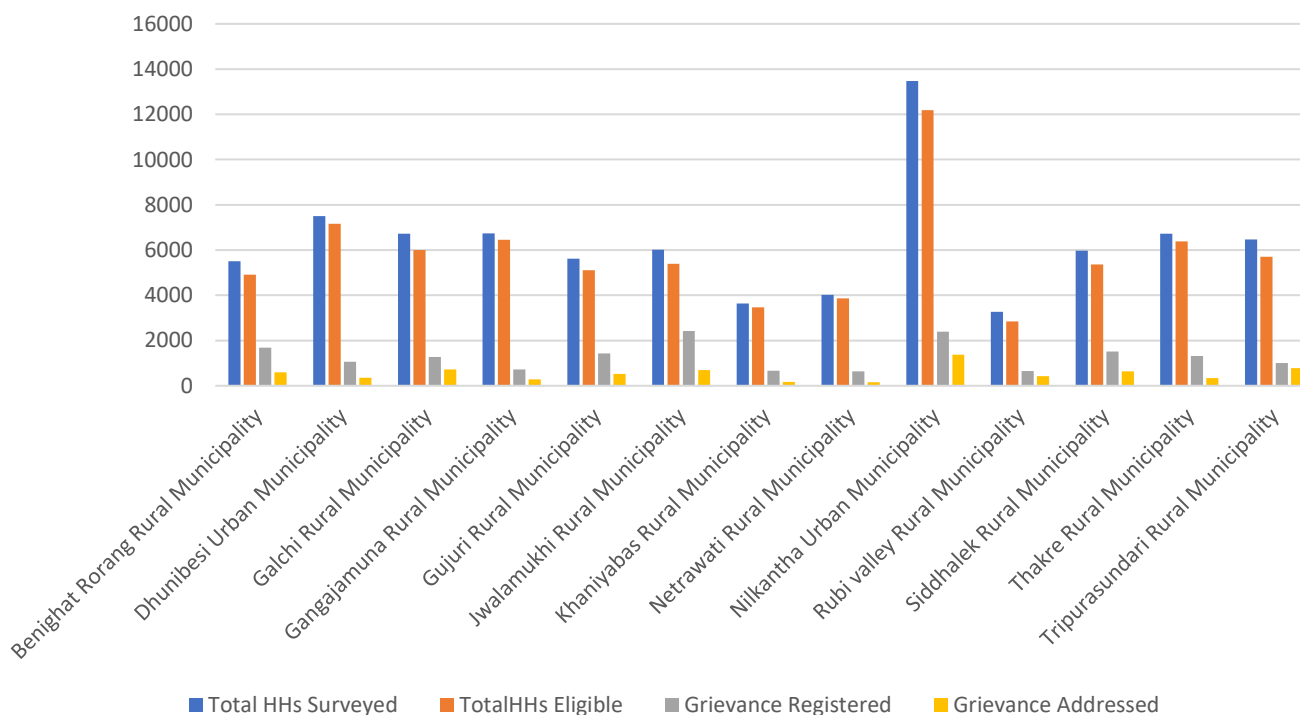

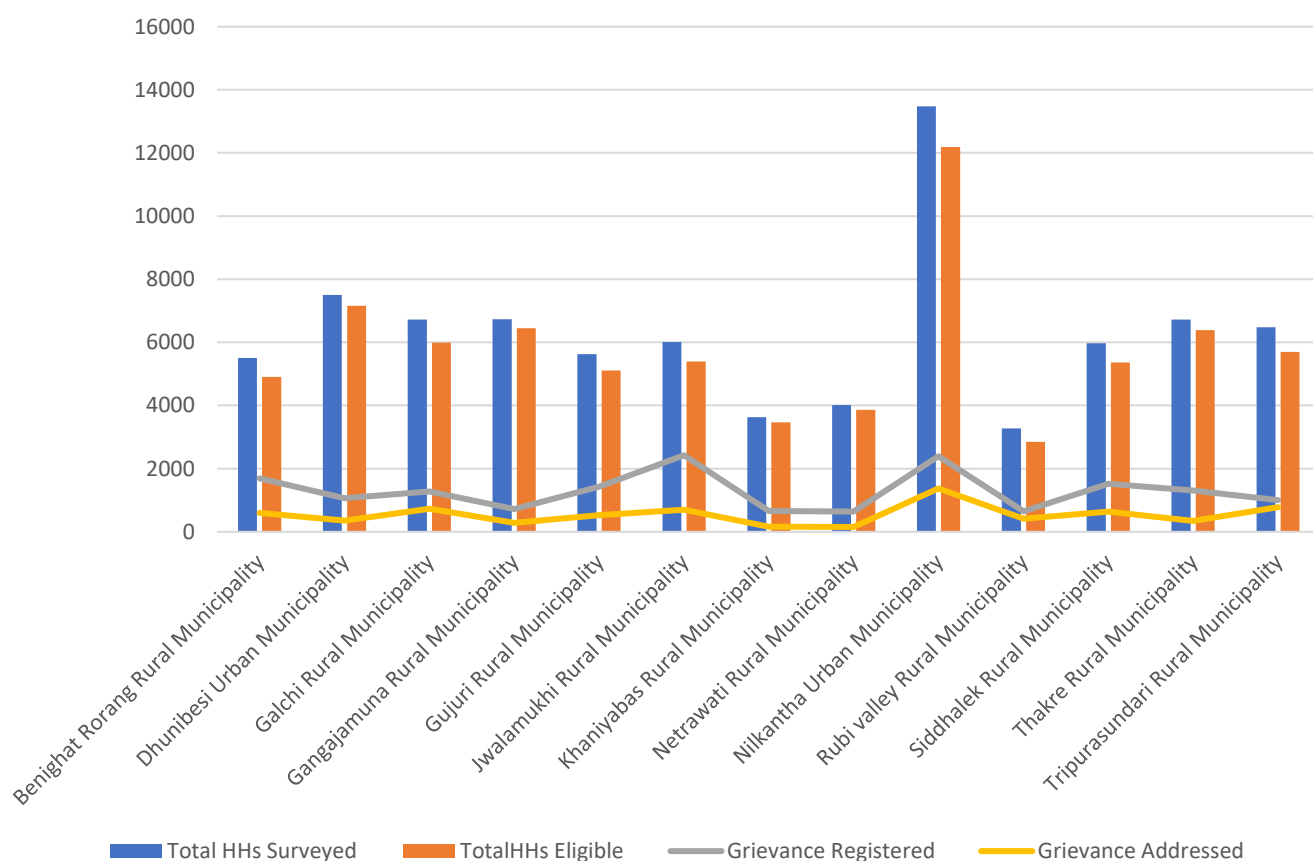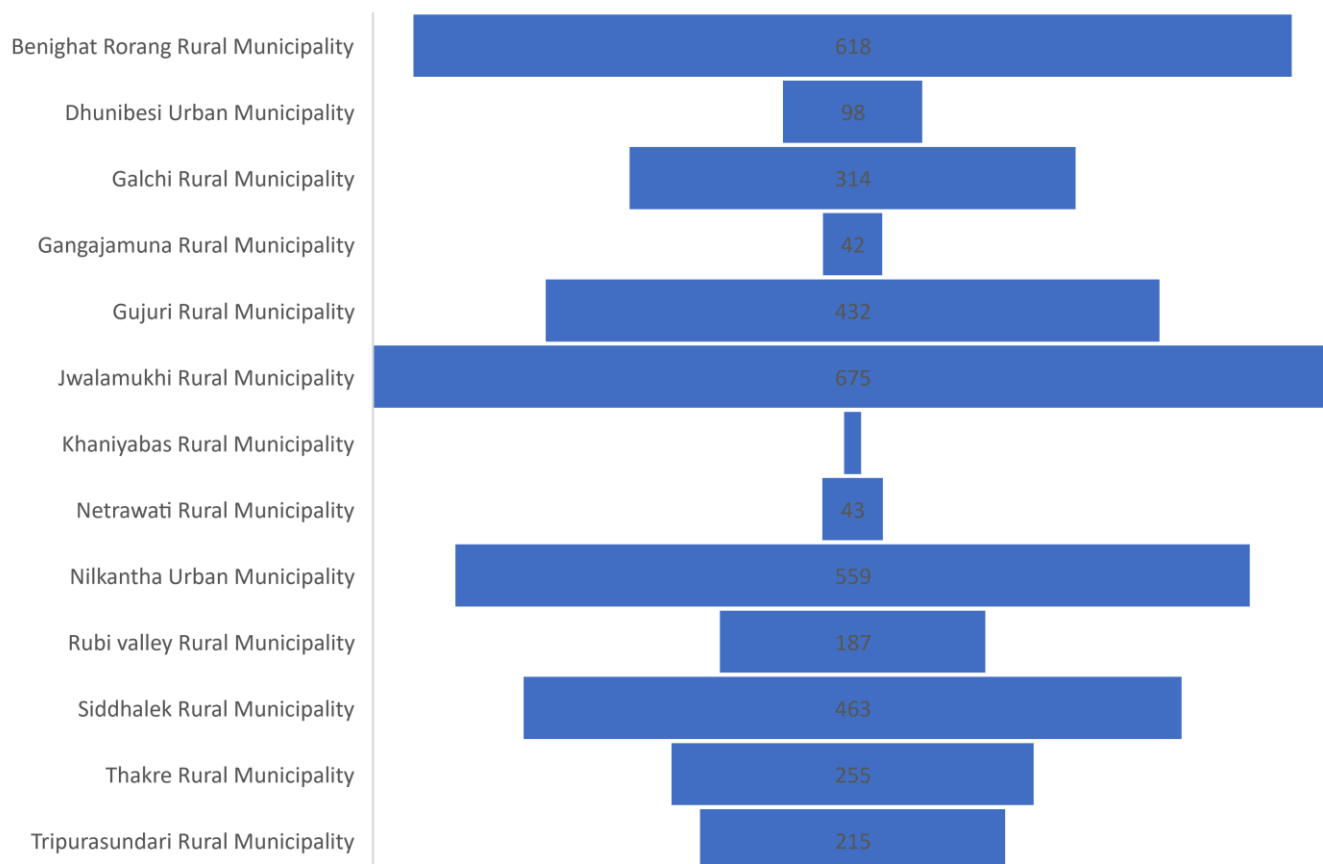

News & Updates

- 1) HRRP Dhading successfully completed Orientation on Hollow Concrete Block (HCB) Manual at RK Hotel, Dhading with 51 participants from NRA DLPIU and Partner Organizations.



- a) Participants in the orientation program on Hollow Concrete Block manual conducted in Dhading district.
- b) DTC Dhading, HRRP is conducting technical session on Hollow Concrete Block manual

[Link to GD Orientation Minute](#)

The orientation program was focused for the technical staffs deployed by DLPIU. The objective of the orientation was to disseminate knowledge on the HCB manual and how it will help the technical staffs during the inspection of the house being constructed using such blocks

The brief introduction to the Hollow Concrete Block structure, the background, objectives and content of the session along with its technical aspects, its applicability and construction practices were presented. Technical specifications for such shelter was discussed in brief.

- 2) The HRRP conducted District coordination meeting on 18th March 2019 at RK Hotel, Dhading

NRA DLPIU technical staff shared their experiences along with the discussion of non-compliance cases.

[Link to GD Meeting Minute](#)

- a) In SMRF (RCC)
 - Plan and elevation irregularities
 - Reinforcement in column < 8 nos. (4-16Ø+4-12Ø)
 - Room area > 13.5 sq. m.
 - Column spacing <2.1m & >4.5 m
 - One bay building
 - Column size <12"x12"
 - Aspect Ratio >3
 - Stepped footing

- b) In Load Bearing Structure (Masonry Building)
 - Horizontal and vertical reinforcement missing
 - Sill band, lintel band, roof band missing
 - Through stone or stitch band missing
 - Concrete blocks
 - Hybrid system
- 3) Dhading DLPIU Building organized one day orientation program on **Re-survey and Reverification** to palika chief, representative and all the partner organisations working on reconstruction sector on 28th March at DCC hall, Dhading Besi, Dhading.



Photo-Participants in the program on Re-survey & Re-verification conducted in Dhading district.

- 4) DhadingvDLPIU Building organized two-day orientation program on **Re-survey and Re-verification** to technical group (Engineer, Sub-Engineer) working on reconstruction sector on (1st & 2nd April) at Building hall, Dhading Besi, Dhading.



Photo-Participants in the program on Re-survey & Re-verification conducted in Dhading district.

5) Updates from Partner Organizations

- a) As reported by **NSET Baliyo Ghar** progress report 19,240 households were directly benefitted through technical assistance, 38,933 individuals were oriented through 1628 orientation events, 2508 existing masons were trained through 84 events, 10 mason TOT, 156 individuals were trained through 5 SM training, 33 Engineers and 19 Sub engineers were participated in Basic retrofit training, 458 Radio program has been broadcast from 2 different radio/Fm stations, 656 new mason were trained through 108 event by Baliyo Ghar and 1339 masons were trained 227 OJT.
- b) As reported by **Durable Solution** there are 388 cases for Reallocation out of which 220 are forwarded
- Land displaced = 12
 - Land Vulnerable = 183
 - Himdung cases = 76
 - Grievance = 112
 - **Grand Total = 388**
- c) Dhading CSRC organize certificate handover program to landless beneficiaries at DCC hall, Dhading Besi, Dhading. The program was chaired by deputy chief Binda Baramu and GMaLI Chief Mr Rajendra K.C with 30 nos of participants.



Photo-Participants (Beneficiaries) in the certificate handover program conducted in DCC hall, Dhading district.

Joint Field Visit Report

Visit 1

Date	Location	Participants from HRRP and stakeholders
25 th March 2019	Jwalamukhi Rural Municipality	- Sachin Sapkota (HRRP-DTC) - Binda Baramu (Deputy Chief-DCC) - Khagendra Awasti (CLPIU-M&E) - Laxmi Shrestha (GMALI-M&E) - Shalikram Ghimire (PIN-PC) - Anil Rijal (PIN)

Objective(s)

- To monitor different houses constructed during reconstruction technically assisted by "Hamro Ghar" of different ward of Juwalamukhi Rural Municipality

Summary

- A field visit was conducted at Jwalamukhi Rural Municipality in presence of Deputy Chief Binda Baramu regarding monitoring of houses constructed during reconstruction technically assisted by "Hamro Ghar"



Photo -Monitoring and observing houses technically supported by Hamro Ghar in presence of deputy chief Binda Baramu and Laxmi Shrestha.

The main objective of Hamro Ghar is to provide technical assistance, Coordination, Training and Awareness at Jwalamukhi Rural Municipality. Hamro Ghar has target to assist for 165 no of households where 10hhs are completed while 57hhs are running. Hamro ghar has support for material, manpower especially skilled mason and has also support for transportation cost. Hamro Ghar is also planning to conduct 42 days on the job training for mason in Jwalamukhi Rural Municipality.

- Replication of VDC by Pos
- Remoteness of district
- Grant driven construction rather than need based
- Dominate system by government
- Improper selection of mason for training.

डाल सिमि 2042 खास बोन 99 गो नमूनाहरूलाई 11/01/2023-2023 का दिन छल नमूनाहरूको सार्वजनिक अन्तर्गत नया नं. 9
 1. 2. 3. 4. 5. 6. 7. 8. 9. 10. 11. 12. 13. 14. 15. 16. 17. 18. 19. 20. 21. 22. 23. 24. 25. 26. 27. 28. 29. 30. 31. 32. 33. 34. 35. 36. 37. 38. 39. 40. 41. 42. 43. 44. 45. 46. 47. 48. 49. 50. 51. 52. 53. 54. 55. 56. 57. 58. 59. 60. 61. 62. 63. 64. 65. 66. 67. 68. 69. 70. 71. 72. 73. 74. 75. 76. 77. 78. 79. 80. 81. 82. 83. 84. 85. 86. 87. 88. 89. 90. 91. 92. 93. 94. 95. 96. 97. 98. 99. 100. 101. 102. 103. 104. 105. 106. 107. 108. 109. 110. 111. 112. 113. 114. 115. 116. 117. 118. 119. 120. 121. 122. 123. 124. 125. 126. 127. 128. 129. 130. 131. 132. 133. 134. 135. 136. 137. 138. 139. 140. 141. 142. 143. 144. 145. 146. 147. 148. 149. 150. 151. 152. 153. 154. 155. 156. 157. 158. 159. 160. 161. 162. 163. 164. 165. 166. 167. 168. 169. 170. 171. 172. 173. 174. 175. 176. 177. 178. 179. 180. 181. 182. 183. 184. 185. 186. 187. 188. 189. 190. 191. 192. 193. 194. 195. 196. 197. 198. 199. 200. 201. 202. 203. 204. 205. 206. 207. 208. 209. 210. 211. 212. 213. 214. 215. 216. 217. 218. 219. 220. 221. 222. 223. 224. 225. 226. 227. 228. 229. 230. 231. 232. 233. 234. 235. 236. 237. 238. 239. 240. 241. 242. 243. 244. 245. 246. 247. 248. 249. 250. 251. 252. 253. 254. 255. 256. 257. 258. 259. 260. 261. 262. 263. 264. 265. 266. 267. 268. 269. 270. 271. 272. 273. 274. 275. 276. 277. 278. 279. 280. 281. 282. 283. 284. 285. 286. 287. 288. 289. 290. 291. 292. 293. 294. 295. 296. 297. 298. 299. 300. 301. 302. 303. 304. 305. 306. 307. 308. 309. 310. 311. 312. 313. 314. 315. 316. 317. 318. 319. 320. 321. 322. 323. 324. 325. 326. 327. 328. 329. 330. 331. 332. 333. 334. 335. 336. 337. 338. 339. 340. 341. 342. 343. 344. 345. 346. 347. 348. 349. 350. 351. 352. 353. 354. 355. 356. 357. 358. 359. 360. 361. 362. 363. 364. 365. 366. 367. 368. 369. 370. 371. 372. 373. 374. 375. 376. 377. 378. 379. 380. 381. 382. 383. 384. 385. 386. 387. 388. 389. 390. 391. 392. 393. 394. 395. 396. 397. 398. 399. 400. 401. 402. 403. 404. 405. 406. 407. 408. 409. 410. 411. 412. 413. 414. 415. 416. 417. 418. 419. 420. 421. 422. 423. 424. 425. 426. 427. 428. 429. 430. 431. 432. 433. 434. 435. 436. 437. 438. 439. 440. 441. 442. 443. 444. 445. 446. 447. 448. 449. 450. 451. 452. 453. 454. 455. 456. 457. 458. 459. 460. 461. 462. 463. 464. 465. 466. 467. 468. 469. 470. 471. 472. 473. 474. 475. 476. 477. 478. 479. 480. 481. 482. 483. 484. 485. 486. 487. 488. 489. 490. 491. 492. 493. 494. 495. 496. 497. 498. 499. 500. 501. 502. 503. 504. 505. 506. 507. 508. 509. 510. 511. 512. 513. 514. 515. 516. 517. 518. 519. 520. 521. 522. 523. 524. 525. 526. 527. 528. 529. 530. 531. 532. 533. 534. 535. 536. 537. 538. 539. 540. 541. 542. 543. 544. 545. 546. 547. 548. 549. 550. 551. 552. 553. 554. 555. 556. 557. 558. 559. 560. 561. 562. 563. 564. 565. 566. 567. 568. 569. 570. 571. 572. 573. 574. 575. 576. 577. 578. 579. 580. 581. 582. 583. 584. 585. 586. 587. 588. 589. 590. 591. 592. 593. 594. 595. 596. 597. 598. 599. 600. 601. 602. 603. 604. 605. 606. 607. 608. 609. 610. 611. 612. 613. 614. 615. 616. 617. 618. 619. 620. 621. 622. 623. 624. 625. 626. 627. 628. 629. 630. 631. 632. 633. 634. 635. 636. 637. 638. 639. 640. 641. 642. 643. 644. 645. 646. 647. 648. 649. 650. 651. 652. 653. 654. 655. 656. 657. 658. 659. 660. 661. 662. 663. 664. 665. 666. 667. 668. 669. 670. 671. 672. 673. 674. 675. 676. 677. 678. 679. 680. 681. 682. 683. 684. 685. 686. 687. 688. 689. 690. 691. 692. 693. 694. 695. 696. 697. 698. 699. 700. 701. 702. 703. 704. 705. 706. 707. 708. 709. 710. 711. 712. 713. 714. 715. 716. 717. 718. 719. 720. 721. 722. 723. 724. 725. 726. 727. 728. 729. 730. 731. 732. 733. 734. 735. 736. 737. 738. 739. 740. 741. 742. 743. 744. 745. 746. 747. 748. 749. 750. 751. 752. 753. 754. 755. 756. 757. 758. 759. 760. 761. 762. 763. 764. 765. 766. 767. 768. 769. 770. 771. 772. 773. 774. 775. 776. 777. 778. 779. 780. 781. 782. 783. 784. 785. 786. 787. 788. 789. 790. 791. 792. 793. 794. 795. 796. 797. 798. 799. 800. 801. 802. 803. 804. 805. 806. 807. 808. 809. 810. 811. 812. 813. 814. 815. 816.

- a) Need to support the vulnerable beneficiaries
- b) Need of supports for grievance handling.
- c) Delay in tranche release and files missing at DLPIUs.
- d) Non-compliance cases; most of them constructed immediately after earthquake and difficulty in encouraging the beneficiaries to carry on the correction measures as suggested by DSE.



Photo -Ward level meeting in presence of deputy chief Binda Baramu, ward chief, PIN, GMALI, DLPIU Building and HRRP.

- 3) Similarly, HRRP conducted ward level meeting at ward 03, Jwalamukhi Rural Municipality in presence of deputy chief of DCC and Palika ward chief **Mr Rudra Man Shrestha**, on 25th March 2019. The meeting was focused on reconstruction burning issues, challenges and support & presence of NGO/INGO.

The common points discussed in the meeting were:

- Some of individuals are still not registered through grievance process and this delay of result publication from NRA has caused misunderstandings among community and palika/ward office.
- A discussion was made regarding distribution of completion certificates to those ward beneficiaries where reconstruction is high.
- Need to support the vulnerable beneficiaries
- Delay in tranche release and files missing at DLPIUs.

| Challenges / Issues Identified | Action Required | Responsible | Timeframe |
|---|--|--|---------------------|
| Remove names of beneficiaries not willing to reconstruct their homes from reconstruction list | Need to collect the names of those beneficiaries who are not willing to reconstruct their home due to various reasons and forward it to GMALI with all the relevant documents for name removal | Ward offices, municipalities and GMALI | As soon as possible |

Housing Typology Report



Name: - Kal Kumari Rana Magar
Location: - Amrai 03, Jwalamukhi Rural Municipality
It is one storey load bearing structure with material used burned brick with cement mortar, its floor area is less than 1000 sqft. The beneficiary has received 2nd tranche of government grants.



Name: - Laxman Sarki
Location: - Ward 04, Jwalamukhi Rural Municipality
It is one storey load bearing, its floor area is less than 1000 sqft. The beneficiary has received 1st tranche of government grants.



Name: - Lok Bahadjur Gharti
Location: - Ward 03, Jwalamukhi Rural Municipality
It is one storey load bearing structure with material used burned brick with cement mortar, its floor area is less than 1000 sqft. The beneficiary has received 1st tranche of government grants.



Name: - Sanu Pariyar
Location: - Devasthan, Jwalamukhi Rural Municipality
It is one storey load bearing structure with material used burned brick with cement mortar, its floor area is less than 1000 sqft. The beneficiary has received 2nd tranche of government grants.



Name: - Pun Shrestha
Location: - Ward 03, Jwalamukhi Rural Municipality
It is one storey load bearing structure with material used burned brick with cement mortar, its floor area is less than 1000 sqft. The beneficiary has received 2nd tranche of government grants.

Joint Monitoring Field Visit Report

Visit 2

| Date | Location | Participants from HRRP and stakeholders |
|------|----------|---|
|------|----------|---|

| | | |
|-----------------------------|---|---|
| 27 th March 2019 | Jyamire ward -09
Nilkhantha Municipality | <ul style="list-style-type: none"> • Rajendra K.C (GMaLI Chief) • Sachin Sapkota (HRRP-DTC) • Rajesh Shrestha (NRA-DSE) • Hariram Pathak (NSET/Baliyo Ghar) |
|-----------------------------|---|---|

Objective(s)

- To monitor "On the Job Training" Program organized by NSET/BALIYO GHAR.
- Housing typology observation and collection.
- Interaction with ward beneficiaries on housing reconstruction issues and collection of success stories.

Summary

- 1) A field visit was conducted at ward 09, Nilkhantha Municipality in presence of GMaLI chief **Mr Rajendra K.C** regarding monitoring of retrofitting stone masonry in mud mortar house supported by "BALIYO GHAR".



Photo: Two storey stone masonry in mud mortar load bearing structure using Splint and bandage along with Galvanized wire during retrofitting supported by NSET BALIYO GHAR.

NSET BALIYO GHAR is mainly working on co-ordination and providing training & Awareness in Dhading. NSET is working as a Blanket technical assistance on different municipality of Dhading district. Recently NSET is providing support on RETROFITTING, has a target of 25 house where 2 are completed and 3 are running in different vdc of Dhading.



House Owner: - Min Kumari Gurung

It is a two storey stone masonry in mud mortar load bearing structure with CGI sheet light roofing. NSET BALIYO GHAR analyze & design this building for simple retrofitting concepts. They provide Splint and Bandages for global failure while Galvanized wire mesh for local failure with 20 mm plaster both sides. The total cost for retrofitting this building is Rs 2,50,000.00. NSET will provide Approx. Rs 1,70,000.00 (Material support + Labor support + Tools & Equipment).



Photo -Monitoring and observing Galvanized wire mesh in presence of GMAI Chief Mr Rajendra K.C and DSE Mr. Rajesh Shrestha

Joint Field Visit Report

Visit 3

| Date | Location | Participants from HRRP and stakeholders |
|--------------------|--|--|
| 01 - 04 April 2019 | (Dhuwakot, Khalte)
Nilkhantha Municipality &
(Katunje, Semjong, Marpak)
Netrawati Rural Municipality. | <ul style="list-style-type: none"> Sachin Sapkota (HRRP-DTC) Khagendra Awasti (CLPIU/building-M&E) Ananda Raj Pandey (GMAI) Sudip Shrestha (NRA-DSE) |

Objective(s)

- Discussion on status of reconstruction.
- Housing typology observation & collection.
- Interaction with ward beneficiaries on housing reconstruction issues.
- Identification of fake beneficiaries.
- Collection of case stories.
- Ward level Meeting
- Palika Level Meeting

Summary

A joint field visit with CLPIU/Building, HRRP, DLPIU Building and GMAI was conducted during 01 -04 April 2019 at (Dhuwakot, Khalte) Nilkhantha Municipality & (Katunje, Semjong, Marpak) Netrawati Rural Municipality. The field level visit was focused on private housing progress of these palikas where different designs of NRA volume I and II were found. It was found that many organizations have been supporting with technical assistance at these localities. They have provided engineers and social mobilizer at the ward to support beneficiary's issues and address in coordination with rural municipality and ward office.



Photo: Palika level coordination meeting at Netrawati Dabjong Rural Municipality

The chief of palika, Mr. Durga Kumar Shakya mentioned that plaika's reconstruction rate has speeded up and it seems that only few beneficiaries are remained to reconstruct their houses.

Some of the major points of discussion are as follows:

- Service provided by Bank to palika Beneficiary
Individuals registered under NRA beneficiary list who are illegible to receive government grant support amount are being delayed from bank for a long duration.
- Victims who have not been listed under beneficiary list from NRA
Individuals who are being left behind to be registered under NRA beneficiary list are deprived of the support for reconstruction, thus palika would like to request NRA to support it to reverify and register those individuals (real victims) as soon as possible.
- Support to establish Bank services at preferred locality for beneficiary
Palika wanted to allow reliable banks to establish its branches at an appropriate locality to facilitate beneficiary with its services so that government tranche amount could be received at convenient manner.

Meeting Minute

आज मिति २०७२ साल चैत्र महिनाको १९ गते भैरवती गाउँपालिकाको
विभिन्न घरहरूको अनुगमन तथा निरीक्षण गरियो। पुनर्निर्माण
सोपानका छेउक सम्पन्न गरियो र हस्तान्तरण ब्यौजाको अन्तर्गत
गरियो।

१) शुक्रपुर्ण पछि लोड र योजनीय तहका प्राविधिकहरू खरिद। पुन
अजोड शुक्रपुर्ण पछि तहका स्वयंसेवक निम्ता गरियो। निम्ति
अध्यासहरूको विपरीत पढाइमा आवश्यक हाथ पढाइ गरि
यथावत उपलब्ध गराइने अनुरोध गरियो।

२) विभिन्न प्राविधिक समूहको योग्य हलफल गरि आवश्यक
सल्लाह, छुट्याइ दिइयो।

१) ह्या कृष्ण शास्त्री - अध्यक्ष - 
२) विनय शास्त्री - कार्यकारी अधिकृत - 
३) रवीन्द्र अधिकारी - MAE (CLPJV) - 
४) आनन्द लाल पाण्डे - FS (NRA/OLJV) - 
५) सत्यदेव श्रेष्ठ - JSE (NRA) - 
६) सचिन सायकीराल - HRRP (GIC) - 

३) अहिले पनि आसन्न घर भन्ने भएका लाभग्राहि को अनुगमन
सुझाई नहुदा गाउँपालिकाको आसन्नको ठुलो समस्या भएको
र यसलाई अघि बढाएर तथा पुनर्निर्माण कार्यक्रमको
द्वितीय चरणमा छिटो हुन गरील शान्ति कार्यक्रमको अधिकतम
ले आफ्नो क्षमता बढाउन अनुरोध गरियो।

४) प्रबलिकाको लाभग्राहि निकै नै कम रहेको र प्रबलिकाको
आनन्दको लागि नैसर्गिकको पाइयो। प्रबलिकाको आनन्दको
लाभग्राहिमा आनन्दको लागि छिटो बढाउन अनुरोध गरियो।

Housing Typology Report



Name: - Manu Paudel
Location: - Borang 02 Marpak, Netrawati Rural Municipality
It is Hybrid structure building with material used Stone with cement mortar in ground floor and light timber structure in first floor, its floor area is less than 1000 sqft. The beneficiary has received all tranches of government grants.



Name: - Ratna Bahadur Thapa
Location: - Borang 02 Marpak, Netrawati Rural Municipality
It is Hybrid structure building with material used Stone with cement mortar in ground floor and light timber structure in first floor, its floor area is less than 1000 sqft. The beneficiary has received all tranches of government grants.



Name: - Sirjana Paudel
Location: - Borang 02 Marpak, Netrawati Rural Municipality
It is Hybrid structure building with material used Stone with cement mortar in ground floor and light timber structure in first floor, its floor area is less than 1000 sqft. The beneficiary has received all tranches of government grants.



Name: - Dip Bahadur Adhikari
Location: - Borang 02 Marpak, Netrawati Rural Municipality
It is a one storey load bearing structure with material used brick with cement, its floor area is less than 1000 sqft. The beneficiary has received all tranches of government grants.

Case Story

Durga Kumar Shakya chair-person of Netrawati Dabjong Rural Municipality, Dhading Monthly Salary: 31,000 Rupees. Key Functions: coordinating with other local levels, calling meetings of the assembly & executive body, tabling agenda in the meeting, assigning responsibilities to deputy chief or members.



Durga Kumar Shakya elected from people having several duties i.e. overseeing fixed and moveable assets of the local level, concluding performance contract with concerned authorities, coordinating with other local levels, provinces and federal government, preparing monthly progress report, monitoring activities of national and international non-governmental organizations, preparing budget and determining price of construction materials, among other things. Despite of being several duties shakya is keen on to complete reconstruction this year. He says that it is very challenging task to reconstruct houses rapidly with limited source, manpower, knowledge and fund. However, Netrawati Dabjong Rural Municipality has completed more than 60% of reconstruction.

At the very beginning stage of reconstruction there was no any policy, system, action, administration, guidelines, management and methods due to which reconstruction was scrambled. Later we came to power where situation was worse, every people comes to us with high faith thinking that they have full authority to do anything.



In my case when I was here I had mainly faced the problem of Grievance. There are many real beneficiaries whose house were damaged during earthquake 2072 but still were not able to register as reconstruction beneficiaries which creates huge problem to elected bodies. But every problem comes with solution NRA has announced re-survey and re-verification which will solve the problem of Grievance.

As reported by Shakya there are many problems in reconstruction: Unavailability of NRA engineers at field level, Insufficient door to door technical Assistance, NRA lengthy approval process, challenge in transportation of construction materials at most of the areas of Dhading, High number of non-compliance houses, Lack of monitoring of trained masons at their locality, Bank issues.
