

Fortnightly District Report

Kathmandu Valley

18 - 31 January 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Joint monitoring visit of DLPIU-Building Kathmandu and HRRP Kathmandu valley team was conducted in Kirtipur Municipality, Kathmandu District	22 Jan 2019	2	4	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
The general ward level coordination meeting was conducted at Ward no. 2, Devdhoka, Kirtipur Municipality, Kathmandu.	22 Jan 2019	2	4	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
Joint monitoring visit of DLPIU-Building Bhaktapur and HRRP Kathmandu valley team was conducted in Changunarayan Municipality, Bhaktapur District	23 Jan 2019	2	6	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org	
The general ward level coordination meeting was conducted at Ward no. 11, Ikachhen, Lalitpur Metropolitan City, Lalitpur district	24 Jan 2019	4	3	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
Joint monitoring visit of DLPIU-Building Kathmandu and HRRP Kathmandu valley team was conducted in Kirtipur Municipality, Kathmandu District	22 Jan 2019	2	4	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
The general ward level coordination meeting was conducted at Ward no. 2, Devdhoka, Kirtipur Municipality, Kathmandu.	22 Jan 2019	2	4	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
Joint monitoring visit of DLPIU-Building Bhaktapur and HRRP Kathmandu valley team was conducted in Changunarayan Municipality, Bhaktapur District	23 Jan 2019	2	6	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org	
The general ward level coordination meeting was conducted at Ward no. 11, Ikachhen, Lalitpur Metropolitan City, Lalitpur district	24 Jan 2019	4	3	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org	
General coordination meeting of DLPIU NRA GMAI and DLPIU Building Bhaktapur was conducted. Chief of DLPIU NRA GMAI and DLPIU Building facilitated the coordination meeting in presence of staffs	24 Jan 2019	18	27	Er. Narakanta Sapkota M & E Consultant Bhaktapur and Kathmandu district CLPIU NRA Building aashrayasap@gmail.com	

Summary of events during this period

of DLPIUs (GMAI/Building) Bhaktapur, Technical staffs deployed in 4 municipalities of Bhaktapur district, HRRP Kathmandu valley team and District Support Engineer. The key highlights of the coordination meeting were –				Contact: 9851090721	
➤ EHRP project/DLPIU GMAI Bhaktapur will prepare environment and social safeguard management plan of Suryabinayak and Changunarayan Municipality. ➤ 30-40 % debris is still found in haphazard condition in various parts of Bhaktapur district. The debris clearance must be given priority for the beneficiaries to be able to reconstruct the houses. ➤ There are many cases of BMC/masonry structures that can be addressed by correction and exception measures to be eligible for the government grant. ➤ Madhyapur Thimi Municipality has received large number of cases related to changing from full damage to retrofitting list. ➤ Non-compliance cases of 9"x12" column is still prevalent in Suryabinayak and Changunarayan Municipality. ➤ Beneficiaries are adding extra storey other than the building permit due to which the non-compliance cases have been increasing.					
Ward-level interaction program with the ward representatives and beneficiaries in Chaughare, Ward no 1, Konjyosom Rural Municipality.	28 Jan 2019	75	20	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org	
The general ward level meeting was conducted at Ward no. 5, Bhardeu, Konjyosom Rural Municipality, Lalitpur.	28 Jan 2019	2	2	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org	
Ward-level interaction program with the Ward representatives and beneficiaries in Chandanpur, Ward no 5, Mahankal Rural Municipality.	29 Jan 2019	32	4	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org	
Upload of training database, update of contact list along with 5 W update	18-31 Jan. 2019			Ms. Manisha Rai IM Officer HRRP Kathmandu Valley im.ktm@hrrpnepal.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Joint Monitoring visit of DLPIU-Building and HRRP Kathmandu Valley team to observe the ongoing reconstruction in Kathmandu Valley	1 st - 3 rd week of February 2019	HRRP Kathmandu valley team	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org
Municipality level and Ward level Coordination meeting to be conducted by HRRP Kathmandu Valley team in coordination with concerned Municipalities of Kathmandu valley	1 st - 3 rd week of February 2019	HRRP Kathmandu valley team	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409
Collection of few case studies of poor and extremely vulnerable beneficiaries from selected locations inside Kathmandu Valley	1 st - 3 rd week of February 2019	HRRP Kathmandu valley team	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409
Coordination with the Municipalities of Kathmandu, Bhaktapur and Lalitpur district to upload the Municipality profile in their respective profile.	1 st - 3 rd week of February 2019	HRRP Kathmandu valley team	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409

News & Updates

- With the announcement of returning the 1st tranche from beneficiaries who are uninterested to reconstruct the earthquake damaged houses, municipalities across the three districts of valley are receiving requests to change from the full damage house to retrofitting list. For example- From Ward locations of Madhyapur Thimi Municipality, large number of requests of shifting full damage house to retrofitting list were filed in reconstruction unit. Number of such request's ranges from 40 households up to 200 households.
- In Bhardeu, ward no 5, Konjyosom Rural Municipality about 240 beneficiaries under retrofitting have requested to change to full damage beneficiaries list. The ward office has prepared the necessary documents and the files are ready to be forwarded to GMaLI office, Lalitpur. Most of the houses under retrofitting are load bearing stone in mud mortar/ brick in mud mortar.

Tranche Update

Kathmandu Reconstruction Update as of 15 Jan 2019

Rural /Municipality	Kageshwori NP	Kathmandu MNP	Kirtipur NP	Gokarneshwor NP	Chandragiri NP	Tokha NP	Tarkeshwor NP	Dakshinkali NP	Nagarjun NP	Budhanilkant ha NP	Shankharapur NP
Total HHs Eligible	3667	7496	2935	2935	5695	1746	6151	4085	4338	2693	6058
Total HHs Enrolled	3279	5973	2475	2523	5041	1579	5191	3784	4106	2056	5545
First Tranche	3306	5958	2459	2517	4986	1550	5160	3755	4102	2056	5510
Second Tranche	1605	1336	893	1267	1367	612	1659	1254	1331	951	2175
Third Tranche	906	1042	709	1001	977	465	1354	816	1024	711	1501
Total HH Constructed	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Grievance Registered	N/A	N/A	1275	1962	1291	369	2493	1096	851	547	1665
Grievance Addressed	N/A	N/A	208	1158	695	335	2186	753	545	308	340
RF HH Eligible	75	173	44	20	128	48	107	52	38	11	110
RF HH Enrolled	23	30	16	7	46	25	33	29	4	2	40
RF 1st Tranche	23	30	16	7	46	25	33	29	4	0	40
RF 2nd Tranche	0	0	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Non-Compliance Addressed	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A




Bhaktapur Reconstruction Update as of 24 Jan 2019

Rural /Municipality	Bhaktapur NP	Changunarayan NP	Madhyapur Thimi NP	Suryabinayak NP
Total HHs Eligible	7622	10937	2333	7416
Total HHs Enrolled	5596	9680	2052	6955
First Tranche	5596	9680	2052	6955
Second Tranche	1528	2758	604	2252
Third Tranche	1354	2624	567	2141
Total HH Constructed	N/A	N/A	N/A	N/A
Grievance Registered	1592	2096	2407	1926
Grievance Addressed	1542	1692	1431	1665
RF HH Eligible	148	212	101	233
RF HH Enrolled	39	85	56	97
RF 1st Tranche	39	85	56	97
RF 2nd Tranche	0	0	0	0
Non-Compliance Registered	N/A	N/A	N/A	N/A
Non-Compliance Addressed	N/A	N/A	N/A	N/A




Lalitpur Reconstruction Update as of 15 Jan 2019

Rural /Municipality	Lalitpur MPC	Godawari UM	Mahalaxmi UM	Mahankal RM	Bagmati RM	Konjyosom RM
Total HHs Eligible	3370	9588	7350	2154	3657	2267
Total HHs Enrolled	3051	7895	6297	2042	3056	2230
First Tranche	3039	7804	6297	2041	3031	2228
Second Tranche	2245	2228	1123	1646	741	1599
Third Tranche	1539	1727	675	1128	613	866
Total HH Constructed	N/A	N/A	N/A	N/A	N/A	N/A
Grievance Registered	2809	N/A	863	549	882	919
Grievance Addressed	865	N/A	795	294	658	484
RF HH Eligible	281	325	90	61	252	372
RF HH Enrolled	119	66	16	43	58	253
RF 1st Tranche	119	66	16	43	58	253
RF 2nd Tranche	0	0	0	0	0	0
Non-Compliance Registered	N/A	N/A	N/A	N/A	N/A	N/A
Non-Compliance Addressed	N/A	N/A	N/A	N/A	N/A	N/A



Graph of Reconstruction Status in Kathmandu as of 15 Jan 2019:

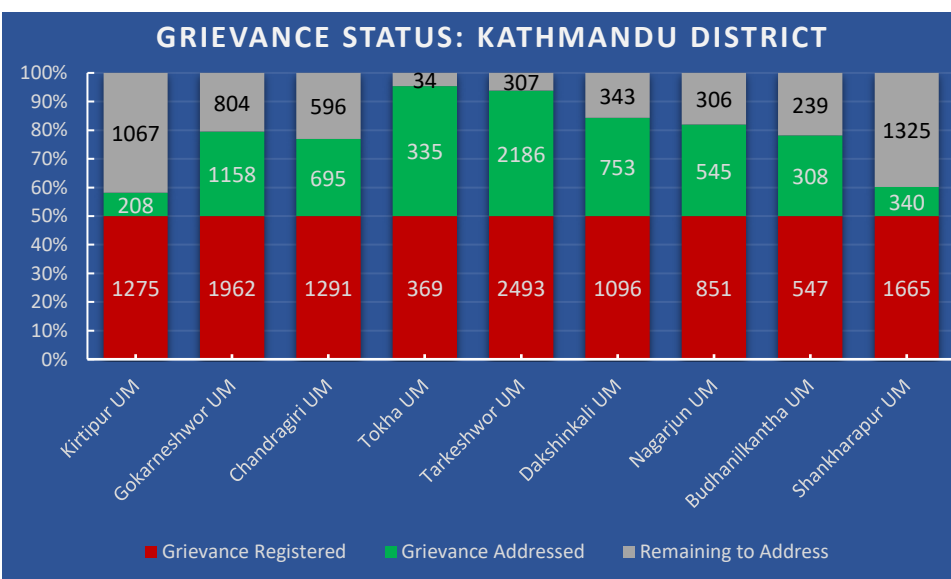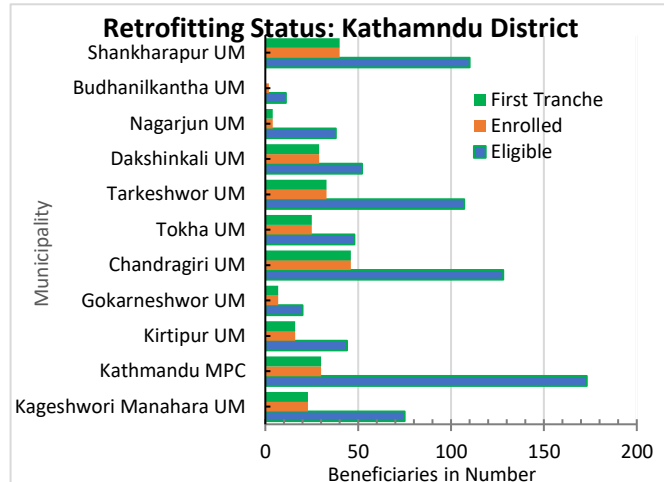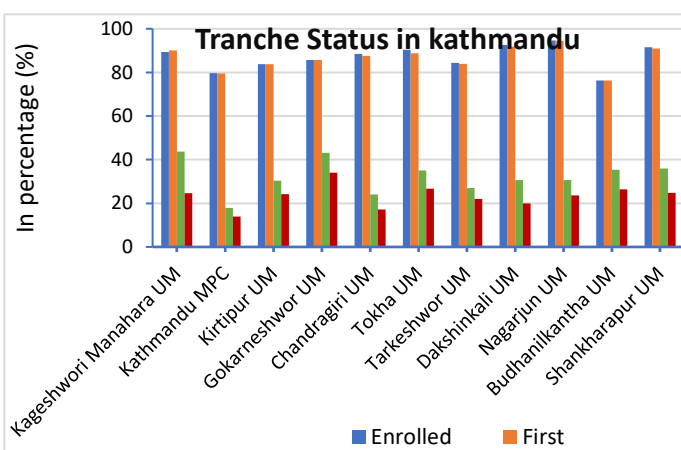


Bhaktapur Reconstruction Update as of 24 Jan 2019

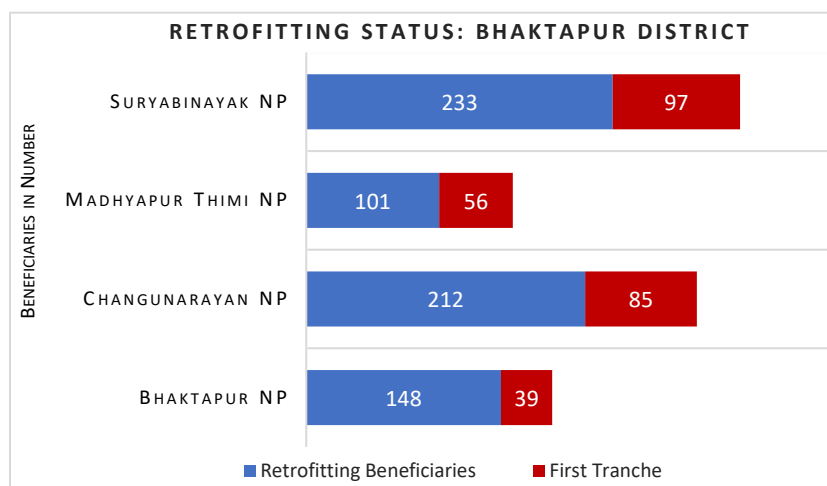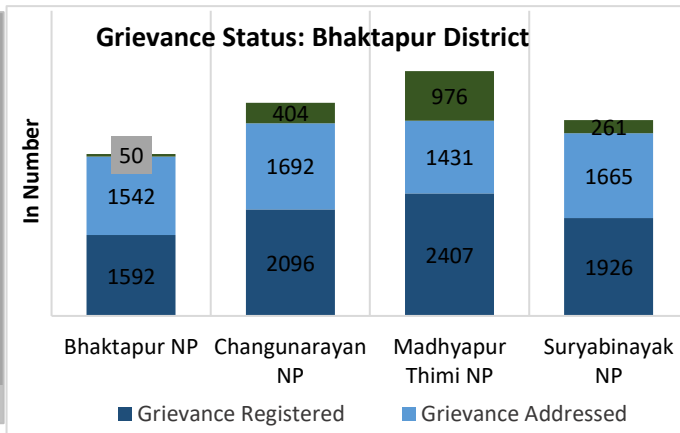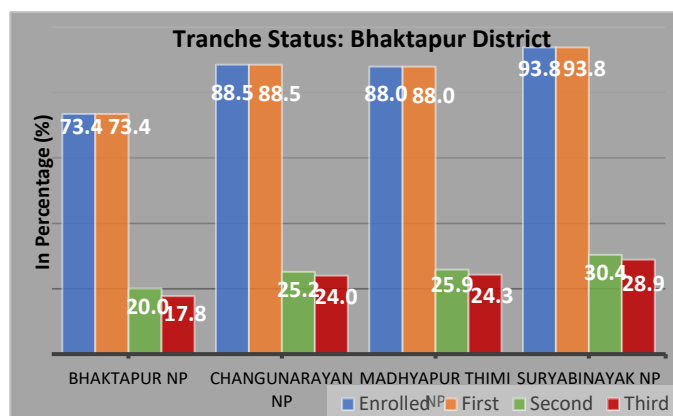

Lalitpur Reconstruction Update as of 15 Jan 2019

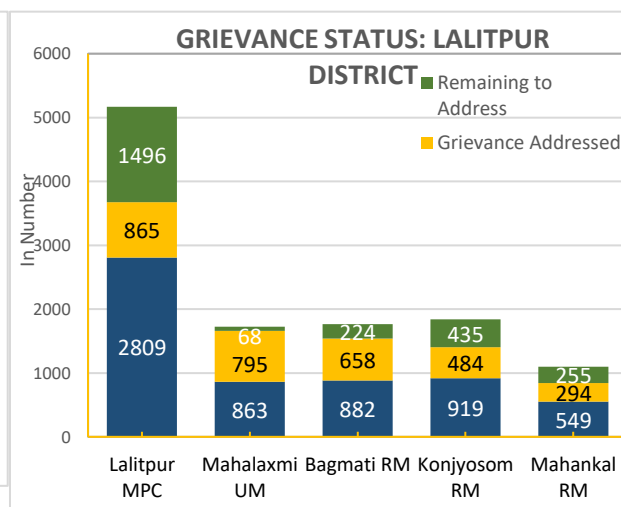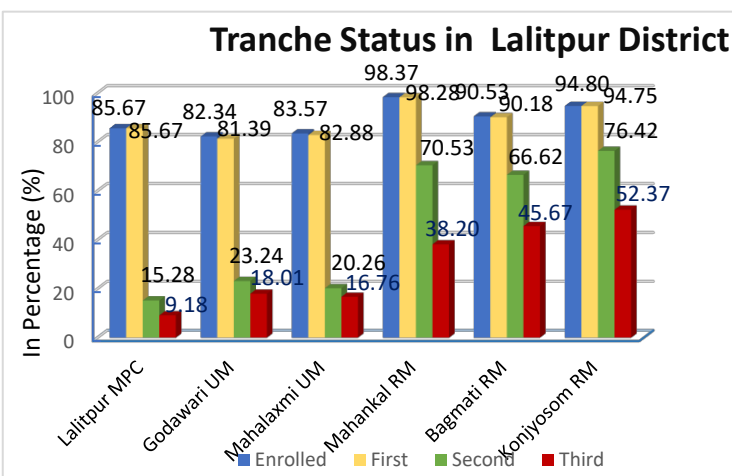

RETROFITTING STATUS: LALITPUR DISTRICT

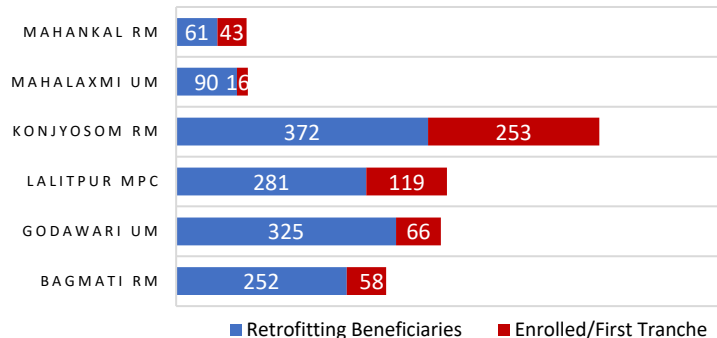

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Visit 1

Date	Location	Participants from HRRP and stakeholders														
22 January 2019	Ward no. 2, 4, 5, 8 of Kirtipur Municipality Ward no. 14 of Kathmandu Metropolitan City	- Ambika Amatya, District Coordinator, HRRP Kathmandu Valley - Narakanta Sapkota, M & E Consultant, CLPIU NRA Building - Bidhya Manandhar, District Support Engineer, DLPIU Building Kathmandu - Prajwol Karki, District Support Engineer, DLPIU Building Kathmandu - Sabi Shrestha, Engineer, Kirtipur Municipality - Sunita Maharjan, Engineer, Kirtipur Municipality														
Objective(s)	- To observe the houses in reconstruction phase, cross check non-compliance structure and suggest the possible correction measures. reconstruction status of the beneficiaries. - To provide inputs to the beneficiaries in regarding the technical assistance.															
Summary	HRRP Kathmandu valley team along with the M & E Consultant from CLPIU Building and team members from DLPIU Building, Kathmandu office conducted joint M & E visit in selected ward areas of Kirtipur Municipality (Ward no. 2, 4, 5, 8) and at Ward no. 14 of Kathmandu Metropolitan City. Devdhoka Ward no. 2, Jwaladevi, Ward no. 4 and panga, Ward no. 8 is one of the core urban ward of Kirtipur Municipality where housing reconstruction has increased after the announcement of the latest deadlines from NRA. Many households have taken 1st tranche and has applied for 2nd and 3rd tranche together. A ward level coordination meeting was conducted with Mr. Ramesh Maharjan, Ward Chief, Ward no.2, Devdhoka, Kirtipur Municipality. <table><tr><th colspan="2">Tranche update of Ward no. 2</th></tr><tr><td>Total Beneficiaries</td><td>93</td></tr><tr><td>PA enrolled</td><td>79</td></tr><tr><td>1st tranche</td><td>73</td></tr><tr><td>2nd tranche</td><td>22</td></tr><tr><td>3rd tranche</td><td>15</td></tr><tr><td>Grievance</td><td>48</td></tr></table> A total of 16 houses were observed by the joint M & E team. Majority of observed RCC houses have received 2nd tranche but 3rd tranche is pending due to addition of storey other than mentioned in the building drawing,		Tranche update of Ward no. 2		Total Beneficiaries	93	PA enrolled	79	1st tranche	73	2nd tranche	22	3rd tranche	15	Grievance	48
Tranche update of Ward no. 2																
Total Beneficiaries	93															
PA enrolled	79															
1st tranche	73															
2nd tranche	22															
3rd tranche	15															
Grievance	48															

further the houses hasn't followed minimum requirements. The key reconstruction issues that were observed during the visit in Ward no. 2, 4, 5 and 8 are as follows:

- very small land parcel (problem of core area)
- multiple beneficiaries residing in same households in smaller units and on multiple storey without any legal documents of land ownership.
- beneficiaries receive building permit from municipality for reconstruction up to 3 storey in single bay RCC house but addition of storey continues up to 5th floor.
- houses were found to have missed addition of columns and bands too.

Special building typologies - one house was made using steel post (composite structure) in each corner whereas concrete blocks are used to construct the wall; few observed houses were made by blocks with truss roof and another house was made by using gypsum board.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
Addition of extra storey than mentioned in approved building drawing increases threat to the resiliency of houses and of neighbors too.	There should be a strong mechanism to cross check the houses that have added extras storey. Already constructed houses can either demolish the added storey or apply retrofitting measures. Houses under current reconstruction phases should be strictly monitored and should sign commitment paper about not adding storey.	Municipality, ward office, DLPIU engineers	As soon as possible

Photos



Beneficiary name: Chandra Maharjan, Ward no. 1, Hwakacha Tole, Kirtipur Municipality. Single bay, 5 storey house of RCC – C category house has received building permit upto 3rd storey only but have added extra 2 storey which has posed threat to the house. The house has received up to 2nd tranche and 3rd tranche is pending till now.



Beneficiary name: Radhakrishna Bista, Ward no. 5, Bista Gaun, Kirtipur Municipality. Single storey house is made of gypsum board (a light weight material) with steel windows and 5 rooms in total. The house has area exceeded and received up to 2nd tranche whereas the 3rd tranche is on hold.



Beneficiary name: Kiran Singh, Ward no. 2, Devdhoka, Kirtipur Municipality. The proposed 4 storey RCC house including basement, is in reconstruction phase. The owner has received 1st tranche and got temporary building permit to reconstruct the house.

The damaged 4 storey BMM house of Ward no. 2, Devdhoka, Kirtipur Municipality belongs to two people, among which one house owner was listed as beneficiary and has received 1st tranche whereas another was addressed by the grievance and is now listed as beneficiary. The beneficiaries had land ownership paper from land revenue office but it's under their name. Each house has 4 rooms.

Visit 2

Date	Location	Participants from HRRP and stakeholders
23 Jan 2019	Ward no. 2, 3 and 4, Changunarayan Municipality	- Narakanta Sapkota, M & E Consultant/ DLPIU NRA-Building - Prabesh Adhikari, DSE, Bhaktapur - Sweata Sijapati, District Technical Coordinator, HRRP Kathmandu Valley Team - Radha Sadh, Engineer, DLPIU, Bhaktapur - Salina Shrestha, Engineer, Changunarayan Municipality, Bhaktapur - Manita Shrestha, Engineer, Changunarayan Municipality, Bhaktapur - Samjhana Rijal, Changunarayan Municipality, Bhaktapur - Kripa Adhikari, Engineer, DLPIU Bhaktapur
Objective(s)	- To observe the non-compliance structure and suggest the possible correction measures. reconstruction status of the beneficiaries. - To provide inputs to the beneficiaries in regarding the technical assistance.	
Summary	HRRP Kathmandu valley team along M & E Consultant from DLPIU NRA Building conducted joint field monitoring at Ward no 2, 3 and 4 of Changunarayan Municipality, Bhaktapur district. The field visit was mainly focused on the observation of the Non-compliance cases and beneficiaries claiming for the 2nd and 3rd tranches in the area. The visit was accompanied by the DSE who suggested the possible correction measures and way forward to the beneficiaries for being eligible for the tranche. In total 13 houses were visited among which majority of the houses had 9"X12" column in more than 2 storey structure and were found unsafe after the structural analysis. Similarly, the other non -compliance case was load bearing structure will larger floor area, 10" masonry wall in two storey structure, larger opening area in load bearing masonry and so on. One case in ward no. 4, Pokhrel gaun of Changunarayan Municipality was visited where the beneficiary had reconstructed house in a landslide risk area. House of Ms. Bhawani Damai is structurally complaint and eligible for 2nd and 3rd tranche but due to the landslide risk the house is at potential threat.	

Challenges / Issues Identified	Action Required	Responsible	Timeframe
Municipality has been approving the design and giving building permit to RC structure with 9"X12" pillar size for 3 storey and more which is found to be unsafe during the structural analysis.	As per MRT the 12"X12" column so Technical staffs of Municipality should not promote such construction practice and disapprove such houses.	Municipality, DLPIU-Building, CLPIU-Building	As soon as possible
Houses in Pokhrel Gaun, ward no. 4 are directly under risk of landslides.	Municipality, DLPIU-GMaLI and NRA should look on the issue and find a way forward to prevent the landslide risk.	Municipality, DLPIU-GMaLI and NRA	

Photos



Beneficiary Name: Laxman Aaganja, ward no 3, Changunarayan Municipality, Bhaktapur. The beneficiary has requested for 2nd and 3rd tranche but the structure was found to be non-compliance. 3 and half storey RC frame structure with 9"X12" column. The structure was found to be unsafe by the structural analysis conducted by the DSE. At present the file cannot be forward for the tranche.



Beneficiary Name: Tulsi Das Sulu, ward no 3, Changunarayan Municipality, Bhaktapur. The beneficiary has requested for 2nd and 3rd tranche but the structure was found to be non-compliance. One storey load bearing brick in cement mortar masonry structure with 2 rolling shutter and larger opening area. The beneficiary was suggested to remove the shutters and construct wall to be eligible for the remaining tranche.

Housing Typology Report



Beneficiary name: Bhimsen Shrestha, Ward no. 8, Pakhure, Nagarjun Municipality, single storey load bearing BMC structure with CGI roof. The beneficiary has requested for 2nd and 3rd tranche together.



Beneficiary name: Gangaram Baskota, ward no 8, Pakhure, Nagarjun Municipality, single storey load bearing BMC structure with rigid roof. Beneficiary has requested 2nd and 3rd tranche together

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Who will take the liability of unusual mishaps as some of the reconstruction engineers are found deployed in Planning Unit of Kirtipur Municipality?	DLPIU engineer	Deploying reconstruction engineers in other works of municipalities is against norms of the MOU between NRA and local bodies that mentions about mobilizing engineers in reconstruction works only. This issue will be taken too CLPIU Building. (M & E Consultant, DLPIU Building Kathmandu)
What will happen to the houses that are reconstructed immediately after earthquake without any technical assistance?	Beneficiary	In case of the houses built immediately after the earthquake without any technical assistance, beneficiaries should consult with the engineers to find the possible measures to be eligible for the government tranche. If the engineers have advised for correction measures for such houses, then beneficiaries should put to make the houses technically compliance. These cases will also be shared to the central level to find a way forward. (M & E Specialist EHRP/DLPIU NRA GMaLI, Lalitpur)

Challenges and Way Forward

Challenge	Way Forward
Some of the DLPIU deployed engineers of Kirtipur Municipality are being performing works in Planning Unit. This issue is against the MOU between NRA and local bodies that mentions about mobilizing engineers in reconstruction works only.	The concerned municipality should review and revisit the MOU that is conducted between NRA and local bodies (dated 4 th Poush 2075) during Kathmandu district reconstruction review meeting. DLPIU deployed engineers should be deployed in reconstruction works only as per the MOU.
The tranche status of houses that were reconstructed before the NRA guidelines are affecting the reconstruction rate within Kathmandu Valley.	Concerned district reconstruction agencies should proactively consult with elected bodies and beneficiaries for applying

Challenges and Way Forward

Challenge	Way Forward
	corrective measures of houses that were rebuilt soon after earthquake without any technical assistance.

Case story

Case story 1

Gyanu Gole, 45 years old married women lives with her 7 family members in Ward no. 5, Chandanpur, Mahankal Rural Municipality. Her husband works as driver in Kathmandu and visits Chandanpur sometimes. Due to 2015 Gorkha Earthquake, her old load bearing SMM house was severely damaged. She along with her other extended family members and relatives were forced to live on temporary shelters for long. After she signed PA agreement with NRA/GON with 1st tranche in hand, she along with her husband started reconstructing the house nearly one year back. She also received approved building permit to rebuild her house. She found a well-trained local mason to rebuild her SMM, single storey, 2 roomed structure with attic. She revealed that she has clearly watched the reconstruction phase of her house and has maintained well equipped toilet too. The trained mason has properly kept all the earthquake resistant elements such as lintel, sill and roof band along with vertical reinforcements in corners and openings. When she applied for 2nd tranche and 3rd tranche, the engineers came to inspect her house time to time. As a result, she was successful in receiving all the tranches from GON/NRA. She revealed that a total of NPR 14 lakh was spend in reconstructing this house.



Case story 2

Bhawani Damai, resident of Pokhrel Gaun, Ward no. 4, Changuarayan Municipality was directly affected by the 2015 Gorkha earthquake. She was listed under beneficiary list for the government grant for the reconstruction. She used to stay with her in-laws in the house which was damaged by the earthquake. As per the government grant process, she reconstructed her house in small plot of land that was under her name after the division of the family property. She constructed 4 roomed one storey RC frame structure which was found compliance during the monitoring visit of team of M&E consultant, District Support Engineer, HRRP Kathmandu Valley and Engineers from DLPIU-Building.



Ms. Bhawani Damai in front of her newly constructed one storey RC structure which is at risk of landslide.

Ms. Damai has family of 6 members including her disabled father-in-law. She earns her living from sewing cloths along with her son. For the reconstruction of the house she has taken loan from people in her community and claims that she has spent around 11 lakhs in the construction. The reconstructed house was in slightly slope area. During the rainy season of 2018 the continuous rainfall loosened the soil in the slope which consequently resulted in the landslide on the morning of July 12, 2018. The landslide swept away the part of the hills nearby exposing the house to edge of the hill.

Ms. Damai has been going to ward office, Municipality to request for the support from the government for the implication of the landslide preventive measures in the area. GMaLI Bhaktapur has also visited the site and has noted down the issue. GMaLI chief, Mr. Durba Gaida has assured that GMaLI will support in all possible way and will discuss the issue with Municipality and NRA.

Ms. Damai says that she is scared that in upcoming rainy season her house will also be swept away. She said “Whenever there is rain, I can’t sleep and keep think what if my house is swept away by the landslide. If I lose this house, I will be drowned in loan and will be left without any place to stay. I will lose everything that I have worked so hard for my entire life.”

At present she is living in a temporary shelter constructed in a public land near by her house. Not only Ms. Damai house but the other 5 houses in the vicinity are at potential threat of landslide.



The newly constructed house of Ms. Bhawani Damai which has been brought on the edge of the hill after the landslide of July 2018.
