

Fortnightly District Report

Sindhupalchok

18 – 31 January 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
Joint Monitoring Field Visit of Panchpokhari Thangpal RM and coordination meeting at ward No.7, Bhotenamlang	22 nd Jan 2019	7	0	im.sindhupalchok@hrrpnepal.org	GD link to the meeting minutes
Joint Monitoring Visit of Panchpokhari Thangpal RM and coordination meeting at ward No -3, Bhotang	23 rd Jan 2019	7	1	im.sindhupalchok@hrrpnepal.org	GD link to the meeting minutes
Joint Monitoring Field Visit of Panchpokhari Thangpal RM and Coordination meeting at Ward No. 5, Gunsa	23 rd Jan, 2019	6	1	im.sindhupalchok@hrrpnepal.org	GD link to the meeting minute
Sindhupalchok District Coordination Meeting, Chautara	31 st Jan, 2019	15	2	im.sindhupalchok@hrrpnepal.org	GD link to the meeting minutes

Upcoming Events & Meetings


Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Joint Monitoring Visit of Jugal RM	6 th Feb 2019 – 8 th Feb 2019	HRRP	Pranjal Bhandari, Binod Sah and Roshan Kesari

Tranche Status


Rural /Municipality	Balefi RM	Barhabise Mun	Bhotekoshi RM	Chautara sangachok gadhi Mun	Helambu RM	Indrawati RM	Jugal RM	Lisankhu Pakhar RM	Melamchi NP	Panch pokhari Thangpal RM	Sunkoshi RM	Tripura Sundari RM
Total HHs Surveyed												
Total HHs Eligible	6043	7811	4214	13961	5348	8301	5585	5213	13325	7030	5616	4554
Total HHs Enrolled	5958	7702	4050	13763	5158	8087	5556	4756	13112	6681	5554	4437
First Tranche	5958	7700	4033	13775	5148	8055	5555	4751	13106	6679	5553	4436
Second Tranche	5593	6934	3198	12811	4392	7328	5235	3811	11403	5279	4947	4085
Third Tranche	4836	4809	1418	11023	3420	5147	3439	2521	7341	2924	4050	3081
Total HH Constructed												
Grievance Registered	1240	2490	1150	3513	1333	2421	1260	2269	2557	2937	1127	930
Grievance Addressed	464	683	439	1512	306	638	285	973	761	1273	682	448

RF HH Eligible	24	72	68	95	45	37	14	39	105	16	31	19
RF HH Enrolled	5	18	8	33	6	7	5	4	5	0	8	5
RF 1 st Tranche	5	18	8	33	6	7	5	4	5	0	8	5
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	0	0	0
Non-Compliance Registered												
Non-Compliance Addressed												


Graph of Tranche Status:

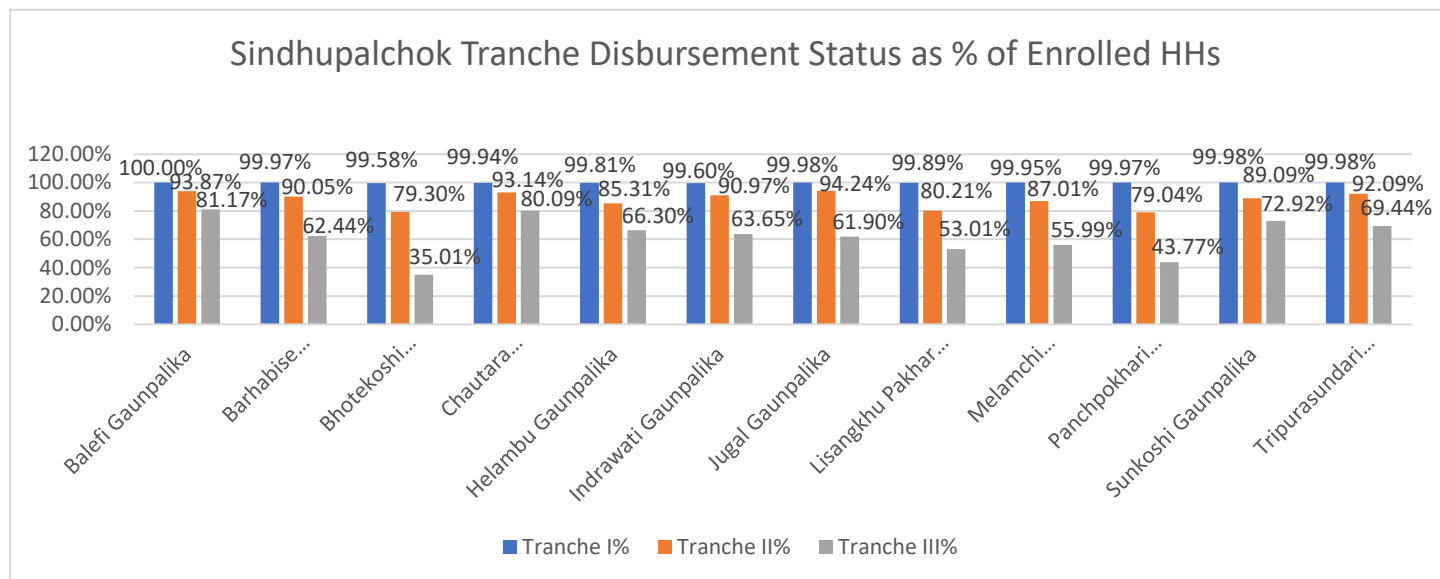

Graph for Retrofitting Status:

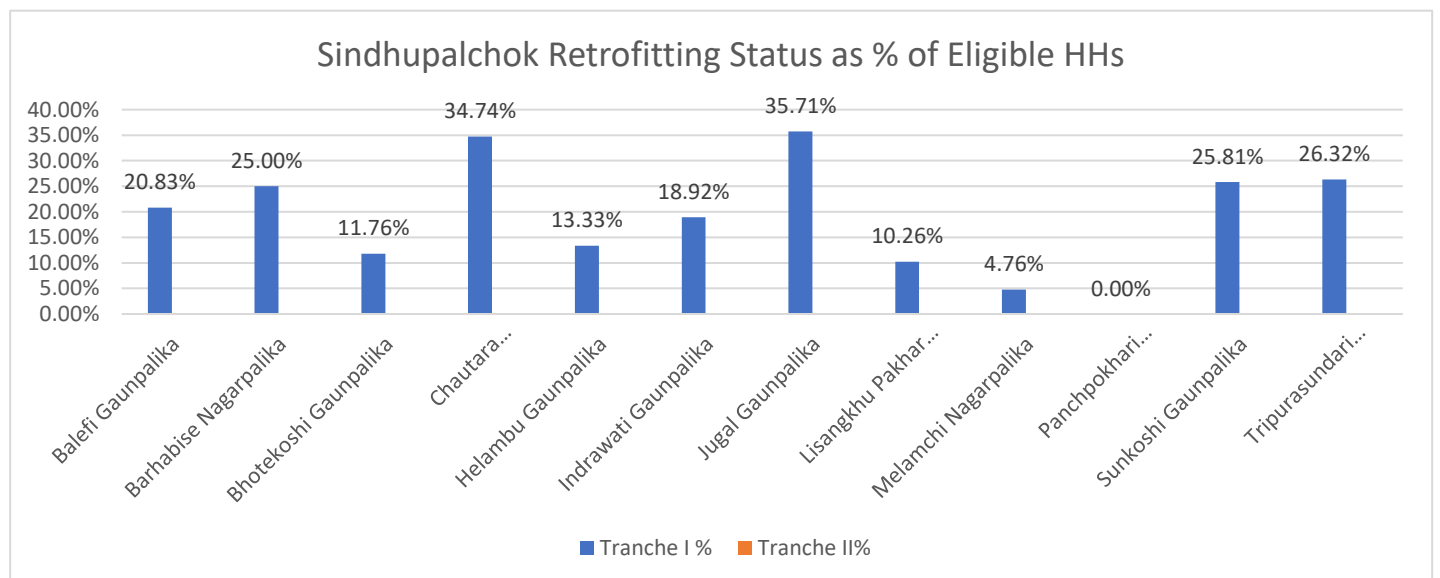

Graph for Grievance Status:

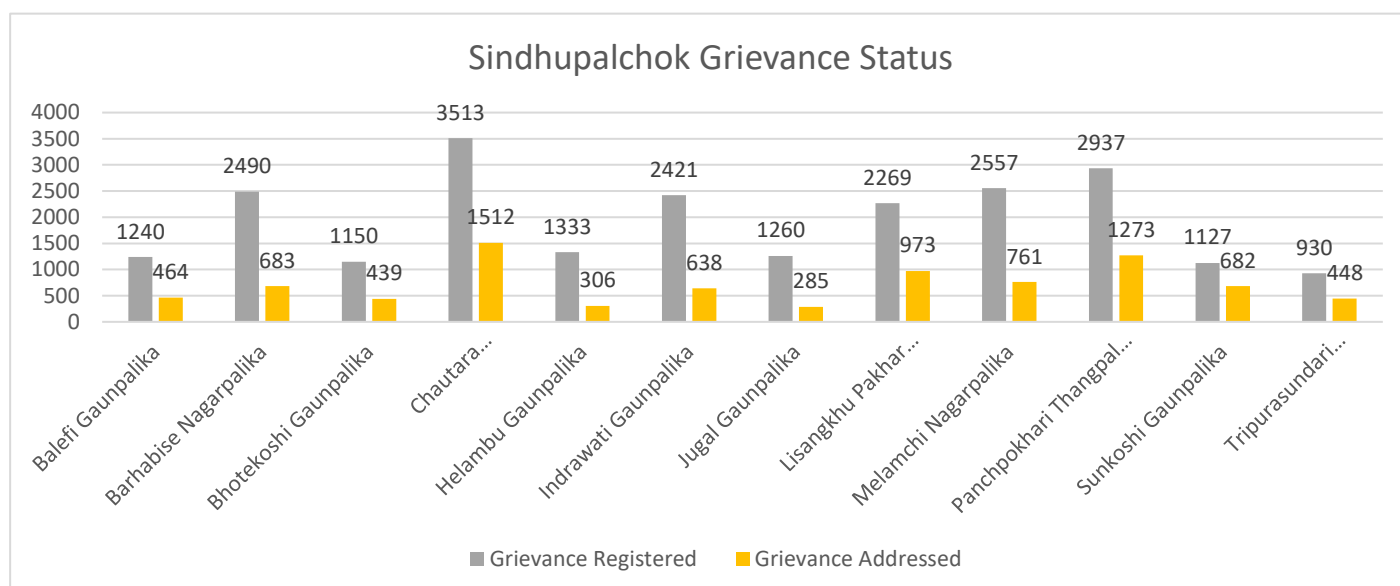

Field Visit /Joint Field Monitoring Visit Event

Visit 1

Date	Location	Participants from HRRP and stakeholders
22nd Jan, 2019	Panchpokhari Thangpal RM Ward No. 7 and 6	Pranjal Singh Bhandari, Pradip Sharma and Roshan Kesari
23 rd Jan, 2019	Panchpokhari Thangpal RM Ward No. 3, 4 and 5	Pranjal Singh Bhandari, Pradip Sharma and Roshan Kesari
24 th Jan, 2019	Panchpokhari Thangpal RM 1 and 2	Binod Sah, DC; Pranjal Bhandari, IMO; Pradip Sharma, HRRP, DTC

Objective(s)

- To know the updates of reconstruction by visiting the private houses.
- Identify the issues and challenges facing at the field level, identify and help correct prevalent non-complaint issues.
- To Collect Housing typologies.
- To conduct Ward level coordination meeting

Summary

Day 1: Visited Panchpokhari Thangpal RM Ward No. 7 and 6 and conducted coordination meeting at Ward No.7

- There are about 20-22 HHs that has not been able to start reconstruction. According to the ward secretary, the reason for not starting the reconstruction is because of the low financial condition.
- The cost of the raw materials would soar up due to remoteness of the village. Also, the availability of the wood is little as the forest area which the village is border with falls under Langtang National Park which is closely monitored by the Army

Day 2: Visited Panchpokhari Thangpal RM Ward No. 3,4 and 5 and conducted coordination meeting at Ward No. 3 and 5

- The ward office of Bhotang is the foremost problem facing the field engineers is the commuting of the files. Getting the files to Chautara takes lot of time and hassle. The engineers requested if some help could be provided by the Rural Municipality office. The Chief Administration Officer of Panchpokhari Thangpal RM was notified of the issue and he advised he would help transporting the files.
- There are about 20-30 households that have not started reconstruction. Most of these HHs are elderly people. When asked when they'll start, they'll say, "after my son returns who resides abroad".

Day 3: Visited Panchpokhari Thangpal RM Ward No. 1 and 2

- The presence of engineers was satisfactory in the wards. The ward chairmen issued the letter to the M&E expert stating their satisfaction.
- About 12 masons who were trained by Poverty Alleviation Fund in February 2017 has not been able to receive the certificates.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
To regularize the presence of engineers in the ward	Attendance sheets to be maintained at each ward.	DLPIU Building, M and E consultant, ward	ASAP
Commuting the files to the district by the field engineers	The POs and the Rural Municipality office should extend the support to the engineers	DLPIU Building, POs, NRA	ASAP

Photos



Picture of the General Coordination meeting that took place on 31st Jan in the presence of GMALI chief.



Some trained local masons constructing a house at Panchpokhari Thangpal RM- 2.



Nepal

Photo



The house is Nepali Typical House. The house is located at Panchpokhari Thangpal Rural Municipality ward no.- 07, Sindhupalchok, the house owner name Mr. Jetha Gole the house owner has not received Second tranche and third tranche. The house belongs to load Bearing structure Stone and Mud Mortar Masonry and two story with attic four rooms, CGI roofing the house is non compliance.

The house is located at Panchpokhari Thangpan Rural Municipality ward no.- 07, Sindhupalchok, the house owner's name Mr. Hire Tamang, the house owner has received Second tranche. The house is load Bearing structure Stone and Mud Mortar Masonry and now under construction.

Photo



Photo

The house is Located at Panchpokhari Thangpal RM Ward No-2, Baruwa. The owner of the house is Mr. Sonam Tamang. The House Owner has received all three tranches but is yet to receive the completion certificate.

The houses are Located at Panchpokhari Thangpal RM Ward No-1, Banskarka. The houses belong to Two beneficiaries: Damai Singh Tamang and Asa Man Tamang. The Houses are joined by single flexible roof. Both the beneficiaries have received all three tranches.
