

Monthly District Report

Khotang, Okhaldhunga, Solukhumbu

Dhankuta, Bhojpur, Sankhuwasava

14 June – 14 July 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Khotang	Field Visit Housing Typology Collection	25 th June 2019	Diktal Rupakot Majhuwagadi Municipality ward 1 and 5	Prakash Basnet, Birodh Kattel, Nabin Singh	
	Ward Level meeting	26 th June 2019	Diktal Rupakot Majhuwagadi Municipality ward no 5 Lafang	Prakash Basnet, Birodh Kattel, Nabin Singh	Minutes LINK
	Palika Level Meeting and Field Visit	27 th June 2019	Diplung Chuichumma Rural Municipality	Prakash Basnet, Birodh Kattel, Nabin Singh	Minute LINK
	Short Review meeting With GMAI Chief Sagar Acharya and travel to Dhankuta	28 th June 2019	At residence of GMAI Chief Dhankuta	Prakash Basnet, Birodh Kattel, Nabin Singh	It was just a review meeting after Palika Meeting to brief about the meeting to the Chief, so no any minute was taken.
Dhankuta	Informal Meeting with GMAI Chief Thierendra Dahal	30 th June 2019	Office Room of GMAI Chief at GMAI Office Dhankuta	Prakash Basnet, Birodh Kattel	No any formal documents were like minutes was taken
	Ward Level Meeting at ward no 7	1 st July 2019	Ward office of ward no 7 Mahalaxmi Municipality Dhankuta	Prakash Basnet, Birodh Kattel	Click HERE for minute
	Palika Level Meeting at Chhatar Jorpati Rural Municipality at jorpati Dhankuta and Municipal survey	2 nd July 2019	Office of Palika Chief at Chhatar Jorpati Rural Municipality, Dhankuta	Prakash Basnet, Birodh Kattel	Click HERE for Minute.
	Field Visit with the field Engineers and Housing	3 July 2019	Ward no 7 of Mahalaxmi Rural municipality and ward no 2	Prakash Basnet, Birodh Kattel	Housing typologies has been sent via KOBO collect

Summary of events during this period

	Typology Collection		and 6 of Chhatar Jorpati Rural Municipality		
Bhojpur	Ward Level Meeting at ward no 12 Bhojpur Municipality	4 th July 2019	Meeting with ward Leader and Technical person of ward no 12 Bhojpur Municipality Bhojpur	Prakash Basnet, Birodh Kattel	Click HERE for minute
	Palika Level Meeting at Arun municipality office Bhojpur	5 th July 2019	Meeting with the Palika chair person in the presence of Vice chairperson and ward leaders	Prakash Basnet, Birodh Kattel	Click HERE for Minute
	Field Visit and Housing Typology collection at ward no 12 of Bhojpur Municipality	7 th July 2019	Ward no 12 and ward no 5 Bhojpur Municipality Bhojpur	Prakash Basnet, Birodh Kattel	Housing typologies has been sent using Kobo collect tool.
	Meeting with GMall Chief Rajan Reddy	8 th July 2019	At Office room of GMaLi Chief Khotang	Prakash Basnet, Birodh Kattel	No any Minutes taken it was just discussion about the reconstruction updates in the district
	Field Visit and Housing Typology collection at ward no 6 of Arun Rural Municipality	9 th July 2019	ward no 6 Arun Rural Municipality Bhojpur	Prakash Basnet, Birodh Kattel	Housing Typologies has been sent using Kobo collect tool.

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Ward Level Meeting	11 July 2019 Ward no 9 Tumningtaar of Khaadbaari Municipality Sankhuwasava	HRRP Solukhumbu Cluster	Prakash Basnet, Birodh Kattel
Field Visit and Housing Typology Collection	12 th July 2019 Ward no 9 Khaadbari Municipality Sankhuwasava	HRRP Solukhumbu Cluster	Prakash Basnet, Birodh Kattel
Field Visit and Housing Typology Collection	13 th July 2019	HRRP Solukhumbu Cluster	Prakash Basnet, Birodh Kattel

Upcoming Events & Meetings

Palika Level Meeting	14 th July 2019 Dharmadevi Rural Municipality Mudhe Sankhuwasava	HRRP Solukhumbu Cluster	Prakash Basnet, Birodh Kattel
One Day Technical Orientation to Engineers	27 th July 2019 at GMAI Office Solkhumbu	HRRP Solukhumbu Cluster	Prakash Basnet, Birodh Kattel


Tranche Status (Solukhumbu)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Dudhkaushika Gaunpalika	3743	2614	1113	1113	1442	1199	20	68	68	
Dudhkoshi Gaunpalika	2071	1226	987	987	785	158	49	38	38	
Khumbupasanglahmu Gaunpalika	1554	1337	1341	1341	691	103	5	0	0	
Likhupike Gaunpalika	1303	1175	503	503	857	285	48	37	37	
Mahakulung Gaunpalika	1136	604	67	67	259	221	92	66	66	
Nechasalyan Gaunpalika	3055	2006	1391	1391	570	560	72	19	19	
Solududhakunda Nagarpalika	3011	2181	1449	1449	1097	765	104	7	7	
Sotang Gaunpalika	1587	903	555	555	290	244	292	9	9	


Graph of Tranche Status:

Reconstruction- Tranche Status

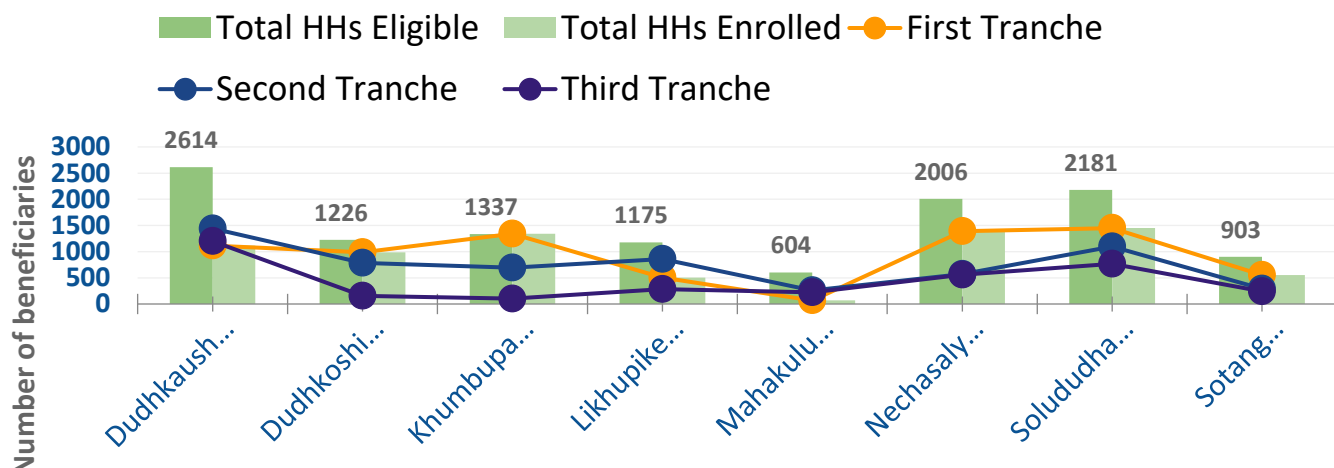

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

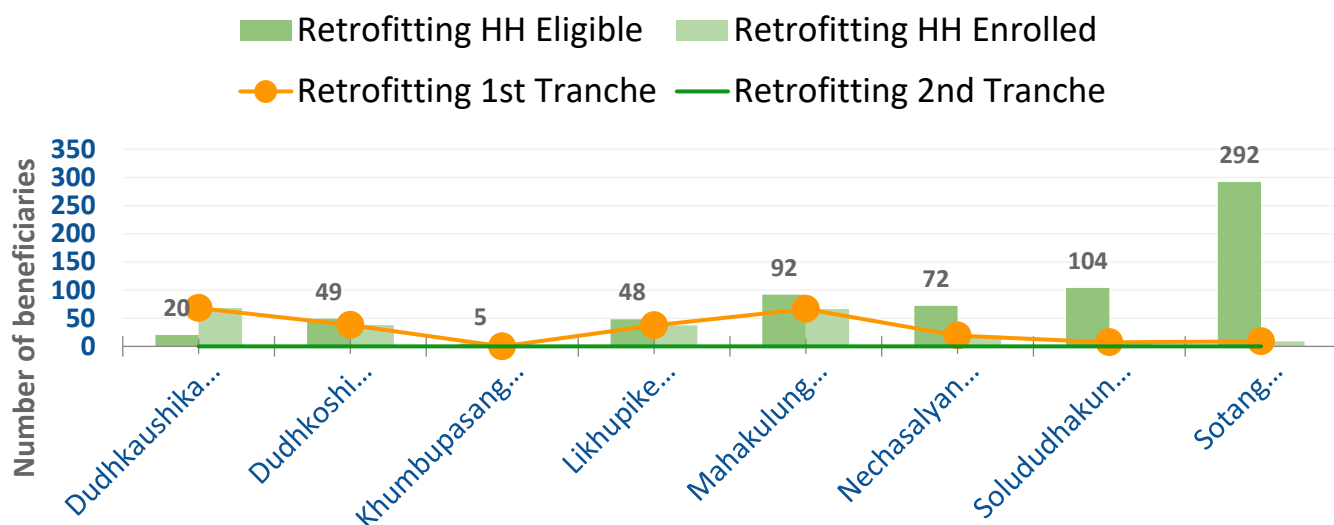


Tranche Status (Okhaldhunga)

Tranche Status Table:

Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche
Champadevi Gaunpalika	4865	3375	3267	3267	3010	2705	743	479	479
Chisankhugadhi Gaunpalika	3708	1067	1003	1003	884	813	276	174	174
Khijidemba Gaunpalika	3965	2926	2906	2806	2672	2498	254	201	201
Likhu Gaunpalika	3879	3261	3211	3211	3006	2734	248	156	156
Manebhanjyang Gaunpalika	5277	1663	1551	1542	1297	1022	461	400	400
Molung Gaunpalika	4707	2977	2889	2888	2561	2287	469	247	247
Siddhicharan Nagarpalika	3741	2681	2457	2456	2440	1655	573	351	347
Sunkoshi									


Graph of Tranche Status:

Reconstruction- Tranche Status

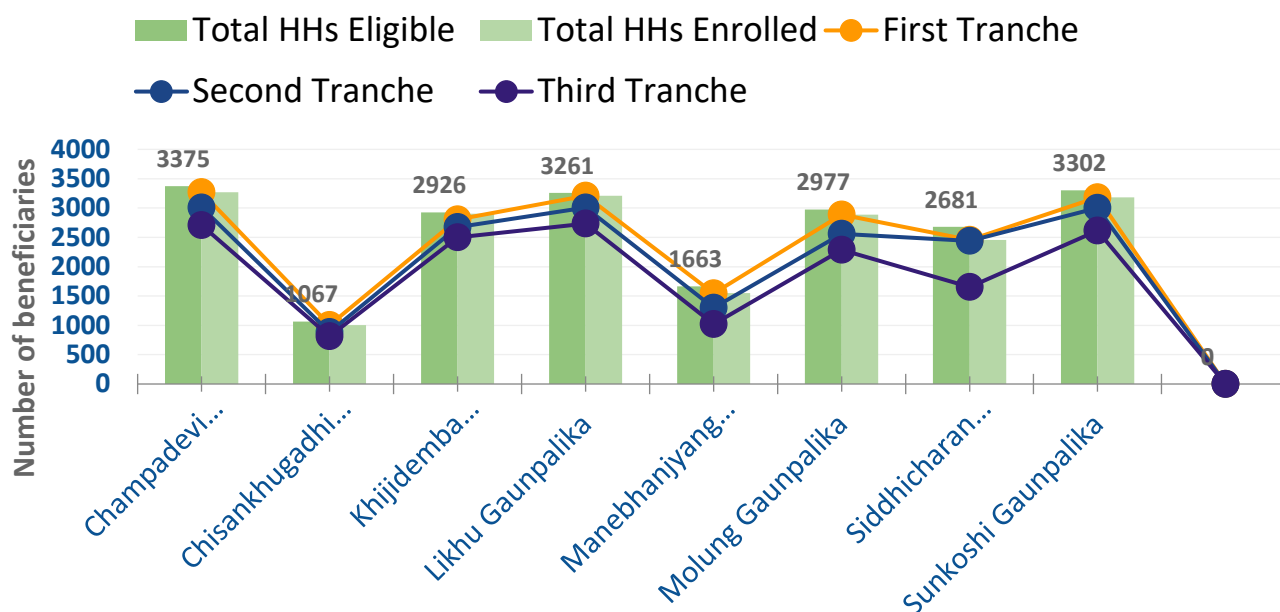

Graph for Retrofitting Status:

Reconstruction - Retrofitting Status

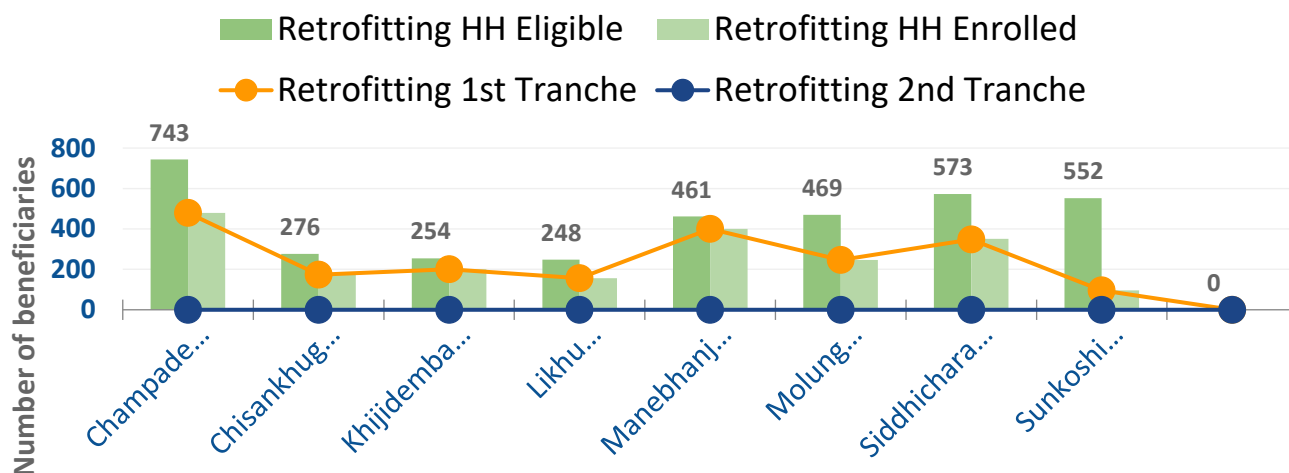


Tranche Status Table:


Name of Palika	Total HHs Surveyed	Total HHs Eligible	Total HHs Enrolled	First Tranche	Second Tranche	Third Tranche	Retrofitting HH Eligible	Retrofitting HH Enrolled	Retrofitting 1st Tranche	Retrofitting 2nd Tranche
Ainselukhark Gaunpalika	1231	775	775	770	532	288	66	66	60	
Barahapokhari Gaunpalika	561	475	475	470	326	177	7	7	6	
Diprung Gaunpalika	1039	524	524	520	360	195	1	1	1	
Halesi Tuwachung Nagarpalika	2526	1754	1754	1734	1204	652	33	33	30	
Jantedhunga Gaunpalika	764	464	464	461	319	172	15	15	14	
Kepilasagadhi Gaunpalika	756	662	662	661	454	246	7	7	6	
Khotelang Gaunpalika	1420	907	907	904	623	337	4	4	4	
Lamidanda Gaunpalika	1553	839	839	810	576	312	48	48	43	
Rupakot huwagadhi Nagarpalika	2278	1511	1511	1480	1037	562	57	57	52	
Sakela Gaunpalika	771	532	532	518	365	198	16	16	14	

Graph of Tranche Status:

Reconstruction- Tranche Status

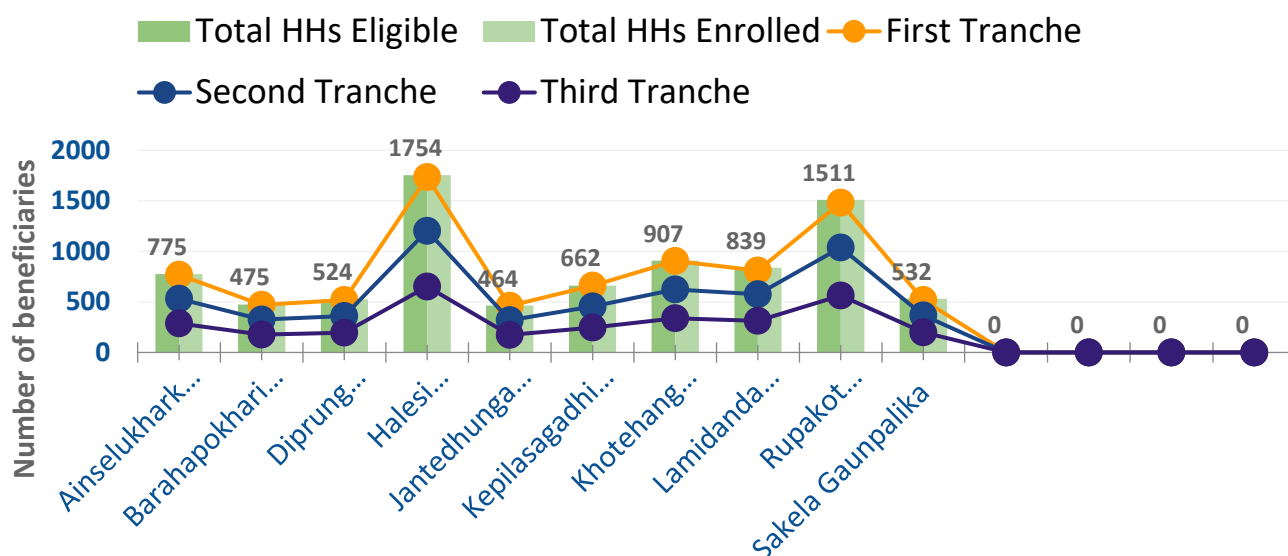

Graph for Retrofitting Status:

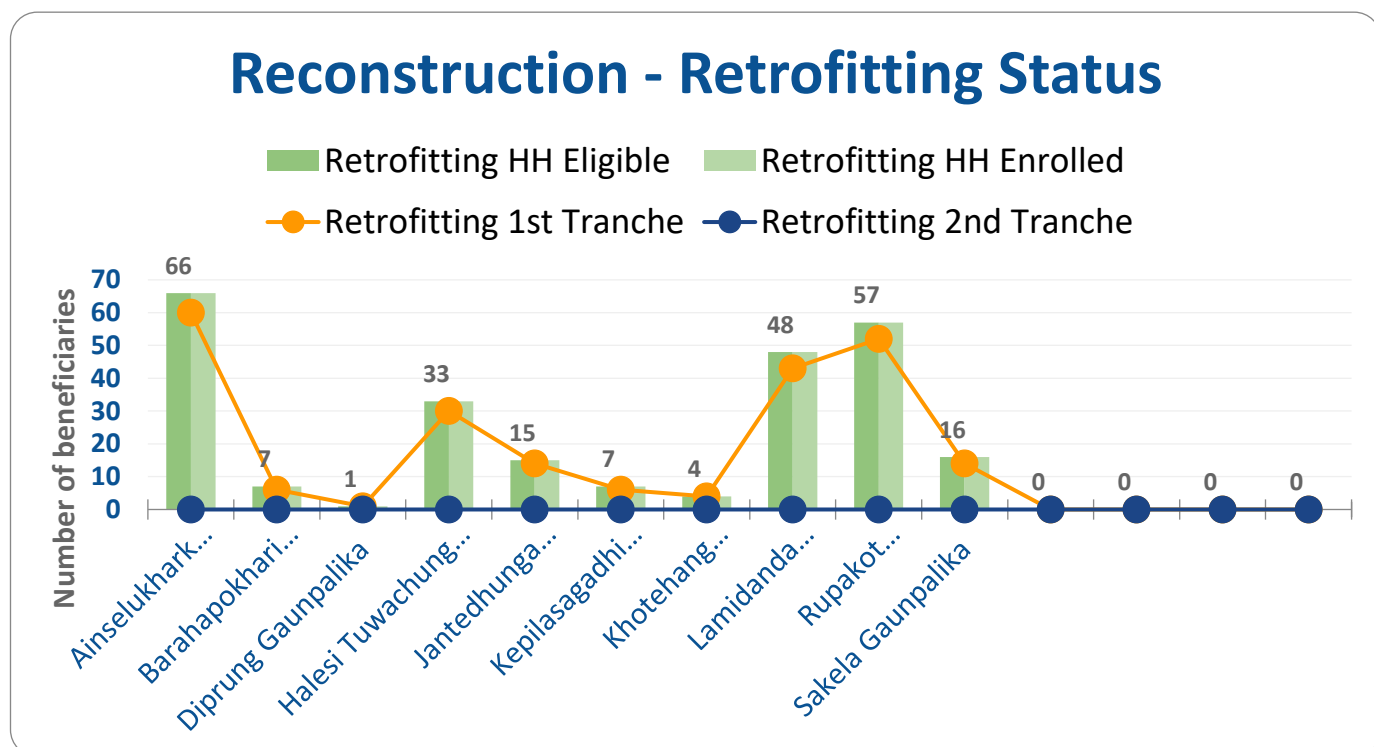

Field Visit Reports (Khotang)

Visit 1

Date	Location	Participants
25 th and 27 th June 2019	Diktal Rupakot Majhuwagadi Municipality ward no 1 and 5 and ward no 3 and 7 of Diplung Chuichumma Rural Municipality Khotang	Prakash Basnet Cluster Coordinator Solukhumbu, Birodh Kattel Cluster Information Management Officer District Support Engineer (DSE) Dinesh Bajrachrya and Focal Engineer Naveen Singh of NRA Khotang
Objective(s)	• To collect the Housing Typology from this location • To Observe the ongoing reconstruction and the major issues of reconstruction in the field level	
Why was the visit carried out in this location?		

These locations are the location with the high number of beneficiaries in khotang district and categorized as the first priority by HRRP for the visit, so this location was selected for the field visit.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

These locations were no visited previously

Summary

Field Visit:

Field Visit was jointly carried out with Prakash Basnet Cluster Coordinator Solukhumbu ,Birodh Kattel Cluster Information Management Officer District Support Engineer (DSE) Dinesh Bajrachrya and Focal Engineer Naveen Singh of NRA Khotang, and also Field Engineer of the respective palika and wards .during the field visit about 8 to 10 houses were visited along with typology collection, during visit one palika and one ward level Palika level meeting at Diplung Chuichumma Rural Municipality in presence all ward Leader in chairmanship of Palika Chief and ward level Meeting at ward no 5 Lafang of Diktal Rupakot majhuwagadi Municipality was carried out

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
One of the main issues and the challenge identified was that to get the third tranches beneficiary should must demolish their old house which was damaged, but the beneficiary is not ok with that	If the beneficiary repairs their damaged houses they could use it for the storage rather than sitting under the same old damaged house by earthquake	Beneficiary should must demolish their house to get the tranches	GMaLI, NRA DLPIU Building and the respective Palika and wards	ASAP
Resurvey and Re-verification are still on going and the time frame was not enough as per the engineers of the respective palika and wards.	Coordinate with the GMaLI and NRA DLPIU Building Khotang	Request with NRA and GMaLI to supply additional Engineers in the required Palikas and wards to complete in time	GMaLI, NRA DLPIU Building and the respective Palika and wards	ASAP
Since this Resurvey and Re-verification is being carried out after four years of earthquake and those hoses which were damaged by earthquake were repaired by beneficiary, so it seems like nothing was happened to those building and it is challenging for engineers to put in damage grade 4 and 5	Engineers must coordinate with the respective palika and ward leader during resurvey and reverification	Requested Engineers working in resurvey and reverification to utilize their technical knowledge to their full extent and use their own ethic and norms while verification	Engineers working in resurvey and reverification and the ward leaders of the respective palika	15 th July 2019
Some of the real beneficiaries are left and some have been duplicated and has got the tranches twice in some wards	Avoid duplication and must include the real beneficiary in resurvey and re verification.	Collect the data of those duplicated beneficiary.	Ward representative and Engineers of the respective palikas	ASAP

Photos



*Figure 1 ward Level Meeting at ward no 5 Lafang of Diktel
Rupakot Majhuwagadi Municipality Khotang*



*Figure 2 Palika Level Meeting at Diplung Chuichumma Rural
Municipality Khotang*

Field Visit Reports (Dhankuta)

Visit 1

Date	Location	Participants
3 rd July 2019 and 4 th July 2019	Ward no 7 Dhermadevi Municipality and ward no 1 ,8, 10 of Chattar Jorpati Rural Municipality	Prakash Basnet Cluster Coordinator Solukhumbu, Birodh Kattel Cluster Information Management Officer Rabin Kattel NRA Field Engineer of Mahalaxmi Municipality and Prasant Jha Sub Engineer Prasant Jha from Chattar Jorpati Rural Municipality
Objective(s)	- The main Objective of the field visit was to conduct the ward level meeting and Palika Level meeting. - To Collect the issues in the ground level and to collect the different housing typologies from the field	

Why was the visit carried out in this location?

- Visit was carried out in these locations because these were the location selected by HRRP as per the beneficiary case load here the beneficiary is little more in comparison to other wards and palikas, so these locations were selected

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

This ward was not visited previously it was the first time that we have visited this location.

Summary

Field Visit:

Field Visit was jointly carried out with Prakash Basnet Cluster Coordinator Solukhumbu, Birodh Kattel Cluster Information Management Officer, Solukhumbu and Field Engineer Rabin Kattel of ward 7 of Mahalaxmi Municipality and Parsant Jha from Chattar Jorpati Rural Municipality joined us during the field visit, Field visit was carried out to collect the housing typology , as per the suggestion from the meeting field visit areas were selected with in the wards and Palikas during the field visit various reconstruction activities were monitored and required suggestion were provided combinedly by the team. During the field visit about 8 to 10 houses were monitored and the typologies were also collected accordingly.

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
One of the Major Challenges identified in Dhankuta district was Non-Compliance Houses which were built immediately after the earthquake of 2015	Suggest applying correction as per the correction manual of NRA under the Supervision of Field Engineers and guidance provided by the District Support Engineer.	Decision was taken to collect the data on such houses and apply correction.	GMaLI Dhankuta, Field Engineers, Ward Leaders and Beneficiaries	ASAP
Lack of trained manpower in the district for the retrofitting as well as for construction of earthquake resilience building	Request NRA Centre to organize the Mason training in the district and deploy those trained masons in the field.	Coordinate with the GMaLI and Building to organize such training.	GMaLI, DLPIU Building and ward	ASAP
Some of the RCC Structure which were found unsafe after the structural analysis has not got the tranches.	Apply necessary correction as per the suggestion of DSE.	Collect all those files and coordinate with the DSE	GMaLI, Field Engineers and local representative	ASAP
There are a lot of Building that needs to be retrofit and due to lack of knowledge this has not been don yet	Coordinate with the GMaLI and DLPIU Building and with the BUILD Change to organize training	To Coordinate with the GMaLI to take the Lead in this work	GMaLI, DSE and DLPIU Building	ASAP

Photos



Figure 3 Ward Level Meeting with Ward leader at ward no 7 of Mahalaxmi Municipality Dhankuta



Figure 4 Palika Level Meeting at Chattar Jorpati Rural Municipality with Palika chief and different ward Leaders at Jorpati Dhankuta

Field Visit Reports (Bhojpur)

Visit 1

Date	Location	Participants
7 th July 2019	Ward No 12 of Bhojpur Rural Municipality	Prakash Basnet Cluster Coordinator Solukhumbu, Birodh Kattel Cluster Information Management Officer Solukhumbu Cluster Aang Dawa Sherpa Ward Technician of ward 12 and Ward Leader Kumar Prashad Shrestha of ward 12 Bhojpur Municipality
9 th July 2019	Ward no 5 and 6 of Arun Rural Municipality	Prakash Basnet Cluster Coordinator Solukhumbu, Birodh Kattel Cluster Information Management Officer Solukhumbu Cluster and Dipak Kumar Sha Palika Focal Engineer of NRA of Arun Rural Municipality.
Objective(s)	- To conduct ward as well as Palika level meeting and collect the burning issues in the respective palikas and wards, - To collect the housing typologies and monitor the ongoing reconstructions in the field.	

Why was the visit carried out in this location?

Visit was carried out in these locations because these were the location selected by HRRP as per the beneficiary case load here the beneficiary is little more in comparison to other wards and palikas, so these locations were selected

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

No this was the first time that we have visited this palika and the wards

Summary

Field Visit:

Field Visit was jointly carried out with Prakash Basnet Cluster Coordinator Solukhumbu, Birodh Kattel Cluster Information Management Officer, Solukhumbu, Aang Dawa Sherpa and Ward Leader Kumar Prashad Shrestha of Ward no 12 Bhojpur Rural Municipality, and the Focal Engineer Dipak Kumar Sha of Arun Rural Municipality joined us during the field visit of the Arun Rural Municipality. During visit one ward level and one palika level meeting was conducted in each palika, about 8 to 10 houses were visited during the visit and the Housing typologies were collected from each field visit. Meeting at Palika and the ward level conducted.

Meeting: put a link to meeting minute (if Municipal/Ward level meetings held)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
One of the Main issues identified was duplication in the Name and the PA number.	Consult with the MIS Expert for the Solution	Contact with the MIS Expert	Data Officer, GMAI and DLPIU	ASAP

	and coordinate with the Central MIS			
Resurvey and Reverification is still not completed in some wards and the palikas even the time line has crossed	Add the no of Engineers and the technician were the resurvey and reverification are to be completed.	To Increase the number of staffs for the survey.	GMaLI, NRA Building and Wards	ASAP
Pressure from the beneficiary to get 3 lakhs at once, who build their houses immediately after earthquake and are non-compliance	To follow the new guideline and work accordingly	Retrofitting as per the correction Manual	NRA Building GMaLI and DSE	ASAP
Most of the houses are made up of water Brick with mud mortar and are two storey	Retrofitting as per the DSE suggestions	Retrofitting and correction	DSE NRA Building and Field Engineers	ASAP

Photos



Figure 5 Palika Level Meeting with the Palika Chair Person and ward leaders at Arun Rural Municipality 5 Pauli Bhojpur



6 Ward Level meeting with Ward chair person Mr Kumar Prasad Shrestha at Ward office of Bhojpur Municipality ward no 12

Housing Typology Report (Max 4 Photos, Select best photos from each district)



Figure 7 House of Madhav Raj Rai Diktal Rupakot Majhuwagadi Municipality, Khotang

This is under construction house of Madhav Raj Rai resident of Diktal Rupakot Majhuwagadi Municipality Khotang house is compliant with stone in mud Mortar (SMM) with wooden bands and RCC band at the plinth level the beneficiary has received his second tranches and the estimated cost till date was about 4.5 lakhs.



Figure 8 House of Dhan Bahadur Shrestha ward no 7 Mahalaxmi RM Dhankuta

The house is made up of Stone in Mud Mortar (SMM) with RCC Bands provided at appropriate position size, Beneficiary has received his all three tranches and waiting for the completion certificates to be provided by NRA Building. The total estimated cost of the building as per the beneficiary was 6.5 lakhs



Figure 9 House of Lim Bahadur Rai ward no 8 leguwa, Mahalaxmi Municipality Dhankuta

The Beneficiary has received all three tranches from the government and waiting for the Completion certificates, the house is compliant with the RCC bands in Stone and Mud Mortar, The total cost of construction as per the beneficiary was 5.8 Lakh and the duration of completion was 3 months.



Figure 10 House of Nar Man Sharki Ward no 12 Daregauda Bhojpur

The House is compliant with RCC bands in the wall with Stone in cement Mortar (SCM) house is two story with 3 rooms in ground floor and four room in the first floor the beneficiary has received his all tranches and waiting for the completion certificates as per the beneficiary the total cost of construction was 11 lakhs and period of construction was about 6 months and the beneficiary is currently living under this house.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
When will the result of this resurvey and reverification publish??	Beneficiaries and the ward leaders	HRRP Field Visit Team
When will the Government Provide the 3 lakhs rupees at once for those who already built their houses?	Beneficiaries and the ward leaders	HRRP Field Visit Team
What about the Bank Loan Process for the Beneficiaries?	Beneficiaries and the ward leaders	HRRP Field Visit Team

Challenges and Way Forward

Challenge	Way Forward
Non-Compliance Issues is one of the major challenges.	Central NRA should be careful about this in time
Lack of trained man power for the retrofitting.	Retrofitting training should be provided as soon as possible.

Case Study

Place Photo here

Write Caption here

Write case study here



Engineer Case
Story_Bhojpur.docx



GMALI
Cheif_Khotang_Exp
