

## Monthly District Report

### Lalitpur, Bhaktapur

9 May - 13 June 2019

#### Summary of events during this period

| Districts | Name of activity/event                                                                                                                                                                                                                                                                                                                                                                                                                                          | Event date  | Location (District, Municipality)               | Contact Person                                                                                                                    | Reference Document                                                                                                                                                                                 |
|-----------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|-------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Lalitpur  | Meeting with representatives of Himalayan Dana Foundation was conducted at DLPIU GMALI Lalitpur. Himalayan Dana Foundation were found to have conducted few houses for earthquake affected beneficiaries in some wards of Mahalaxmi Municipality.                                                                                                                                                                                                               | 13 May 2019 | DLPIU NRA GMALI Lalitpur                        | Mr. Yamnath Giri<br>M & E Specialist<br>DLPIU NRA GMALI Lalitpur<br>Manbhawan<br>yamnathgiri2014@gmail.com<br>Contact: 9851239785 | Letter was issued from GMALI Lalitpur to Himalayan Dana Foundation for submitting necessary details of reconstruction support provided to beneficiaries of various wards of Mahalaxmi Municipality |
|           | The ward level general coordination meeting was conducted at Ward no 8, Lubhu, Mahalaxmi Municipality. The coordination meeting was attended by Ward Chief, Ward Member, M & E consultant of DLPIU Building Lalitpur, M & E Specialist of DLPIU GMALI Lalitpur and District Coordinator of HRRP. The main objective of the meeting was to discuss on shelter reconstruction taken forward by Himalayan Dana Foundation in Ward no. 8 of Mahalaxmi Municipality. | 16 May 2019 | Ward office, Ward no. 8, Mahalaxmi Municipality | Mr. Yamnath Giri<br>M & E Specialist<br>DLPIU NRA GMALI Lalitpur<br>Manbhawan<br>yamnathgiri2014@gmail.com<br>Contact: 9851239785 | Ward -level coordination meeting minute<br><br><a href="https://drive.google.com/open?id=1702ncZfKPFZwVxOCzYWxvQnnhxDk6JYg">https://drive.google.com/open?id=1702ncZfKPFZwVxOCzYWxvQnnhxDk6JYg</a> |
|           | Joint M & E Visit was conducted at Ward no. 8, Lubhu, Mahalaxmi Municipality by HRRP Lalitpur District Coordination Team along with M & E Consultant (CLPIU Building), M & E Specialist, EHRP/DLPIU GMALI Lalitpur, DLPIU Engineer and technical personnel from Mahalaxmi Municipality. The main objective of the field visit was to observe the reconstruction status of houses reconstructed by Himalayan Dana Foundation.                                    | 16 May 2019 | Ward no 8, Mahalaxmi Municipality               | Mr. Yamnath Giri<br>M & E Specialist<br>DLPIU NRA GMALI Lalitpur<br>Manbhawan<br>yamnathgiri2014@gmail.com<br>Contact: 9851239785 | Joint M & E visit section                                                                                                                                                                          |
|           | Skype orientation to all DCTs regarding meeting minutes upload to website and Google Calendar                                                                                                                                                                                                                                                                                                                                                                   | 20 May 2019 |                                                 | Ambika Amatya<br>District Coordinator, HRRP<br><br>Sachin Malego,<br>IM Officer, HRRP                                             |                                                                                                                                                                                                    |
|           | Tranche status of Lalitpur updated to GD sheet in Palika Profile                                                                                                                                                                                                                                                                                                                                                                                                | 21 May 2019 |                                                 | Ambika Amatya<br>District Coordinator, HRRP<br><br>Sachin Malego<br>IM Officer, HRRP                                              | <a href="#">Palika data</a>                                                                                                                                                                        |
|           | Segregation of 5W data from all POs of Lalitpur completed                                                                                                                                                                                                                                                                                                                                                                                                       | 21 May 2019 |                                                 | Sachin Malego<br>IM Officer, HRRP                                                                                                 | <a href="#">Segregated data</a>                                                                                                                                                                    |

## Summary of events during this period

|           |                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |             |                                           |                                                                                                                                   |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |
|-----------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|-------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|           | The general coordination meeting of Lalitpur was organized at DLPIU- GMaLI Lalitpur office. The coordination meeting was attended by officials of DLPIU- GMaLI Lalitpur, POs, staff members of EHRP/DLPIU GMaLI Lalitpur, DLPIU- Education Lalitpur, DLPIU Building Lalitpur, Patan Durbar Square Monument Protection Office and HRRP. The main objective of the meeting was to discuss on reconstruction status and updates from government and Partner Organization. | 21 May 2019 | DLPIU NRA GMALI Lalitpur                  | Mr. Yamnath Giri<br>M & E Specialist<br>DLPIU NRA GMALI Lalitpur<br>Manbhawan<br>yamnathgiri2014@gmail.com<br>Contact: 9851239785 | <a href="#">District general coordination meeting minute</a><br><br><a href="#">District general coordination meeting weblink</a>                                                                                                                                                                                                                                                                                                                                                                                  |
|           | Meeting with representatives of Maya Foundation was conducted at DLPIU GMaLI Lalitpur. Maya Foundation were found to have provided support in reconstructing houses for earthquake affected beneficiaries in Ward no 7, Pilachhen at Lalitpur Metropolitan City. Maya Foundation were issued letter to submit all the details about housing project at Pilachhen within 7 days.                                                                                        | 21 May 2019 | DLPIU NRA GMALI Lalitpur                  | Mr. Yamnath Giri<br>M & E Specialist<br>DLPIU NRA GMALI Lalitpur<br>Manbhawan<br>yamnathgiri2014@gmail.com<br>Contact: 9851239785 | Letter was issued from GMALI Lalitpur to Himalayan Dana Foundation for submitting necessary details of reconstruction support provided to beneficiaries of various wards of Mahalaxmi Municipality                                                                                                                                                                                                                                                                                                                 |
|           | Support for preparation of Tranche Map in one sheet and Meeting with M&E Specialist, EHRP/DLPIU GMALI Lalitpur                                                                                                                                                                                                                                                                                                                                                         | 24 May 2019 |                                           | Sachin Malego<br>IM Officer, HRRP                                                                                                 |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |
|           | Meeting with SOUP/ Shaplaneer for timely update of 5W and PO's participation in meetings.                                                                                                                                                                                                                                                                                                                                                                              | 24 May 2019 | SOUP Office                               | Ambika Amatya<br>District Coordinator, HRRP<br><br>Sachin Malego<br>IM Officer, HRRP                                              | Remarks:<br>SOUP/Shaplaneer has now started a timely 5W update from this month's 5W.                                                                                                                                                                                                                                                                                                                                                                                                                               |
|           | List preparation of all POs whose data needs to be verified for 5W and maintain gaps in 5W                                                                                                                                                                                                                                                                                                                                                                             | 29 May 2019 |                                           | Sachin Malego<br>IM Officer, HRRP                                                                                                 |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |
|           | Support to National HRRP for design and publication of Experiences booklet                                                                                                                                                                                                                                                                                                                                                                                             | Ongoing     |                                           | Sachin Malego,<br>IM Officer, HRRP<br><br>Monika Bajimaya Shrestha,<br>DMT IM Coordinator, HRRP                                   |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |
| Bhaktapur | Segregation of 5W data from all POs of Bhaktapur completed                                                                                                                                                                                                                                                                                                                                                                                                             | 21 May 2019 |                                           | Sachin Malego,<br>IM Officer, HRRP                                                                                                | <a href="#">Segregated data</a>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                    |
|           | The general ward-level coordination meeting was conducted at Ward office, Ward no. 2 (Byasi), Ward no. 3 (Banshgopal) and Ward no. 4 (Bolachhen), Bhaktapur Municipality. Ward Chief in presence of ward members, representatives of EHRP/DLPIU NRA GMALI Bhaktapur and HRRP Lalitpur Cluster attended the meeting. The main agenda of the meeting was to discuss on the reconstruction updates, issues and challenges at ward level.                                  | 23 May 2019 | Ward offices of Ward no 2, 3 & 4          | Mr. Bibek Gautam<br>M & E Specialist<br>EHRP/DLPIU NRA GMALI Bhaktapur<br>vibek.gautam@gmail.com<br>Contact: 9847054816           | Ward -level coordination meeting minute<br><a href="https://drive.google.com/open?id=16ur3fGdnySYsOf4nSB2Ust18WnCb7GI">https://drive.google.com/open?id=16ur3fGdnySYsOf4nSB2Ust18WnCb7GI</a><br><br><a href="https://drive.google.com/open?id=16j1bqlznYVkgN6JPNwQUXGwgKA0pPiH">https://drive.google.com/open?id=16j1bqlznYVkgN6JPNwQUXGwgKA0pPiH</a><br><br><a href="https://drive.google.com/open?id=16yMv1-W2E69roTStB1iKSegg3iYeHb4hU">https://drive.google.com/open?id=16yMv1-W2E69roTStB1iKSegg3iYeHb4hU</a> |
|           | Joint M & E Visit was conducted at Ward no. 5 & 6, Changunarayan Municipality by HRRP Lalitpur District Coordination Team along with M & E Consultant (CLPIU Building), District Support Engineer (DLPIU Building Bhaktapur), DLPIU Engineers. The main objective of the field visit was to                                                                                                                                                                            | 30 May 2019 | Ward no. 5 & 6 Changunarayan Municipality | Er. Roshan Keshari<br>M & E Consultant,<br>DLPIU Building Bhaktapur<br>roshankesari20@gmail.com<br>9841640357                     | Joint M & E visit section                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |

## Summary of events during this period

|                                                                                                                                                                                                                                                                                                                                                                                                                                        |             |                                                                      |                                                                                                                                                                        |                                                                                                                                                                                                    |  |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------|----------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|
| observe the reconstruction status of houses along with inspect the non compliance cases                                                                                                                                                                                                                                                                                                                                                |             |                                                                      |                                                                                                                                                                        |                                                                                                                                                                                                    |  |
| Joint M & E Visit was conducted at Ward no. 4 & 10, Suryabinayak Municipality by HRRP Lalitpur District Coordination Team along with M & E Consultant (CLPIU Building), District Support Engineer (DLPIU Building Bhaktapur), DLPIU Engineers. The main objective of the field visit was to observe the reconstruction status of houses along with inspect the non compliant cases                                                     | 31 May 2019 | Ward no. 4 (Balkot) & 10 (Chitapol), Suryabinayak Municipality       | Er. Roshan Keshari<br>M & E Consultant,<br>DLPIU Building Bhaktapur<br><a href="mailto:roshankesari20@gmail.com">roshankesari20@gmail.com</a><br>9841640357            | Joint M & E visit section                                                                                                                                                                          |  |
| The general ward-level coordination meeting was conducted at Ward office, Ward no. 7, Bahakha Bazar, Madhyapur Thimi Municipality, Bhaktapur district. Ward Chief in presence of ward secretary, representatives of EHRP/DLPIU NRA GMALI Bhaktapur and HRRP Lalitpur Cluster attended the meeting. The main agenda of the meeting was to discuss on the reconstruction updates, issues and way forward to meet reconstruction targets. | 6 June 2019 | Ward office, Ward no. 7, Bahakha Bazar, Madhyapur Thimi Municipality | Mr. Bibek Gautam<br>M & E Specialist<br>EHRP/DLPIU NRA<br>GMALI Bhaktapur<br><a href="mailto:vibek.gautam@gmail.com">vibek.gautam@gmail.com</a><br>Contact: 9847054816 | Ward -level coordination meeting minute<br><br><a href="https://drive.google.com/open?id=18ERpK03eJDjLTuWhs5_Ds8la6X-KX6Z7">https://drive.google.com/open?id=18ERpK03eJDjLTuWhs5_Ds8la6X-KX6Z7</a> |  |
| The general ward-level coordination meeting was conducted at Ward office, Ward no. 5, Chaling, Changunarayan Municipality, Bhaktapur district. Ward Chief in presence of ward member, representatives of EHRP/DLPIU NRA GMALI Bhaktapur and HRRP Lalitpur Cluster attended the meeting. The main agenda of the meeting was to discuss on the reconstruction updates, issues and way forward to meet reconstruction targets.            | 7 June 2019 | Ward office, Ward no. 5, Chaling, Changunarayan Municipality         | Mr. Bibek Gautam<br>M & E Specialist<br>EHRP/DLPIU NRA<br>GMALI Bhaktapur<br><a href="mailto:vibek.gautam@gmail.com">vibek.gautam@gmail.com</a><br>Contact: 9847054816 | Ward -level coordination meeting minute<br><br><a href="https://drive.google.com/open?id=18E9io9dw_xmsyXXMsZaeWGlO3-uSFtm6">https://drive.google.com/open?id=18E9io9dw_xmsyXXMsZaeWGlO3-uSFtm6</a> |  |

## Upcoming Events & Meetings

| Name of activity/event                                                                                                                                                                       | Date, Time, and Location (District, Municipality)                                       | Organizer                                                                            | Contact Person                                                                                                                                                                       |
|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Joint M & E visit to observe reconstruction efforts of beneficiaries in Bhaktapur and Lalitpur districts                                                                                     | 14- 11 July 2019/<br>Various wards of Municipalities of Lalitpur and Bhaktapur district | DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team | Ms. Ambika Amatya<br>District Coordinator<br>HRRP Lalitpur and Myagdi Cluster<br><a href="mailto:ambika.amatya@hrrpnepal.org">ambika.amatya@hrrpnepal.org</a><br>Contact: 9841356409 |
| General Palika level and Ward level meeting and consultation with elected ward officials over the reconstruction progress and status of the visited wards of Bhaktapur and Lalitpur district | 14- 11 July 2019/<br>Various wards of Municipalities of Lalitpur and Bhaktapur district | DLPIUs (Building and GMALI) of Lalitpur and Bhaktapur and HRRP Lalitpur Cluster team | Ms. Ambika Amatya<br>District Coordinator<br>HRRP Lalitpur and Myagdi Cluster<br><a href="mailto:ambika.amatya@hrrpnepal.org">ambika.amatya@hrrpnepal.org</a><br>Contact: 9841356409 |

## News & Updates


1. Resurvey and reverification of grievances and beneficiaries are in progress in various wards of Palikas of Lalitpur and Bhaktapur districts.
2. DLPIU NRA GMALI Bhaktapur had been conducting general ward-level coordination and consultation meetings in each wards of 4 palikas of Bhaktapur district. The main focus of the said ward level meeting is to discuss on way forward for non-enrolled beneficiaries and to further stimulate beneficiaries in shelter reconstruction by making conducive environment for them.

## Tranche Status (Lalitpur)

**Tranche Status Table:**


| Name of Palika           | Total HHs Surveyed | Total HHs Eligible | Total HHs Enrolled | First Tranche | Second Tranche | Third Tranche | Retrofitting HH Eligible | Retrofitting HH Enrolled | Retrofitting 1st Tranche | Retrofitting 2nd Tranche |
|--------------------------|--------------------|--------------------|--------------------|---------------|----------------|---------------|--------------------------|--------------------------|--------------------------|--------------------------|
| Bagmati Gaunpalika       | 3361               | 3370               | 3099               | 3089          | 2530           | 1854          | 252                      | 110                      | 107                      | 0                        |
| Godawari Nagarpalika     | 10950              | 9598               | 7938               | 7870          | 2587           | 2122          | 323                      | 89                       | 87                       | 0                        |
| Konjyosom Gaunpalika     | 2580               | 2154               | 2066               | 2060          | 1761           | 1343          | 372                      | 257                      | 246                      | 0                        |
| Lalitpur Mahanagarpalika | 6594               | 7373               | 6332               | 6311          | 1270           | 815           | 275                      | 119                      | 115                      | 0                        |
| Mahalaxmi Nagarpalika    | 4409               | 3669               | 3096               | 3068          | 858            | 711           | 83                       | 31                       | 29                       | 0                        |
| Mahankal Gaunpalika      | 2451               | 2271               | 2236               | 2235          | 1767           | 1058          | 61                       | 55                       | 54                       | 0                        |

**Graph of Tranche Status:**

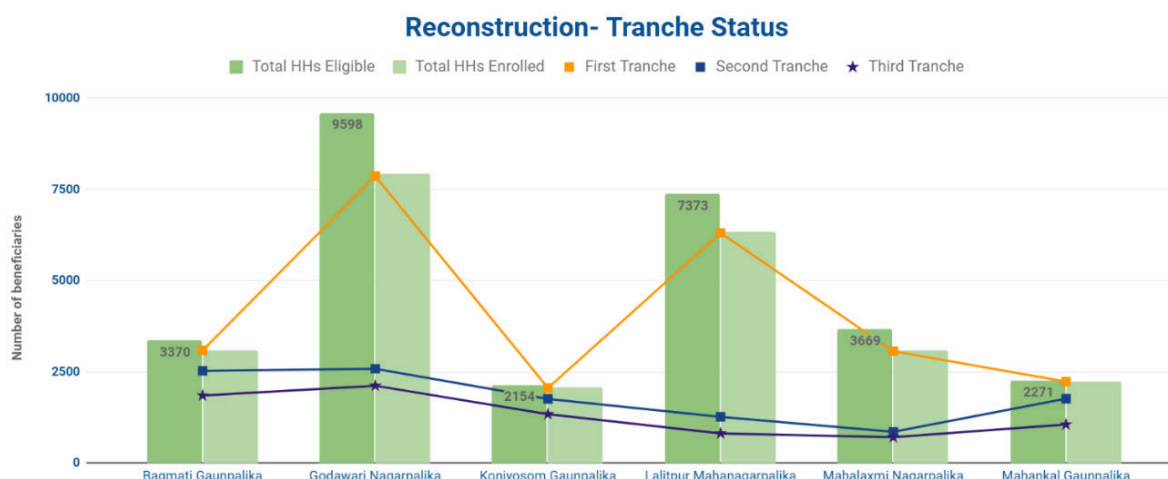

**Graph for Retrofitting Status:**

### Reconstruction - Retrofitting Status

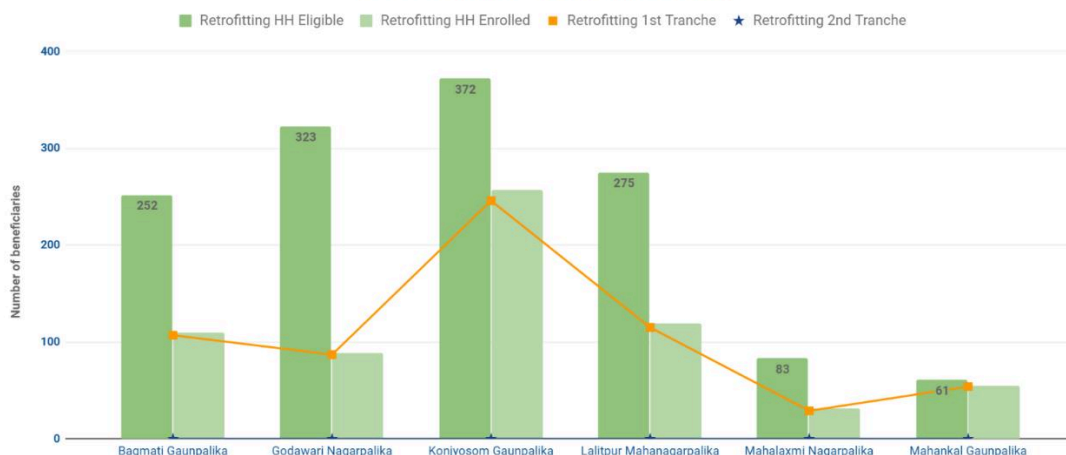


## Tranche Status (Bhaktapur)

**Tranche Status Table:**

| Name of Palika              | Total HHs Surveyed | Total HHs Eligible | Total HHs Enrolled | First Tranche | Second Tranche | Third Tranche | Retrofitting HH Eligible | Retrofitting HH Enrolled | Retrofitting 1st Tranche | Retrofitting 2nd Tranche |
|-----------------------------|--------------------|--------------------|--------------------|---------------|----------------|---------------|--------------------------|--------------------------|--------------------------|--------------------------|
| Bhaktapur Nagarpalika       | 8175               | 7622               | 5612               | 5612          | 1635           | 1449          | 148                      | 42                       | 42                       | 0                        |
| Changunarayan Nagarpalika   | 11059              | 10937              | 9716               | 9716          | 3128           | 2868          | 212                      | 88                       | 88                       | 0                        |
| Madhyapur Thimi Nagarpalika | 3015               | 2333               | 2060               | 2060          | 681            | 638           | 101                      | 56                       | 56                       | 0                        |
| Suryabinayak Nagarpalika    | 7948               | 7416               | 6970               | 6970          | 2517           | 2336          | 233                      | 101                      | 101                      | 0                        |


### Graph of Tranche Status:

### Reconstruction- Tranche Status

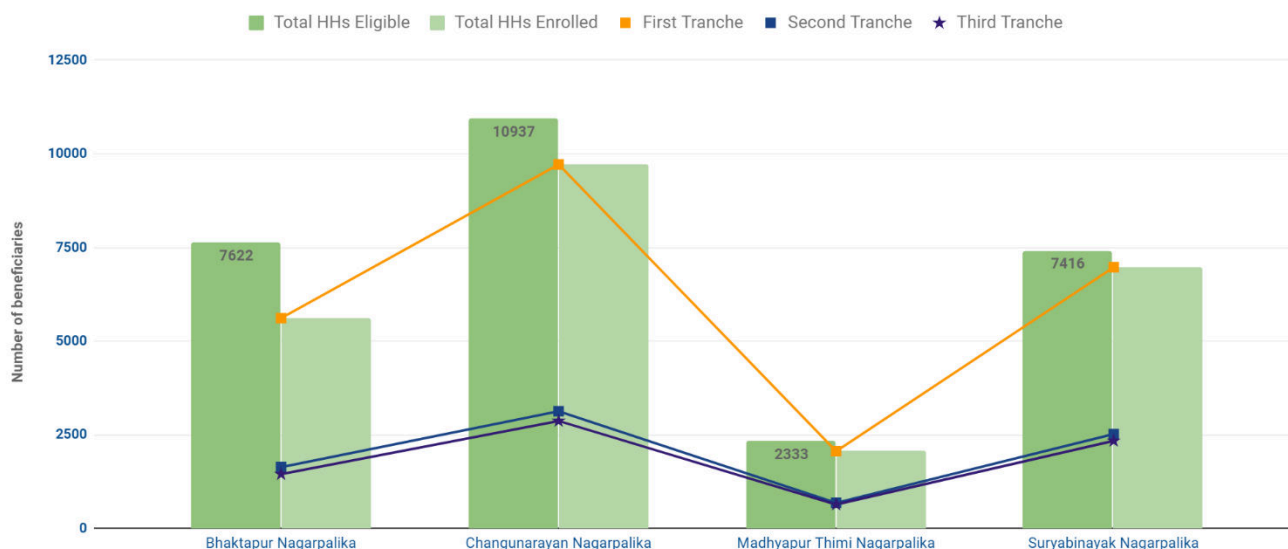

### Graph for Retrofitting Status:

### Reconstruction - Retrofitting Status

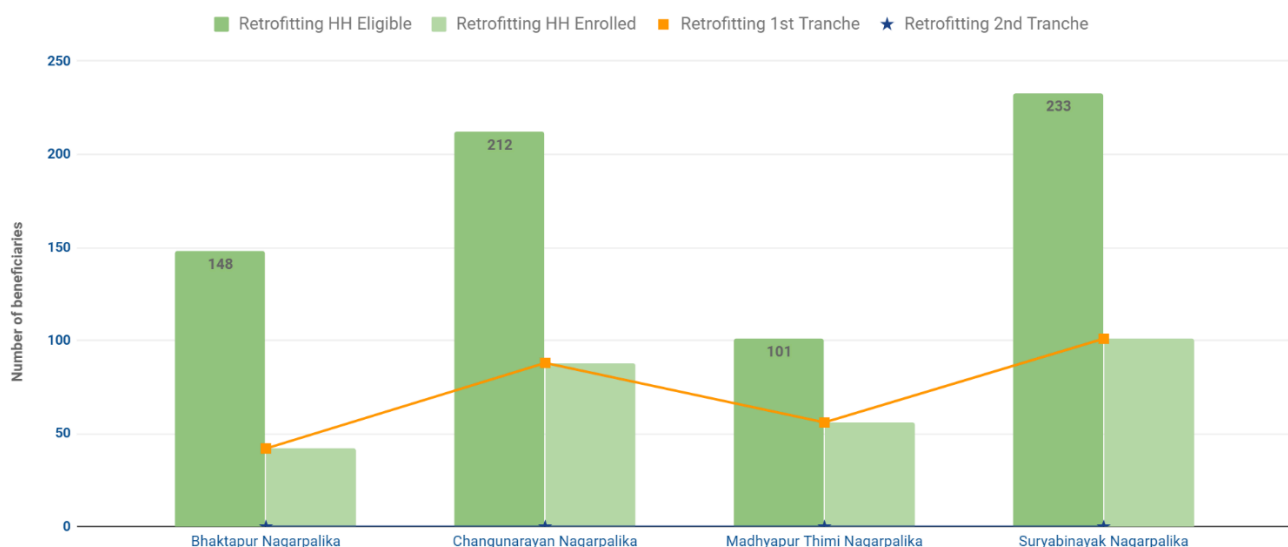

## Field Visit Reports (Lalitpur)

### Visit 1

| Date                | Location                                                                                                                                          | Participants                                                                                                                                                                                                                                                                                                                                                                                                                                                                                  |
|---------------------|---------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 16 May 2019         | Ward no. 8, Lubhu, Mahalaxmi Municipality, Lalitpur district                                                                                      | <ul style="list-style-type: none"> <li>Roshan Raj Giri, M &amp; E Consultant, NRA CLPIU Building</li> <li>Yamnath Giri, M &amp; E Specialist, EHRP/DLPIU GMaLI Lalitpur</li> <li>Ambika Amatya, District Coordinator, HRRP Lalitpur Cluster</li> <li>Amresh Man Shrestha, Engineer, Himalayan Dana Foundation</li> <li>Dipendra Bajracharya and Lasata Shakya, Himalayan Dana Foundation</li> <li>Angana Shrestha &amp; Reshu Poudel (technical personnel), Mahalaxmi Municipality</li> </ul> |
| <b>Objective(s)</b> | <ul style="list-style-type: none"> <li>To interact with elected ward officials about shelter reconstruction taking place in Ward no 8.</li> </ul> |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                               |



|  |                                                                                                                                                                                       |
|--|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
|  | <ul style="list-style-type: none"> <li>To observe the shelter reconstruction taken forward by Himalayan Dana Foundation.</li> <li>To collect housing typology in KoBo App.</li> </ul> |
|--|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|

#### Why was the visit carried out in this location?

- To check whether the houses constructed by Himalayan Dana Foundation is complaint or not.
- To observe the shelter reconstruction taken forward by Himalayan Dana Foundation.
- To take details of technical parts of the houses conducted by Himalayan Dana Foundation.

#### 'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

None of the visit was made in this Ward no .8

#### Summary

Joint M & E Visit was conducted at Ward no. 8, Lubhu, Mahalaxmi Municipality by HRRP Lalitpur District Coordination Team along with M & E Consultant (CLPIU Building), M & E Specialist, EHRP/DLPIU GMALI Lalitpur, DLPIU Engineer and technical personnel from Mahalaxmi Municipality. The field visit team observed 6 houses in total that were technically assisted and supported by Himalayan Dana Foundation. The houses has steel post as frame and in fill wall done by brick and cement with flexible roof. The District Support Engineer has approved for technical requirements of the houses supported by Himalayan Dana Foundation. The inner wall of the said houses was made by plyboard. A total of around 6-7 NPR were invested in making the houses by Himalayan Dana Foundation. The observed houses are usually 4 roomed and 2 storey.

#### Field Visit:

- No. of HHs visited: 6
- No. of meetings with engineers: 1
- No. of meetings with local officials: 1

Meeting: <https://drive.google.com/open?id=1702ncZfKPFZwVxOCzYWxvQnnhxDk6JYg>

| Challenges / Issues Identified                                                                    | Solutions Provided                                                                                                                | Decision Taken                                                                                                              | Responsible                                                                   | Timeframe           |
|---------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------|---------------------|
| Check and balance of POs interventions in shelter reconstruction have not been properly monitored | POs work should be brought into notifications for mainstreaming check and balance of their initiatives in shelter reconstruction. | Concerned POs have decided to submit all relevant details and documents that shows their support to shelter reconstruction. | DLPIU GMALI Lalitpur, DLPIU Building Lalitpur, Municipality, Ward office, POs | As soon as possible |
| Beneficiaries supported by POs have also been found taking grants from government.                | Ward office and grant providing bank was informed for reducing the duplication of grant.                                          | Ward office decided to inform beneficiary to return the grant taken from government                                         | DLPIU GMALI Lalitpur, DLPIU Building Lalitpur, Municipality, Ward office, POs | As soon as possible |

#### Photos



|                                                                                                                                                                                                                                                                                                                 |                                                                                                                                                                                                                                                                                                                                                                                                                                                                   |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Beneficiary name: Joint house of Mandevi Shahi and Jit Govinda Shahi, Ward no 8, Lubhu, Mahalaxmi Municipality. The houses has steel post as frame and in fill wall done by brick and cement with flexible roof. Himalayan Dana Foundation provided financial support of nearly 6-7 lakh to rebuild this house. | Made on public land at Ward no 28, Harisiddhi, Lalitpur Metropolitan City. Each houses are made by water proof plyboard of 10 mm thickness, with 4 rooms in 1 unit. 2 families have shifted to newly reconstructed house and 4 family are still residing. Himalayan Dana Foundation initiated this playboard housing unit, which they further have planned to use as health centers or community facility centers. Cost per unit of house comes around Rs 5 lakh. |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|

## Field Visit Reports (Bhaktapur)

### Visit 2

| Date                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        | Location                                                                                                                                                                                                                                                                         | Participants                                                                                                                                                                                                                                                                                                                         |                                             |                   |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------|-------------------|
| 30 May 2019                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                 | Ward no. 5 & 6, Changunarayan Municipality, Lalitpur district                                                                                                                                                                                                                    | <ul style="list-style-type: none"><li>Ambika Amatya, District Coordinator, HRRP Lalitpur and Bhaktapur District Team</li><li>Roshan Kesari, M &amp; E Consultant, CLPIU Building</li><li>Prabesh Adhikari, DSE, DLPIU Building Bhaktapur</li><li>Engineers (Bhargav Aryal, Kundan Jung Thapa, Nilam Moktan, Ranjana Suwal)</li></ul> |                                             |                   |
| Objective(s)                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                | <ul style="list-style-type: none"><li>To observe the reconstruction status of the houses and inspect the non-compliance cases.</li><li>To interact with beneficiaries and provide relevant suggestions further.</li><li>To take building typology on KoBo Collect App.</li></ul> |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| Why was the visit carried out in this location?                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| This Joint Monitoring Visit was the first visit of M & E Consultant, Er. Roshan Kesari, CLPIU Building/ DLPIU Building Bhaktapur. Therefore this field visit was the exposure to different kinds of shelter reconstruction taking place in different areas in Ward no. 5 & 6. The visit was carried out to observe some of the pending 2 <sup>nd</sup> tranche file of houses. The inputs from Er. Roshan Kesari, M & E Consultant has paved way forward for engineers to proceed further tranche approval of beneficiaries.                                                                                                                                                |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| 'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                        |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| <a href="https://drive.google.com/open?id=1EWErBpv2LEn-8YXV1FTUGRCjk0USubh3">https://drive.google.com/open?id=1EWErBpv2LEn-8YXV1FTUGRCjk0USubh3</a>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| <a href="https://drive.google.com/open?id=1Vo7EEB8RtR41q2BFS1Qku1aBbrS8lqW9">https://drive.google.com/open?id=1Vo7EEB8RtR41q2BFS1Qku1aBbrS8lqW9</a>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| Summary                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                     |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| HRRP Lalitpur and Bhaktapur Coordination Team along with M & E Consultant (CLPIU Building Bhaktapur), District Support Engineer and engineers of DLPIU Building Bhaktapur and of Suryabinayak Municipality conducted field visit Ward no 5 & 6 of Changunarayan Municipality. The field visit team observed nearly 6 houses in total. The field visit team observed various housing typologies, some of which were build before placement of engineers in municipality. One of the observed houses were in risk of landslide danger and was suggested to construct sheer wall or apply wall jacketing on back side of houses to ensure security of houses to maximum level. |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| Meeting with Technical personnel of Changunarayan Municipality                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| M and E Consultant advised technical personnel (engineers, sub engineers) of reconstruction unit to deliver as per the case load on their responsibilities. They were informed to conduct 3 <sup>rd</sup> inspection of the reconstructed houses regularly before the end of current fiscal year.                                                                                                                                                                                                                                                                                                                                                                           |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| Field Visit:                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| <ul style="list-style-type: none"><li>No. of HHs visited: 6</li><li>No. of meetings with engineers: 1</li><li>No. of meetings with local officials: None</li></ul>                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| Challenges / Issues Identified                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                              | Solutions Provided                                                                                                                                                                                                                                                               | Decision Taken                                                                                                                                                                                                                                                                                                                       | Responsible                                 | Timeframe         |
| Technical personnel of reconstruction unit in Palikas have increased volume of managing 3 <sup>rd</sup> inspection of houses as well as regular works.                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      | Technical personnel were informed to manage conducting 3 <sup>rd</sup> inspection of houses along with their regular works by end of Ashad 2076                                                                                                                                  | To conduct 3 <sup>rd</sup> inspection of reconstructed houses and fulfill the case loads.                                                                                                                                                                                                                                            | Engineers, DLPIU Building, M & E Consultant | By Ashad end 2076 |
|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |
| Photos                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |                                                                                                                                                                                                                                                                                  |                                                                                                                                                                                                                                                                                                                                      |                                             |                   |





Beneficiary name: Vikram Tamang, Ward no 6, Nagarkot, Naya Gaun, Changunarayan Municipality. 2.5 storey 6 roomed house is made from hollow concrete blocks. Lintel and sill band were found to be missing in infill however frame structure was found compliant. Beneficiary has received 1<sup>st</sup> tranche and M & E Consultant and DSE advised that house has eligibility to receive 2<sup>nd</sup> and 3<sup>rd</sup> tranche too.



Beneficiary name: Krishna Murai Khanal, Ward no 4, Sangda, Changunarayan Municipality. The beneficiary has been amended into retrofitting list. Nepal earthquake 2015 have made cracks on outer and inner walls, which was retrofitted by making retrofitting designs in consultation with certified agencies. Beneficiary has received 1<sup>st</sup> tranche and M & E Consultant advised for approval of further tranche too.

## Field Visit Reports (Bhaktapur)

### Visit 3

| Date                | Location                                                                                                                                                                                                                                                 | Participants                                                                                                                                                                                                                                                                                                               |
|---------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| 31 May 2019         | Ward no 4 (Balkot) and Ward no 10 (Chitapol), Suryabinayak Municipality                                                                                                                                                                                  | <ul style="list-style-type: none"> <li>Ambika Amatya, District Coordinator, HRRP Lalitpur and Bhaktapur District Team</li> <li>Roshan Kesari, M &amp; E Consultant, CLPIU Building</li> <li>Prabesh Adhikari, DSE, DLPIU Building Bhaktapur</li> <li>Engineers (Sandhya Dhakal, Pratima Neupane, Sweta Acharya)</li> </ul> |
| <b>Objective(s)</b> | <ul style="list-style-type: none"> <li>To observe the reconstruction status of the houses.</li> <li>To observe non-compliance cases. To provide inputs to beneficiary as way forward.</li> <li>To take building typology on KoBo Collect App.</li> </ul> |                                                                                                                                                                                                                                                                                                                            |

### Why was the visit carried out in this location?

The visit was carried out to observe some of the pending 2<sup>nd</sup> tranche file of houses. The visit was necessary in some wards as engineers were facing some pressures from beneficiaries in forwarding their 2<sup>nd</sup> tranche file in reconstructed houses in question with non-compliance. The inputs from Er. Roshan Kesari, M & E Consultant has paved way forward for engineers to proceed further tranche approval of beneficiaries.

### Summary

#### Field Visit:

- No. of HHs visited: 12
- No. of meetings with engineers: 1
- No. of meetings with local officials:

HRRP Lalitpur and Bhaktapur Coordination Team along with M & E Consultant (CLPIU Building Bhaktapur), District Support Engineer and engineers of DLPIU Building Bhaktapur and of Suryabinayak Municipality conducted field visit Ward no 4 and 10 of Suryabinayak Municipality. The field visit team observed nearly 12 houses in total. The field visit team observed various housing typologies in Ward no. 10, Chitapol. Load bearing BMC with flexible roof and RCC structures predominant in Chitapol areas. Majority of beneficiaries have received upto 2<sup>nd</sup> tranche and some houses were inspected for 3<sup>rd</sup> tranche. 3<sup>rd</sup> inspection was also conducted by technical personnel. Some beneficiaries have kept proper roof bands to become eligible for 3<sup>rd</sup> tranche. One beneficiary in retrofitting list at Ward no. 4, Balkot was suggested to conduct standard retrofitting of reinforcement jacketing whereby consulting with certified agencies.

#### Meeting with DLPIU GMALI Chief Bhaktapur

Joint M and E team interacted with Chief of GMALI Bhaktapur along with Specialist team of EHRP/GMALI Bhaktapur. Sharing of updated database of beneficiaries with their contact number and grant status was the main agenda of the interaction. The meeting also explored



possibilities of increasing coordination between DLPIU Building and GMALI offices to mobilise engineers in concerned ward offices of the assigned Palikas

| Challenges / Issues Identified                                                                      | Solutions Provided                                                                                                           | Decision Taken                                                                  | Responsible                 | Timeframe           |
|-----------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------|-----------------------------|---------------------|
| Beneficiaries are confused with repair works and standard retrofitting of the quake damaged houses. | Beneficiaries in question were informed to take advice from engineers of their palikas on retrofitting and standard designs. | To contact engineers for retrofitting designs and for further advice vice versa | Beneficiaries and engineers | As soon as possible |
|                                                                                                     |                                                                                                                              |                                                                                 |                             |                     |

#### Photos



Beneficiary name: Bhimsen Thapa, Ward no. 10 Chitapol, Suryabinayak Municipality, 2 storey, 8 roomed BMC wall system house is under reconstruction with rigid roof works going on. 3<sup>rd</sup> tranche process of the beneficiary is undergoing.




Beneficiary name: Deepak Thapa, Ward no. 10, Chitapol, Suryabinayak Municipality, 1.5 storey, 2 roomed BMC house with flexible roof has attic with 9 inch wall. Beneficiary has received 3<sup>rd</sup> tranche but were found to be non-complaint by M & E Consultant. RCC bands were used but beam were found missing. Engineers were advised to disallow giving house completion certificate to the beneficiary.

## Housing Typology Report



Beneficiary name: Amrit Lama, Ward no. 3, Bhattedanda, Bagmati Rural Municipality. Load bearing SMC. The house owner has request 2<sup>nd</sup> and 3<sup>rd</sup> tranche at the time of inspection in 13092018

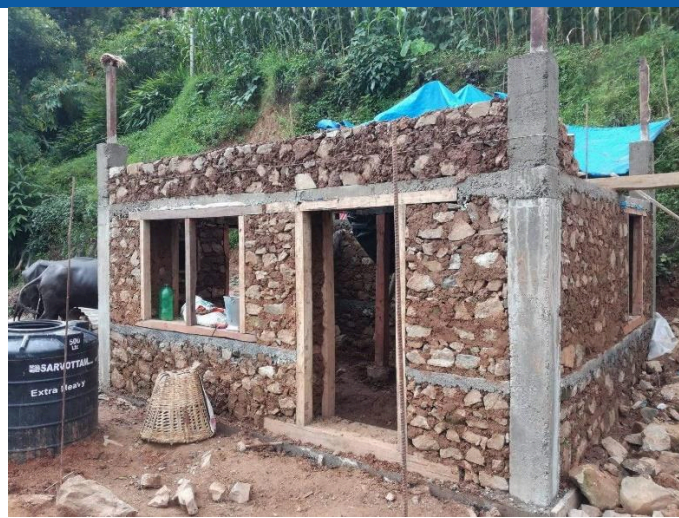

Beneficiary name: Sitaram Timilsina, Ward no. Bhattedanda, Bagmati Rural Municipality. 1 roomed Load bearing SMM with steel post and RC band. The house owner has request 2<sup>nd</sup> and 3<sup>rd</sup> tranche at the time of inspection in 14092018





Beneficiary name: Surya Basnet, Ward no. 5, Suryabinayak Municipality. RCC pillar system house has received all tranches at the time of inspection.



Beneficiary name: Laxmi Lal Shrestha, Ward no. 5, Madhyapur Thimi Municipality. RCC frame structure building has requested for 2<sup>nd</sup> and 3<sup>rd</sup> tranche at the time of inspection.

## Questions Collected

| Question                                                                     | Who Asked the Question? | Response Provided (By Whom)                                                                                                                                                                                                                                                                          |
|------------------------------------------------------------------------------|-------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| How can I receive further tranche in face of belonging to retrofitting list? | Beneficiary             | Intending beneficiary should take advice from engineers and from DLPIU Building office about needful retrofitting designs. Beneficiary have to conduct refotitting of their houses from trained masons after approved retrofitting designs are provided from technical personnel. (M & E Consultant) |

## Challenges and Way Forward

| Challenge                                                                                                          | Way Forward                                                                                                                                                                                                                                                                                                                                                                   |
|--------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| Non-enrolled beneficiaries are about to miss deadline of taking 1 <sup>st</sup> tranche for reconstruction purpose | Ward office should take affirmative actions as early as possible to inform non-enrolled beneficiaries before the closure of fiscal year of government of Nepal so that they can be brought into mainstream of housing reconstruction. If they are unintending to become beneficiaries of housing grant, then they should be encouraged to be removed from beneficiaries list. |
| Gaps between beneficiaries taking 1 <sup>st</sup> and 2 <sup>nd</sup> tranche is widening in many palikas.         | Concerned ward office and municipalities should immediately take proactive steps to inform beneficiaries to reconstruct their houses. For intending beneficiaries, concerned local bodies should inform them to return 1 <sup>st</sup> tranche.                                                                                                                               |

## Case Study



### **Regaining life through newly reconstructed house**

Rajesh Gopali was spending his days happily with his elderly mother, wife and one daughter Ward no 12, Thecho, Godawari Municipality. Nepal earthquake 2015 devastated his small family that took away life of his dear wife. His old house has hybrid structure with topmost floor done with concrete made and the rest of other floors with mud and bricks was destroyed. During the earthquake, floors with mud and bricks collapsed but the topmost concrete block remained as it is. Rajesh recalls, "even the rescue team was so scared to demolish the house and tried to use explosive which was not possible as it would affect the whole community.

After more than a week-long hardship under the open sky with just some sheets of tarpaulins, Lumanti, PO working in shelter sector in Kathmandu valley supported Rajesh Gopali with CGI sheets and bamboos to construct the temporary shelter in the neighboring land. Rajesh stated, "We were blessed to have Lumanti and their support for the needy people who are in poor and vulnerable situation in post earthquake situations. Life became more relatively easier in the temporary shelter soon after earthquake.

Now with the technical assistance and grant support from Lumanti, Rajesh has completed rebuilding of his 2 storey and 4 roomed house. Apart from grant support, he has also taken loan of NRs. 400,000 from local finance company with the interest rate of 11 percent. Rajesh has used portion of the his land for rebuilding house because of the budget constraints. Besides to minimize the cost, he also used salvaged materials. Rajesh is the only earning member of his family. Now life has returned to normalcy for Rajesh and to her old mother. He has accepted the reality that life must go on. He continues working as part time computer teacher in private school and runs coaching classes to meet the daily expenses.
