

Fortnightly District Report

Kathmandu Valley

1 – 14 February 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
A joint monitoring visit of DLPIU building Kathmandu and HRRP Kathmandu valley team to Ward no 1, 3, 7 of Dakshinkali Municipality, Kathmandu district was conducted.	31 Jan. 2019	4	2	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
A joint monitoring visit of DLPIU building Kathmandu and HRRP Kathmandu valley team to Ward no 3 and 8 of Shankharapur Municipality, Kathmandu district was conducted.	11 Feb 2019	4	1	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409	
HRRP Kathmandu Valley team together with National Team of HRRP conducted Municipality level coordination meeting at Lalitpur Metropolitan City (LMC), Pulchowk, Lalitpur. The coordination meeting has participation of Advisor of LMC, Ward Chairpersons of two wards-9 & 12 and focal Person of Reconstruction Unit of LMC. The meeting focused around the efforts taken by LMC regarding post-earthquake reconstruction and the initiatives related with disaster risk management.	14 Feb 2019	4	2	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley Team dc.ktm@hrrpnepal.org Contact: 9841356409	
HRRP Kathmandu Valley team together with National Team of HRRP coordinated the field visit for the representative of Active Learning Network for Accountability and Performance in Humanitarian Network (ALNAP) at Ward no.22, Bungamati, Lalitpur Metropolitan City.	14 Feb 2019	2	2	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley Team dc.ktm@hrrpnepal.org Contact: 9841356409	
Ward-level coordination meeting at Ward no. 22, Bungamati in presence of Ward Chairperson of Ward no. 22 along with members from HRRP, ALNAP, Lumanti and Bungamati Area Reconstruction Development Committee (BARDEC) was conducted.	14 Feb 2019	3	4	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley Team dc.ktm@hrrpnepal.org Contact: 9841356409	
Upload of training database and relevant other information has been updated in 5W.	1-14 Feb 2019			Ms. Manisha Rai IM Officer HRRP Kathmandu Valley im.ktm@hrrpnepal.org Contact: 9842062006	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Joint M & E visit to observe reconstruction efforts of beneficiaries in districts of Kathmandu Valley	Date- 2 nd - 4 th week of February 2019	HRRP Kathmandu valley team	Ms. Sweata Sijapati District Technical Coordinator HRRP Kathmandu Valley techcord.ktm@hrrpnepal.org
Municipality level and Ward level Coordination meeting to be conducted by HRRP Kathmandu Valley team in coordination with concerned Municipalities of Kathmandu valley	Date: 2 nd - 4 th week of February 2019	HRRP Kathmandu valley team	Ms. Ambika Amatya District Coordinator HRRP Kathmandu Valley dc.ktm@hrrpnepal.org Contact: 9841356409

News & Updates

- The NRA Steering Committee changed the tranche disbursement deadlines during the committee's meeting on 17 January 2019. The deadline for receiving the first tranche has been extended to the end of Asadh 2076 (16 July 2019). The deadline for receiving the second and third tranches has been removed, but households are requested to apply for the tranches as soon as possible.
- The survey of the beneficiaries conducted in Rural Municipalities of the Lalitpur with initiation from DLPIU- GMaLi Lalitpur and support from HRRP showed that the delay in the tranche disbursement was mainly due to inadequate construction space, Weak financial condition and the beneficiaries being involved in foreign employment. The finding showed around 44% of the surveyed beneficiaries are have not able to get the 2nd and 3rd tranche as they build their houses before the introduction of the technical guideline by NRA. *(For further details on this contact Mr. Yamnath Giri, M&E specialist, DLPIU-GMALI; contact no. 9851239785)*

Tranche Update

Kathmandu Reconstruction Update as of 15 Jan 2019

Rural /Municipality	Kageshwori NP	Kathmandu MNP	Kirtipur NP	Gokarneshwor NP	Chandragiri NP	Tokha NP	Tarkeshwor NP	Dakshinkali NP	Nagarjun NP	Budhanilkant ha NP	Shankharapur NP
Total HHs Eligible	3667	7496	2935	2935	5695	1746	6151	4085	4338	2693	6058
Total HHs Enrolled	3279	5973	2475	2523	5041	1579	5191	3784	4106	2056	5545
First Tranche	3306	5958	2459	2517	4986	1550	5160	3755	4102	2056	5510
Second Tranche	1605	1336	893	1267	1367	612	1659	1254	1331	951	2175
Third Tranche	906	1042	709	1001	977	465	1354	816	1024	711	1501
Total HH Constructed	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Grievance Registered	N/A	N/A	1275	1962	1291	369	2493	1096	851	547	1665
Grievance Addressed	N/A	N/A	208	1158	695	335	2186	753	545	308	340
RF HH Eligible	75	173	44	20	128	48	107	52	38	11	110

RF HH Enrolled	23	30	16	7	46	25	33	29	4	2	40
RF 1st Tranche	23	30	16	7	46	25	33	29	4	0	40
RF 2nd Tranche	0	0	0	0	0	0	0	0	0	0	0
Non-Compliance Registered	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Non-Compliance Addressed	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A

Bhaktapur Reconstruction Update as of 24 Jan 2019


Rural /Municipality	Bhaktapur NP	Changunarayan NP	Madhyapur Thimi NP	Suryabinayak NP
Total HHs Eligible	7622	10937	2333	7416
Total HHs Enrolled	5596	9680	2052	6955
First Tranche	5596	9680	2052	6955
Second Tranche	1528	2758	604	2252
Third Tranche	1354	2624	567	2141
Total HH Constructed	N/A	N/A	N/A	N/A
Grievance Registered	1592	2096	2407	1926
Grievance Addressed	1542	1692	1431	1665
RF HH Eligible	148	212	101	233
RF HH Enrolled	39	85	56	97
RF 1st Tranche	39	85	56	97
RF 2nd Tranche	0	0	0	0
Non-Compliance Registered	N/A	N/A	N/A	N/A
Non-Compliance Addressed	N/A	N/A	N/A	N/A

Lalitpur Reconstruction Update as of 15 Jan 2019


Rural /Municipality	Lalitpur MPC	Godawari UM	Mahalaxmi UM	Mahankal RM	Bagmati RM	Konjyosom RM
Total HHs Eligible	3370	9588	7350	2154	3657	2267
Total HHs Enrolled	3051	7895	6297	2042	3056	2230
First Tranche	3039	7804	6297	2041	3031	2228
Second Tranche	2245	2228	1123	1646	741	1599
Third Tranche	1539	1727	675	1128	613	866
Total HH Constructed	N/A	N/A	N/A	N/A	N/A	N/A
Grievance Registered	2809	N/A	863	549	882	919
Grievance Addressed	865	N/A	795	294	658	484
RF HH Eligible	281	325	90	61	252	372
RF HH Enrolled	119	66	16	43	58	253
RF 1st Tranche	119	66	16	43	58	253
RF 2nd Tranche	0	0	0	0	0	0
Non-Compliance Registered	N/A	N/A	N/A	N/A	N/A	N/A

Non-Compliance Addressed	N/A	N/A	N/A	N/A	N/A	N/A
--------------------------	-----	-----	-----	-----	-----	-----


Graph of Reconstruction Status in Kathmandu as of 15 Jan 2019:

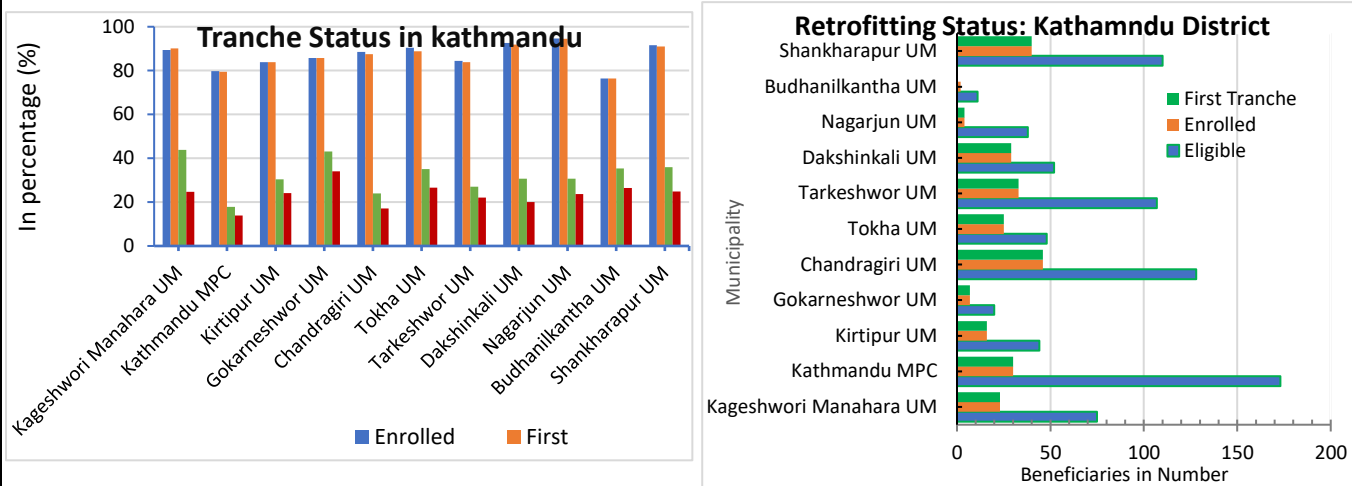


GRIEVANCE STATUS: KATHMANDU DISTRICT

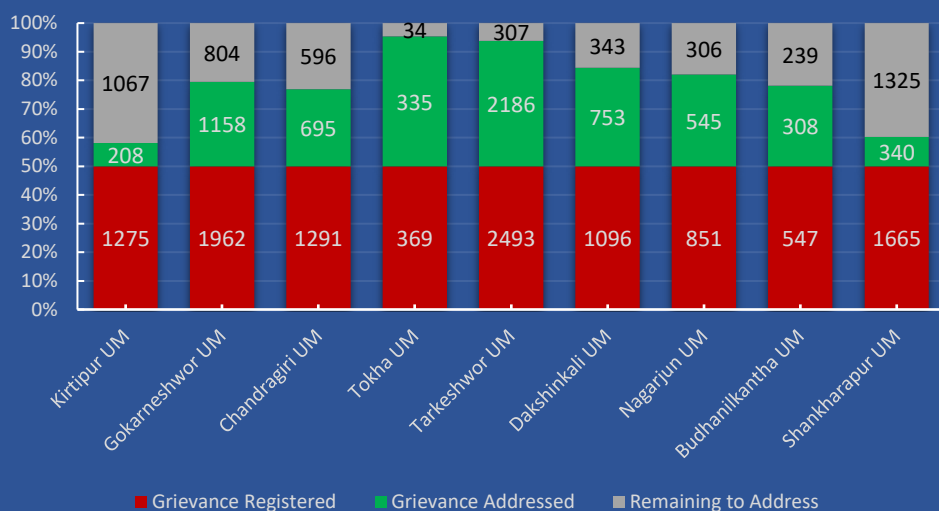

Bhaktapur Reconstruction Update as of 24 Jan 2019

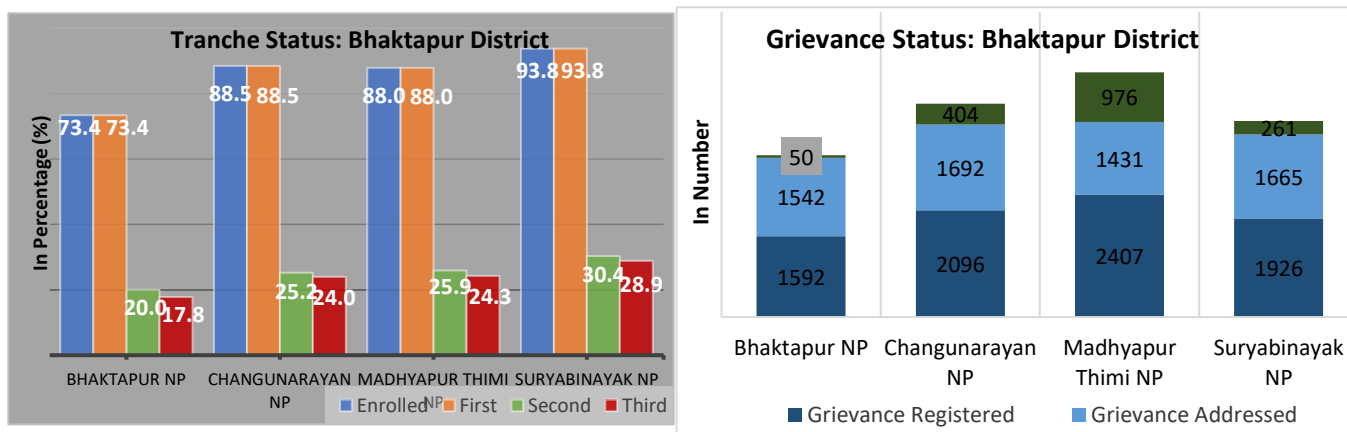


RETROFITTING STATUS: BHAKTAPUR DISTRICT

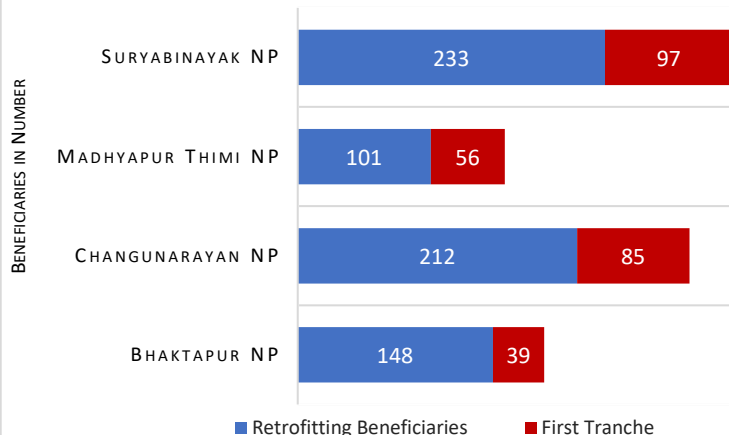


Lalitpur Reconstruction Update as of 15 Jan 2019


Tranche Status in Lalitpur District

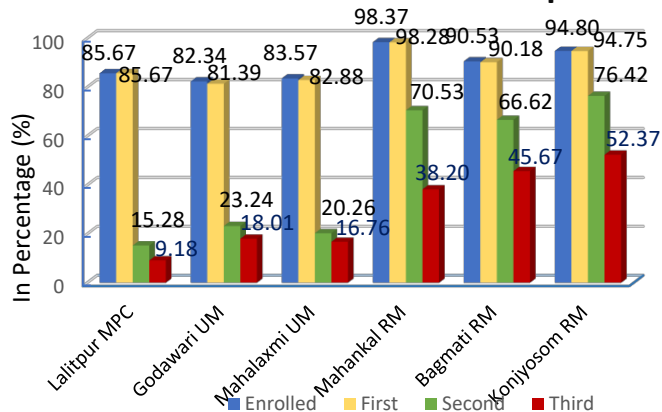

GRIEVANCE STATUS: LALITPUR DISTRICT

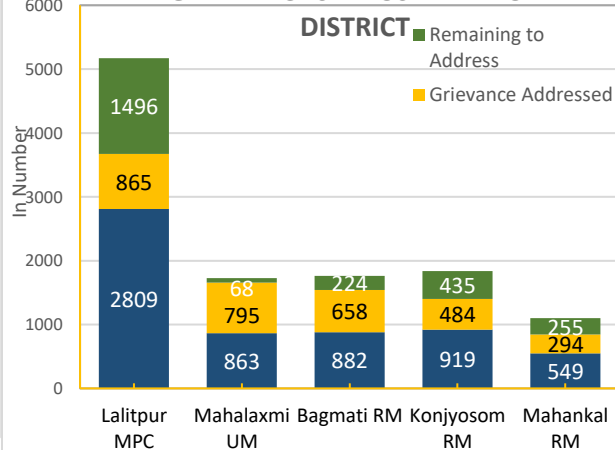

RETROFITTING STATUS: LALITPUR DISTRICT

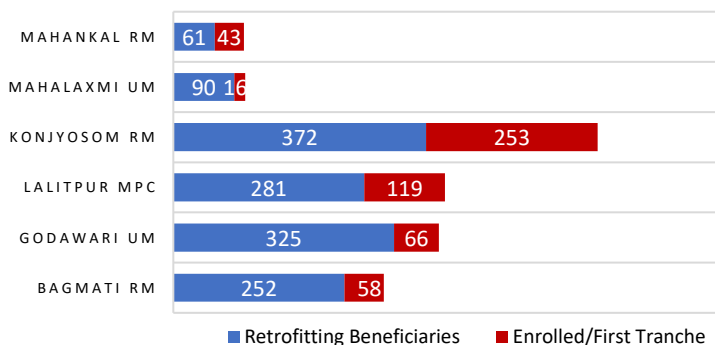

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders	
31 January 2018	Ward no 1, 3, 7 Dakshinkali Municipality	- Ambika Amatya, District Coordinator, HRRP Kathmandu Valley - Narakanta Sapkota, M & E Consultant, DLPIU NRA Building Kathmandu - Bidhya Manandhar, District Support Engineer, DLPIU NRA Building Kathmandu - Prajwol Karki, District Support Engineer, DLPIU NRA Building Kathmandu - Dinesh Bista, Engineer, Dakshinkali Municipality - Prithvi Man Shrestha, Engineer, Dakshinkali Municipality	
Objective(s)		- To conduct Municipality and Ward-level coordination meeting regarding the joint M & E visit - To observe houses in reconstruction phases as well as to observe non-compliance cases. - To interact with beneficiaries and provide suggestions for correcting the non-complaint structures. - To take case study of vulnerable beneficiaries that have taken up to 1st tranche but not reconstructed houses.	
Summary		HRRP Kathmandu valley team along M & E Consultant and District Support Engineer from DLPIU Building Kathmandu conducted joint M & E visit at Ward no. 7, 3, 1 of Dakshinkali Municipality on 31st January 2019. A total of 20 houses were observed during the visit. The field visit started with a brief interacted with the Executive Officer of Dakshinkali Municipality and Ward Chief of Ward no. 3, Bhangyang. The team focused on interacting with beneficiaries whose house was listed as non-compliance and suggested the correction measures to be eligible for the government tranche. Many houses were found to be in the reconstruction stage while few had completed the construction and applied for the 2nd and 3rd tranche. District Support Engineer clearly cross checked the non-compliant cases and suggested beneficiaries for applying appropriate correction measures or retrofitting procedures. Some of the observed houses have kept rolling shutters but had maintained minimum standards too. Few case studies of vulnerable beneficiaries were collected from Ward no. 3, who have yet not rebuilt their houses as being single women and disabled has added to difficulty in getting timely information on the reconstruction process, lack of easy access to banks and so on.	
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Many beneficiaries who are vulnerable and will not be able to reconstruct even a low-cost housing unit.	Concerned Ward office should compile and report this issue to Municipality board. If needed such issues should be taken to concerned unit at NRA for its proper address	Ward office, Municipality office, DLPIU Engineers	As soon as possible
Construction of one roomed house are increasing in number.	One room structure needs to be discouraged as such houses may not meet the shelter	Ward office, Municipality office, DLPIU Engineers	As soon as possible

	requirements of beneficiaries for longer terms. Further, 1 room structures were found to be reconstructed for taking government tranches only and were found to have missed minimum requirements too.		

Photos



Beneficiary name: Akrur Acharya, Ward no 7, Ratmate, Gopaleswor, Dakshinkali Municipality. 1.5 storey, 4 roomed BMC structure. The cantilever part of this house is supported by 4 show columns just started from plinth beam to 1st floor beam. The beneficiary has received all three tranches from government. A total of 34 lakh were spend in reconstruction of this structure as reveled by beneficiary. During M & E visit, District Support Engineer has discovered flaws on column, so the beneficiary was suggested to provide jacketing to the columns for that the house to be safe. Further, DSE of DLPIU Building Kathmandu will study the file of this house in detail.



Beneficiary name: Sanubhai Acharya, Ward no. 7, Yutiki, Dakshinkali Municipality. 2 storey RC frame structure. The beneficiary has received all 3 tranches from government.



Beneficiary name: Laxman Rimal, Ward no .7, Yutiki, Dakshinkali Municipality. Single storey 1 room BMC house with CGI sheets has missed majority of bands. Beneficiary has received 1st tranche only and were suggested to keep bands to become eligible for further tranches.



Beneficiary name: Kale Nagarkoti, Ward no. 1, Champadevi, Dakshinkali Municipality. Single storey BMC structure has 2 rooms with rolling shutters. M & E consultant has suggested to keep I- beam on two sides of shutters to make the structure safe. The beneficiary has received up to 2nd tranche from government.

Visit 2			
Date	Location	Participants from HRRP and stakeholders	
11 February 2019	Ward no. 3, Jaharsinghpauwa and Ward no 8, Bajrayogini of Shankarapur Municipality, Kathmandu	- Ambika Amatya, District Coordinator, HRRP Kathmandu Valley - Narakanta Sapkota, M & E Consultant, DLPIU NRA Building Kathmandu - Naveen Chaudhary, Engineer, Shankharapur Municipality - Aman Shrestha, Engineer, Shankharapur Municipality - Sunil Bhatt, Sub-Engineer, Shankharapur Municipality	
Objective(s)		- To conduct Ward- level coordination meeting and discuss on reconstruction related issues and challenges in the ward. - To observe houses in reconstruction phases as well as to observe non-compliance cases. - To interact with beneficiaries and provide suggestions for correcting the non-complaint structures.	
Summary		HRRP Kathmandu valley team along M & E Consultant from DLPIU Building Kathmandu conducted joint M & E visit at Ward no. 8, 3 of Shankharapur Municipality on 11th January 2019. A total of 12 houses were observed by the joint monitoring team. The team interacted with Ward Secretary of Ward no. 4, Phedi, Shankharapur Municipality. It was found that in Ward no. 4 Phedi, LWF have supported to rebuild 6-7 houses in total and few houses by Lumanti. These POs provided material support worth NRP.300,000 to the beneficiaries. Reported by Ward office, Ward no. 4, few beneficiaries in Phedi areas are living on Aelani land (Government land) without any legal documents. The visit team informed the Ward Secretary for mainstreaming the unheard beneficiaries through the last grievances process so that they can access reconstruction grant from the Government. In Jaharsinghpauwa, Ward no. 3 and ward no 8 majority of building typology were single storey made by hollow concrete block, interlocking bricks with flexible roof and BMC in single storey and maximum of 4 rooms houses with flexible roof. Many of such houses in have accessed up to 3rd tranche while some have processed documents for 2nd tranche. The team also interacted with beneficiaries and suggested for correction measures for their non-complaint houses. The engineer responsible for Ward no. 8 has revealed that delay in reconstruction of majority of houses is due to land ownership issues and multiple beneficiaries residing in the damaged house. Because of this, most of the beneficiaries are forced to continue living in the damaged houses and have not initiated the reconstruction work.	
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Many beneficiaries in Ward no. 4, Phedi, Shankharapur Municipality who are residing on government owned land without authorized land ownership documents are likely to be missed from mainstream reconstruction process.	Ward officials should proactively address land ownership issues particularly of beneficiaries living on government owned lands. Public inquiry deed process can be applied to solve this kind of issues.	Municipality, Ward office	By Baishak 2076

Photos



Beneficiary name: Gyanu Lama, Ward no. 3 Jaharsinghpauwa, Shankharapur Municipality, Kathmandu. Single storey, 4 roomed BMC house has plan to keep 1 rolling shutter. The beneficiary has received up to 2nd tranche. M & E consultant have suggested beneficiary to keep reinforcements and to do casting of 4 inch on two sides each to be eligible for the grant.



Beneficiary name: Biman Moktan, Ward no. 8, Moktan Tole, Bajrayogini, Shankharapur Municipality, Kathmandu. 4 roomed BMC house has approved building drawing up to 1st storey only. Beneficiary has received up to 2nd tranche. M & E Consultant have suggested this house as complaint house and is eligible for 3rd tranche too. Beneficiary were suggested not to add another storey.



Ward no. 8, Moktan Tole, Bajrayogini, Shankharapur Municipality. Out of 591 beneficiaries of Ward no .8, around 60-65 houses belong to beneficiaries of Moktan Tole. 2015 Gorkha Earthquake had damaged most of the BMM 2 storey with attic houses in Moktan Tole. Majority of beneficiaries of Moktan Tole have received 1st tranche however very less have started reconstruction of their houses. Few beneficiaries have accessed up to 3rd tranche while few of them have submitted documents for 2nd and 3rd tranche together.



Beneficiary name: Som Maya Tamang, Ward no. 8, Moktan Tole, Bajrayogini, Shankharapur Municipality. 3 roomed single storey house is made of interlocking bricks with CGI roof. Beneficiary has accessed up to 2nd tranche. M & E Consultant have suggested this house as a complaint house and is eligible for 3rd tranche too and thus informed ward engineer to forward documents for 3rd tranche approval.

Visit 3

Date	Location	Participants from HRRP and stakeholders
14 February 2019	Ward no. 22, Bungamati, Lalitpur Metropolitan City	- Leah Campbell, Senior Research officer, ALNAP - Ruplal Aidi, National Coordination Officer, HRRP - Ambika Amatya, District Coordinator, HRRP Kathmandu Valley - Newton Maharjan, Monitoring and Documentation Officer, Lumanti

Objective(s)	• To conduct Ward- level coordination meeting and discuss on reconstruction related issues and challenges in the ward. • To observe reconstruction efforts undertaken in Ward no. 22. • To interact with beneficiaries living in temporary shelters.		
Summary	HRRP Kathmandu Valley team together with National Team of HRRP coordinated the field visit for representative of Active Learning Network for Accountability and Performance in Humanitarian Network (ALNAP) at Ward no. 22, Bungmati, Lalitpur Metropolitan City dated 14 February 2019. The visit team also interacted with Ward Chairperson of Ward no. 22, Bungamati, Lalitpur Metropolitan City in presence of Ward members, staff from Lumanti and Bungamati Area Reconstruction Development Committee (BARDEC). There are four POs involved in reconstruction efforts taking place in Bungamati; Center for Integrated Urban Development (CIUD) in infrastructure development, Lumanti in social mobilization, Sabah Nepal in carrying forward income generation initiatives and BARDEC looking after regeneration and reconstruction of culturally important heritage monuments. Currently NRA in direct coordinating with BARDEC is reconstructing Rato Machhindranath temple, which is financially supported by the Government of Srilanka. The main highlight of Bungmati is the temple of Rato Machhindranath, where the idol of Machhindranath, or Bungadya, is placed for six months each year. Bungamati was also one of the worst-hit locations in the valley by the 2015 earthquake. A Newa village with most of its construction being traditional-style homes, recorded damage of over 800 houses. The key challenges of reconstruction highlighted in Ward no. 22 is related with maintaining the cultural authenticity of heritage areas, addition of extra storeys by beneficiaries other than mentioned in building drawing, disputes over land ownership among multiple beneficiaries and small land parcel. Lack of proper awareness among beneficiaries about building bylaws and minimum requirements have questioned the resilience capacity of the reconstructed houses		
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Beneficiaries from around 15-16 households are still residing in temporary shelters as their land ownership cases were not solved.	Ward officials should proactively address land ownership issues particularly of multiple beneficiaries living on small parcel.	Municipality, Ward office	By Baishak 2076
Photos			
			
The reconstruction and restoration project of the Rato Machhindranath Temple located at Ward no. 22 Bungamati, Lalitpur Metropolitan City is underway. Government of Srilanka is providing support for reconstruction of culturally important heritage monument. NRA is directly coordinating		Photo: The reconstruction of <i>Satta</i> - in Nepali (religious houses in English) was supported by UN-Habitat after it was damaged by the 2015 earthquake. Cultural authenticity of this culturally important religious house was maintained during its reconstruction process. Bungamati Area Reconstruction	

with Bungmati Area Reconstruction Development Committee (BARDEC) for reconstruction of Bungamati temple as well as regeneration of other heritage monuments.

Development Committee (BARDEC) has set up its contact office in the 2nd floor of the *Sattal*.



This house on reconstruction process is standing alone in between the earthquake damaged BMM houses on same row at Ward no. 22 Bungmati, Lalitpur Metropolitan City. The earthquake damaged houses belongs to multiple beneficiaries who are still residing in temporary shelters.



Beneficiary name: Ramkrishna Tuladhar, Ward no. 22, Bungmati, Lalitpur Metropolitan City. Single bay and 3.5 storey BMC structure has received 1st tranche only and applied for 2nd tranche. The beneficiary still resides in temporary shelters.

Housing Typology Report




Beneficiary name: Mangal Tamang Ward no. 8, Pakhure, Nagarjun Municipality. RC frame structure has 3 rooms with single storey. The beneficiary has received all tranches



Beneficiary name: Dhalak Bahadur Tamang, Ward no 8, Bhirkot. Load bearing BMC structure with CGI covering in the second floor. The beneficiary has already received 2nd tranche and requested for 3rd tranche but as the room size is larger the house was found to be non-compliance. The correction measure was suggested to be eligible for the tranche.



Beneficiary name: Shyam Prasad Gartaula, Ward no 8, Pakhure, Nagarjun Municipality. Load bearing BMC structure in 1 storey house with 4 rooms. Beneficiary has received all three tranches.

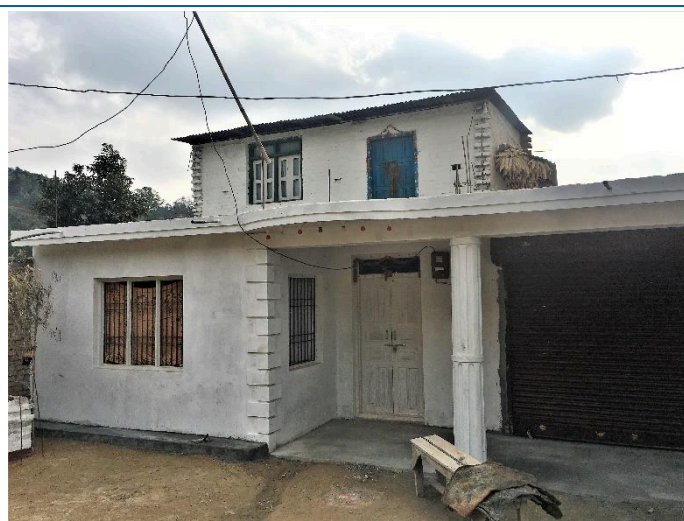

Beneficiary name: Ajay Khadka, Ward no 10, Suryabinayak Municipality. Load bearing wall system BMC house, single storey with 14 inch and with rolling shutter with proper connection.

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Is government going to extend the deadlines to claim 2 nd and 3 rd tranche?	Ward Secretary, Ward no. 4, Shankharapur Municipality	Even though the government plans to extend the deadlines to claim 2 nd and 3 rd tranche, it is solely the first responsibility of beneficiaries to remain alert about government tranches and its timeline. The ward office is equally responsible to inform its ward residents to undertake reconstruction as early as possible as well as to collect unsolved grievances for the last time. All the efforts contribute to accessing government grants in time. (M & E Consultant, CLPIU Building)

Challenges and Way Forward

Challenge	Way Forward
The unsolved cases of land ownership among multiple beneficiaries could further delay the reconstruction of houses.	The elected ward officials should broadly and proactively take this issue and consult with beneficiaries and their siblings for addressing the land ownership issues as early as possible so that deadlines of accessing 2 nd and 3 rd tranche can be met on time.
