

District Report

Dhading

15 February - 14 March 2019

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
HRRP Dhading Team together with GMaLI, Building DLPIU & DCC conducted informal meeting regarding District coordination meeting.	15 Feb. 2019			dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org	NA
The HRRP conducted District coordination meeting on 18th February 2019 at District coordination committee office. CDO Mr. Bhagirath Pandey was invited as chief guest where the meeting was chaired by DCC chief Mr. Jagannath Nepal. DAO, DCC, NRA/GMaLI, DLPIU/Building, SSN, CARE-Nepal, ICDC-Nepal, PIN, HIMS-Nepal, NGO Federation-Dhading, CSRC, NSET, TI Nepal, Purnima Mott Mac Donald, DEC Nepal shared their monthly update.	18 Feb 2019			techcord.dhading@hrrpnepal.org	Link to GD Meeting Minute
HRRP Dhading Team together with Building DLPIU Team, NSET, M & E CLPIU, DSE conducted informal meeting regarding issues occurred in Salyantar, Tripurasundari Rural Municipality	21 Feb 2019			dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org	NA
A joint monitoring visit of CLPIU M & E and HRRP team to Thakre & Siddhalekh Rural Municipality was conducted. The visit was focused on collecting data and updating Palika Profiles in Municipal websites	26-28 Feb 2019			dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org	Field Visit Section below
A joint monitoring visit of DLPIU Building and HRRP team to Salyantar of Tripurasundari Rural Municipality was conducted. The visit was also focused on collecting data and updating Palika Profiles in Municipal websites	26-28 Feb 2019			dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org	Field Visit Section below
Data Collection and Updating Palika Profiles in Municipal websites of different palikas of Dhading. i.e. Dhunebesi Municipality, Thakre Rural Municipality, Gajuri Rura Municipality, Benighat Rorang Rural Municipality and Nilkhantha Municipality.	25-28 Feb 2019			dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org	NA

Summary of events during this period

District coordination Committee conducted bi-Annual progress review and interactive program at DCC hall, Dhading where 13 Palikas presented their progress respectively.	27 Feb 2019			techord.dhading@hrrpnepal.org	Refer News & Update Section
Housing Typology Update	1 March 2019			techord.dhading@hrrpnepal.org	
Palika Action plan update and upload at palika websites: 9 out of 13 palika action plans have been compiled and uploaded at respective palika website.	5-8 March 2019			dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org	
Joint field visit with CLPIU- M & E, TI-Nepal, DLPIU/building and HRRP team at Jwalamukhi RM, Siddhalekh RM (Salang VDC) and Nilkhantha municipality – 6 (Sunaulobazar) was conducted. The visit was focused on typology collection, palika action plan and palika/ward meeting on reconstruction.	11-14 March 2019			dc.dhading@hrrpnepal.org	Field Visit Section below



Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
Orientation on Hollow Concrete Block (HCB)	18th March 2018. at Hotel R.K.	HRRP	dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org
District Coordination meeting	18th March 2018 on 3:00 PM. at Hotel R.K.	HRRP	dc.dhading@hrrpnepal.org techord.dhading@hrrpnepal.org


Tranche Status

Rural /Municipality	Beni Ghat Rorang RM	Dhuni Besi M	Galthi RM	Gangajamuna RM	Gajuri RM	Jwalamukhi RM	Khaniyabas RM	Netrawati RM	Nilkhanta M	Ruby Valley RM	Siddhalekh RM	Thakur RM	Tripurasundari Rm	Total
Total HHs Surveyed	5501	7499	6724	6732	5625	6014	3632	4016	13471	3270	5975	6722	6474	81655
Total HHs Eligible	4910	7158	5997	6447	5105	5390	3469	3866	12183	2850	5359	6384	5697	74815
Total HHs Enrolled	4349	6582	5657	6339	4655	4910	3392	3694	11601	2734	5034	6024	5561	70532
First Tranche	4349	6582	5657	6339	4655	4910	3392	3694	11601	2734	5034	6024	5561	70532
Second Tranche	3682	4328	4978	5637	4100	3760	2948	3274	9514	2282	4358	4753	4878	58492
Third Tranche	2393	2901	2300	3958	2602	2664	1837	2708	7134	1537	3045	2751	3343	39173
Total HH Constructed	2507	3177	2545	4252	2731	2848	1874	2782	7826	1615	3395	3419	3499	49470
Grievance Registered	1690	1067	1273	720	1427	2424	658	641	2394	650	1521	1310	1002	16777
Grievance Addressed	599	356	728	285	530	700	164	153	1374	420	640	341	785	7075
RF HH Eligible	618	98	314	42	432	675	12	43	559	187	463	255	215	3913
RF HH Enrolled	618	98	314	42	432	675	12	43	559	187	463	255	215	3913
RF 1 st Tranche	0	9	36	2	45	35	0	1	53	43	0	10	10	244
RF 2 nd Tranche	0	0	0	0	0	0	0	0	0	0	0	0	0	0
NC Registered	22	252	130	31	268	87	7	27	281	0	291	275	144	1815
NC Addressed	20	174	91	27	207	73	7	22	210	0	219	160	126	1336


Palika wise Trache Status :-

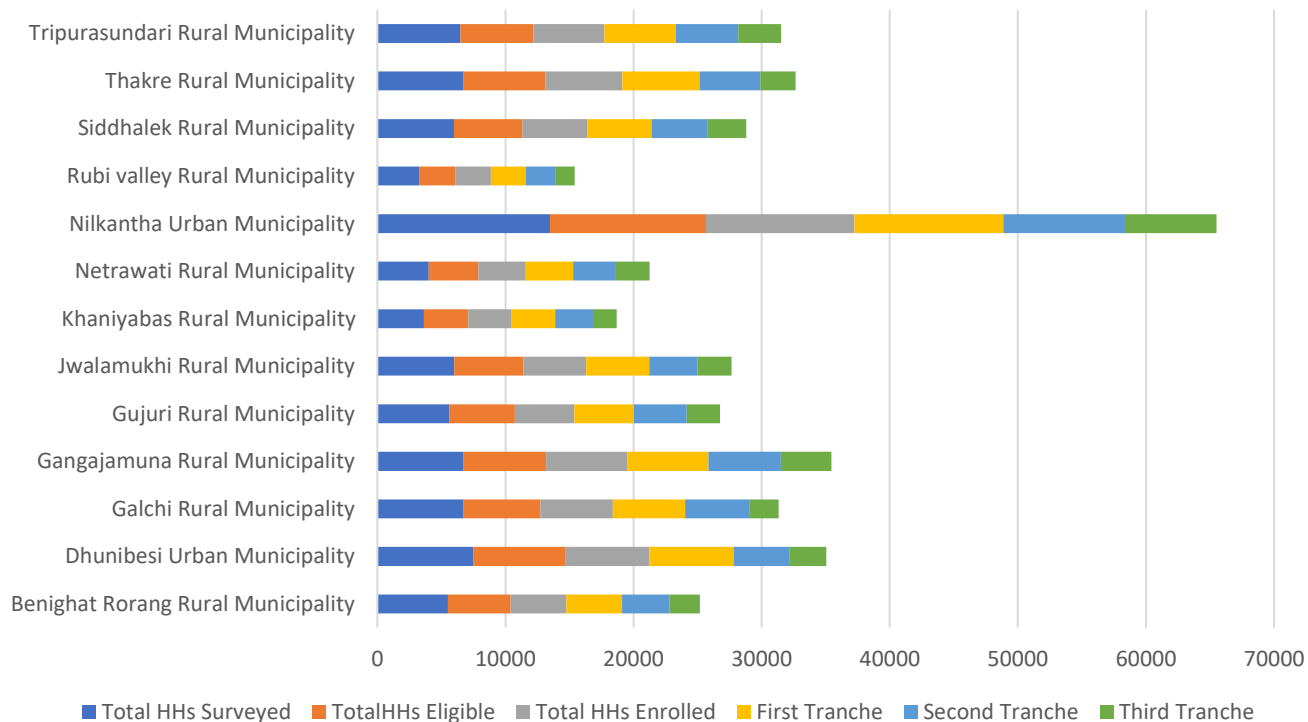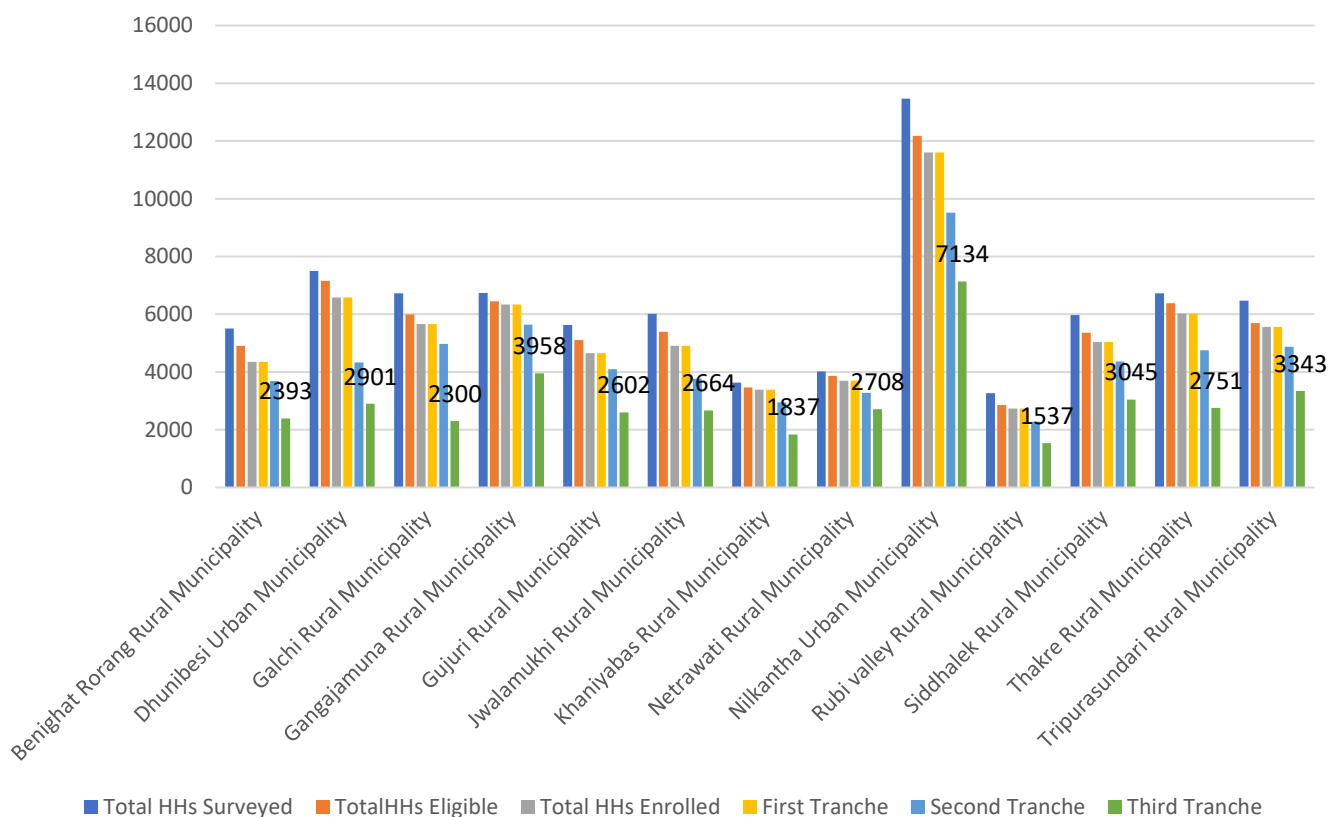


Total HH Constructed

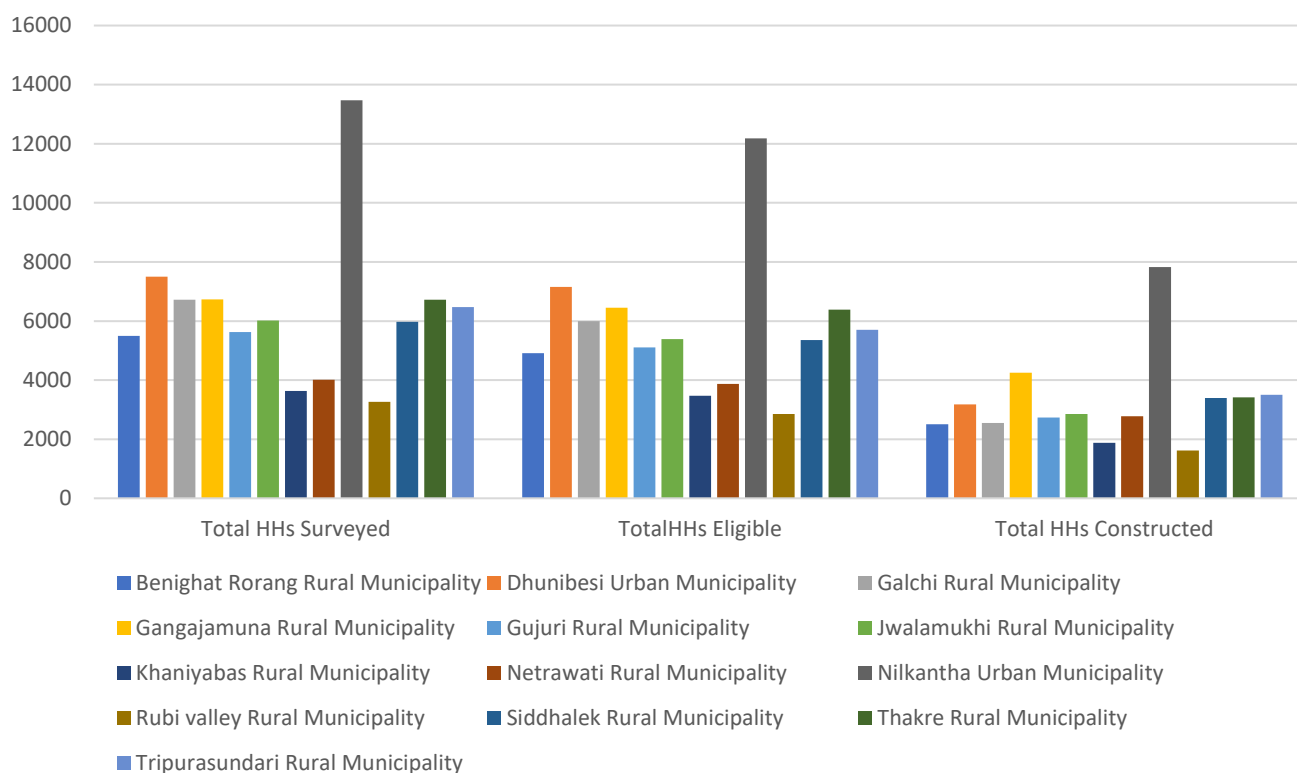




Palika wise Retrofitting Status :-

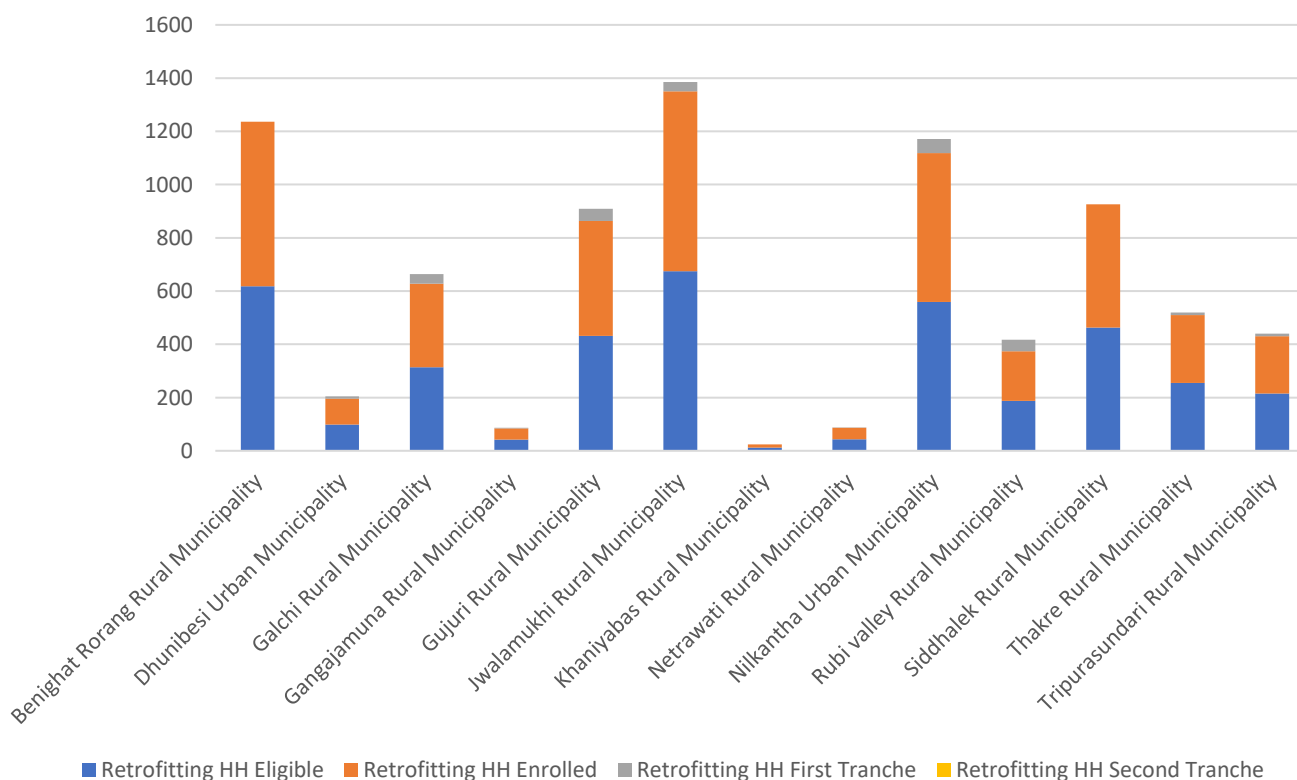

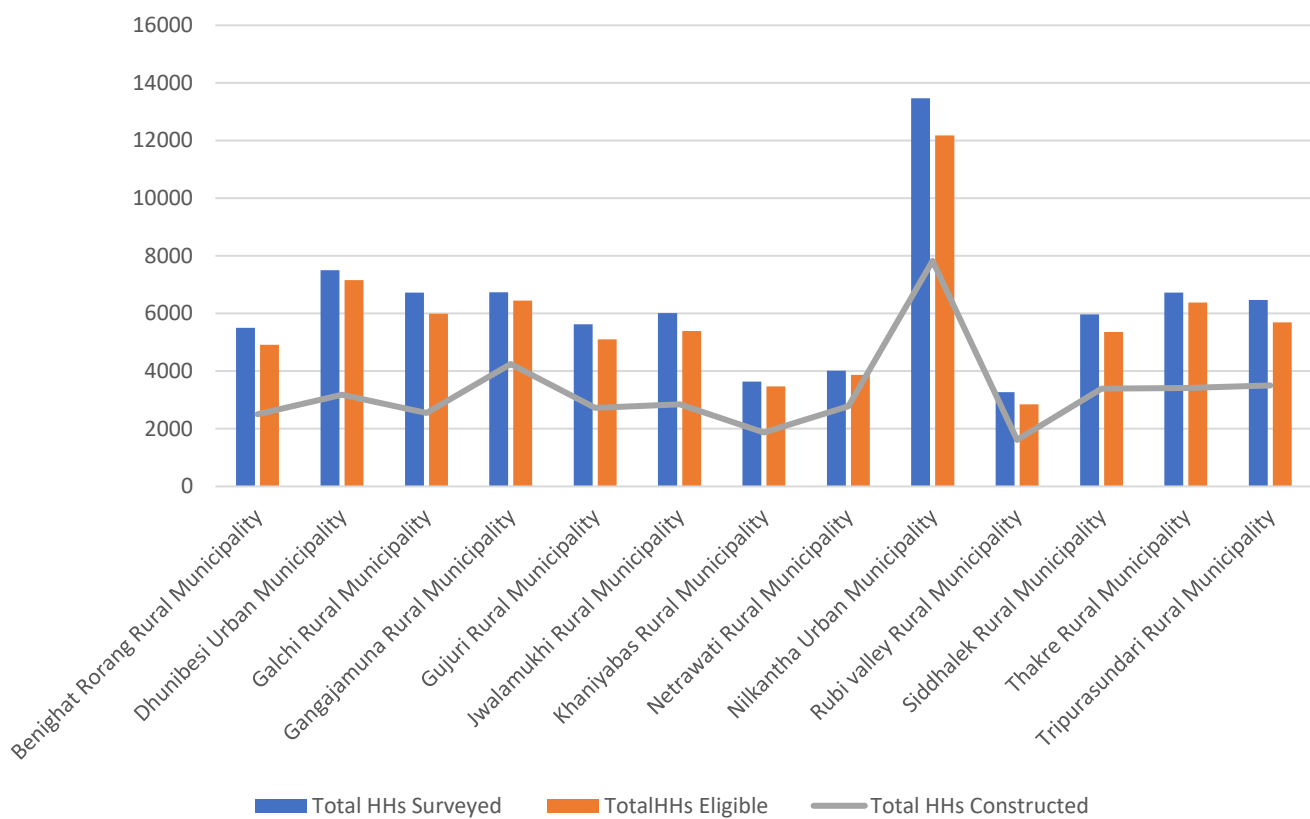

Grievance Status

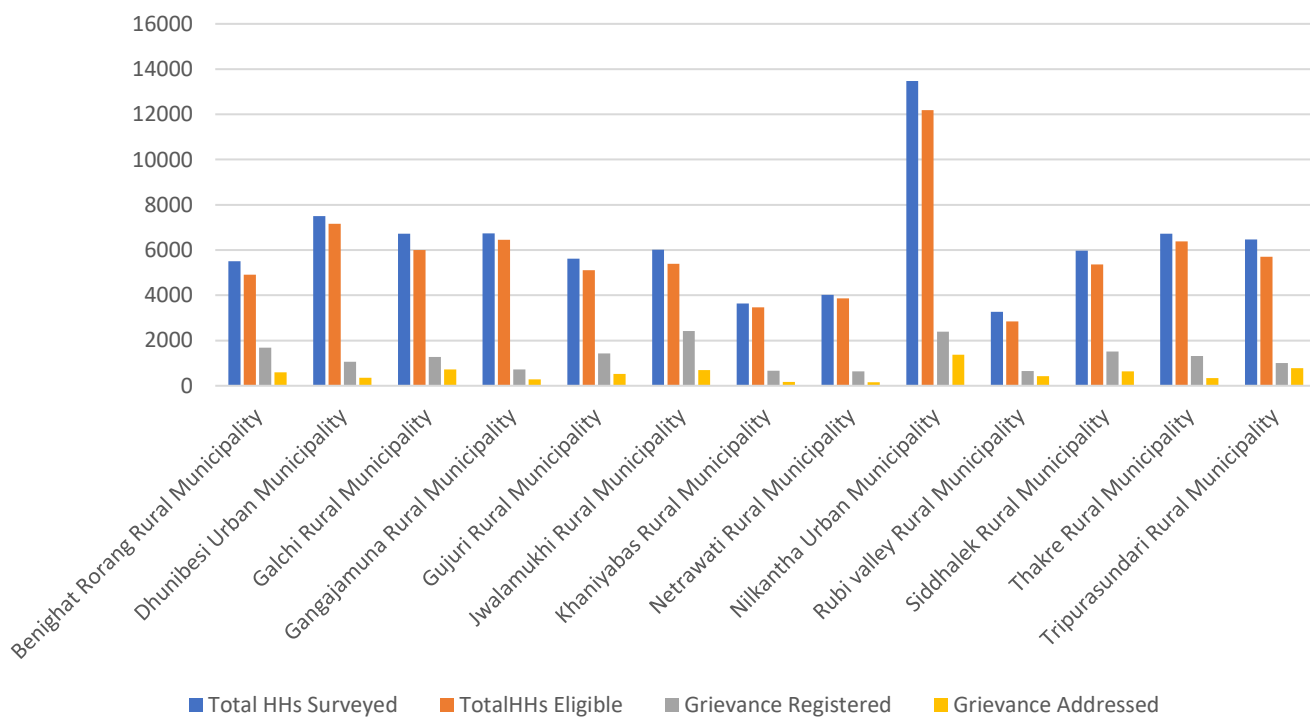

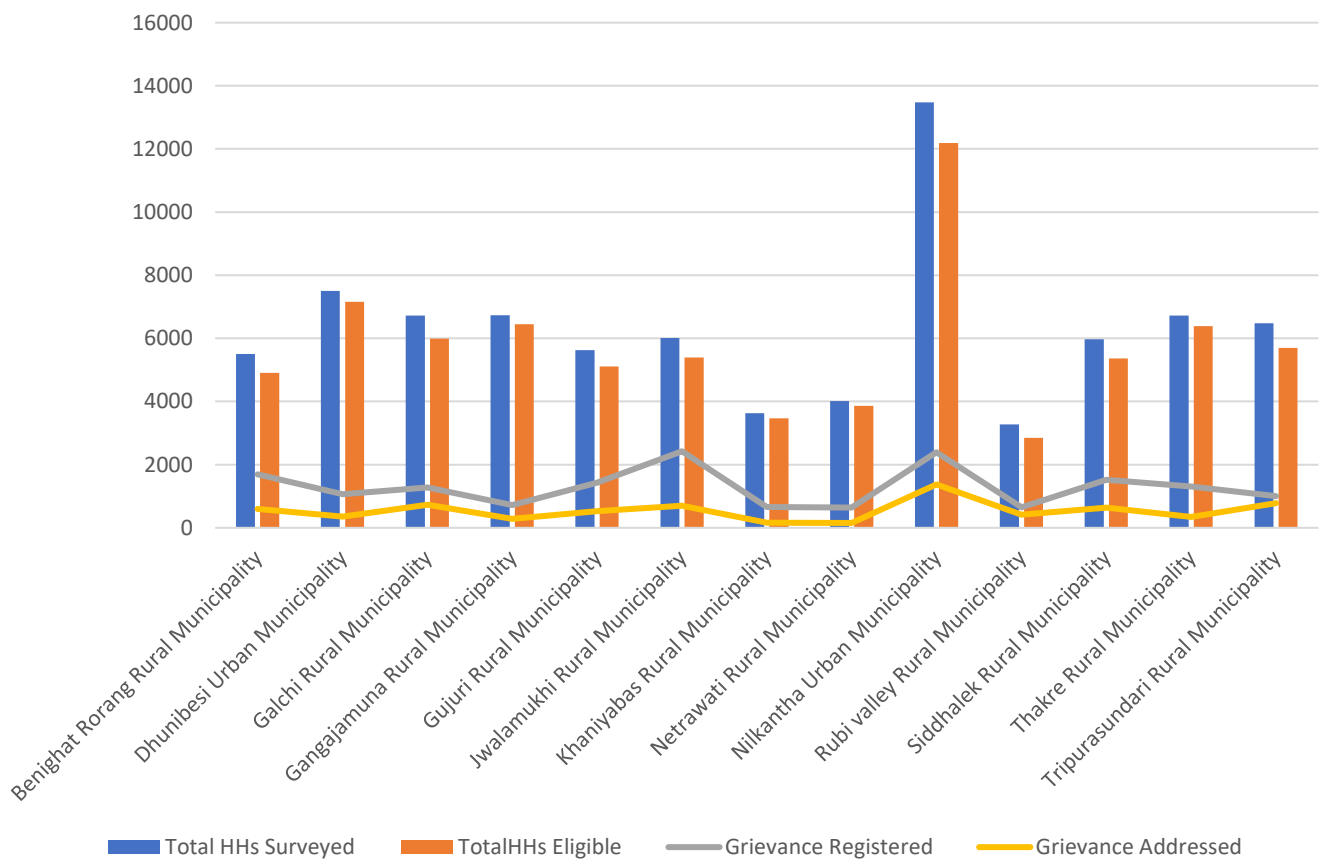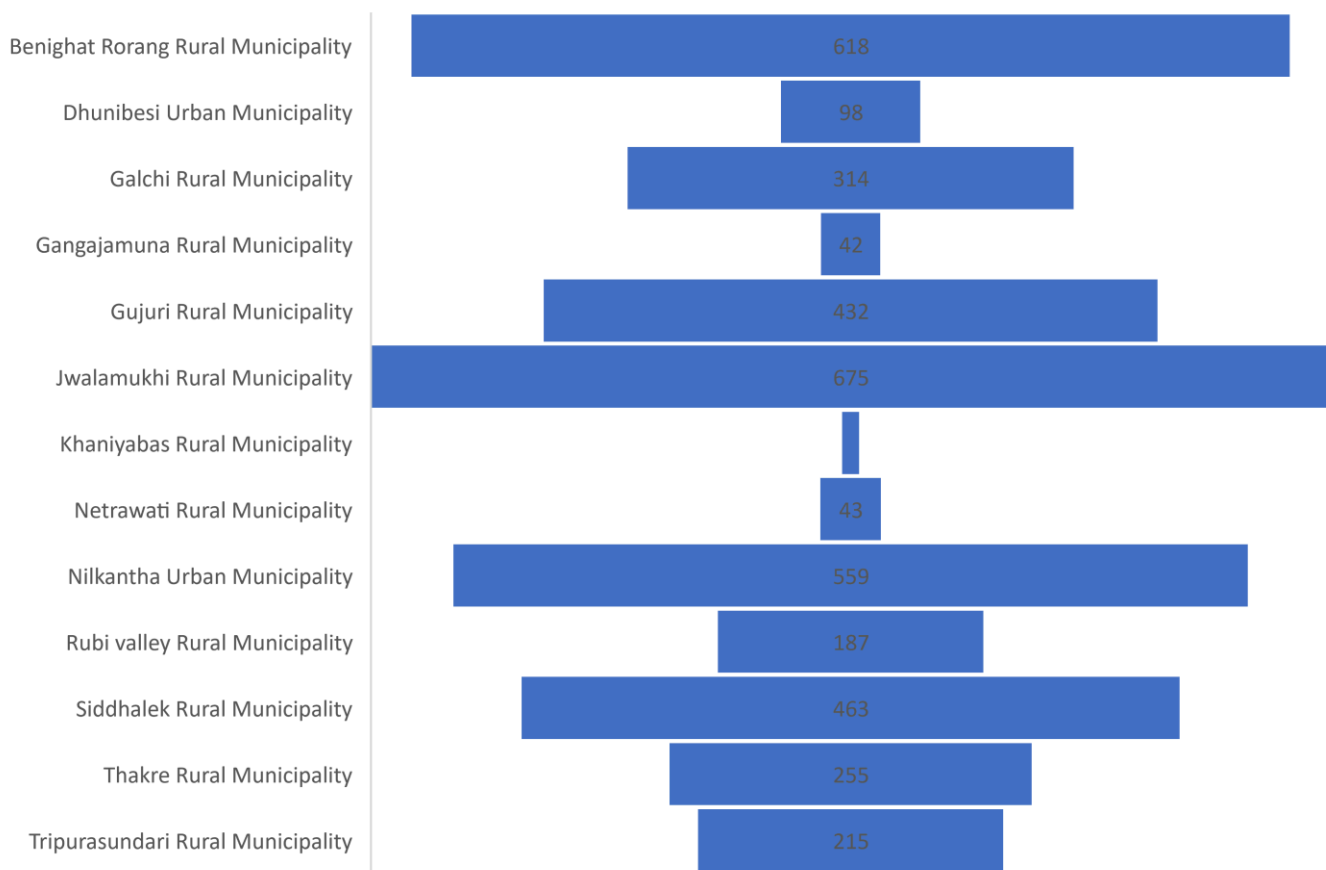

News & Updates

- District coordination Committee (DCC) conducted bi-Annual progress review and interaction program at DCC Hall, Dhading. All Palikas of Dhading presented their progress Report respectively.



Photo: Participants at bi-Annual progress review and interaction program

Updates from Partner Organizations

- According to NSET Baliyo Ghar progress report 19,240 households were directly benefitted through technical assistance, 38,933 individuals were oriented through 1628 orientation events, 2508 existing masons were trained through 84 events, 10 mason TOT, 156 individuals were trained through 5 SM training, 33 Engineers and 19 Sub engineers were participated in Basic retrofit training, 458 Radio program has been broadcast from 2 different radio/Fm stations, 656 new mason were trained through 108 event by Baliyo Ghar and 1339 masons were trained 227 OJT.
- Purnima Project support by DFID and Mott Mac Donald mainly focus on community infrastructure and supported by many partner organizations i.e. WFP, OXFARM, DCA, GEOC etc. WFP works in Foot Trail, OXFARM and DCA works in water supply while GEOC provide Engineering support in school and suspension bridge. Also, Purnima Project provide technical support to Gangajamuna RM, Khaniyabas RM and Gajuri RM with 1 Engineer and 1 RM Advisor to each palika. OXFARM completed 10 water supply schemes while 7 schemes are ongoing, and 11 schemes are ongoing supported by DCA. Foot Trail in Ruby Valley RM are yet to complete within 1 months.

- Single room status was found through survey in following VDC by NSET Baliyo Ghar
 - a) Kumpur - 783 houses are single room out of 2221 houses i.e. 35.25 %
 - b) Kalleri - 608 houses are single room out of 1996 houses i.e. 17.27 %
 - c) Khalte - 240 houses are single room out of 1390 houses i.e. 23.45 %
 - d) Nalang - 330 houses are single room out of 1407 houses i.e. 35.25 %
 - e) Jyamrung - 1189 houses are single room out of 1722 houses i.e. 69.00 %
 - f) Tipling - 578 houses are single room out of 707 houses i.e. 81.75 %
 - g) Sertung - 607 houses are single room out of 659 houses i.e. 92.10 %
 - h) Darkha - 954 houses are single room out of 1214 houses i.e. 78.58%
 - i) Marpak - 395 houses are single room out of 830 houses i.e. 47.60 %
 - j) Semjong - 165 houses are single room out of 937 houses i.e. 17.60 %
- Durable Solution presented their updates regarding Resettlement and landless, a total of 388 cases out of which 193 are solved and remaining 195 are in progress.

Joint Field Visit Report

Visit 1

Date	Location	Participants from HRRP and stakeholders	
21 st – 22 nd Feb 2019	Thakre Rural Municipality and Siddhalekh RM	• Prabin Gautam (HRRP-DC) • Sachin Sapkota (HRRP-DTC) • Khagendra Awasti (M&E)	
Objective(s)		• Palika interaction for Non-Compliance list of beneficiaries. • Collection of palika action plan with Palika/ward meeting.	
Summary		A field visit was conducted at Siddhalekh rural municipality and Thakre rural municipality regarding the priority of Palika Action Plan update and upload at palika website. The focal person of Siddhalekh rural municipality Miss. Muna had coordinated with all ward chiefs regarding preparation of palika action plan and its importance in upcoming days. As the Action Plan was in the process of finalization, we kept the email contact of Siddhalekh rural municipality IT officer Miss. Laxmi Paudel to follow as per need. Similarly, the visit was made at Thakre rural municipality where an informal talk was made between Mayor Mr. Ram Kumar Acharya and NRA field engineer regarding Thakre reconstruction action plan.	
Challenges / Issues Identified	Action Required	Responsible	Timeframe
Limited internet access and less maintenance of palika website.	Palika IT officer must have full speed internet facility.	Palika office	As soon as possible

Joint Monitoring Field Visit Report

Visit 2

Date	Location	Participants from HRRP and stakeholders
26 th - 28 th Feb 2019	DhuneBesi Rural Municipality Gajuri Rural Municipality Benighat Rorang Rural Municipality Tripurasundari Rural Municipality	• Prabin Gautam (HRRP-DC) • Sachin Sapkota (HRRP-DTC) • Sudip Shrestha (NRA/DSE) • Suvir Budhathoki (DLPIU Building) • Rabin Shrestha (DLPIU Building)

Objective(s)

- Palika level meeting and discussion on status of reconstruction.
- Housing typology observation and collection.
- Preparation of Palika's Action Plan.
- Interaction with ward beneficiaries on housing reconstruction issues and collection of success stories.
- High number of fake beneficiaries registered.
- Non-Compliance issues at these rural municipalities.
- Discussion on palika action plan at all palikas.

Summary

- A joint field visit was conducted at different palikas of Dhading regarding Palika Action Plans, Palika profile and Burning issues regarding reconstructions.

The joint monitoring field visit was conducted at Salyantar, Tripurasundari Rural Municipality with an intention to find out the fake beneficiaries. As per information there are numbers of beneficiaries who have received all three tranches without constructing their houses in salyantar vdc. DLPIU Building Team along with HRRP team survey thoroughly in different houses. An interaction program was organized with beneficiaries, ward chief and field visit team. The visit provided chances to find enquiries and verify them as per our information. Open conversation was made between local people and interactive talks were carried out regarding reconstruction and related issues.

- HRRP conducted Palika level meeting at Tripurasundari Rural Municipality in presence of Palika deputy chief, Technical Group and Beneficiaries on 27th Feb 2019. The meeting was focused on preparing Palika Action plan, Palika profile, reconstruction burning issues & challenges.



Pics: - Palika level Meeting at Tripurasundari RM

- Few case studies of vulnerable beneficiaries were collected who have yet not rebuilt their houses as being single women and disabled has added to difficulty in getting timely information on the reconstruction process, lack of easy access to banks and so on.
- Some of individuals are still not registered through grievance process and this delay of result publication from NRA has caused misunderstandings among community and palika/ward office.
- We requested them to prepare and submit the list of beneficiaries to building DLPIU, the no of houses constructed before the deployment of engineers.
- A discussion was made regarding distribution of completion certificates to those ward beneficiaries where reconstruction is high.

Challenges / Issues Identified	Action Required	Responsible	Timeframe
Construction of one roomed house are increasing in number.	One room structure needs to be discouraged as such houses may not meet the shelter	Ward office, Municipality office, DLPIU Engineers	As soon as possible
Unknown of the process on how to claim for registration under beneficiary list from non-beneficiary.	HRRP suggests step-by-step process on how they can claim it.	Ward office.	As soon as possible
Issue on delay of grievance resolving from NRA. Beneficiaries claim that they have registered grievance more than two times but, yet no result/solutions have come out.	Grievance resolved list must be provided at ward office.	GMaLI-Dhading and ward office.	As soon as possible

Joint Field Visit Report

Visit 3

Date	Location	Participants from HRRP and stakeholders
11 th - 14 th March 2019	Jwalamukhi RM, and Nilkhantha municipality – 6 (Sunaulobazar)	• Prabin Gautam (HRRP-DC) • Sanobabu Timalisina (TI-Nepal) • Khagendra Awasti (CLPIU/building-M&E)

Objective(s)

- Follow up for palika action plan.
- Identification of fake beneficiaries and interaction with beneficiaries on housing reconstruction grant reimbursement.
- Housing typology collection.
- Palika/ward level meeting on reconstruction.
- Support on preparation of non-compliance list of beneficiaries at palika office.

Summary

A joint field visit with CLPIU/building, HRRP, PIN-Nepal and TI was conducted on 12 and 13 March 2019 at Sunaulo Bazar, Nilkhantha ward no.: 6 and Jwalamukhi rural municipality. The field level visit was focused on private housing progress of these palikas where different designs of NRA volume I and II were found. It was found that many organizations has been supporting with technical assistance at these locality. They have provided engineers and social mobilizer at the ward to support beneficiary's issues and address in coordination with rural municipality and ward office.



Photo: Palika level coordination meeting at Jwalamukhi rural municipality

The chief of palika, Mr. Binodraj Timalsina mentioned that palika's reconstruction rate has speeded up and it seems that only 3%-8% beneficiaries are remained to reconstruct their houses. Some of the major points of discussion are as follows:

- a. Service provided by Bank to palika Beneficiary
Individuals registered under NRA beneficiary list who are illegible to receive government grant support amount are being delayed from bank for a long duration.
- b. Victims who have not been listed under beneficiary list from NRA
Individuals who are being left behind to be registered under NRA beneficiary list are deprived of the support for reconstruction, thus palika would like to request NRA to support it to reverify and register those individuals (real victims) as soon as possible.
- c. Palika Reconstruction Action Plan
Palika prepared its reconstruction Action Plan in support of HRRP and published it at its website.
- d. Support to establish Bank services at preferred locality for beneficiary
Palika wanted to allow reliable banks to establish its branches at an appropriate locality to facilitate beneficiary with its services so that government tranche amount could be received at convenient manner.

Also, ward level meeting at Jwalamukhi rural municipality, ward no.: 5 was conducted where ward chief Mr. Krishna Prasad Kapri mentioned that the Budhi-Gandaki submersed land households are gradually receiving final tranche amount to construct temporary structure. Gradually, the Budhi-Gandaki hydor power project office have distributed compensation amount to affected households.

Housing Typology Report



Name: - Ram Bahadur Burlakoti
Location: - Salyantar, Tripurasundari Rural Municipality
It is one storey RCC framed structure building with material used burned brick with cement mortar, its floor area is less than 1000 sqft. The beneficiary has received 2nd tranche of government grants.



Location: - Tripureshor Vdc, Tripuraundari Rural Municipality
It is one storey load bearing structure with material used stone with cement mortar, its floor area is less than 1000 sqft.



Name: - Mani Ram Tamang
Location: - Latap Ree Vdc, Gangajamuna Rural Municipality
It is two storey Hybrid structure with material used brick with cement mortar in ground floor and CGI sheet in second floor, its floor area is less than 1000 sqft. The beneficiary has received all tranche of government grants.



Name: - Uttam Tamang
Location: - Latap Ree Vdc, Gangajamuna Rural Municipality
It is two storey Hybrid structure with material used brick with cement mortar in ground floor and CGI sheet in second floor, its floor area is less than 1000 sqft. The beneficiary has received all tranche of government grants.

Case Story

Story from Semjong-8 (Tanjomane), Dhading: -

House of Nar Bahadur Tamang was severely damaged by Gorkha earthquake 2015. And he was in temporary shelter for about one and half year. And he also received first installment of rupees fifty thousand from Government of Nepal. He was planning to reconstruct house. He was confused a bit about the earthquake resistant construction. He thought that it would take huge money for Earthquake resistant construction. He had participated in Mason training organized under NSET Baliyo ghar. And yet he was confused about how to reconstruct his house. There was gap between the training which he undertook during the monsoon month August and the construction of his house in the month of November.

He was planning to construct stone masonry house in Mud mortar with wooden band. He was influenced by the neighboring C-shaped house in which CGI sheet was used in the front face. Then the mobile team of the Baliyo ghar program in Semjong VDC reached to the site and then he got an opportunity to understand about the importance of various ERCs and



Photo: House owner Nar Bahadur Tamang

various precautions he should apply during the construction time. Also, his learning from the mason training was refreshed. His whole family was convinced about the earthquake resistant construction both from the safety point of view and from getting other installments from the government. He was then getting confidence about the construction and then he started the construction work with the help of local masons. After 1 month he completed construction of his house. His was more encouraged



Photo: Use of CHUKUL in NIDAL

when the Baliyo Ghar TV program covered

his house when it was in initial construction stage.

With the use of locally available construction material, and from constant supervision of BG mobile team Mr. Nar Bahadur Tamang was able to construct an earthquake resistant house in his village. Now he is looking forward for getting other installment from the Government of Nepal. He has set an example that earthquake resistant house can be constructed with the locally available material and the cost is not too high.



Supported by: NSET-Baliyo Ghar, Dhading.
