

District Report

Dolakha

20 July to 2 August 2018

Summary of events during this period

Name of activity/event	Event date	Participants summary		Contact Person	Reference Document
		Male	Female		
July District General Coordination Meeting completed: NRA/GMaLI Dolakha completed the District General Coordination Meeting with Partner Organizations working in Dolakha. The key decisions taken in the meeting were NRA/GMaLI requested POs to verification of vulnerable households lists in Dolakha; to update name lists of beneficiaries and reconstruction status of the wards of Gaunpalikas/Municipalities of Dolakha which was not updated till date(ward chairs know the numbers of beneficiaries but they don't know/record of the beneficiaries name lists and don't know how many houses reconstructed) ; to wish the speedy recovery of the recently wounded focal person/engineer of NRA/GMaLI Dolakha Mr. Narayan Prasad Siwakoti. Additionally, POs updated the progress of their work and review of the last meeting. The meeting was chaired by Mr. Nirmal Darshan Acharya, chief, NRA/GMaLI, Dolakha.	26 July	M: 16	F: 1	dc.dolakha@hrrpnepal.org techcord.dolakha@hrrpnepal.org ravi@hrrpnepal.org	
Light Timber/IM Orientation completed in Jiri: HRRP Dolakha in coordination with NRA DLPIU (Building) Dolakha completed light timber/ manual and IM orientation in Jiri, Dolakha to the Engineers, Sub engineers, and Assistant Sub engineers of the Jiri municipality. Importantly, DSE Mr. Gopal Kharel and DLPIU (Building) information officer Mr. Bhogendra Sah addressed the issues in reconstruction in Jiri raised by the technicians working in Jiri and suggested necessary suggestions to them on the reconstruction issues. The light timber houses built by beneficiaries could not approved by the Municipality is the main issue in Jiri municipality.	20 July	M: 24	F: 1	dc.dolakha@hrrpnepal.org techcord.dolakha@hrrpnepal.org ravi@hrrpnepal.org	

Summary of events during this period

EHRP Mid-Term Review Mission Team in Dolakha: Nepal Earthquake Housing Reconstruction (NEHR) Mid-term review mission team has been visiting Dolakha. The team interacted among the NRA/GMaLI officials, DLPIU (Building/Education), District Treasury Comptroller Office (DTCO) officials. Significantly, they have visited to observe reconstruction of houses, visited Bosipma/Panipokhari (resettlement); have interacted beneficiaries, masons and engineers, schools; planning to meet local Civil Society Organizations(CSOs) tomorrow(3 Aug); field trip of Third Party Monitoring Agency(TPMA). The team comprised of NRA (Central officials), CLPIU, and World Bank Officials.	1-3 August	M: 6	F: 2	dc.dolakha@hrrpnepal.org techcord.dolakha@hrrpnepal.org ravi@hrrpnepal.org	
Orientation on NRA 5W completed : HRRP Dolakha in coordination with NRA Dolakha completed orientation on NRA 5W. Participants from DLPIU (Building/Education), POs oriented about the 5W. Significantly, the issues raised by the participants were recorded/addressed by the HRRP Dolakha team.	24 July	M: 20	F: 1	dc.dolakha@hrrpnepal.org techcord.dolakha@hrrpnepal.org ravi@hrrpnepal.org	
NRA DLPIU(Education) monitored the Schools building: NRA DLPIU (Education) officials monitored Dhungeshwori secondary school building supported by the Asian Development Bank in Manedanda Bazaar, Jiri municipality, Dolakha. The school construction work has been in progress instead of rainfall.	20 July	M:3	F: 0	dc.dolakha@hrrpnepal.org techcord.dolakha@hrrpnepal.org ravi@hrrpnepal.org	
Civil Society Organizations and local government talk programme concluded: INSEC Dolakha in the support of FHI 360/USAID organized a talk programme among civil society organizations and local government representatives in Dolakha. The deputy mayor of the Bhimeshwor municipality and other local representatives and civil society members including media persons, HRRP DC participated in the programme. The participants concluded that the coordination and cooperation among the local government and CSOs	24 July	M: 21	F: 9	dc.dolakha@hrrpnepal.org techcord.dolakha@hrrpnepal.org ravi@hrrpnepal.org	

Summary of events during this period

should be essential for the progress of Dolakha.					
Orientation on Upper Tamakoshi Share collection to the local level representatives completed : On 1 st August, Energy, Water Resources and Irrigation Minister of federal government, Mr. Barsha Man Pun inaugurated a programme on share collection orientation to the local level representatives organized by District Coordination Committee (DCC), Dolakha. He asserted that the all Dolakhalis who could purchase share or not should provide shares. Further, he assured that he will work on the road upgrading of the Dolakha. He handover the share form to the two most remote Gaunpalika's ward chairs Mr Hiranya B Gurung, Bigu Gaunpalika-1 and Chhiring Sherpa, Gaurishankar-1 respectively telling them to not leave any household to fill the share form. The orientation programme was attended by all Mayors, deputy mayors and 74 ward chairs of the 9 local bodies of Dolakha.	1 August	M: 142	F: 54	dc.dolakha@hrrpnepal.org techcord.dolakha@hrrpnepal.org ravi@hrrpnepal.org	
5 Mason Training completed in parallel: In Dolakha, 5 Mason training completed in the district in this reporting period. Altogether 165 masons participated in the training. The training held in Chilankha, Babare, Bigu and Japhe of the district. With this training, total 71 mason training producing 2100 masons so far completed by NRA/GMaLI, Bigu Gaunpalikas, Bhimeshwor Municipality with the support of Baliyo Ghar Programme/USAID Nepal. From this training enhanced the technical knowledge and skills of the local masons.	22-29 July(some are ongoing)	M:152	F:13	dc.dolakha@hrrpnepal.org techcord.dolakha@hrrpnepal.org ravi@hrrpnepal.org	
4 Days Training of Engineers on Seismic Retrofitting of Rural Housing in Nepal completed: 4 Days residential training of Engineers on Seismic Retrofitting of Rural Housing in Nepal is ongoing in Charikot to the Engineers working in local bodies in Dolakha. The training was organized by DUDBC (Building) with support from UNOPS/Build Change.	July 31-Aug 3	M:30	F: 0	dc.dolakha@hrrpnepal.org techcord.dolakha@hrrpnepal.org ravi@hrrpnepal.org	

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location	Organizer	Contact Person
NRA, CLPIU, World Bank Mid-term Review Mission team interaction with CSOs working in Dolakha	3 August 2018, NRA GMaLI Meeting Hall, Simpani, Charikot Time: 8:30 am- 10:00 am	NRA/GMaLI, Dolakha	dc.dolakha@hrrpnepal.org techcord.dolakha@hrrpnepal.org ravi@hrrpnepal.org
Training of Engineers on Seismic Retrofitting of Rural Housing in Nepal	5-8 August 2018, Hotel Pawan, Charikot	NRA/UNOPS/Build Change	dc.dolakha@hrrpnepal.org techcord.dolakha@hrrpnepal.org ravi@hrrpnepal.org

News & Updates

दोलखामा ३६ हजार घर पुनर्निर्माण

रवीन्द्र गौतम | चरकोट

निजी आवास पुनर्निर्माण सुरु भएको २८ महिनामा दोलखा जिल्लामा साढे ३६ हजार घरको पुनर्निर्माण सम्पन्न भएको छ।

राष्ट्रिय पुनर्निर्माण प्राधिकरण दोलखाको ७७५ असार बसालसम्मको तथ्यांकअनुसार कुल सम्पत्ता गरेको लक्ष्यमाथि ३६ हजार ६ सयले निजी आवास पुनर्निर्माण सम्पन्न गरेका हुन्। निजी आवास पुनर्निर्माणका लागि असार महानगरमा दोलखामा ६० हजार ७ सय ४६ ले अनुदान सम्पन्न गरेको प्राधिकरण चरकोटले जनाएको छ। निजी आवास अनुदानका लागि कोष तथा लेखाविभाग कार्यालय चरकोटबाट हालसम्म १३ अर्ब ५० करोड ५९ लाख रुपैयाँ निकासी भएको पाइएको छ।

दोलखा जिल्लाका ६० दशमलव २५ प्रतिशतले निजी आवास पुनर्निर्माण सम्पन्न गरेको राष्ट्रिय पुनर्निर्माण प्राधिकरण चरकोटका प्रमुख निर्देशन आवासले जानकारी दिए। असार ३१ गतेसम्मको प्रति प्रतिवेदनअनुसार ४७ हजार ७ सय

निजी आवास पुनर्निर्माणका लागि असार महानगरमा दोलखामा ६० हजार ७ सय ४६ ले अनुदान सम्पन्न गरेका थिए।

६७ लाखमाथि ले दोस्रो किस्ता लिएको पाइएको छ। त्यसैगरी, ५८ हजार ६ सय १७ ले पहिलो किस्ताबाट लिएको अनुदान बुझेको कार्यालयको तथ्यांक छ। प्रत्येकवारलेको सुचीमा परेका ६ सय ३७ लक्षमाथि २५ जनाले मात्र सम्पत्ता गरेको पाइएको छ।

भूकम्पपछि रहेको भवन निर्माण मापदण्ड स्वीकृत हुनुअघि नै निर्माण सम्पन्न भइसकेका ६ हजार ८ सय ९० घरमध्ये २ हजार २८ घरको पनि निर्माण किस्ताका लागि सिपअर्थस भइसकेको कार्यालय प्रमुख आचार्यले बताए।

36,000 households constructed so far (Source: Rabindra Gautam, Correspondent, Annapurna Post Daily)

7000 beneficiaries added after the grievance addressed in Dolakha:

Total 7,238 families' grievances addressed so far. Among them, 5728 families added to enlist in beneficiaries list and 1510 families added in retrofitting list. Now, in total 68,561 families listed in beneficiaries list and 2,147 families in retrofitting list. The 1,047 beneficiaries list added in Bhimeshwar municipality the most in local levels and retrofitting list is 491 the most (source: edolakha.com).



Karobar Daily News on the rise of Yarsa settlement, in Baiteshwar Gaunpalika which was completed in June, 2018 published recently (reported by Dil Sagar Paudel, Correspondent)

Field Visit /Joint Field Monitoring Visit Reports

Visit 1

Date	Location	Participants from HRRP and stakeholders
Date: 25 th July 2018	Location: Panipokhari, Bhimeshwar Municipality-1	Participants from HRRP and Stakeholders
Objective(s)	- To discuss the reconstruction progresses of Integrated Settlement in Panipokhari; - To find out the grievances of the Thami community in the integrated settlement; - To advocate for the speedy reconstruction for the integrated settlement among concerned stakeholders	

Summary

We visited at Bhimeshwor Municipality-1, Panipokhari where integrated settlement for 78 HHs has been proposed for construction. The households plots construction work has been in progress with the contractor however the beneficiaries have been concerning about the quality of the work of contractor.

The Thami community in Bosimpa faced at least 3 landslides triggered in their remembrance so far including 2015 earthquake period. Currently, they have been staying in temporary shelters paying around NRs 45,000 rent/year.

The lactating and pregnant women, children have been facing difficulties due to rainy season; not partitioned narrow rooms shared with other family members.

There is no electricity, drinking water, modern latrines facilities in the temporary shelter.

Further, the integrated settlement members worried about the quality of the plots area construction which is ongoing.

Worriedly, they have not reliable sources for livelihood. Their agriculture hardly sufficient them for 2 months.

They are eagerly waiting for the houses built by the support of Nepal government and any other organizations.

Challenges / Issues Identified

They have been staying in temporary shelters and permanent houses construction are uncertain

Action Required

Speed up the reconstruction of the houses of them with special provisions/priority

Responsible

NRA/DPs

Timeframe

Till the integrated settlement completed

Photos



Figure 1 : Women and children in front of their temporary shelter Pic: Ravi Pajiyar



Figure 2 : Proposed Integrated settlement area under construction in Panipokhari Pic: Ravi Pajiyar

Housing Typology Report



Caption: At Jilu, 4 No ward of Bhimeshwar municipality, dry Stone Masonry in ground floor and light timber structure in first floor building has been constructed by Mr. Ram Bahadur Shrestha. He has received second tranche till date.




Caption: Dry Stone Masonry Building of one story has been constructed in Jilu, 4 No Ward of Bhimeshwar Municipality. Mr. Kedar Bahadur Shrestha is the house owner and he has received all the three tranches of housing reconstruction grant.



Caption: Two Buildings constructed with in same foundation. Mr. Lava Shrestha and Mr. Bishnu Shrestha are the house owners. They have received second tranche of housing reconstruction grant. Building lies in the 4 no ward of Bhimeshwar Municipality.



Caption: This Building belongs to Mr. Bikesh Shrestha of Jilu, 4 no ward of Bhimeshwar Municipality and he has received first tranche also the second tranche is in process.

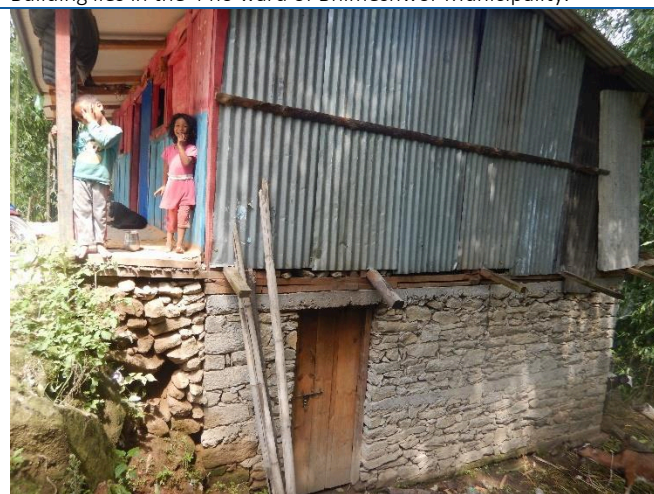

Caption: Stone Masonry in ground floor and Light timber structure in First floor building has been constructed in Jilu, 4 no ward of Bhimeshwor Municipality. Mr. Ganga Bahadur Khatri is the house owner. Initially, one story was constructed, and he received all three tranches of housing reconstruction grant. After that, he felt lack of space for his family and added another story of light timber structure to meet the space requirement.



Caption: This building belongs to Mr. Bal Krishna Khatri of Jilu, 4 no ward of Bhimeshwor Municipality where DPC work has been finished and waiting for the material delivery from local crusher for the construction of superstructure. He has received first tranche and for second tranche inspection form has been recently filled up by DLPIU Engineer.

Caption: This Building belongs to Mr. Shanta Khatri of Jilu, 4 no ward of Bhimeshwor Municipality where foundation work for RCC building is ongoing. He has received first tranche. Trained masons have been employed in the construction of building.



Caption: Excavation and laying of foundation stone work is in progress of a one-story stone masonry building at Jilu, 4 no ward of Bhimeshwor Municipality which has been given to a contractor from Mugu district for the construction. Contractor has not received any kind of mason training till date but has constructed more than 5 houses till date.

Challenge

DLPIU (Building) Engineers told that Jiri municipality is not approving building drawing of Light timber structures saying that timber structures are temporary not permanent, so Engineers are facing problem in forwarding the inspection file for tranche release. Further, Municipality has formed a rule that for the release of second and third tranche building drawing should be approved. Thus, Engineers are in dilemma regarding these provisions.

Way Forward

An understanding has been made to organize a meeting with the officials of Jiri municipality including DLPIU (Building), GMaLI, M&E and HRRP to make them clear about Light Timber Frame Structure.

Case Study

Panipokhari: Towards Integrated Settlement

Panipokhari, which situated in ward no. 1 of Bhimeshwor Municipality have been planning to construct the integrated settlement for 78 households. The community is Thami which is enlisted as indigenous nationalities in Nepal.



The contractor has been constructing the plots for houses.

The Thami community has just shifted in the midst of rainy season to the temporary shelters built by the CGI sheet supported by the NRA.

Manisha Thami, 20, studying 12 told us that they have been facing difficulties in the temporary shelter. Further, she added, “we (female) have been facing difficulties to stay with the same room (temporary shelter) with male family members. In one cottage brothers and parents have been living together. She added, ‘Even difficult to changing clothes’. Further, Sumita Thami told that the temporary shelter have not partitioned and weighted ground, so this is hard for us women especially lactating and pregnant and children. Currently, there are 2 pregnant and 3 lactating women. Further, she told, “children have to take the health post in every

week due to pneumonia, cold suffering caused by these temporary makeshift.” Kumar Thami, the chair of the proposed Integrated settlement told in the discussion with us that in Kartik, Mangsir, Poush (during winter season), this is hard to stay in the temporary makeshift. They have to pay around NRs 45,000 rent for the land/year.

The nearby health post situated in one hour walking distance. Additionally, they constructed a school which runs till class 3 near by the temporary shelters. The nearby 10+2 school is one and half hour walking distance from their settlement. There are 60 children who have been going schools.

There are not any facility for light and drinking water. They built few temporary latrines for them. For drinking water, currently, they depended on the nearby water source which is available in only rainy season.

After earthquake, NGOs distributed some soaps, sanitary pads and utensils for women at once.

They told that the three landslides triggered on their settlements that including 2044 BS (1987), 2015 so far. After the landslides they moved from one place to another for safe settlement.

For living, most of them have been doing labor work for fulfill their daily needs. Agriculture hardly covers their household need for 2 months. The labors came from outside districts have taken their jobs because they are cheap than them after earthquake.

Some of the organizations have interested to support to construct the houses for them. But the concrete proposal has not been yet. Firstly and most significantly, the under construction integrated settlement plots construction must be maintain quality, the members of the integrated settlement worry about the quality of the construction of the plot area, which they have been seeing daily but couldn't do anything to maintain the quality of the construction.

They had received first tranche NRs 50,000 each household. Kumar Thami, chair, integrated settlement told that if any Nepal government or any other organization that commit and construct the earthquake resilient houses for them they are ready to return the first tranche of NRs 50,000 which each household received.

According to the NRA/DLPIU (Building) Dolakha, the integrated settlement file has forwarded to the central level and after the decision came from Kathmandu. They will speed up the integrated settlement work.

As NRA prepared the Directives of Integrated Settlement Development 2018(2074 BS) we could hope that they will be able to have earthquake resilient houses in the integrated settlement within this year.
