

Monthly District Report

Kavrepalanchok, Sindhupalchok

9 May - 13 June 2019

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Kavrepalanchok	Technical Meetings and Info Packs distribution at palika level with Ghumti Toli	20-23 May	Namobuddha NP, Mandandeupur NP, Panchkhal NP, Chaurideurali GP, Bhumlu GP, Temal GP, Roshi GP	reshma@hrrpnepal.org	Field Visit Section below
	Technical Meetings and Info Packs distribution at palika level with Ghumti Toli	28-29 May	Khanikhola GP	reshma@hrrpnepal.org	Field Visit Section below
	5W Update	25 May	NA	im.kavrepalanchok@hrrpnepal.org	GD
	District Facilitation Meeting	3 June	DCC Hall, Dhulikhel	reshma@hrrpnepal.org	Meeting Minutes
	Number of Staff Survey	3 June	NA	reshma@hrrpnepal.org	Mail
	Construction Material Cost Survey	3 June	NA	im.kavrepalanchok@hrrpnepal.org	Mail
	Contact List Update	4 June	NA	im.kavrepalanchok@hrrpnepal.org	GD
	Collection of data on POs who have signed tripartite agreement with NRA to work in NRA and submission of same to GMALI	6-10 June	NA	reshma@hrrpnepal.org	NA
	Meetings for Urban Housing Reconstruction Status Update	12-13 June	Banepa NP, Ward 5,6,7,8,9	reshma@hrrpnepal.org	NA
	Data Cleaning Support, Data Reconciliation Support and Grievance Handling Support at GMALI	11 May-13 June	NA	reshma@hrrpnepal.org	NA

Summary of events during this period

Districts	Name of activity/event	Event date	Location (District, Municipality)	Contact Person	Reference Document
Sindhupalchok	Technical Meetings at palika level with Ghumti Toli	8-9 May	Bhotekoshi RM, Barhabise Municipality, Tripura Sundari RM	pradip.sharma@hrrpnepal.org	Field Visit Section below
	District Facilitation and Coordination Meeting	23 May	DCC Hall, Chautara	pradip.sharma@hrrpnepal.org	Meeting Minutes
	Number of Staffs Survey	27 May	NA	pradip.sharma@hrrpnepal.org	Mail
	Construction Material Cost Survey	3 June	NA	pradip.sharma@hrrpnepal.org	Mail

Upcoming Events & Meetings

Name of activity/event	Date, Time, and Location (District, Municipality)	Organizer	Contact Person
Meetings for Urban Housing Reconstruction Status Update	9AM-5PM, 17-18 June, Dhulikhel NP, Ward 5, 6, 7, 8, 9	HRRP Kavre	reshma@hrrpnepal.org
Meetings for Urban Housing Reconstruction Status Update	9AM-5PM, 19-20 June, Panauti NP, Ward 4, 5, 6, 7, 8	HRRP Kavre	reshma@hrrpnepal.org
Palika level meeting at Panchkhal NP to collect updates on retrofit and urban issues	9AM-5PM, 24 June, Panchkhal NP	HRRP Kavre	reshma@hrrpnepal.org
Palika level meeting at Banepa NP to collect updates on retrofit and urban issues	9AM-5PM, 27 June, Panchkhal NP	HRRP Kavre	reshma@hrrpnepal.org
Joint Monitoring Field Visit to Roshi GP	9AM-5PM, 3-4 July, Roshi GP	HRRP Kavre	reshma@hrrpnepal.org

Tranche Status (Kavrepalanchok)

Table of Tranche Status: As of 12th June 2019


Municipality	Reconstruction				Retrofit			Grievances	
	Eligible HHs	1st Tranche	2nd Tranche	3rd Tranche	Eligible HHs	1st Tranche	2nd Tranche	Registered	Addressed
Banepa NP	7,129	6,371	3,266	2,392	276	77	2	2226	2031
Bethanchowk GP	4,377	3,775	2,897	1,722	553	73	0	1202	1202
Bhumlu GP	6,208	5,842	4,947	3,963	89	14	1	1038	971
Chaurideurali GP	6,417	5,558	4,230	2,648	442	46	0	1578	1517
Dhulikhel NP	6,014	5,233	2,954	1,894	376	40	0	2151	1919
Khanikhola GP	2,864	2,740	2,238	914	233	43	0	683	681
Mahabharat GP	2,963	2,875	2,422	1,623	226	143	1	1075	1055
Mandandeupur NP	9,237	8,531	6,908	4,825	157	25	0	2300	1762
Namobuddha NP	7,659	6,325	3,537	2,107	700	20	0	2814	2296
Panauti NP	9,960	8,978	6,391	4,147	404	110	14	3041	2932
Panchkhal NP	9,254	8,115	4,719	3,302	862	128	0	2874	2851
Roshi GP	6,433	5,480	4,165	2,507	764	129	0	2257	2203
Temal GP	4,850	4,176	3,119	2,081	598	106	2	2101	2069

Graph of Tranche Status: As of 12th June 2019

Reconstruction- Tranche Status




Graph for Retrofitting Status: As of 12th June 2019

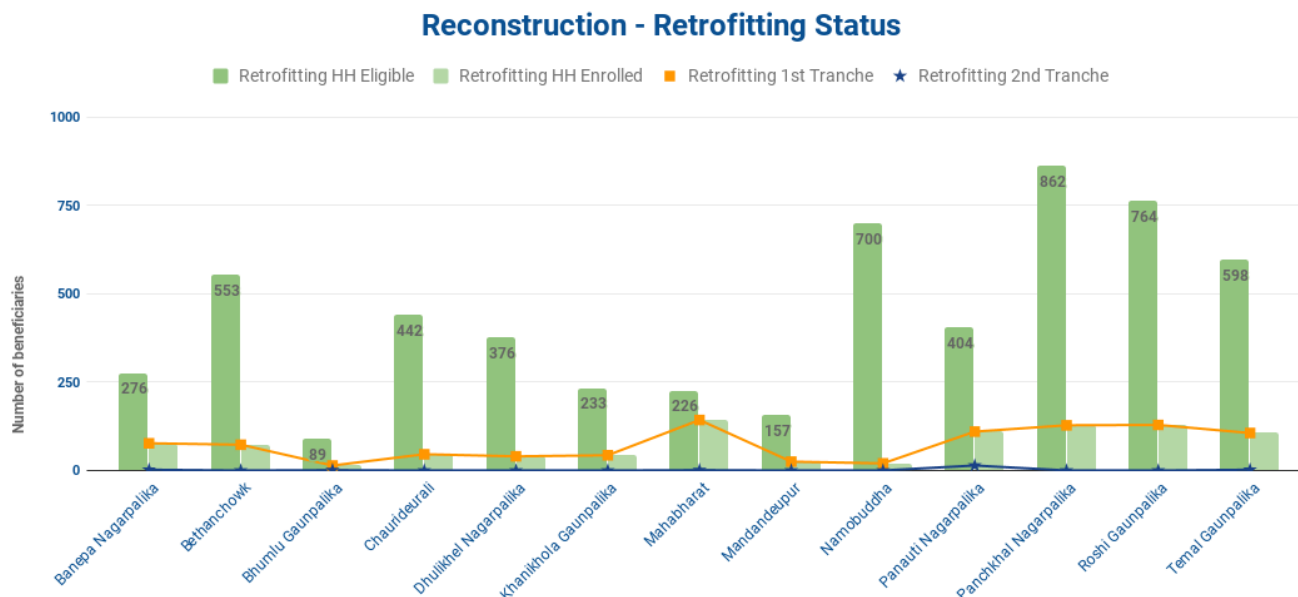


Tranche Status (Sindhupalchok)

Graph of Tranche Status: As of 12th June 2019

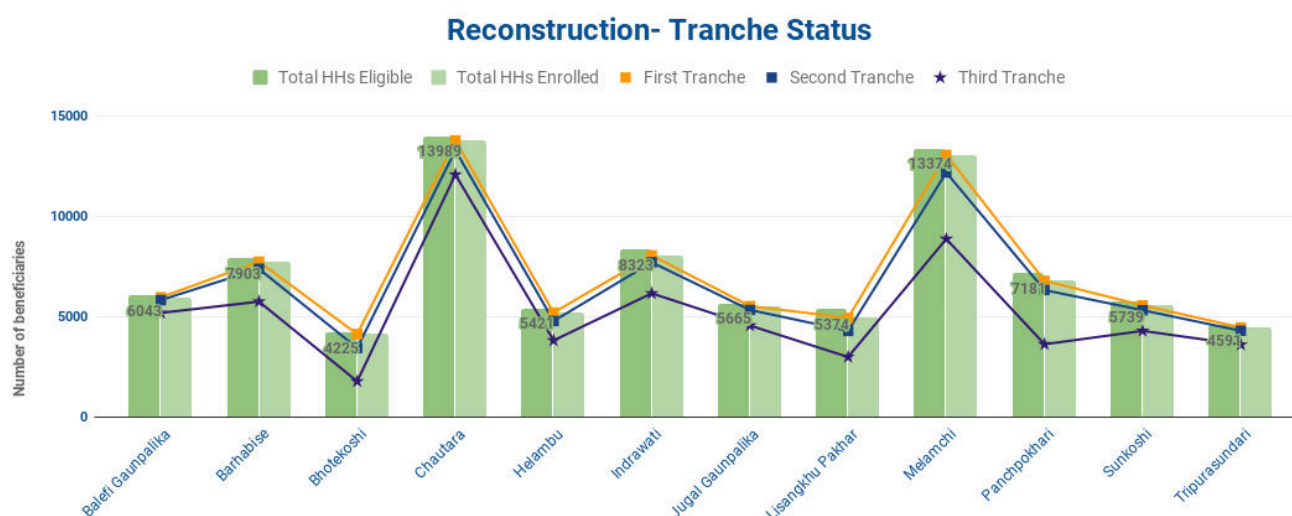

Graph for Retrofitting Status: As of 12th June 2019

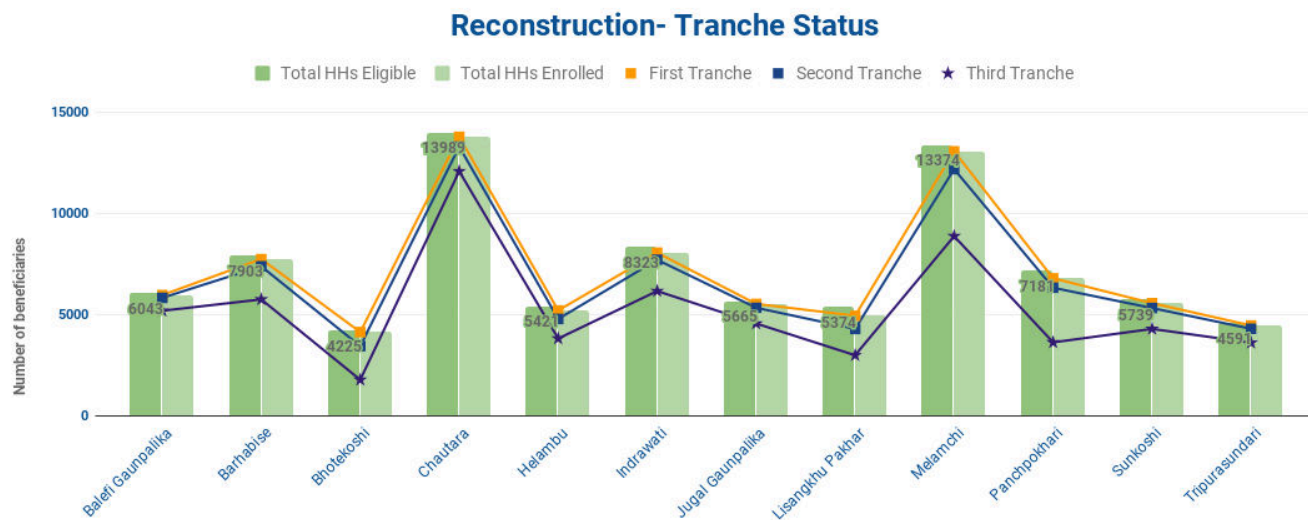

Field Visit Report (Kavrepalanchok)

Visit 1

Date	Location	Participants
20-23 May 2019 28-29 May 2019	Namobuddha NP, Mandandeupur NP, Panchkhal NP, Chaurideurali GP, Bhumlu GP, Temal GP, Roshi GP, Khanikhola GP	M&E Consultant Roshan Kesari, MIS Officer Arun Bhandari, DSE Jyotshana Shrestha, DSE Swapnil Ojha, Er. Reena Suwal, Er. Ranjana Acharya, Er. Pradeep Basnet, HRRP Reshma Shrestha, HRRP Ishor Neupane
Objective(s)	- Technical meeting with all the technical persons of respective palikas on case-loads, third inspection and CS Entry. - Info pack distribution and Contact list update of palikas.	

Why was the visit carried out in this location?

Under the direction of CLPIU/Building, DLPIU/Building Kavre formed a Ghumti Toli and scheduled palika level visits and meetings to all the thirteen palikas of the district. HRRP Kavre joined the team to eight of the palikas with an extra objective to brief and share palika profiles along with updating the palika contact list.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

NA

Summary

Field Visit:

- No. of HHs visited: 8
- No. of meetings with engineers: 8
- No. of meetings with local officials: 0

Meeting: [Meeting Minutes Link](#)

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe
Low progress of case load inspection	Complete the inspection and CS Entry by Jestha 2076	Complete the inspection and CS Entry by Jestha 2076	Ward Engineers	Jestha 2076
Low progress third inspection	Complete the third inspection of 60-75% beneficiaries who have received third tranche by Asadh 2076	Complete the third inspection of 60-75% beneficiaries who have received third tranche by Asadh 2076	Ward Engineers	Asadh 2076

Photos



Ghumti Toli technical meeting with technical persons of all wards of Panchkhal NP at Panchkhal NP Hall.



Ghumti Toli technical meeting with technical persons of all wards of Khanikhola GP at Khanikhola GP Hall.

Field Visit Report (Sindhupalchok)

Visit 1

Date	Location	Participants
8-9 May 2019	Bhotekoshi RM, Barhabise Municipality, Tripura Sundari RM	DLPIU Building Focal Person Rakes Dev, MIS Officer Binod, DLPIU Engineer Sunita Shrestha HRRP Pradip Sharma Municipality Chairperson
Objective(s)	- Technical meeting with all the technical persons of respective palikas on case-loads, third inspection and CS Entry. - Info pack distribution and Contact list update of palikas.	

Why was the visit carried out in this location?

Under the direction of CLPIU/Building, DLPIU/Building Sindhupalchok formed a Ghumti Toli and scheduled palika level visits and meetings to the above local levels.

'If this municipality / ward was visited previously, please provide dates of previous visits and links to relevant district reports'

NA

Summary

Field Visit:

- No. of HHs visited:19
- No. of meetings with engineers:3
- No. of meetings with local officials:3

Meeting: Meeting Minutes Link

Challenges / Issues Identified	Solutions Provided	Decision Taken	Responsible	Timeframe

Photos



Ghumti Toli technical meeting with technical persons of all wards of Tripura Sundari RM NP at Tripura Sundari RM Hall.



District Facilitation and Coordination meeting with all stakeholders at DCC Hall Chautara.

Housing Typology Report



Address: Kavrepalanchok, Bethanchok-1

Building Typology: Brick in Cement

Description: Purna Bahadur Syangtan constructed two roomed earthquake house besides his pre earthquake house and is yet to move to the reconstructed house. He plans to shift bed rooms in the new house and conduct other activities in the pre earthquake house.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Khanikhola-5

Building Typology: Hybrid Structure

Description: Ram Krishna Raut had his house non-compliant for the upper storey and technical persons suggested cross bracing which still does not meet the standards. He has received second tranche of housing reconstruction grant.

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Khanikhola-5

Building Typology: Stone in Cement

Description: Hem Lal Bajgai

Photographed By: Reshma Shrestha



Address: Kavrepalanchok, Khanikhola-5

Building Typology: Hybrid Structure

Description: Khada Nanda Acharya is under the process to shift to his newly constructed house and has received all three tranches of housing reconstruction grant.

Photographed By: Reshma Shrestha

Housing Typology Report



Address: Sindhupalchok, Bhotekoshi GP-5

Building Typology: Brick in Cement

Description: The house owner Purna Raj Shakya has received all tranches of housing reconstruction grant for his two roomed structure.

Photographed By: Pradip Sharma



Address: Sindhupalchok, Lisankhupakhar GP-4

Building Typology: Brick in Cement

Description: The house owner Chandra Lama has received all tranches of housing reconstruction grant for his two roomed structure.

Photographed By: Pradip Sharma



Address: Sindhupalchok, Lisankhupakhar GP-4

Building Typology: Brick in Cement

Description: The house owner Dawa Ghyamju Lama has received all tranches of housing reconstruction grant for his two roomed structure.

Photographed By: Pradip Sharma



Address: Sindhupalchok, Lisankhupakhar GP-4

Building Typology: Brick in Cement

Description: The house owner Dev Dorje Lama has received all tranches of housing reconstruction grant for his two roomed structure.

Photographed By: Pradip Sharma

Questions Collected

Question	Who Asked the Question?	Response Provided (By Whom)
Can non beneficiaries apply for resurvey and reverification?	Non beneficiary	The only process for non-beneficiary as listed by NRA is to go through the Appellate Process.
What is the deadline for receiving third tranche?	Beneficiary	Kavre district has set the deadline for beneficiaries who received second tranche within Chaitra 2075 as Falgun 2076.

Challenges and Way Forward

Challenge	Way Forward
Data Discrepancy during reconciliation of POs support	Request Ujyalo Gaun Nirman Abhiyan and Caritas Nepal to provide the required beneficiary details for the reconciliation
